


# SCOUT REPORT

## NEW MEXICO OIL CONSERVATION COMMISSION

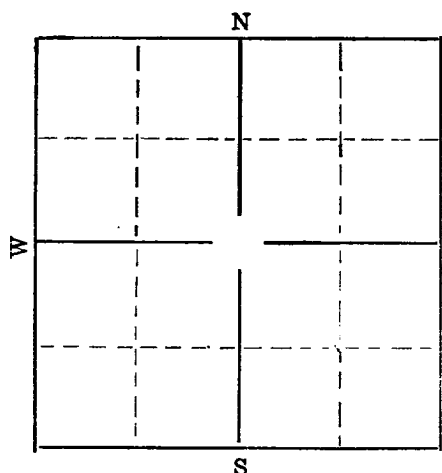

### AMOUNT CASING & CEMENTING RECORD

| Size   | Feet | Inches | Sax<br>Cement |
|--------|------|--------|---------------|
| 10 3/4 | 238  |        | 125           |
| 6 7/8  | 2978 |        | 600           |
|        |      |        |               |
|        |      |        |               |
|        |      |        |               |
|        |      |        |               |
|        |      |        |               |
|        |      |        |               |

### TUBING RECORD

|              |
|--------------|
| 2" Hy @ 3230 |
|              |
|              |
|              |

PACKER

Company Great Western Prod.

Farm Name State N Well No. 2

Sec. 18 Twp. 13 Range 32 County Lea

Feet from Line: 660 N. S. 660 E. W.

Elevation 4374 Method  

Contractor  

Spudded 8-2-47 Completed 9-15-47

### ACID RECORD Gals.

|                     |       |
|---------------------|-------|
| TA                  | TG    |
| TX                  | TSA   |
| TCA                 | TGI   |
| BX                  | TYo   |
| TY                  | TABo  |
| TSR                 | TPenn |
| Top Pay <u>3045</u> | TQ    |
|                     | TOrd  |

### SHOOTING RECORD

| No. of Quarts | From | To |
|---------------|------|----|
| No. of Quarts | From | To |
| S/            | S/   | S/ |
| S/            | S/   | S/ |
| S/            | S/   | S/ |

| Date |                                         | Date |  |
|------|-----------------------------------------|------|--|
| 8-6  | JD 260 RB WOC                           |      |  |
| 8-13 | JD 3025 a Moving in cable<br>tools      |      |  |
| 8-20 | JD 3060 a Prep to test 1000'<br>24 hrs. |      |  |
| 8-27 | Intg.                                   |      |  |
| 9-3  | Rigging up pump                         |      |  |
| 9-11 | Run rods                                |      |  |
| 9-24 | JD 3060 a S.P. Pump<br>60 BOPD          |      |  |

