

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPLI
(Other instructions
verse side)

Form approved.
Budget Bureau No. 1004-0135
Expires August 31, 1985

88240

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug back to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals.)

1. OIL WELL ☒ GAS WELL ☐ OTHER ☒ <i>Injection</i>	7. UNIT AGREEMENT NAME <i>MCA</i>
2. NAME OF OPERATOR <i>Conoco Inc.</i>	8. FARM OR LEASE NAME <i>MCA Unit Bty 3</i>
3. ADDRESS OF OPERATOR <i>P. O. Box 460, Hobbs, NM 88240</i>	9. WELL NO. <i>203</i>
4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements. See also space 17 below.) At surface <i>Unit P</i> <i>660' JSL & 660' JEL</i>	10. FIELD AND POOL, OR WILDCAT <i>Mariamar A-SA</i>
14. PERMIT NO. <i>Not available</i>	11. SEC. T., R., M., OR BLK. AND SURVEY OR AREA <i>Sec. 27, T17S, R32E</i>
15. ELEVATIONS (Show whether DP, RT, GR, etc.)	12. COUNTY OR PARISH <i>Lea</i>
	13. STATE <i>NM</i>

16. Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

TEST WATER SHUT-OFF

FRACTURE TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other) *P + A*

PULL OR ALTER CASING

MULTIPLE COMPLETION

ABANDON*

CHANGE PLANS

SUBSEQUENT REPORT OF:

WATER SHUT-OFF

FRACTURE TREATMENT

SHOOTING OR ACIDIZING

(Other)

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

(NOTE: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

1. M&L RU. GIH w/4-3/4" bit, 5-1/2" CSG scraper + 2-3/8" workstring. Scrape CSG from Surface to 2625'. Circ. w/75 bls mud. Shoot 4 squeeze holes at 2175'. Set retainer @ 2150'. Pressure test to 500 psi. Attempt to establish pump-in rate at 2175 psi.

2. If pump-in rate established pump 75 SXS Class C Cement w/2% CaCl2 below retainer. Spot 25 SXS cement. If no pump-in rate established Squeeze above Set zone - set retainer at 700', pump 50 bls 2% KCl + monitor for communication. If communication exists mix + pump 75 SXS Class H Cement w/3% CaCl2 below retainer, spot 25 SXS above retainer. If no communication establish pump-in rate + pump 2 bls fresh water tagged with Rhodine 131. Squeeze annulus w/65 SXS Class H w/3% CaCl2. Mix + pump 25 SXS Class H + spot 25 SXS cement on top.

18. I hereby certify that the foregoing is true and correct

SIGNED *John Finney* J. FINNEY

TITLE *Administrative Supervisor*

DATE *March 6, 1987*

OFFICE OF THE GENERAL OF STATE OFFICE USE

SIGNED *John Finney* J. FINNEY

TITLE *Administrative Supervisor*

DATE *3-26-87*

COMMENTS OF APPROVAL, IF ANY:

*See instructions on Reverse Side

19. The Bureau of Land Management makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

BLM-Carlsbad (6) ARCO (2) AMOCO (2) Chevron (1) File

RECEIVED


MAR 23 1987

OCD

HOEBS OFFICE

3. Spot 26 set Class H w/3% CaCl₂ Cement plug from 200' to surface.
Cut off csg at base of collar or 3' below ground level. Fill csg from
Cement plug back to surface w/sand, cement or gravel. Weld a 1/4" steel
plate over wellbore.
4. Install P+A marker, rig down + clean location.
5. Proposed P+A attached.

MCA No. 203
Proposed P&A

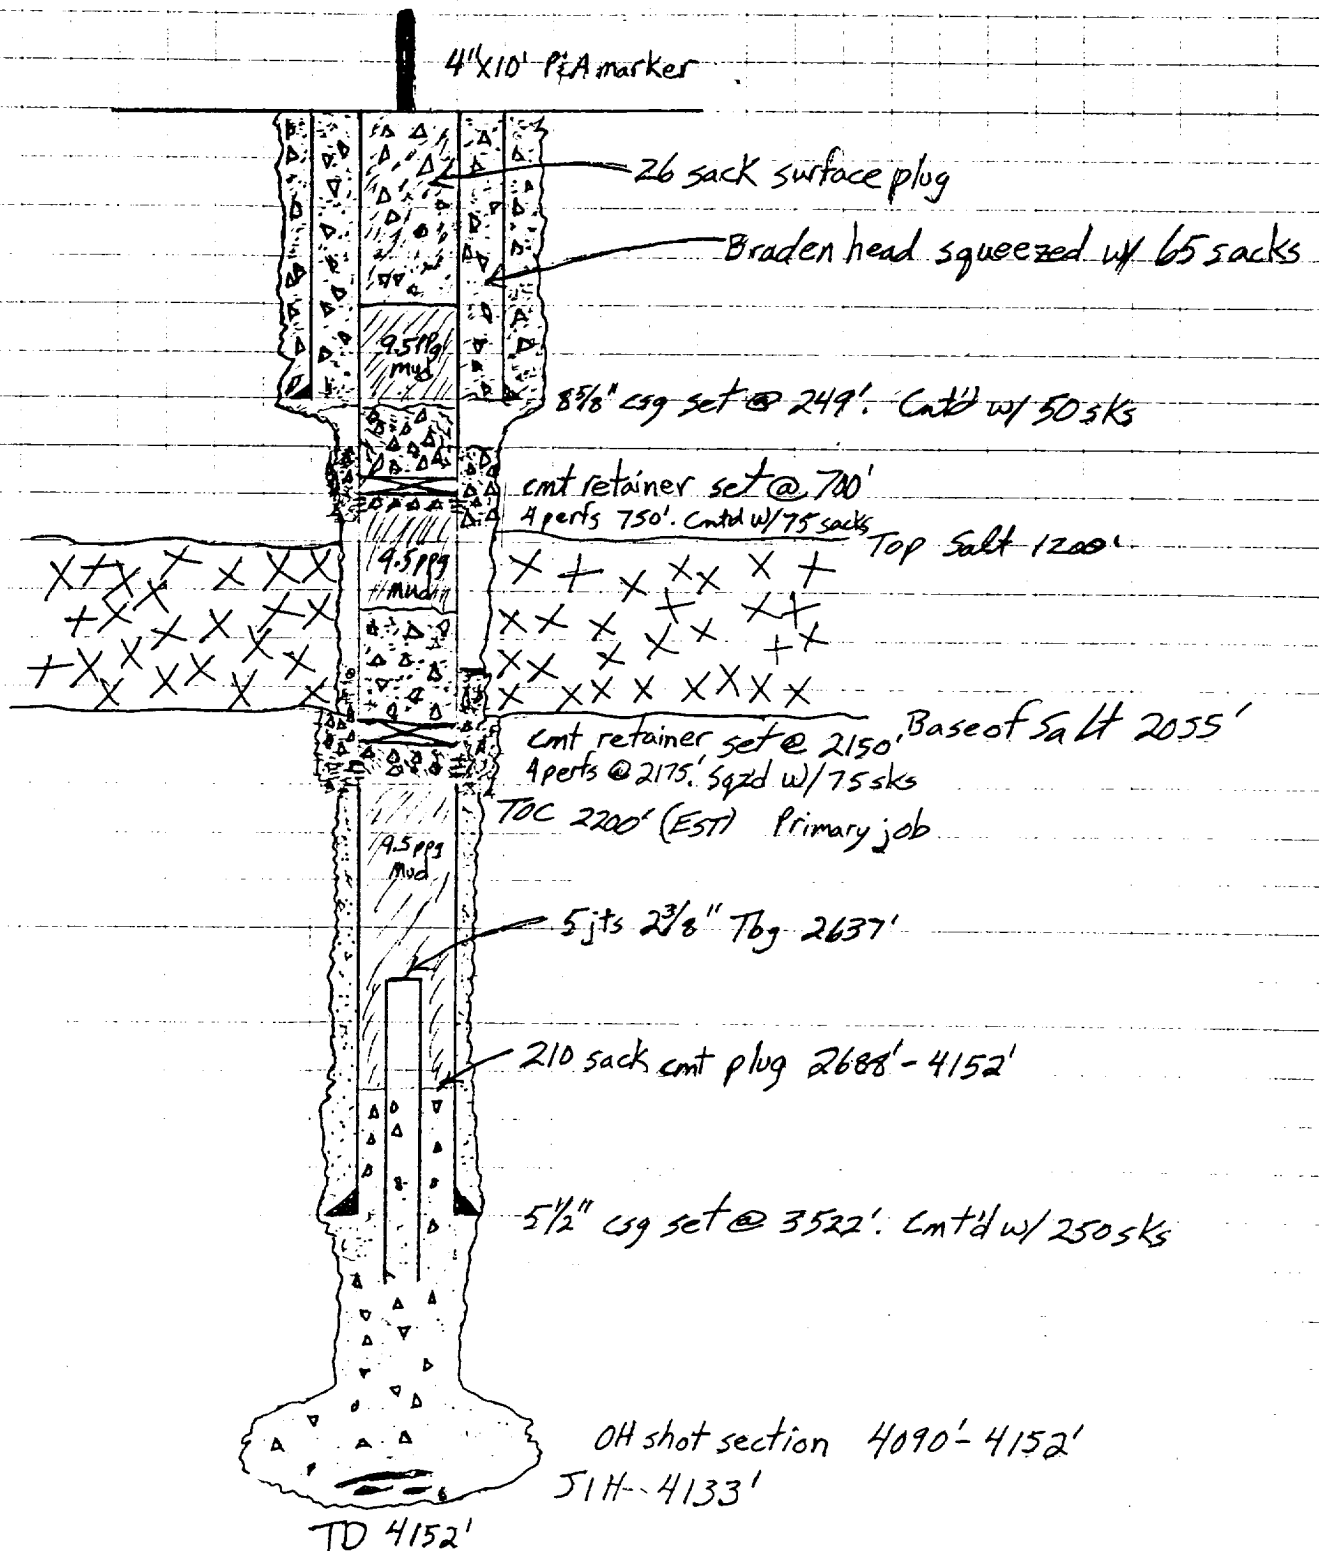

RECEIVED

MAR 23 1987

OCD

HQCBBS OFFICE
