

DISTRICT I
P.O. Box 1980, Hobbs, NM 88240

DISTRICT II
P.O. Drawer DD, Artesia, NM 88210

DISTRICT III
1000 Rio Brazos Rd, Aztec, NM
87410

OIL CONSERVATION DIVISION

P.O. Box 2088
Santa Fe, New Mexico 87504-2088

WELL API NO. 30-025-05138
5. Indicate Type of Lease STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>
6. State Oil & Gas Lease No. N/A
7. Lease Name or Unit Agreement Name LEE WHITMAN "A"
8. Well No. 4
9. Pool name or Wildcat Denton (Devonian)

SUNDRY NOTICES AND REPORTS ON WELLS

(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A
DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT"
(FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well
☒ Oil Well ☐ Gas Well ☒ Other TA'd ✓

2. Name of Operator
DEVON ENERGY CORPORATION (NEVADA)

3. Address of Operator
20 NORTH BROADWAY, SUITE 1500, OKLAHOMA CITY, OKLAHOMA 73102 (405) 235-3611

4. Well Location

Unit Letter H : 1980 Feet From The NORTH Line and 825 Feet From The EAST Line

Section 26 Township 14S Range 37E NMPM LEA County

10. Elevation (Show whether DF, RKB, RT, GR, etc.)
GL 3821'

Check Appropriate Box To Indicate Nature Of Notice, Report, Or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐
OTHER: ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ PLUG AND ABANDONMENT ☐
CASING TEST AND CEMENT JOB ☐
OTHER: MIT ✓ ☒

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work.) SEE RULE 1103.

01-14-98 HU Sonny's pump truck. Loaded casing with 5 BW. Ran mechanical integrity test. Press'd on casing to 500 psi for 30 mins. Tested OK. See attached chart. OCD notified of test.
Devon Energy Corporation (Nevada) requests 12 months TA status. We plan to review reactivating this well based on outcome of other well work in this area.

Cement retainer was already set at 9330' with 50 sx cement on top, TOC at 8960'
Cement retainer was already set at 12,148' with 5 sx cement on top, hole filled with brine

This Approval of Temporary
Abandonment Expires 8/18/2003

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Candi Graham

TITLE ENGINEERING TECHNICIAN

DATE April 2, 1998

TYPE OR PRINT NAME Candi Graham

TELEPHONE NO. (405) 235-3611

(This space for State use)

ORIGINAL SIGNED BY CHRIS WILLIAMS
DISTRICT I SUPERVISOR

Approved by _____

TITLE _____


DATE AUG 18 1998

Conditions of approval, if any:

JC GNS

dp



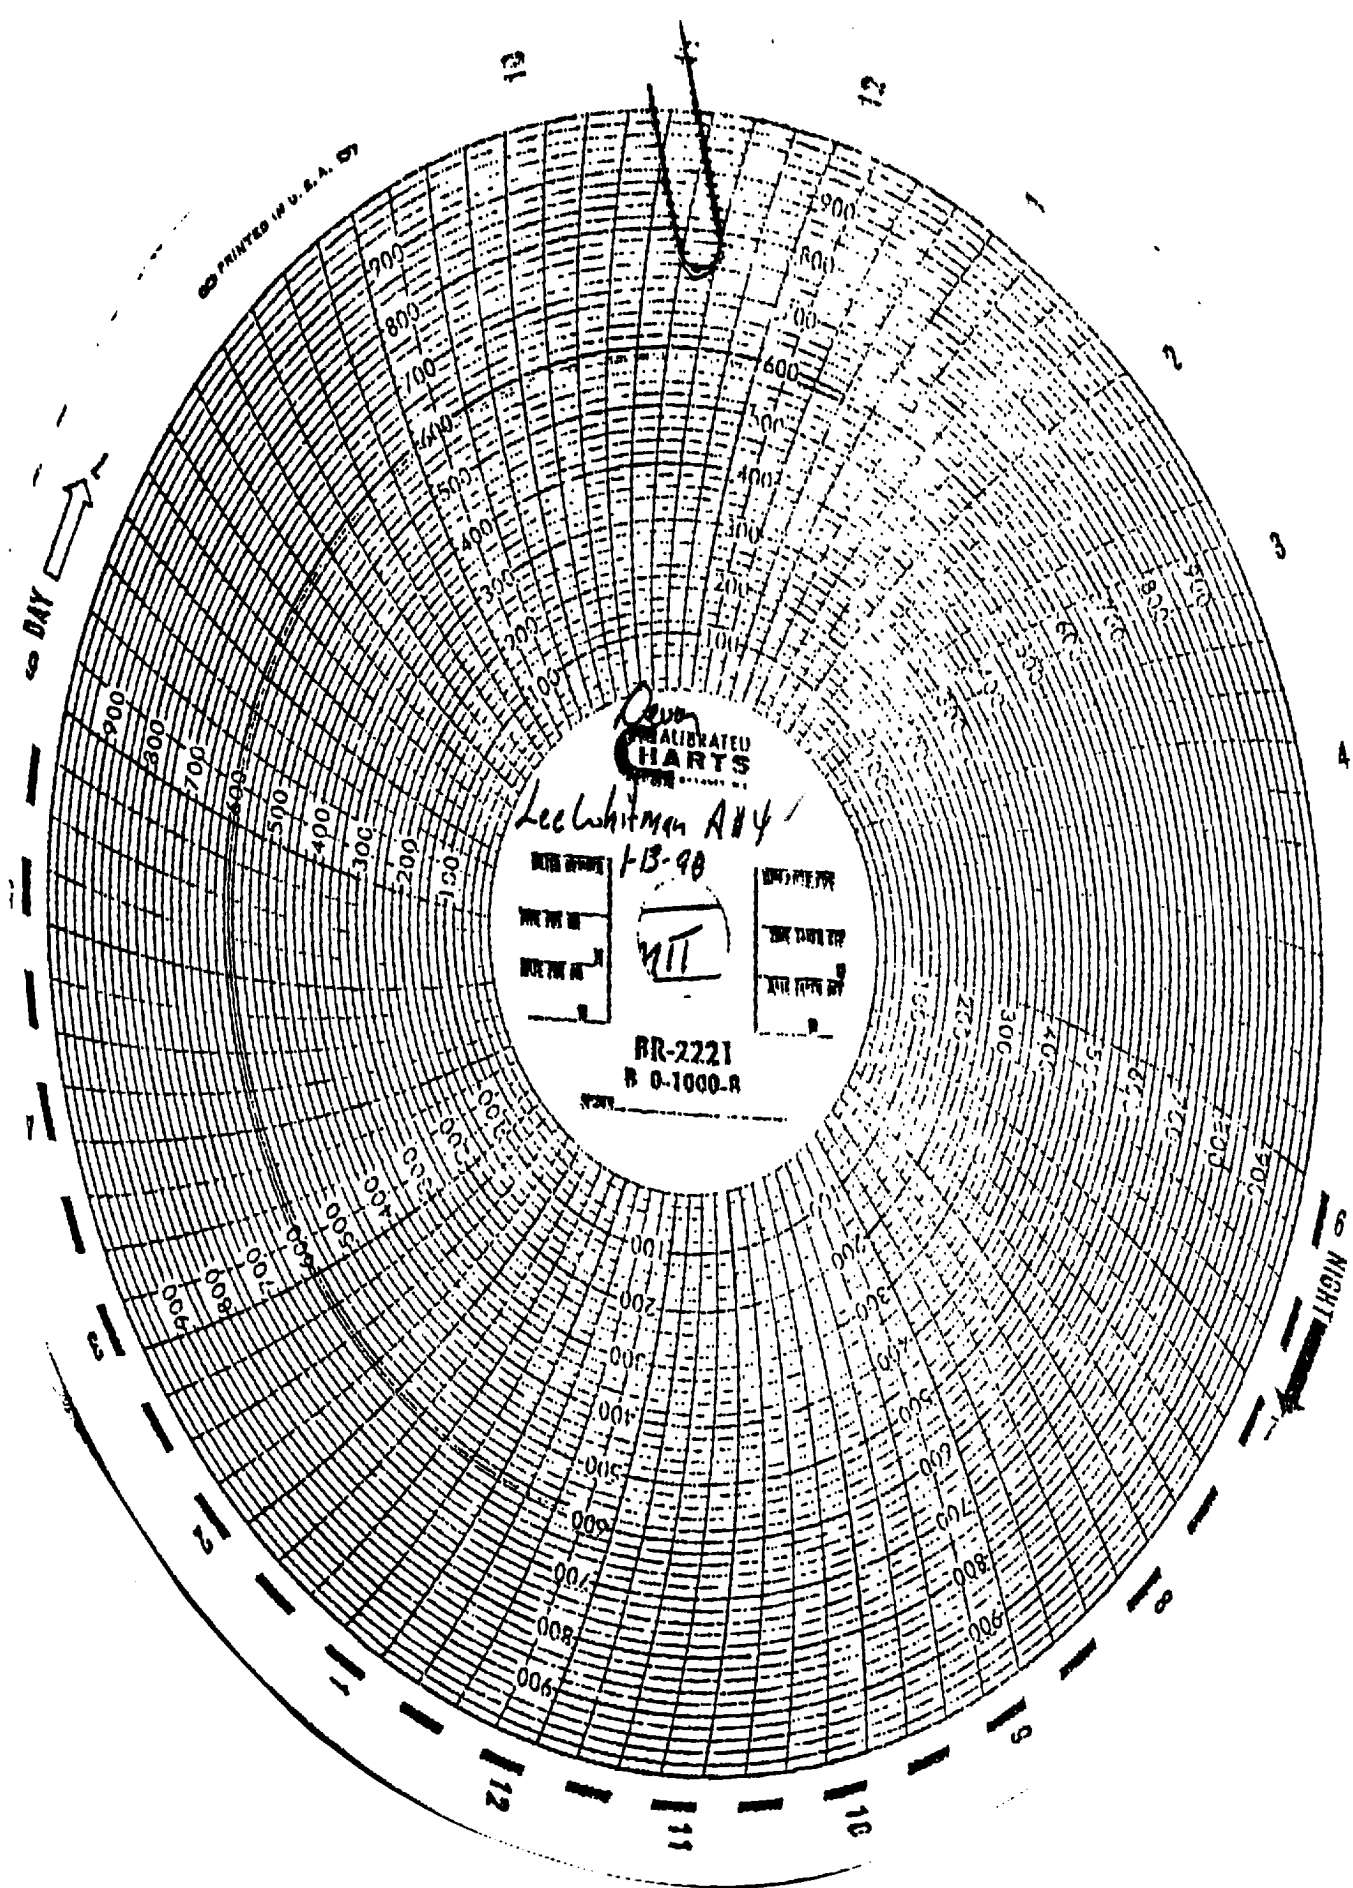

PRINTED IN U.S.A. 57

CALIBRATED
HARTS
RR-2221
R 0-1000-A
Lee Whitman A14
FB-90

DAY

NIGHT

PRINTED IN U.S.A. ©

DAY

4

5

5

NIGHT

8

6

10

11

12

11

2

3

4

5

Devon
CALIBRATED
HARTS
BATAVIA, N.Y.

Lee Whitman A#4
F-13-98

METER NUMBER
TIME PUT ON
DATE PUT ON

TIME & DATE USED
TIME TAKEN OFF
DATE TAKEN OFF

BR-2221
B 0-1000-8

H-26-14-37

D. von
Lee Whitman A#4
Rob Keeler
1-13-98

