


## BURLINGTON RESOURCES

South Corbin Federal #3  
South Corbin (Wolfcamp) Field  
T18S, R33E, Section 20  
Lea County, New Mexico

Proposed Completion

KB 3,827'

GL 3,806'

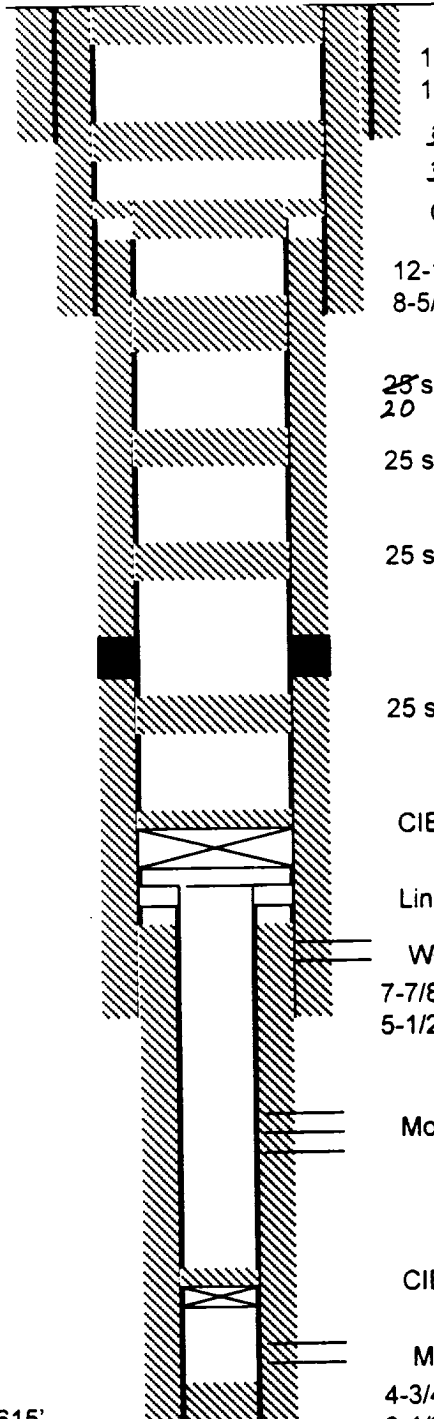

15 sx cement plug from surface to 50'.

17-1/2" hole.

13-3/8" 48# H-40 Casing set at 395'. Cemented with 425 sx. TOC at surface (Circ).

35 3/8" sx cement plug from 345' to 445'.

35 sx " " from 1444' to 1344'. T/salt

Cut off casing at 2350'. Set 25 sx cement plug from 2300' to 2400'.

12-1/4" hole

8-5/8" 28# K-55 Casing set at 2,917'. Cemented with 1200 sx.

Top of Cement at surface (Circ).

25 sx cement plug from 3040' to 2790'. 2795' - 2695' B/salt

25 sx cement plug from 5100' to 4850'.

25 sx cement plug from 7300' to 7050'.

25 sx cement plug from 9250' to 9050'.

CIBP at 10,650'. Capped with 50' cement (15sx).

Lindsey Liner Hanger at 10,655'. 20' PBR

Wolfcamp Perforations 10,954' to 11,370'.

7-7/8" hole.

5-1/2" 17# N-80/K-55 Casing set at 11,500'. Cemented with 1200 sx.

DV Tool at 8,010'. Top of Cement at 2,410' (CBL).

Morrow Perforations 13,233' to 13,318'.

CIBP at 13,460'. Capped with 17' cement.

Morrow Perforations 13,484' to 13,544'.

4-3/4" hole

3-1/2" 10.3# L-80 FL4S set at 13,615'. Cemented with ??.

Top of cement at 10,800'.

TD 13,615'.
