

DISTRICT I
P.O. Box 1980, Hobbs, NM 88240

DISTRICT II
P.O. Drawer DD, Artesia, NM 88210

DISTRICT III
1000 Rio Brazos Rd., Artesia, NM 87410

OIL CONSERVATION DIVISION
P.O. Box 2088
Santa Fe, New Mexico 87504-2088

WELL API NO. 30-025-20319
5. Indicate Type of Lease STATE ☒ FEE ☐
6. State Oil & Gas Lease No. B-155-1
7. Lease Name or Unit Agreement Name NEW MEXICO "O" STATE NCT-1
8. Well No. 22
9. Pool name or Wildcat VACUUM GLORIETA/BLINEBRY

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)	
1. Type of Well: OIL WELL ☒ GAS WELL ☐ OTHER ☐	
2. Name of Operator TEXACO E & P INC.	
3. Address of Operator PO BOX 3109; MIDLAND, TEXAS 79701	
4. Well Location Unit Letter <u>M</u> : <u>500</u> Feet From The <u>SOUTH</u> Line and <u>560</u> Feet From The <u>WEST</u> Line Section <u>36</u> Township <u>175</u> Range <u>34E</u> NMPM LEA County 10. Elevation (Show whether DF, RKB, RT, GR, etc.) 4010 (DF)	

11. Check Appropriate Box to Indicate Nature of Notice, Report, or Other Data	
NOTICE OF INTENTION TO:	SUBSEQUENT REPORT OF:
PERFORM REMEDIAL WORK ☐	REMEDIAL WORK ☐
TEMPORARILY ABANDON ☐	ALTERING CASING ☐
PULL OR ALTER CASING ☐	COMMENCE DRILLING OPNS. ☐
OTHER: ☐	PLUG AND ABANDONMENT ☐
	CASING TEST AND CEMENT JOB ☐
	OTHER: ☐

12. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.

- 1) NOTIFY NMOC D OF INTENT TO PLUG AND ABANDON WELL.
- 2) RIG UP ON Z-SIDE OF WELL. (THIS IS A DUAL COMPLETION W/ 2 STRINGS OF 2 7/8" TUB AS CSG.
- 3) SET CMT RETAINER @ 5820' & SQZ 45 SX CMT INTO PERFS @ 5861'-6012'
- 4) SPOT 10 SX CMT F/ 5820'-5520' (MIX 25# PER BBL SALT GEL MUD & CIRC CSG)
- 5) SPOT 10 SX CMT F/ 4550'-4250' (T-SAN ANDRES 4500)
- 6) SPOT 10 SX CMT F/ 3733'-3433' (T-QUEENS 3683)
- 7) PERF @ 2800' & SQZ YATES W/ 45 SX CMT W/ CMT RETAINER @ 2750'.
- 8) SPOT 10 SX CMT F/ 2750'-2450'
- 9) SPOT 10 SX CMT F/ 1600'-1300' (11 3/4" CSG SET @ 1549')
- 10) RIG UP ON Y-SIDE. SET CIRC @ 6000' & SQZ 45 SX CMT INTO PERF @ 6021'-6120'
- 11) SPOT 10 SX CMT F/ 6000'-5700' MIX 25# PER BBL SALT GEL MUD & CIRC CSG
- 12) SPOT 10 SX 4550'-4250'
- 13) SPOT 10 SX 3733'-3433'

I hereby certify that the information above is true and accurate to the best of my knowledge and belief.

SIGNATURE R.J. Harding III TITLE OPERATIONS ENGINEER DATE 915/688/4816
TYPE OR PRINT NAME R.J. HARDING III TELEPHONE NO. 915/688/4816

(This space for use later)


APPROVED BY DATE TITLE DATE
CONDITIONS OF APPROVAL, IF ANY:

JUL 27 1995

- 14) SPOT 10 SX CMT F/ 2800'-2500'
- 15) SPOT 10 SX CMT F/ 1600'-1300'
- 16) CUT & PULL 2 7/8" CSG @ 1000'
- 17) SPOT 100 SX CMT F/ 1050'-950'
- 18) SPOT 50 SX CMT F/ 50'-SURFACE
- 19) CUT OFF WELL HEAD; CAP WELL; INSTALL DRY HOLE MARKER
- 20) CLEAN UP LOCATION RIG DOWN & MOVE OFF.

RECEIVED

TEXACO
NM O STATE NCT-1 NO. 22
API# 30025203190000

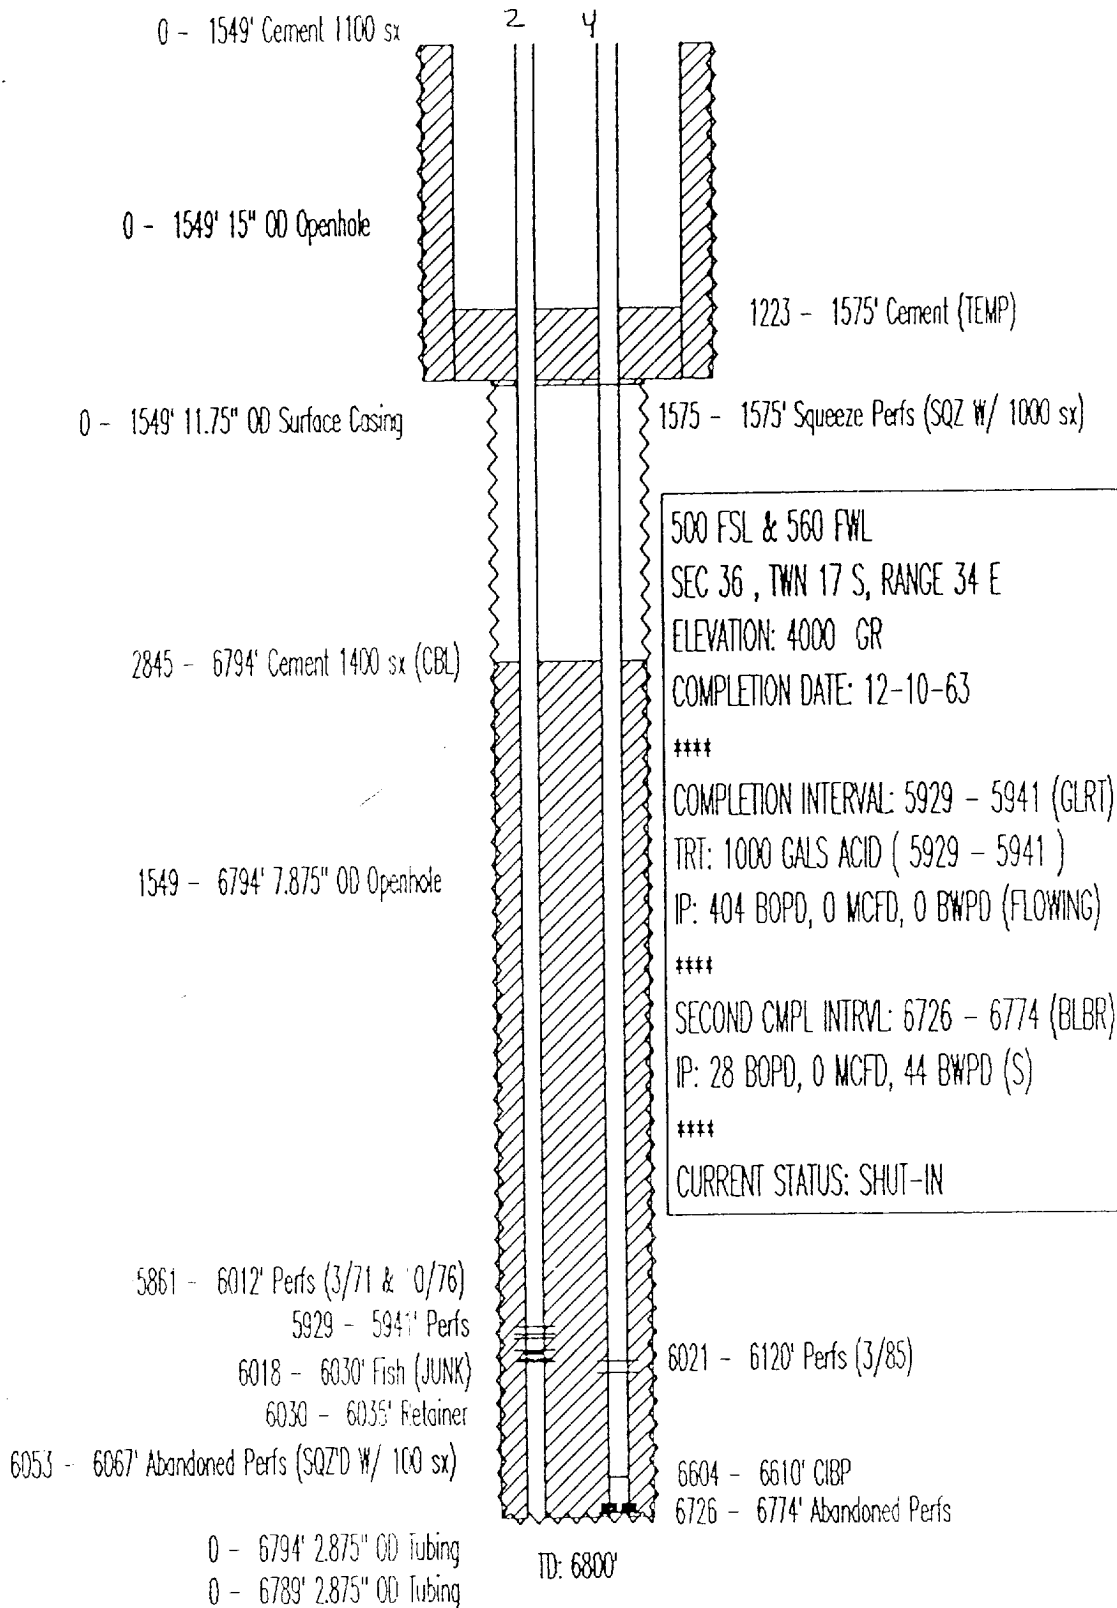

TEXACO
NM O STATE NCT-1 NO. 22
API# 30025203190000
PROPOSED

0 - 1549' Cement 1100 sx

2 4

SPOT 50SX 50' - SURFACE
SPOT 100 SXs. cmt # 1050' - 950'
CUT & PULL 2 7/8" CSG @ 1000'


0 - 1549' 15" OD Openhole

10SX - 1600 - 1300'

1223 - 1575' Cement (TEMP)
W/ 1000 SXs. CLASS H

10SX 1600 - 1300'

0 - 1549' 11.75" OD Surface Casing

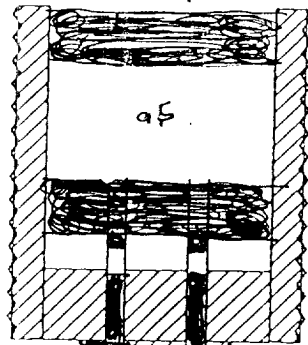

SPOT 10SX 2750 - 2450

2845 - 6794' Cement 1400 sx (CBL)
Perf @ 2800' & SQZ PATES
W/ 45 SXs. cmt.
SET CIRC @ 2750'

SPOT 10SX 2800' - 2500'
- 2845 (TOC)

1549 - 6794' 7.875" OD Openhole
SPOT 10SX 3733 - 3433
(T-QUEEN 3683)

SPOT 10SX 3733 - 3433

10 SX cmt # 4550' - 4250' (T-SAN ANTONIO)

10SX cmt # 4550 - 4250

SPOT 10 SXs. # 5820' - 5520'

SET CIRC @ 5820' SQZ 45 SXs.
INTO PERF.

5861 - 6012' Perfs (3/71 & 10/76)

5929 - 5941' Perfs

6018 - 6030' Fish (JUNK)

6030 - 6035' Retainer

6053 - 6067' Abandoned Perfs (SQZD W/ 100 sx)

SPOT 10 SX 6000' - 5700'

SET CIRC @ 6000' & SQZ 45 SXs. cmt INTO PERF @ 6021 - 6120'

6021 - 6120' Perfs (3/85)


6604 - 6610' CIBP

6726 - 6774' ABANDONED PERF

0 - 6794' 2.875" OD Tubing

0 - 6789' 2.875" OD Tubing

TD: 6800'



RECEIVED

DEC 1985

7/8
