


CONTINENTAL OIL COMPANY
VACUUM FIELD
STATE H-35 NO. 7
PROPOSED DUAL COMPLETION
ABO-WOLFCAMP (OIL-OIL)

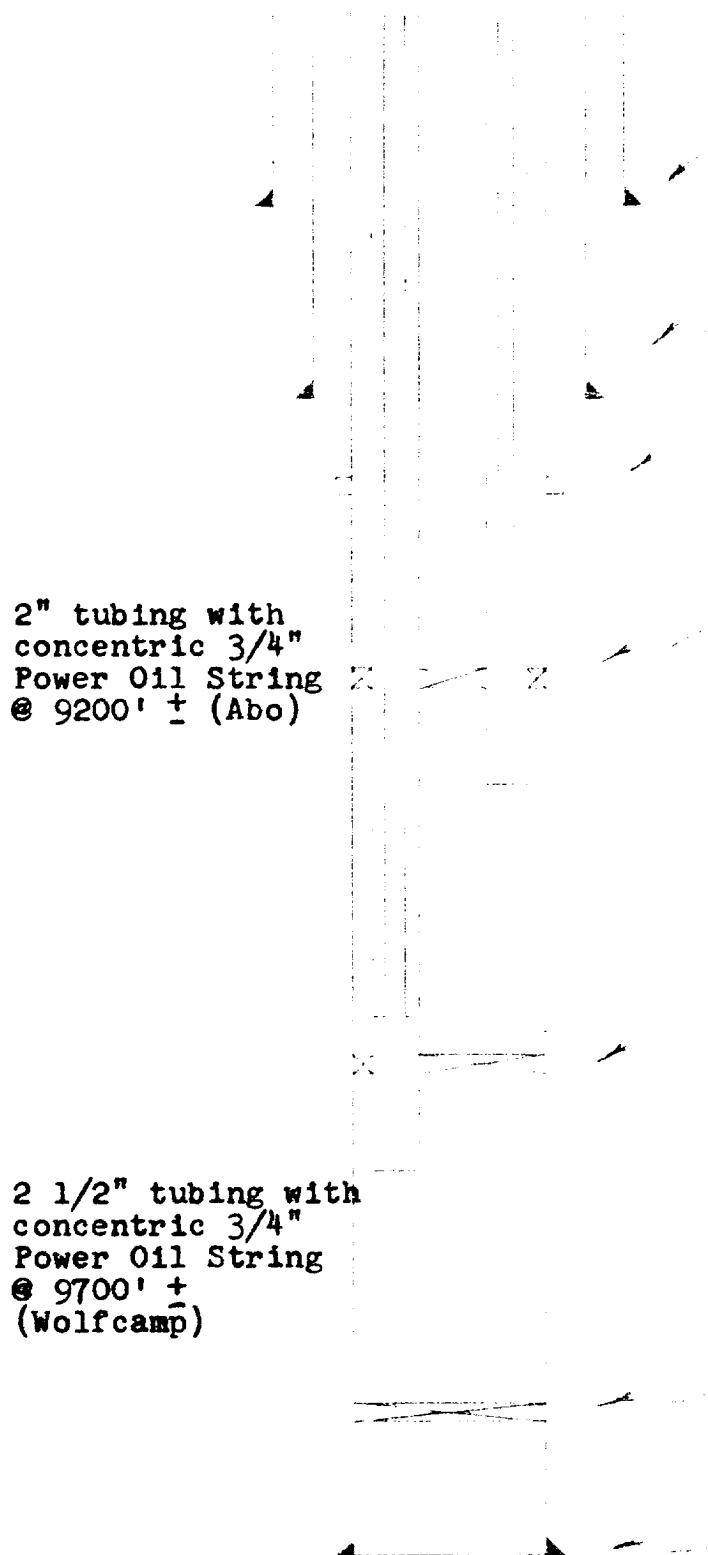

13 3/8" O.D. Casing
set @ 375' w/375 sks.
Cement circulated.

9 5/8" O.D. Casing
set @ 4950' w/250 sks
CEMENT TOP 3600'

D.V. Tool @ 6680'
Top of Cement 6680'

Branch
7" Retrievable Dual Packer
set @ 9100' ±

Abo Completion Interval
9154-9256' (Overall)

Revised 6/6
7" Production Packer *Subsided K 10.30*
set @ 9500' ± *to pump down*

Wolfcamp Completion Interval
9620-10,066' (Overall)

Plug Back Depth 10,550'

7" O.D. Casing
set @ 12,413' w/1750 sks

Total Depth 12,414'
