



COLEMAN PETROLEUM ENGINEERING COMPANY

PHONE EXPRESS 3-3813
611 GRIMES
P O BOX 1829
HOBBS, NEW MEXICO

TEMPERATURE SURVEY

OPERATOR Pubco Petroleum Corporation

FIELD Humble City Strawn

LEASE Shipp

DATE 3-15-73

RECORDED BY Weaver

WITNESSED BY Driller

REMARKS:

WELL No. 4

TIME RUN 6:30 Am

PIPE SIZE 5 1/2"

SET @ 11760'

TIME PLUG DOWN 10:30 Pm 3-14-73

CEMENTED BY DOWELL

ZERO POINT GL

CEMENT 330 Sks expanding cement w/2%
D-8 & .2% D-65

HOLE SIZE 8 1/2"

TYPE STRING Oil

INST. NO. 224

Dowell Stage collar set @ 9852'


TOP CEMENT

8500'

MAX. DEPTH OF SURVEY

9717'

7000 100 110 120 130 140 150 160 170 180 190 200

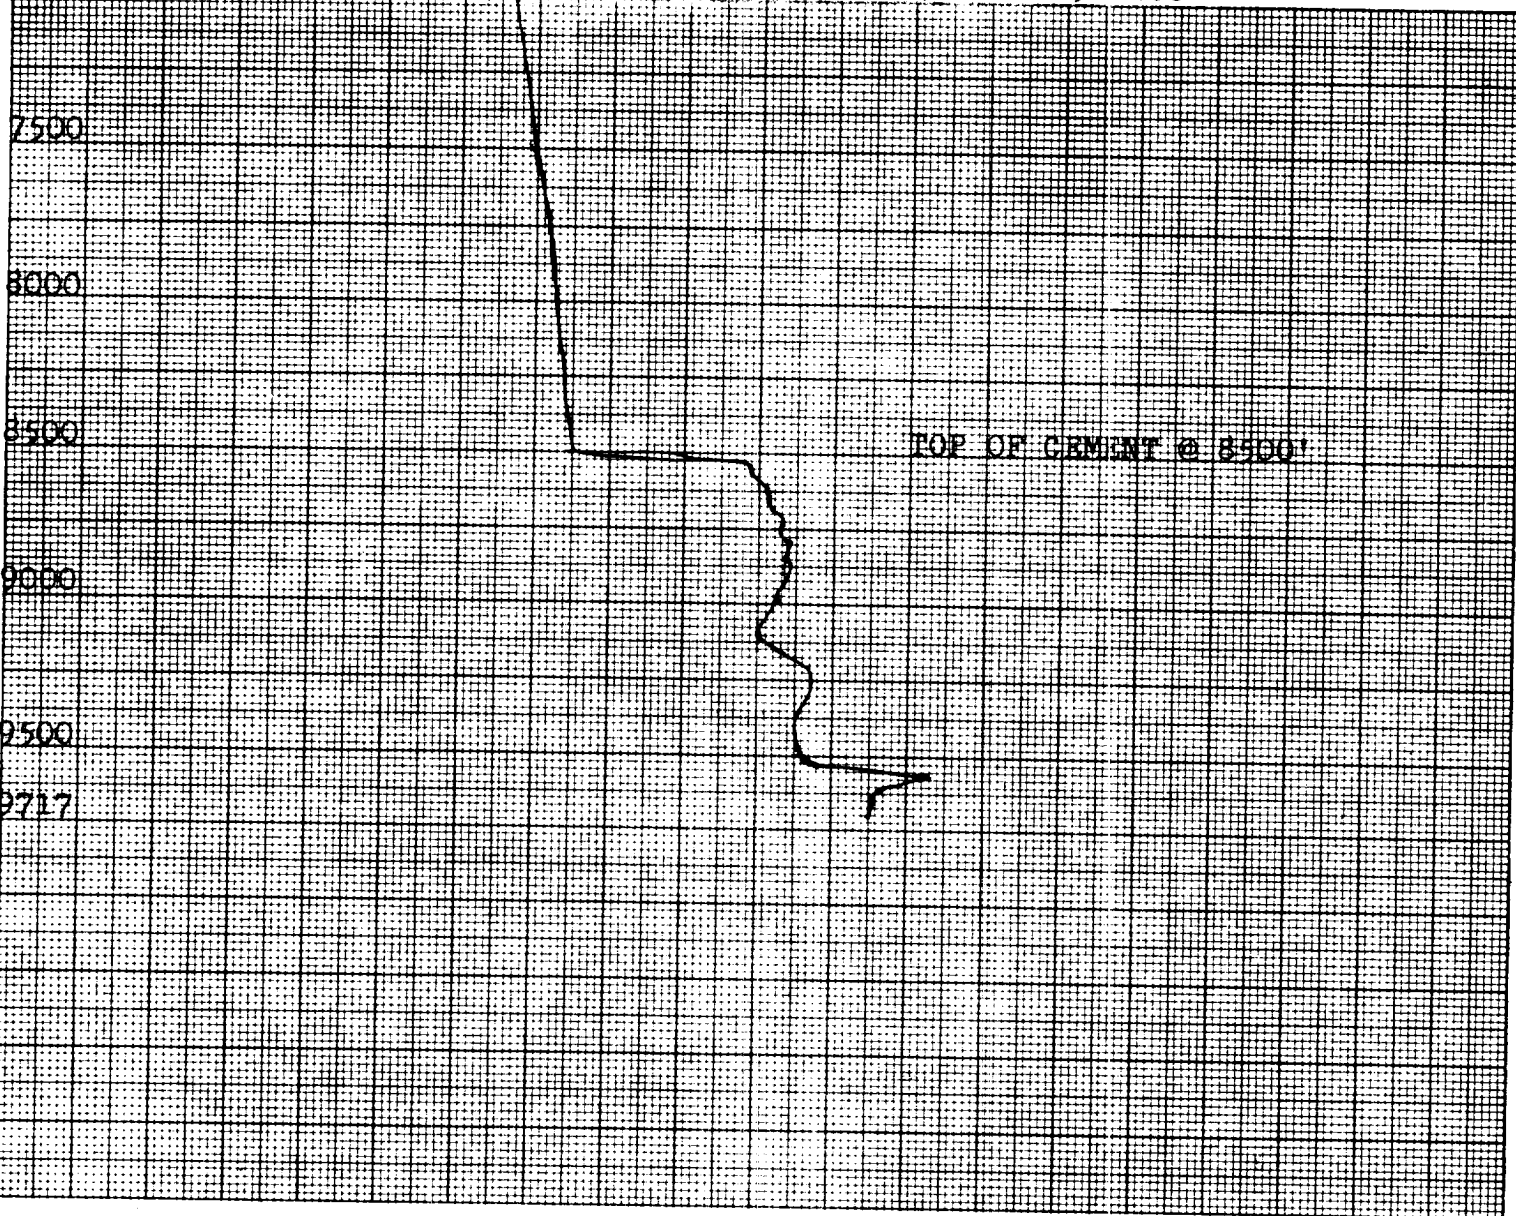



LTR



Job separation sheet

NO. OF COPIES RECEIVED	
DISTRIBUTION	
SANTA FE	
FILE	
U.S.G.S.	
LAND OFFICE	
OPERATOR	

NEW MEXICO OIL CONSERVATION COMMISSION

Form C-103
Supersedes Old
C-102 and C-103
Effective 1-1-65

5a. Indicate Type of Lease State ☐ Fee ☒
5. State Oil & Gas Lease No. --
7. Unit Agreement Name --
8. Farm or Lease Name Shipp
9. Well No. 4
10. Field and Pool, or Wildcat Humble City Strawn
12. County Lea

SUNDRY NOTICES AND REPORTS ON WELLS

(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT -" (FORM C-101) FOR SUCH PROPOSALS.)

1. OIL WELL ☒ GAS WELL ☐ OTHER- ☐
2. Name of Operator Pubco Petroleum Corporation
3. Address of Operator P. O. Box 869, Albuquerque, New Mexico 87103
4. Location of Well UNIT LETTER <u>L</u> <u>1874</u> FEET FROM THE <u>South</u> LINE AND <u>554</u> FEET FROM THE <u>West</u> LINE, SECTION <u>11</u> TOWNSHIP <u>17S</u> RANGE <u>37E</u> HMPM.
15. Elevation (Show whether DF, RT, CR, etc.) 3748' GL

Check Appropriate Box To Indicate Nature of Notice, Report or Other Data
NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐
TEMPORARILY ABANDON ☐
PULL OR ALTER CASING ☐
OTHER ☐

PLUG AND ABANDON ☐
CHANGE PLANS ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐
COMMENCE DRILLING OPNS. ☐
CASING TEST AND CEMENT JOB ☒
OTHER Intermediate Casing ☒
ALTERING CASING ☐
PLUG AND ABANDONMENT ☐

17. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.

Ran 120 joints (4750') 9-5/8" K-55, 36# casing. Set @ 4750' with 375 sacks Hallibuton lightweight and 300 sacks Class "C", 2% CaCl. P.D. @ 4 p.m. 2/11/73. Ran temperature survey. Top of cement @ 3200'. Use thread lock on bottom three joints. Tack-welded in 4 quadrants on bottom two collars.

WOC 16 hours. Pressure tested casing and blind rams to 1000 psi for 30 minutes, held okay. Starting drilling out @ 10:00 a.m. 2/12/73.

18. I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNED J. C. Johnson
J. C. Johnson

TITLE Vice President Production

DATE 2/13/73

APPROVED BY Joe D. Ramey
Dist. I, Supv.

TITLE _____

DATE 2/13/73

CONDITIONS OF APPROVAL, IF ANY:
