


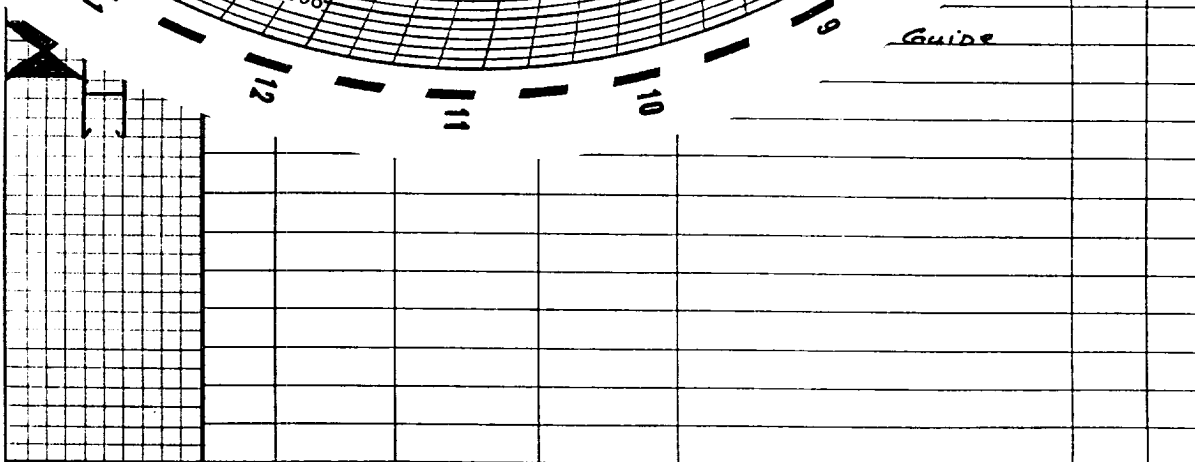

DELIVERY TICKET NUMBER

Guide

PACKER INSTALLATION PLAN

GA-688

GB-698

PREPARED FOR

Mike Elmore

COMPANY

TEXACO EEP

DATE

12-5-92

LEASE

V6W4

WELL NO.

80

FIELD

Buckeye

CO.

LEA

STATE

NM

☒ NEW COMPLETION

☐ RIGGING

INSTALLATION

ITEM	LENGTH	FROM	TO	DESCRIPTION	OD	ID
	14.00	0	14.00	K.B. Connection		
	5861.76	14.00	5875.76	181 joints 2 3/4 BOD EUE Cement-Lined tubing	2.375	1.56
	.76	5875.76	5876.52	2 3/8 BOD S.S. Nipple w/ collar	2.375	1.687
	1.97	5876.52	5878.49	Gamberson 5 1/2 x 2 3/8 X/L on-off tool w/ 1.43 E S.S. Profile	4.37	1.43
	3.74	5878.49	5882.23	Gamberson 5 1/2 x 2 3/8 Plastic Coated 17-70# G-RT Injection Pktr	4.675	1.41
	.52	5882.23	5882.75	2 3/8 Nickel Plated Pump out Plug Assy. Cineline Guide	3.063	2.65

GENERAL REMARKS

Backside tested 500# 30 min.
Packer Set w/ 10,000# Tension
Completion Fluid Type and Weight
Packer Fluid Circulated

AREA
Hobbs

OPERATOR'S NAME
Bruce Johnson

RETRIEVING METHOD - INCLUDE SHEAR RELEASE VALUE OR COLLET SNAP OUT VALUE

TOP PACKER:
MIDDLE PACKER:
LOWER PACKER:

DATE
12-5-92

DELIVERY TICKET NUMBER
