

COMPANY: JOHN WEST ENGINEERING COMPANY
CLIENT: MARALO INC.
GAUGE NUMBER: 29240
WELL NAME: CORBIN 13 FEDERAL "A"
WELL NUMBER: 2
TEST NUMBER: 93-14-2021
LOCATION: LEA COUNTY, NEW MEXICO
TEST OPERATOR: BJT & RW
COMMENTS: TEMPERATURE

POSITION GAUGE SERIAL NUMBER
1

DATE AND TIME CEMENT JOB COMPLETE: OCTOBER 12, 1993 @ 6:15 AM

DATE AND TIME SURVEY MADE: OCTOBER 12, 1993 @ 4:15 PM

AMOUNT AND TYPE OF CEMENT USED: 915 SACKS HALLIBURTON LT.WT. 9# SALT,
1/4# FLOSEAL; 300 SACKS 50:50 POSMIX, 4/10 of
1% HALAD-91, 3# KCL RAN BEHIND 5300' of 5 1/2"
CASING IN A 7-7/8" HOLE.

DEPTH FIGURED FROM: FLOOR

PAGE START DATE: 10/12/93
PAGE START TIME: 16:57: 0
DATA FILE: 10

DELTA TIME HRS	DEPTH FEET	TEMPERATURE 'F	COMMENTS
0.000	0.00	66.50	
0.350	554.00	70.50	BREAK
0.364	587.00	87.50	
0.381	665.00	81.25	
0.417	828.00	86.00	
0.433	896.00	75.50	
0.450	954.00	85.00	
0.483	1082.00	83.00	
0.533	1282.00	92.00	
0.550	1356.00	83.25	
0.567	1420.00	122.50	
0.581	1451.00	89.50	
0.617	1605.00	123.50	
0.633	1669.00	106.75	
0.650	1734.00	122.50	
0.664	1767.00	111.50	
0.681	1833.00	120.00	
0.717	2003.00	101.25	
0.731	2038.00	105.50	
0.747	2108.00	97.50	
0.750	2142.00	99.75	
0.764	2177.00	96.50	
0.767	2212.00	98.00	
0.781	2246.00	96.50	
0.783	2280.00	100.50	
0.800	2334.00	98.75	
0.831	2425.00	101.50	
0.833	2454.00	94.75	
0.867	2572.00	104.25	
0.883	2630.00	90.75	
0.897	2662.00	95.25	
0.900	2695.00	91.75	
0.914	2725.00	96.50	
0.917	2755.00	88.00	
0.933	2816.00	92.00	
0.947	2847.00	90.00	
0.950	2878.00	93.50	
0.967	2942.00	90.50	
0.981	2977.00	93.50	
0.983	3014.00	91.00	
0.997	3043.00	94.50	
1.000	3072.00	92.50	
1.014	3103.00	93.50	
1.017	3135.00	92.25	
1.031	3167.00	93.50	
1.033	3200.00	92.50	
1.047	3233.00	93.50	
1.050	3267.00	91.75	
1.064	3298.00	93.50	
1.067	3330.00	91.00	


PAGE START DATE: 10/12/93

PAGE START TIME: 18: 2:50

DATA FILE: 10

DELTA TIME HRS	DEPTH FEET	TEMPERATURE 'F	COMMENTS
1.097	3430.00	93.00	
1.100	3464.00	91.75	
1.117	3529.00	93.00	
1.131	3562.00	92.25	
1.133	3596.00	94.50	
1.167	3732.00	94.00	
1.183	3800.00	99.00	
1.197	3833.00	96.00	
1.200	3867.00	97.00	
1.214	3902.00	95.25	
1.231	3971.00	96.75	
1.233	4006.00	95.25	
1.250	4076.00	102.00	
1.264	4111.00	97.25	
1.267	4146.00	98.25	
1.281	4181.00	98.00	
1.283	4216.00	101.25	
1.297	4251.00	96.50	
1.300	4286.00	98.00	
1.314	4331.00	97.50	
1.317	4357.00	101.00	
1.333	4428.00	98.25	
1.347	4464.00	100.00	
1.350	4500.00	97.75	
1.364	4535.00	109.75	
1.367	4570.00	100.00	
1.383	4644.00	104.00	
1.397	4679.00	97.00	
1.414	4750.00	100.75	
1.417	4786.00	99.50	
1.431	4823.00	100.75	
1.433	4860.00	97.50	
1.450	4930.00	100.50	
1.467	5004.00	98.50	
1.483	5076.00	101.75	
1.497	5113.00	99.00	
1.500	5150.00	100.00	
1.514	5187.00	97.50	
1.517	5225.00	100.00	MDR

MARALO INC.
CORBIN 13 FEDERAL "A" NO. 2
LEA COUNTY, NEW MEXICO
OCTOBER 12, 1993
TEMPERATURE SURVEY

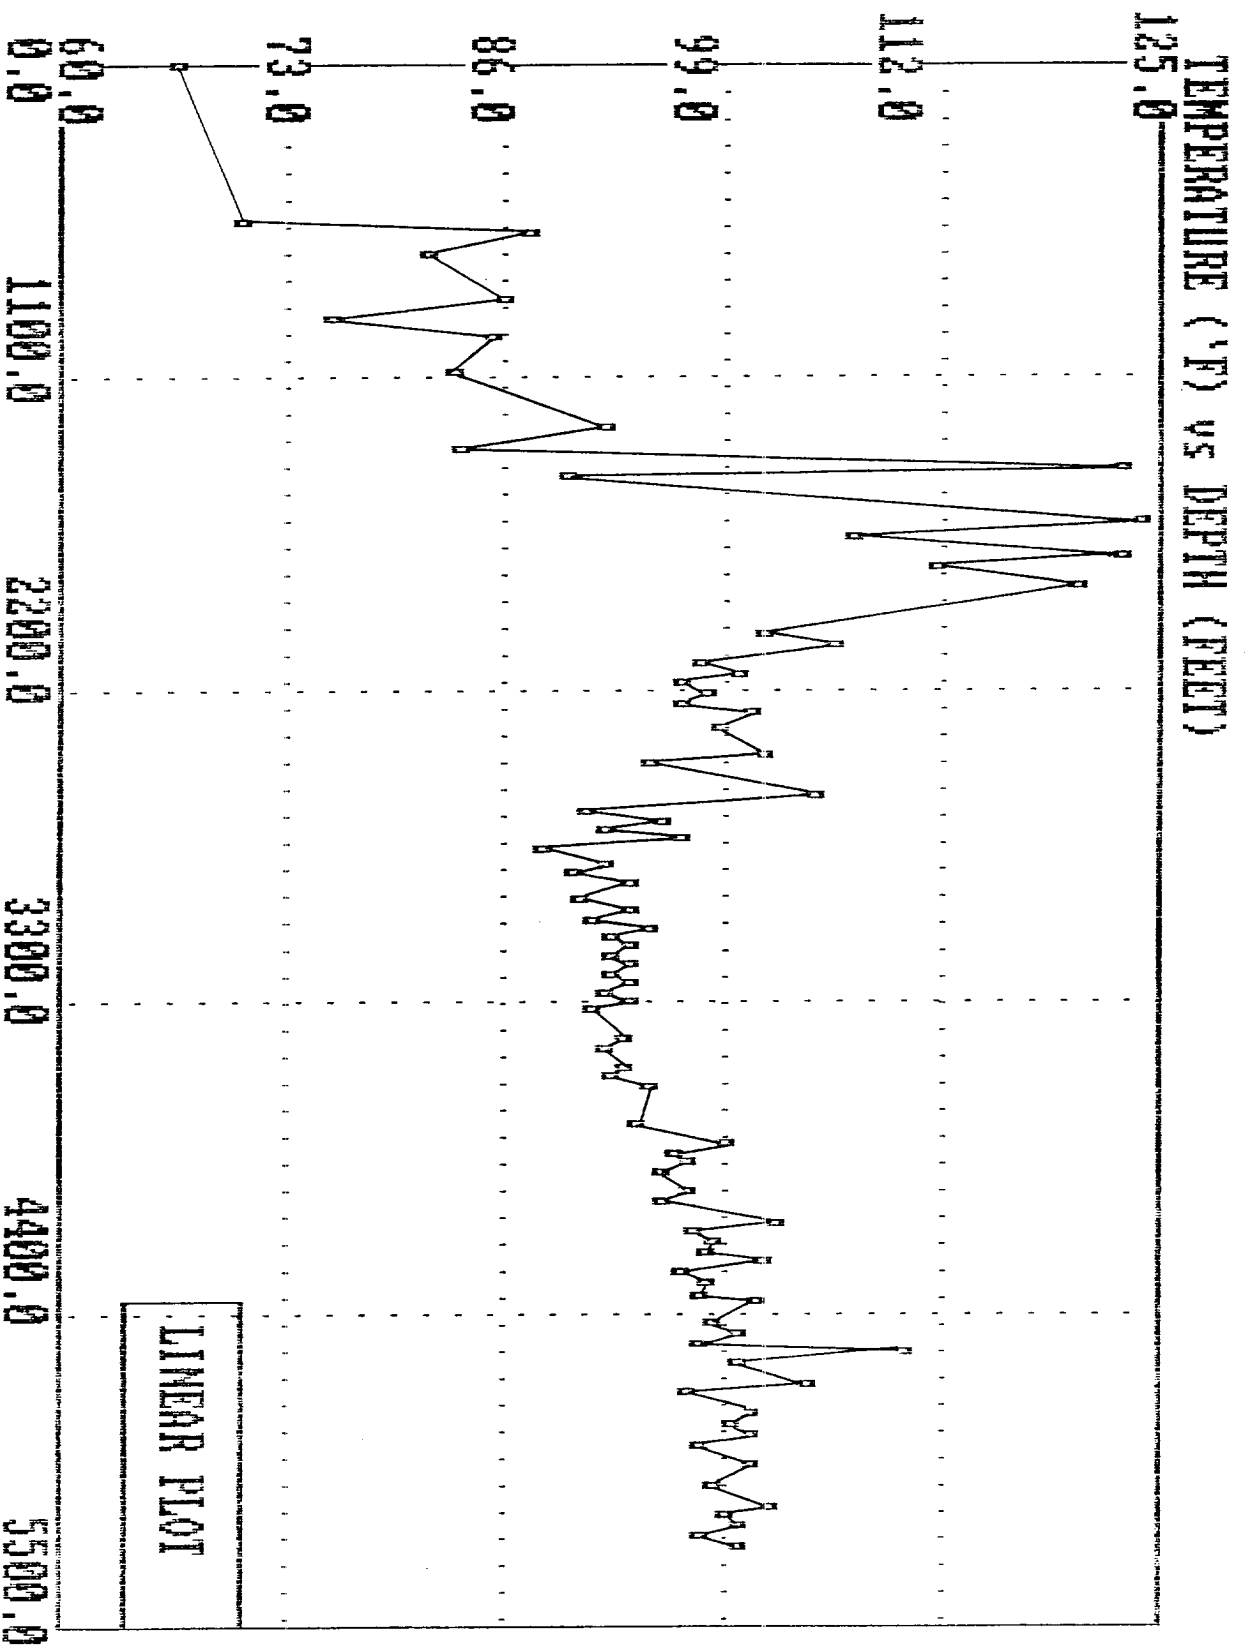

TOP CEMENT: 550'

MDR: 5225'
