

1980 FNL & 330 FEL
 Sec 21, T-22S, R-36E
 Elev: 3527' NF; 0'-10" H


Completion History:

- 11-12-54: Perf 3723'-3832'
- Frac w/15,000 gals + 1st gal sd
- 3-25-63: Acid w/1000 gals 15% MCA
- left 3 wireline bit + 110' 5/16" wire in hole
- 3-1-72: SI
- 5-24-74: Enter H₂O Flood
- 8-8-75: Pump chg
- 12-10-75: Acid w/500 gals 15% HCl
- Frac w/4000 gals Prod + 20,000 gals
- T6w + 40,000th sd
- 12-15-76: Rod part
- 2-13-77: Replace rod string
- 6-14-82: Pump chg
- 7-17-85: Pump chg
- 9-11-86: CO-3826, pump chg
- 11-25-86: Rod part
- 12-7-87: Rod part

8 5/8" 32th
 2301' w/300 SA
 (Circ)

Top Salt : 1520'
 Base Salt : 3690'
 Yares : 3026'
 TIR : 3400'
 Queen : 3758'

123 jets 2 3/8" hys w/SN @ ±3800'
 OPSMA @ ±3830'

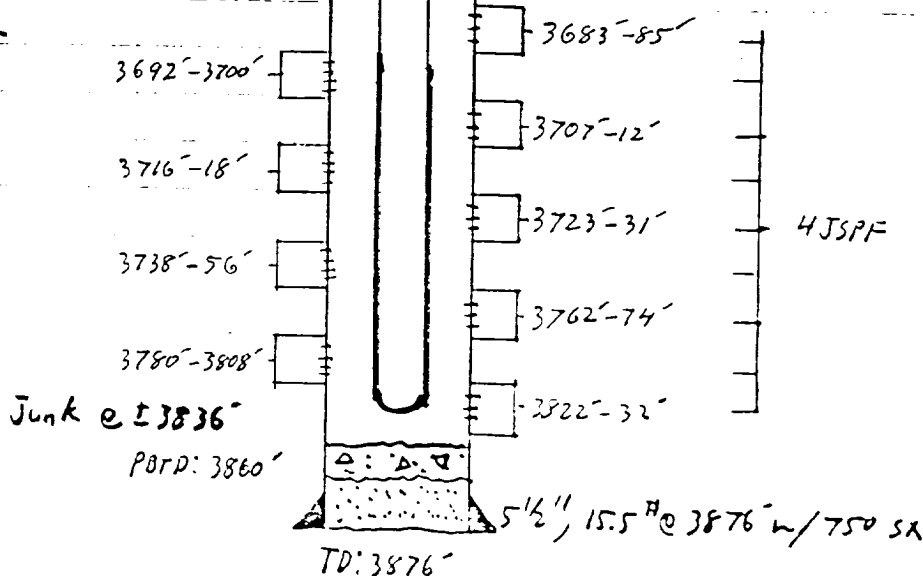

Made By JDL
 Checked By
 Date 10-7-87
 Page of

Genoco Inc.
 Calculation Sheet

Title South Eunice Unit Well
 Proposed

Job No.
 Field NMFV
 State NM
