


1-18-02 MTRU - Shut dn.


1-21-02 Installed BOP, WIH w/ PKR. & 2 7/8" TBG. Tested TBG. to #8000. Set PKR @ 4840' & Spotted 500 gals of 30% HCL Acid. Pulled up to 4560' & Acidized Annulus w/ 9500 gals of 30% HCL Acid. Shut In overnight.

1-22-02 Had 100# on TBG. Rigged up pump truck to est. a pump Rate. POOH w/ 2 7/8" TBG & PKR. Shut In overnight.

1-23-02 WIH w/ Nickel plated treating PKR. & 2 3/8" Plastic Coated TBG. Circulated Back Hole w/ Packer Fluid Set PKR @ 4392' tested Backside to 500# for 30 min. Est. pump Rate. Shut In overnight.

1-24-02 Rigged dn & Shut In waiting on injection equipment.



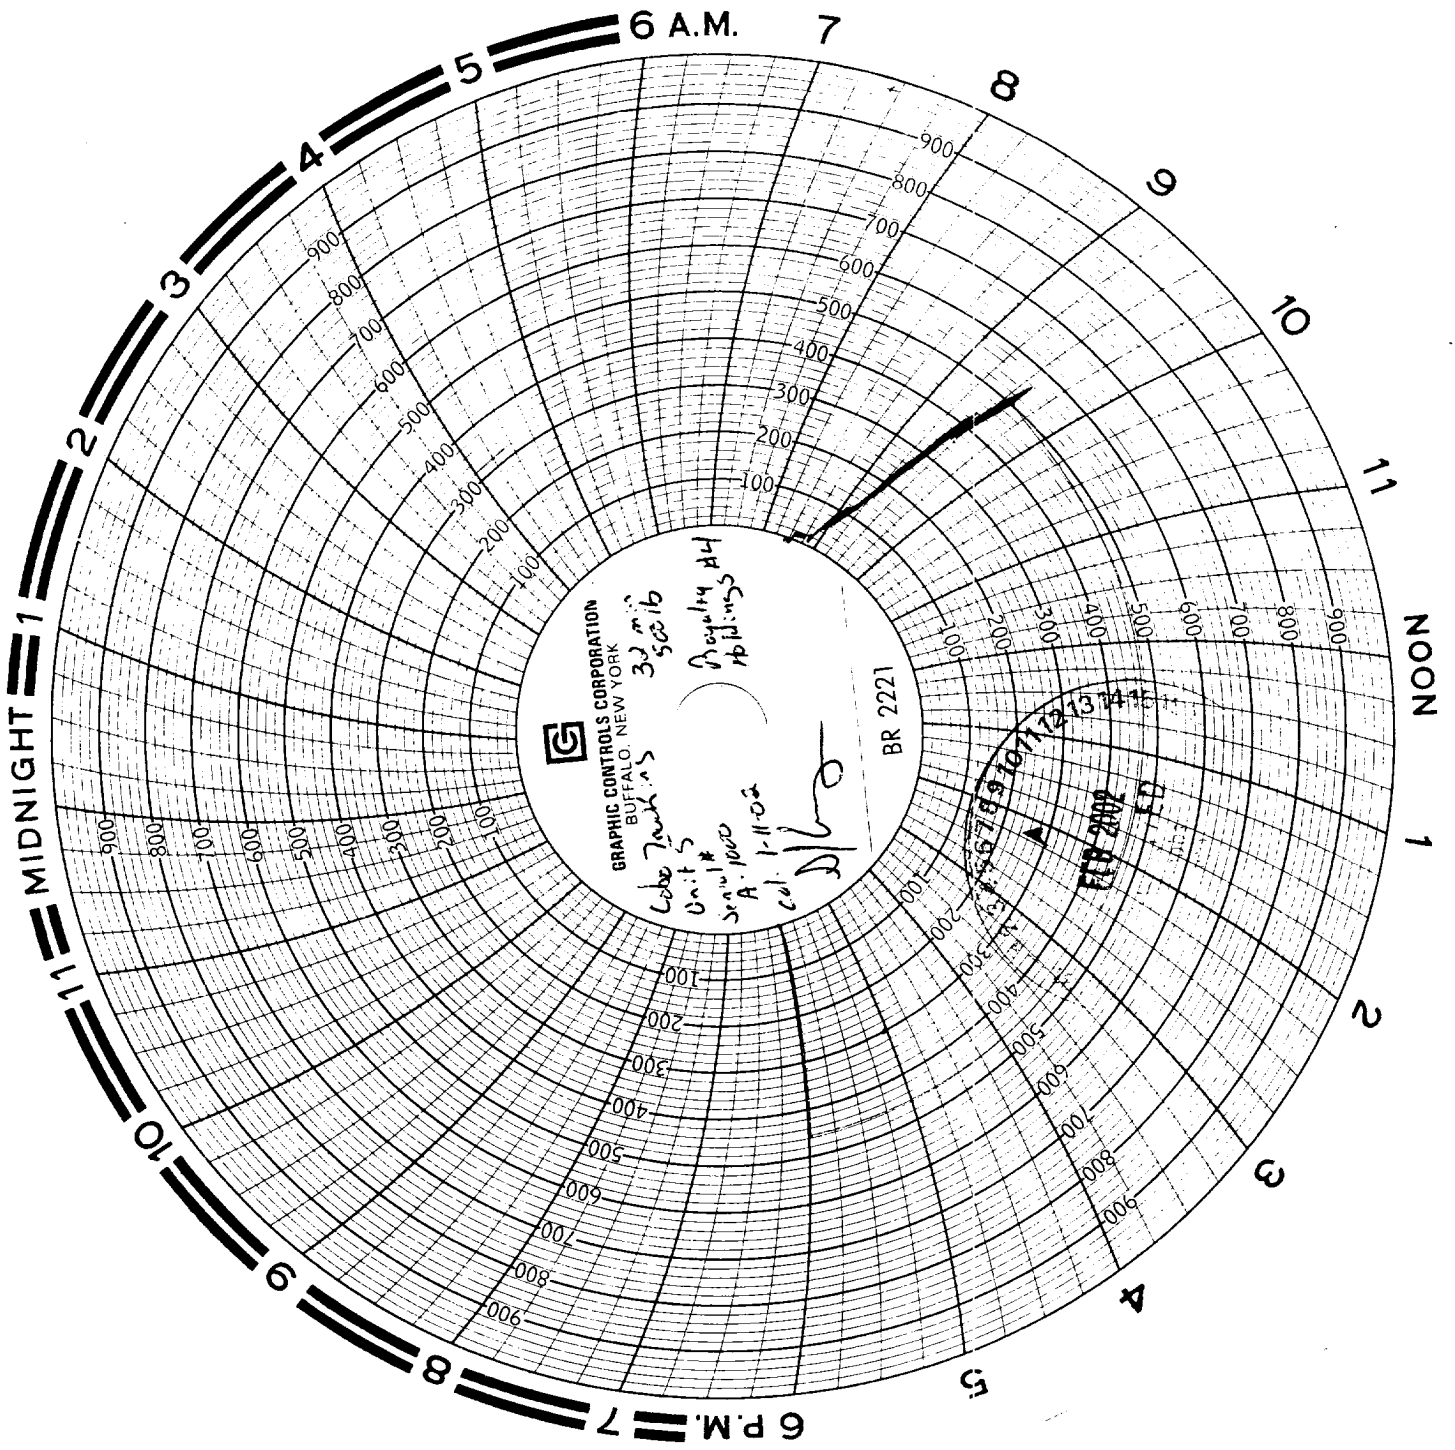

1/24/02

SUNDANCE SWD
Royalty Holdings #4
SEC 25 T21S R37E

Gerald Hudson
Hudson Packer @ lue.
(505) 393-5837

7" NICKLE PLETED LOK SET
W/ 1.78 F ON/OFF TOOL

Bottom of Packer @ 292

140 JTS 23/8 PC + 60
