

IP (Yates) Perfs 3442-3580' P 10 BOPD. Pot lased on 24 hr
test. GOR (NR); gty (NR)

F.R. 9-17-79
11-1-79 Drlg 3909'
11-13-79 TD 3950'; WOCT
12-5-79 TD 3950'; PBD 3710'; Prep Frac
Perf (Seven Rivers) @ 3752', 3756', 3769', 3801',
3892', 3894'
Acid (3752-3894') 1780 gals (15%)
Swbd dry w/NS (3752-3894')
Sqzd 3752-3894' w/300 sx & DOC
Perf (Yates) @ 3442', 3451', 3463', 3482', 3495',
3515', 3518', 3522', 3580' w/2 SPI
Acid (3442-3580') 1850 gals (15%)
12-12-79 TD 3950'; PBD 3710'; WOCT
Frac (3442-3580') 40,000 gals + 82,000# sd
3-3-80 TD 3950'; PBD 3710'; Complete
Rig Released 11-3-79
3-8-80 COMPLETION ISSUED

3-2-9 NM
IC 30-025-703 5-79

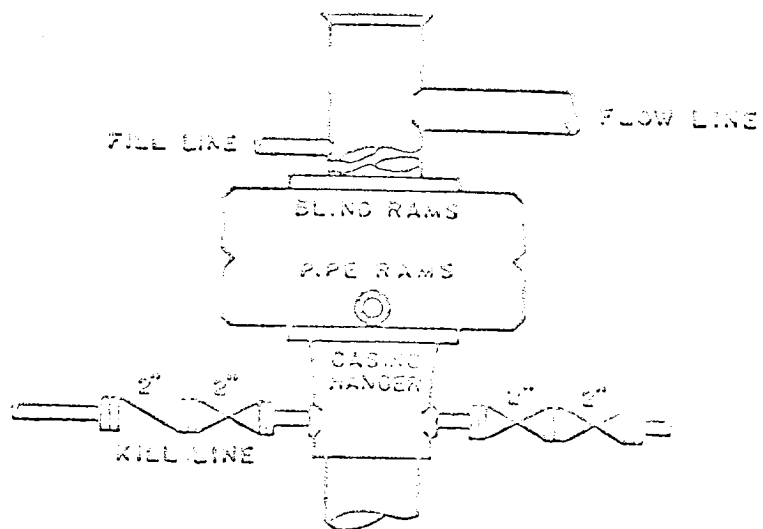


Exhibit WQ
