

VII. DATE OF NOTIFICATION TO THE SECRETARY OF THE TAXATION AND REVENUE DEPARTMENT:

30025349600000

5/22/2002

VIL - 11  
Sec 31  
20538E  
2310'S 1600'W

|                                          |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
|------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------|--------------------|-------------------------|----------|------------|-------|
| <b>MEYER B-31 #5(BBS1/18/2002)</b>       |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| API No.                                  |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 30025349600000          |          |            |       |
| Spud                                     |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 4/16/2000               |          |            |       |
| Completion                               |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Abandoned                                |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Frm. Prod.                               |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Well No.                                 |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Field                                    |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Init. Well Class.                        |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | Strawn                  |          |            |       |
| Status                                   |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Permit                                   |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 4/5/2000                |          |            |       |
| RR                                       |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 5/1/2000                |          |            |       |
| Last Act.                                |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| TD                                       |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 7830.0 ftKB             |          |            |       |
| PBTD                                     |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 7747.0 ftKB             |          |            |       |
| Operator                                 |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | New Mexico              |          |            |       |
| Permit No.                               |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | Hobbs O.U.              |          |            |       |
| District                                 |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | Hobbs O.U.              |          |            |       |
| Final Well Class.                        |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | North Hardy Strawn Pool |          |            |       |
| Frm. at TD                               |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| <b>Elevations</b>                        |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| KB-Grd                                   |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 11.0 ft                 |          |            |       |
| Grd                                      |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 3494.0 ft               |          |            |       |
| Tub Head                                 |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 0.0 ft                  |          |            |       |
| KB                                       |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 3505.0 ft               |          |            |       |
| Cas Fing                                 |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 0.0 ft                  |          |            |       |
| <b>Bore Hole Data</b>                    |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Size (in)                                |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | Depth (ftKB)            |          |            |       |
| 12.2500                                  |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 1525.0                  |          |            |       |
| 7.8750                                   |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | 7830.0                  |          |            |       |
| <b>Casing String - SURFACE CASING</b>    |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Grd                                      | Item (in)                                                                                                                                                                                                                                                                                                                                                 | Btm (ftKB)                                                            | Comments           | ID                      | Thd      | Jnts       | Wt    |
| J-55                                     | 8.6250 in Surface Casing                                                                                                                                                                                                                                                                                                                                  | 1525.0                                                                |                    | 8.0970                  | ST&C 8RD |            | 24.00 |
| <b>Casing String - PRODUCTION CASING</b> |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Grd                                      | Item (in)                                                                                                                                                                                                                                                                                                                                                 | Btm (ftKB)                                                            | Comments           | ID                      | Thd      | Jnts       | Wt    |
| J-55                                     | 5.5000 in PRODUCITON CASING                                                                                                                                                                                                                                                                                                                               | 7830.0                                                                |                    | 4.8720                  | LT&C 8rd |            | 17.00 |
| <b>Casing String - conductor pipe</b>    |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Grd                                      | Item (in)                                                                                                                                                                                                                                                                                                                                                 | Btm (ftKB)                                                            | Comments           | ID                      | Thd      | Jnts       | Wt    |
|                                          | 16.0000 in CONDUCTOR PIPE                                                                                                                                                                                                                                                                                                                                 | 51.0                                                                  |                    | 0.0000                  |          |            | 0.00  |
| <b>Casing Cement</b>                     |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Amount (sx)                              | Comments                                                                                                                                                                                                                                                                                                                                                  |                                                                       |                    | Casing String           |          | Top (ftKB) |       |
| 0                                        |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    | SURFACE CASING          |          | 0.0        |       |
| 1717                                     | 1st stage-24 BBL pre-flush. 200 sxs class C w/ 2#/sk KCL + 4% CD-32 + FL-5 + .2% SMS + 1% BA-58.<br>2nd stage- Lead-1135 sxs C+POZ 35:65 + 6% gel + 1/4#/sk celloflake. Tail-382 sxs C + 2#/sk KCL + .4% CD-32 + .7% FL-32 + 2% SMS + 1% BA-58.<br>Circ. 48 sxs out on first stage. Circ. 134 sxs out on 2nd stage. Bumped plug to 3700 psi. Floats held. |                                                                       |                    | PRODUCTION CASING       |          | 0.0        |       |
| <b>Perforations</b>                      |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Int                                      | Shots (/ft)                                                                                                                                                                                                                                                                                                                                               | Comments                                                              |                    |                         | Type     | Date       |       |
| 7568.0 - 7574.0                          | 4.0                                                                                                                                                                                                                                                                                                                                                       |                                                                       |                    |                         |          | 5/17/2000  |       |
| 7592.0 - 7606.0                          | 4.0                                                                                                                                                                                                                                                                                                                                                       |                                                                       |                    |                         |          | 5/17/2000  |       |
| 7628.0 - 7644.0                          | 4.0                                                                                                                                                                                                                                                                                                                                                       |                                                                       |                    |                         |          | 5/17/2000  |       |
| <b>Stimulations &amp; Treatments</b>     |                                                                                                                                                                                                                                                                                                                                                           |                                                                       |                    |                         |          |            |       |
| Int                                      | Zone                                                                                                                                                                                                                                                                                                                                                      | Comments                                                              | Type               | Date                    | Fluid    |            |       |
| 7568.0 - 7574.0                          |                                                                                                                                                                                                                                                                                                                                                           | Treated Strawn w/ PPI tool in three settings w/ 1500 gal 15% NEFE HCL | PPI Acid Breakdown | 5/19/2000               |          |            |       |


30025349600000

5/22/2002

| Stimulations & Treatments (con't) |                          |                                                                                                                                                                                                                                                                       |           |           |            |          |            |      |
|-----------------------------------|--------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|-----------|------------|----------|------------|------|
| Int                               | Zone                     | Comments                                                                                                                                                                                                                                                              | Type      | Date      | Fluid      |          |            |      |
| 7568.0 - 7574.0                   |                          | Acidized Strawn w/ 3000 gal. 15% NEFE HCL & 175 1.3 ball sealers @ 5-6 BPM. AIP-4000psi, MIP-4300psi. Fair ball action. ISIP-3050, 5MSI-2680, 10MSI-2490, 15MSI-2332                                                                                                  | Acidize   | 5/22/2000 |            |          |            |      |
| 7568.0 - 7574.0                   |                          | . Acid Fractured Strawn w/ 1000 gal 20% NEFE HCL & 7000 gal 20% gelled acid & 6000 gal 20% x-linked acid & 75 1.3 ball sealers tagged w/ RA material @ 11.5 to 17.5 BPM. AIP-5700 psi, MIP- 5920 psi. Poor ball action. ISIP-2780, 5MSI-1950, 10MSI-1400, 15MSI-1000. | Acid Frac | 5/25/2000 |            |          |            |      |
| Tubing String - Production String |                          |                                                                                                                                                                                                                                                                       |           |           |            |          |            |      |
| Grd                               | Item (in)                | Comments                                                                                                                                                                                                                                                              | ID (in)   | Thd       | Jnts       | Len (ft) | Top (ftKB) | Wt   |
| L-80                              | 2.8740 in Tubing         |                                                                                                                                                                                                                                                                       | 2.4409    | EUE8rd    | 236        | 7459.0   | 0.0        | 6.50 |
|                                   | 4.7500 in TAC            |                                                                                                                                                                                                                                                                       | 2.4409    | EUE8rd    |            | 3.0      | 7459.0     | 0.00 |
| L-80                              | 2.8740 in Tubing         |                                                                                                                                                                                                                                                                       | 2.4409    | EUE8rd    | 7          | 220.0    | 7462.0     | 6.50 |
|                                   | 2.8740 in Seating Nipple |                                                                                                                                                                                                                                                                       | 2.2800    | EUE8rd    |            | 1.0      | 7682.0     | 0.00 |
|                                   | 2.8740 in SOPMA          |                                                                                                                                                                                                                                                                       | 2.4409    | EUE8rd    |            | 6.0      | 7683.0     | 0.00 |
| Rod String - Tapered rod string   |                          |                                                                                                                                                                                                                                                                       |           |           |            |          |            |      |
| Type                              | Comments                 | Size (in)                                                                                                                                                                                                                                                             | No.       | Len (ft)  | Top (ftKB) |          |            |      |
| Polished rod                      |                          | 1.5000                                                                                                                                                                                                                                                                |           | 15.0      | 0.0        |          |            |      |
| 1" Rod                            |                          | 1.0000                                                                                                                                                                                                                                                                | 94        | 2350.0    | 15.0       |          |            |      |
| 7/8" Rod                          |                          | 0.8750                                                                                                                                                                                                                                                                | 103       | 2575.0    | 2365.0     |          |            |      |
| 3/4" Rod                          |                          | 0.7500                                                                                                                                                                                                                                                                | 104       | 2600.0    | 4940.0     |          |            |      |
| Guided sinker bars                |                          | 1.5000                                                                                                                                                                                                                                                                | 5         | 133.0     | 7540.0     |          |            |      |
| 2.5x2x24 HVR RHBC                 |                          | 2.2500                                                                                                                                                                                                                                                                |           | 24.0      | 7673.0     |          |            |      |
| Strainer                          |                          | 1.2500                                                                                                                                                                                                                                                                |           | 1.0       | 7697.0     |          |            |      |

| Completions & Workovers |                         |            |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |
|-------------------------|-------------------------|------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Reason for Workover     | Reason for Failure      | Date       | Summary                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
| Initial Completion      | Initial Completion      | 5/15/2000  | <p>Initial Completion - MIRU. NU &amp; tested BOP. Began PU &amp; RIH w/ 4-3/4" bit, 6-3-1/2" D.C. &amp; 2-7/8" L-80 tbg. SION. Prep to drill out.</p> <p>Resumed RIH w/ D.E. Tagged up @ 6971'. Drilled out D.V. tool. RIH &amp; tagged up @ 7732'. Circ bottoms up.</p> <p>PU to 7654. Displaced hole w/ TFW. Spotted 200 Gal 15% NEFE HCL from 7654'. POOH. Prep to log &amp; perforate. SION.</p> <p>RUWL. Ran GR/CBL/CBL from PBTD to 100'. Prep to perforate. SD due to high wind.</p> <p>RUWL. Perforated Strawn 4spf @ 7568-74, 7592-7606, 7628-44. RIH w/ PPI tool. Prep to acidize. SION.</p> <p>Set &amp; tested PPI tool to 5000 psi. Broke &amp; treated Strawn perforations in three setting w/ 1500 gal. 15% NEFE HCL. PU &amp; set PKR @ 7477'. Unsuccessfully attempted to fish standing valve for 4hrs. Released PKR. Began POOH. SIOWE. Prep to run Production equipment &amp; acidize.</p> <p>Finished POOH. RIH w/ Re-entry guide, 2.25-F-nipple, 10' sub, M1-X packer w/ 2.25 R-nipple &amp; on/off tool testing tubing to 8000 psi. Circulated packer fluid. Set pkr @ 7449'. Acidized Strawn w/ 3000 gal. 15% NEFE HCL &amp; 175 1.3 ball sealers @ 5-6 BPM. AIP-4000psi, MIP-4300psi. Fair ball action. ISIP-3050, 5MSI-2680, 10MSI-2490, 15MSI-2332. RDBJ. Began flowback @ 1350 psi. Flowed 11BBL. RIH w/ swab. Recovered 24 BBL water. FL @ 2170'. SION.</p> <p>SITP-10 psi. RIH w/ swab. FL @ 2170'. Recovered 152 BBL, oil cut increased to +- 50%. Ending FL scattered to 6000'. SION</p> <p>SITP-1120 psi. Flowed 19 BBL 90% oil before loading up. Shut well in. RDMO. Prep to Acid-Frac</p> <p>RU Tree saver. SITP-720 psi. Acid Fractured Strawn w/ 1000 gal 20% NEFE HCL &amp; 7000 gal 20% gelled acid &amp; 6000 gal 20% x-linked acid &amp; 75 1.3 ball sealers tagged w/ RA material @ 11.5 to 17.5 BPM.</p> <p>AIP-5700 psi, MIP- 5920 psi. Poor ball action. ISIP-2780, 5MSI-1950, 10MSI-1400, 15MSI-1000.</p> <p>RU swab unit. SITP-vacuum. RIH w/ swab. FL @ 1500'. Kicked well off in seven runs. Recovered 10 BO &amp; 43 BW. Status @ 6:00 A.M. Total Recovered in 12 hrs- 167 oil, 29 water. Current rate-17 BOPH, 1 BWPH, 389 MCFD @ 520 psi</p> <p>FTP on 18/64" choke.</p> |
| Put on pump             | Convert to Pumping Well | 8/20/2001  | Put on pump - Put well on Beam Pump.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |
| Repair rod part         | Makeup                  | 12/14/2001 | Repair rod part                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |

\*--- Cal Day Oil - Bbl/d  
 Cum: 170.126 MSTB  
 \*--- Prod Eng 2002 Forc O - Bbl/d  
 versus time  
 Qi: 163.723 Bbl/d, Jan, 2002  
 Qf: 0.00137798 Bbl/d, Aug, 2100  
 Di:(Hyp->Exp) : 33.6456  
 n: 1.22816  
 RR: 296.651 MSTB  
 EUR: 466.777 MSTB  
 Corr coeff: N/A  
 ---□--- Cal Day Gas1 - mcf/d  
 Cum: 275.897 MMSCF  
 \*--- Prod Eng 2002 Forc G - mcf/d  
 versus time  
 Qi: 369.875 mcf/d, Jan, 2002  
 Qf: 56.7359 mcf/d, Mar, 2011  
 Di:(Harmonic) : 37.5851  
 RR: 389.648 MMSCF  
 EUR: 665.545 MMSCF  
 Corr coeff: N/A

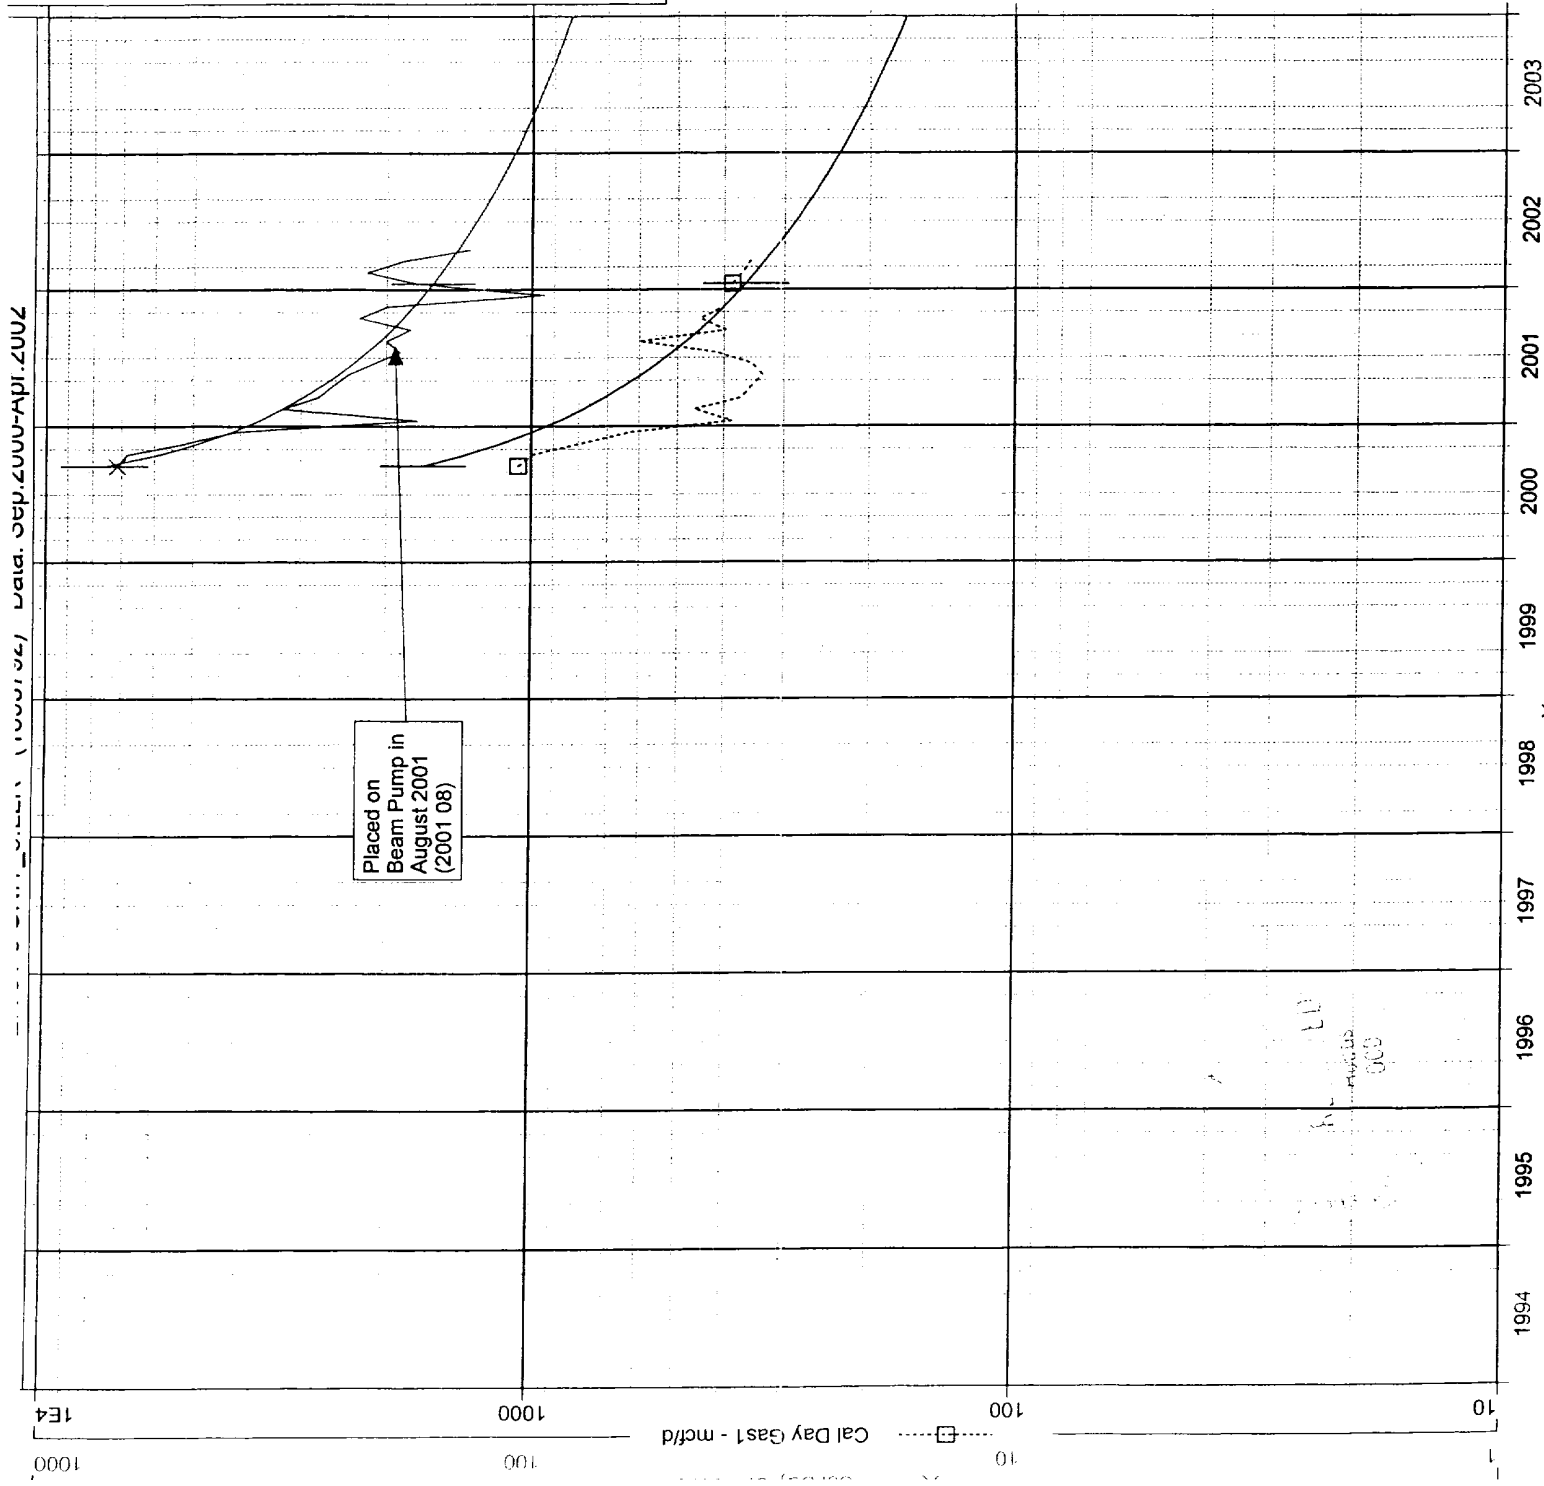

myrb31-5 Beam Pump.txt  
wellview Daily Completion Report ASCII Export (ver 1.0)

\*\*\*\*\*

\* Lease Name: MEYER B-31 #5

No.: 1 TD: 7830.0 ftKB AFE: 51-61-9022  
Date: 8/20/2001 PBDT: 7830.0 ftKB Amnt: 117,000

Casing: 8.6250 @ 1525.0, 5.5000 @ 7830.0, 16.0000 @ 51.0  
Tubing: 2.8750 in 6.40 lbs/ft @ 7468.0 ftKB  
Perforations: 7568.0-7574.0, 7592.0-7606.0, 7628.0-7644.0

Objective: Put on pump  
Present Operation: MIRU.

Operations Summary:  
MIRU. Killed well w/ 50 bbl fresh water. ND tree. NU & tested BOP  
to 5000 psi. Released packer. POOH. Began RIH w/ tubing for  
pumping completion. Rig broke down. SION.

|                     |         |
|---------------------|---------|
| Daily Cost Item:    | Amount: |
| Rig                 | 2,000   |
| Rods / pump / misc. | 750     |
| Kill truck          | 500     |
| Rental Equipment    | 350     |
| Transportation      | 250     |
| Contract Labor      | 235     |
| Daily Cost:         | 4,085   |
| Previous Cost:      |         |
| Cumulative Cost:    | 4,085   |

|                  |                   |
|------------------|-------------------|
| Load Oil:        | Load Water:       |
| Used: 0.0        | Used: 50.0        |
| Rec. daily: 0.0  | Rec. daily: 0.0   |
| Cum. rec: 0.0    | Cum. rec: 0.0     |
| Left to rec: 0.0 | Left to rec: 50.0 |

Rig Hrs: 0.0 Cum: 0.0

|            |        |
|------------|--------|
| Personnel: |        |
| Rig:       | Gulf:  |
| Service:   | Total: |

Equipment:  
Weather:  
Road Conditions:

\*\*\*\*\*

Lease Name: MEYER B-31 #5

No.: 2 TD: 7830.0 ftKB AFE: 51-61-9022  
Date: 8/21/2001 PBDT: 7830.0 ftKB Amnt: 117,000

Casing: 8.6250 @ 1525.0, 5.5000 @ 7830.0, 16.0000 @ 51.0  
Tubing: 2.8750 in 6.40 lbs/ft @ 7468.0 ftKB  
Perforations: 7568.0-7574.0, 7592.0-7606.0, 7628.0-7644.0

Objective: Put on pump  
Present Operation: Rig repairs.

Operations Summary:  
Made rig repairs. Finished RIH w/ production string. Pumped 60

myrb31-5 Beam Pump.txt  
bbl water down annulus. NDBOP. NUWH. Hot oiled tubing. SION.

|                     |                    |
|---------------------|--------------------|
| Daily Cost Item:    | Amount:            |
| Rig                 | 1,200              |
| Rods / pump / misc. |                    |
| Kill truck          | 500                |
| Rental Equipment    | 350                |
| Transportation      |                    |
| Contract Labor      | 235                |
| Daily Cost:         | 2,285              |
| Previous Cost:      | 4,085              |
| Cumulative Cost:    | 6,370              |
| Load Oil:           | Load Water:        |
| Used: 35.0          | Used: 60.0         |
| Rec. daily: 0.0     | Rec. daily: 0.0    |
| Cum. rec: 0.0       | Cum. rec: 0.0      |
| Left to rec: 35.0   | Left to rec: 110.0 |
| Rig Hrs: 0.0        | Cum: 0.0           |
| Personnel:          |                    |
| Rig:                | Gulf:              |
| Service:            | Total:             |

Equipment:  
Weather:  
Road Conditions:

\*\*\*\*\*

Conoco Inc New Mexico Well Workover Application MCF History

Well Workover Date = 08/20/2001

Compl Name - Compl  
MEYER B-31 NO. 5 / 5LLR

Compl ID - Compl  
1893792

Compl Legacy Cd -  
6823138 5LLR

API Well Cd - Compl  
300253496000

Rsvr Name - Compl  
HARDY STRAWN;NORTH

PUN / SUFFIX  
1208467 F 2530

Compl  
LEA

Sect  
31

TWN  
20

RNG  
38

Dir  
E

Cnty  
Name -

| Production Date | Workover Indicator                                      | HARDY<br>STRAWN;NORTH | Period MCF<br>Summed | Average MCF For the<br>Period |
|-----------------|---------------------------------------------------------|-----------------------|----------------------|-------------------------------|
| Aug-00          | Pre Workover Period                                     | 28,150                |                      |                               |
| Sep-00          | Pre Workover Period                                     | 31,866                |                      |                               |
| Oct-00          | Pre Workover Period                                     | 30,893                |                      |                               |
| Nov-00          | Pre Workover Period                                     | 17,444                |                      |                               |
| Dec-00          | Pre Workover Period                                     | 19,322                |                      |                               |
| Jan-01          | Pre Workover Period                                     | 17,131                |                      |                               |
| Feb-01          | Pre Workover Period                                     | 12,912                |                      |                               |
| Mar-01          | Pre Workover Period                                     | 11,395                |                      |                               |
| Apr-01          | Pre Workover Period                                     | 10,523                |                      |                               |
| May-01          | Pre Workover Period                                     | 10,294                |                      |                               |
| Jun-01          | Pre Workover Period                                     | 10,481                |                      |                               |
| Jul-01          | Pre Workover Period                                     | 12,862                | 213,273              | 17,773                        |
| Aug-01          | Post Workover Period --> Installed Beamer Pump 08/20/01 | 18,571                |                      |                               |
| Sep-01          | Post Workover Period                                    | 26,457                |                      |                               |
| Oct-01          | Post Workover Period                                    | 13,905                | 58,933               | 19,644                        |

