


W. W. WEATHERLY No. 2

PRESENT CONDITIONS

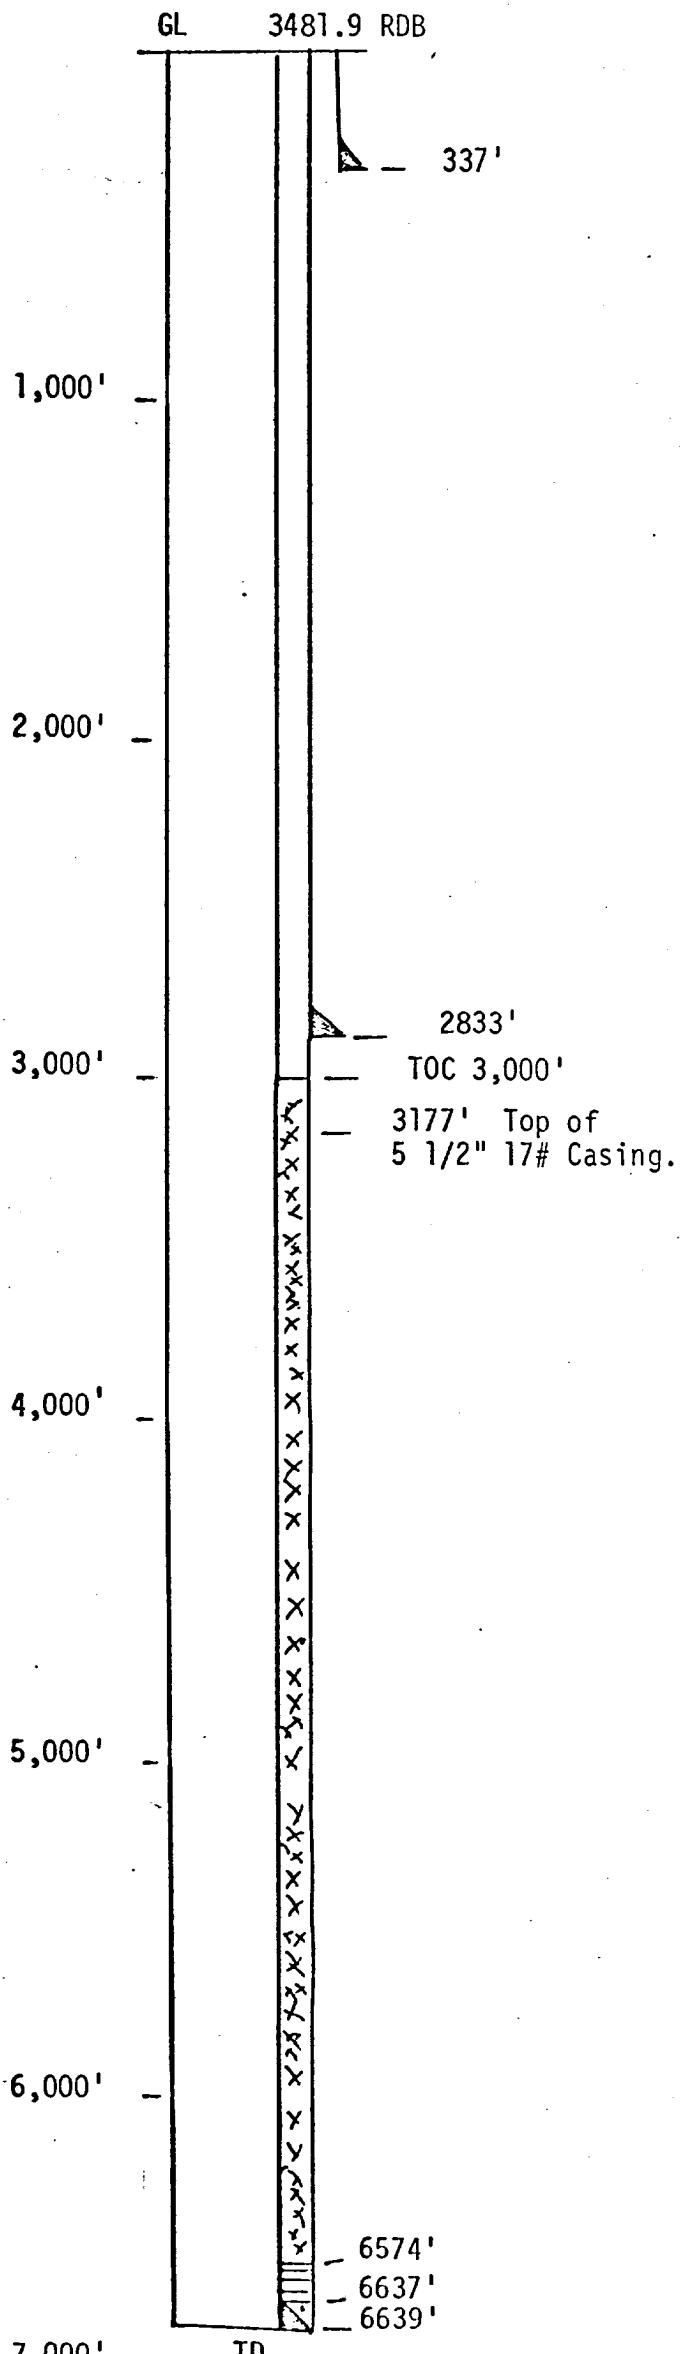

Completed 9-10-47

Casing

10 3/4" @ 337' 32.75#, H-40, 8 Rd
Cement w/300 sacks to surface in 13 3/8" hole
7 5/8" @ 2833.26', 26.4#, J-55, 8 Rd.
Cement w/1200 sacks to surface in 9 7/8" hole

5 1/2" casing @ 6639', 15.5#, J-55 3177' Top
17# J-55, 3451' bot.
Cement w/550 sacks, Top cement 3,000' TS,
in 6 3/4" hole

Completion

Perf. 6574-6584 w/8 SPD (15/32")
Test 200' oil and gas cut mud
Perf. 6584-6637 w/8 SPF (15/32')

Acidized

2000 gal. 15% HCL
Test 109 BO, 33 BAW
Flowed 115 BO 2% BS&W TP 325#

WO #1 6-30-57

Fraced w/20,000 gal. oil w/15,000# sand down
5 1/2" casing and tubing. BDP 3500#, MP 3500#
Minimum Pressure 3500#, 5 Min. SI 2200#,
Flushed w/210 bbls. oil Max. IR 7.3 BPM,
AIR 4.7 BPM

Before WO 19 BO, Flowing TP 150#

After WO 73 BO, Flowing TP 150#

RECEIVED

APR 1 1971

OIL CONSERVATION COMM.
HOBBBS, N. M.
