

#65 30-039-07593
#537 30-039-25021 4535

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit NE Sec. 22 Twp 29 Rng 7

Name of Well/Wells or Pipeline Serviced SAN JUAN 29-7 UNIT #65, #537

cps 97w

Elevation 6783' Completion Date 6/3/68 Total Depth 425' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:

Fresh, Clear, Salty, Sulphur, Etc. 300'

Depths gas encountered: N/A

Type & amount of coke breeze used: 8760 lbs.

Depths anodes placed: 402', 396', 390', 384', 378', 350', 344', 338', 309'

Depths vent pipes placed: 402' OF 3/4" HOSE

Vent pipe perforations: 402'

Remarks: gb #2 & gb #1

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

CATHODIC PROTECTION CONSTRUCTION REPORT

DAILY LOG

N/O 2 GB.

Date 6-3-68

$$4^3 \times 1 \neq 67 = 300$$

Well Name San Juan 29-7 #65				CPS No. 97 W1			
Location NE 22-29-7				Work Order No. 184-53546-50-20			
Anode Hole Depth 425		Total Drilling Rig Time 37 1/2 Hrs		Type & Size Bit Used 7 3/8, 55615 = 340		No. Sacks Mud Used 1	
No. Sacks Lost Circulation Mat'l Used 1		Anode Depth					
		# 1 402	# 2 396	# 3 390	# 4 384	# 5 378	# 6 350
Total Lbs. Coke Used 8760		Anode Output (Volts)					
		# 1 3.2	# 2 4.7	# 3 5.0	# 4 4.0	# 5 2.4	# 6 3.5
Total Circuit Resistance				No. Ft. Surface Cable Conduit			
Volts 12.9		Amps 10.3	Ohms 1.25	347' on Anodes 174' surface 3645			

Drilling Log (Attach Hereto). ☐

Remarks:

3/4" Hose to No1 Anode, Perforated all
20 lbs Barafos Circulated thru. Hole


8 Anodes = 13.0 V 9.2 A = 1.41 V

All Construction Completed

Arrels

(Signature)

GROUND BED LAYOUT SKETCH

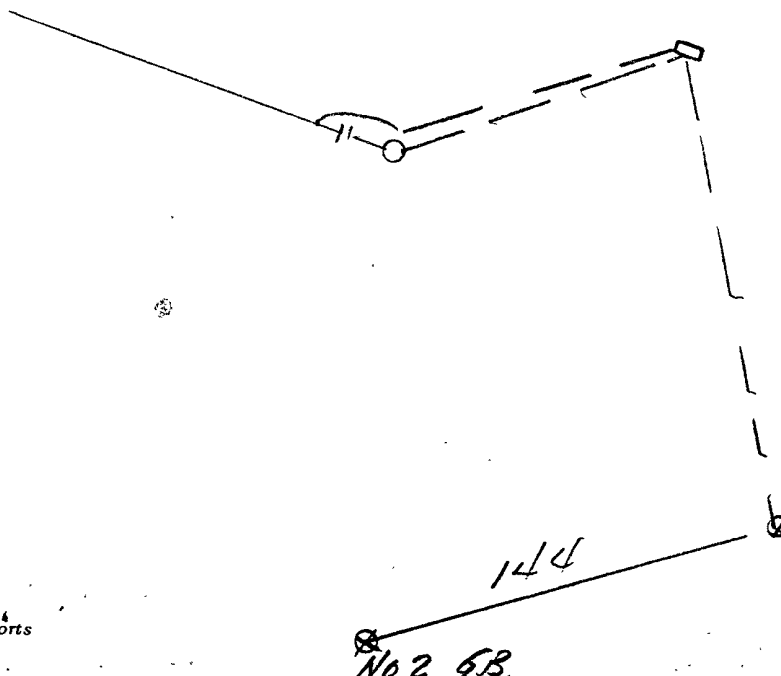

Annexa

Company Supervisor:
