

submitted in lieu of Form 3160-5

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Sundry Notices and Reports on Wells

1. Type of Well
GAS

2. Name of Operator
BURLINGTON
RESOURCES OIL & GAS COMPANY

3. Address & Phone No. of Operator
PO Box 4289, Farmington, NM 87499 (505) 326-9700

4. Location of Well, Footage, Sec., T, R, M
1450' FNL, 1785' FWL, Sec.19, T-30-N, R-6-W, NMPM

5. Lease Number
SF-080711
6. If Indian, All. or
Tribe Name
7. Unit Agreement Name
San Juan 30-6 Unit
8. Well Name & Number
San Juan 30-6 U #139
9. API Well No.
30-039-26509
10. Field and Pool
Basin Dakota
11. County and State
Rio Arriba Co, NM

12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Type of Submission

Type of Action

☐ Notice of Intent	☐ Abandonment	☐ Change of Plans
☒ Subsequent Report	☐ Recompletion	☐ New Construction
☐ Final Abandonment	☐ Plugging Back	☐ Non-Routine Fracturing
	☐ Casing Repair	☐ Water Shut off
	☐ Altering Casing	☐ Conversion to Injection
	☒ Other -	

13. Describe Proposed or Completed Operations

Attached is a revised blow-out preventer diagram for the subject well.

14. I hereby certify that the foregoing is true and correct.

Signed [Signature] Title Regulatory Supervisor Date 10/5/00
no

(This space for Federal or State Office use)

APPROVED BY _____ Title _____


CONDITION OF APPROVAL, if any:

ACCEPTED FOR RECORD

NOV 22 2000

Date [Signature]
FARMINGTON FIELD OFFICE


Completion/Workover Rig
BOP Configuration
3,000 psi System

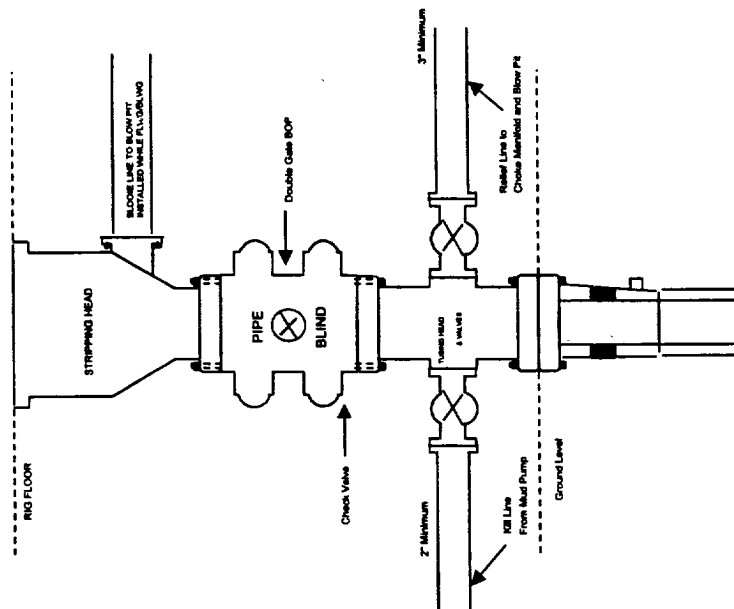

Minimum BOP installation for all Completion/Workover Operations. 7-1/16" bore, 3000 psi minimum working pressure double gate BOP to be equipped with blind and pipe rams. A stripping head to be installed on the top of the BOP. All equipment is 3000 psi working pressure or greater.

Figure #3


Drilling Rig
Choke Manifold Configuration
3000 psi System

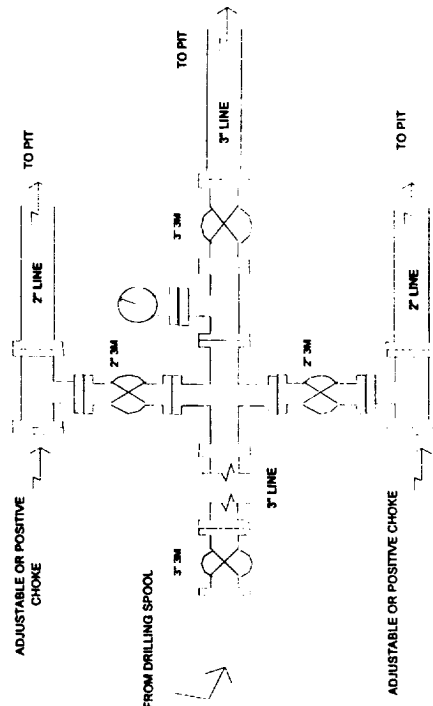

Choke manifold installation from Surface Casing Point to Total Depth. 3,000psi working pressure equipment with two chokes.

Figure #2

Drilling Rig
3000 psi System

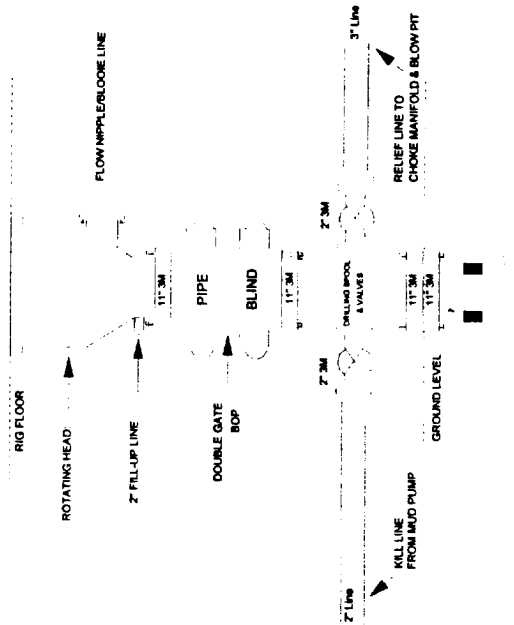

BOP installation from Surface Casing Point to Total Depth. 1 1/2" Bore 10" Nominal, 3000 psi working pressure double gate BOP to be equipped with blind rams and pipe rams. A rotating head on top of ram preventers. All BOP equipment is 3,000 psi working pressure

Figure #1
