

U.S. Department of the Interior BUREAU OF LAND MANAGEMENT Sundry Print Report 10 06/17/2022

Well Name: SCHWERDTFERGER Well Location: T27N / R11W / SEC 5 / County or Parish/State: SAN

NESE / 36.6014 / -108.02094 JUAN / NM

Well Number: 14 Type of Well: CONVENTIONAL GAS Allottee or Tribe Name:

VELL

Lease Number: NMSF080382A Unit or CA Name: Unit or CA Number:

US Well Number: 3004506827 Well Status: Gas Well Shut In Operator: HILCORP ENERGY

COMPANY

Notice of Intent

Sundry ID: 2677229

Type of Submission: Notice of Intent

Type of Action: Plug and Abandonment

Date Sundry Submitted: 06/16/2022 Time Sundry Submitted: 08:57

Date proposed operation will begin: 07/01/2022

Procedure Description: Hilcorp Energy Company requests permission to P&A the subject well per the attached procedures, current and proposed wellbore schematics. The Pre-Disturbance Site Visit was held on 4/6/2022 with Roger Herrera/BLM. The Re-Vegetation Plan is attached. A closed loop system will be used.

Surface Disturbance

Is any additional surface disturbance proposed?: No

NOI Attachments

Procedure Description

 $Schwerdtfeger_14_NOI_P_A_Packet_20220616085703.pdf$

Page 1 of 2

eived by OCD: 6/17/2022 1:06:26 PM Well Name: SCHWERDTFERGER Well Location: T27N / R11W / SEC 5 /

NESE / 36.6014 / -108.02094

County or Parish/State: SAN 2 of

JUAN / NM

Well Number: 14 Type of Well: CONVENTIONAL GAS **Allottee or Tribe Name:**

Unit or CA Name: Lease Number: NMSF080382A **Unit or CA Number:**

US Well Number: 3004506827 Well Status: Gas Well Shut In **Operator: HILCORP ENERGY**

COMPANY

Conditions of Approval

Specialist Review

General_Requirement_PxA_20220616113541.pdf

2677229_NOIA_14_3004506827_KR_06162022_20220616113523.pdf

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: AMANDA WALKER Signed on: JUN 16, 2022 08:57 AM

Name: HILCORP ENERGY COMPANY Title: Operations/Regulatory Technician

Street Address: 1111 TRAVIS ST.

City: HOUSTON State: TX

Phone: (346) 237-2177

Email address: mwalker@hilcorp.com

Field

Representative Name:

Street Address:

City: State: Zip:

Phone:

Email address:

BLM Point of Contact

Signature: Kenneth Rennick

BLM POC Name: KENNETH G RENNICK BLM POC Title: Petroleum Engineer

BLM POC Phone: 5055647742 BLM POC Email Address: krennick@blm.gov

Disposition: Approved Disposition Date: 06/16/2022



P&A Procedure

General Information				
Well Name	Schwerdtfeger #14	Date:	6/15/2022	
API:	30-045-06827	AFE#		
Field:	San Juan South	County	San Juan	
Status:	ACOI			
Subject:	Permanently P&A wellbore			
Ву:	Michael Wissing			

Well Data

Surface Casing: 9-5/8" 29.3# F-25 at 103'

Intermediate Casing: 5-1/2" 14# H-40 csg at 1,883'

Production Casing: 4" 10.46# UTFJ J-55 at 2,080'

Production Tubing: 2-3/8" 4.7# J-55 at 1,712 (4/2004)

Rod String: 3/4" guided/slick rods + insert pump (7/2009)

Current PBTD: 2,032' (cement plug)

KB: 9'

Bradenhead: 2018-2022 had all 5 BH tests at 0 psi

Hold PJSM prior to begin all operations. Properly document all operations via the JSA process. Ensure that all personnel onsite abide by HEC safety protocol, including PPE, housekeeping, and standard guidelines. Verify cathodic protection is off and wellhead instrumentation is properly disconnected from the wellhead. Comply with all NMOCD, BLM, Navajo Nation, and HEC safety and environmental regulations. Verify there is no H2S present prior to beginning operations. If any H2S is present, take the necessary actions to ensure that the location is safe prior to beginning operations. Observe and record pressures across all strings daily, prior to beginning operations. TA work will be completed by a rig. The P&A work will be completed rigless.

Remember to notify NMOCD and BLM 24 hours prior to starting operations on location. This procedure is contingent upon P&A sundry approval by the NMOCD & BLM.

P&A Rig Procedure


Part I:

- 1. MIRU P&A rig and equipment. Record pressures on all strings.
 - a. Record daily pressures on all casing strings.
 - b. Document all onsite agency agents and all approved changes to approved P&A NOI.
- 2. Unseat rod pump from seat nipple and POOH with rod string/pump. NU BOP & test. TOOH with 2-3/8" production tbg.
- 3. RIH with 4" casing scraper or gauge ring to +/- 1,855'.
- 4. MU 4" CIBP and RIH. Set CIBP at 1,850'.
- 5. Load wellbore with water and circulate wellbore clean. Pressure test the casing to 500 psi to verify wellbore integrity and plug is set.
- 6. ND BOP and RD P&A rig.


Part II:

- 1. MIRU cement pump truck & poly pipe spool.
 - a. Record daily pressures on all casing strings.
 - b. Document all onsite agency agents and all approved changes to approved P&A NOI.
- 2. ND whd, NU circulation pump equipment and poly pipe spooling unit, RIH with 2" poly tbg to +/-1,850'.
- 3. Plug #1 (Surface, Shoe at 103', Ojo top at XXX', Kirtland top at 840', FRC top at 1,600', PC top 1,860', top PC perf at 1,900'): RU cementers and establish circulation back to surface with water. Pump a 1,850' cmt plug inside the 4" csg & 2" poly pipe from Surface 1,850' using 22.7 bbls (93 sx) of Type III, 14.6 ppg, 1.37 yield cement.
- 4. Verify all pressures on all strings are at 0 psi.
- 5. Cut off the wellhead & poly pipe. Weld on labeled P&A marker. Top off all casing strings (if needed) and a portion of the well cellar with cement.
- 6. RDMO cement pump and equipment.



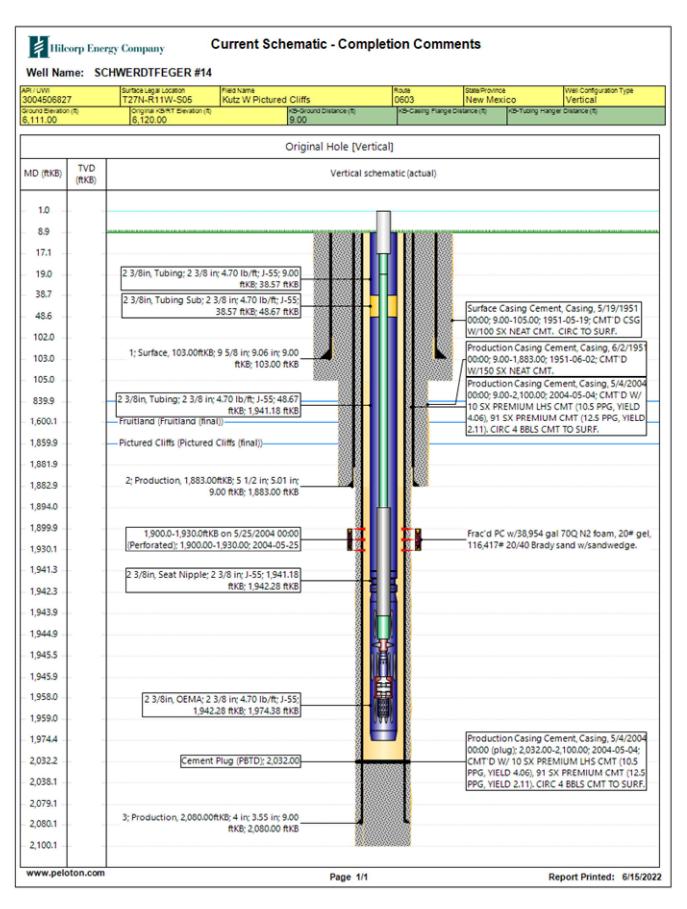



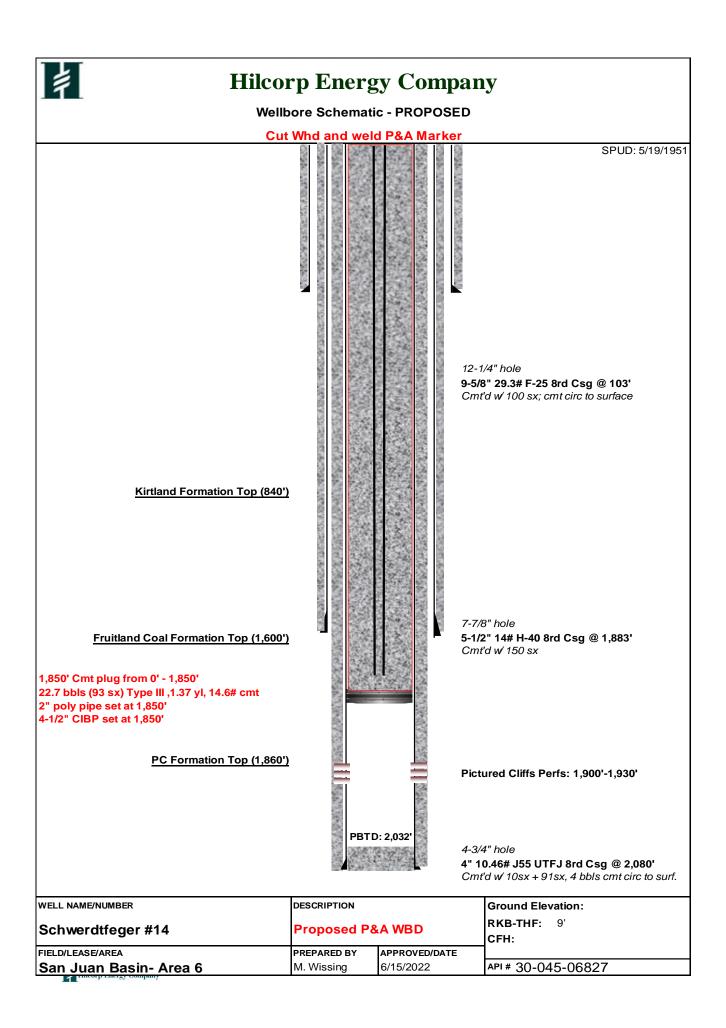

Hilcorp Energy
P&A Final Reclamation Plan
Schwerdtfeger 14
API: 30-045-06827
T27N-R11W-Sec. 5-Unit I
LAT: 36.601445 LONG: -108.020893 NAD 27
Footage: 1650' FNL & 990' FWL

San Juan County, NM

1. PRE- RECLAMATION SITE INSPECTION

A pre-reclamation site inspection was completed with Roger Herrera from the BLM and Eufracio Trujillo, Hilcorp Energy SJ South Construction Foreman on April 6, 2022.

2. LOCATION RECLAMATION PROCEDURE

- 1. Reclamation work will begin in summer.
- 2. Removal of all equipment, anchors, flowlines, cathodic, and pipelines.
- 3. All trash and debris will be removed within a 50' buffer outside of the location disturbance during reclamation.
- 4. Close out BGT that are currently on location when results are clear.
- 5. Location will be reclaimed when twinned well is plugged.
- 6. Remove junk pipe from road into location.
- 7. Remove all gravel from berms, pads, and meter run and use on lease road where needed.
- 8. Enterprise meter run will need to blind and barricade riser.

3. ACCESS ROAD RECLAMATION PROCEDURE

The well access road will not be reclaimed at this time.

4. SEEDING PROCEDURE

No seeding will be done at this time.

5. WEED MANAGEMENT

1. No noxious weeds were identified during this onsite.

GENERAL REQUIREMENTS FOR PERMANENT ABANDONMENT OF WELLS ON FEDERAL AND INDIAN LEASES FARMINGTON FIELD OFFICE

- 1.0 The approved plugging plans may contain variances from the following <u>minimum general</u> requirements.
 - 1.1 Modification of the approved plugging procedure is allowed only with the prior approval of the Authorized Officer, Farmington Field Office.
 - 1.2 Requirements may be added to address specific well conditions.
- 2.0 Materials used must be accurately measured. (densometer/scales)
- 3.0 A tank or lined pit must be used for containment of any fluids from the wellbore during plugging operations and all pits are to be fenced with woven wire. These pits will be fenced on three sides and once the rig leaves location, the fourth side will be fenced.
 - 3.1 Pits are not to be used for disposal of any hydrocarbons. If hydrocarbons are present in the pit, the fluids must be removed prior to filling in.
- 4.0 All cement plugs are to be placed through a work string. Cement may be bull-headed down the casing with prior approval. Cement caps on top of bridge plugs or cement retainers may be placed by dump bailer.
 - 4.1 The cement shall be as specified in the approved plugging plan.
 - 4.2 All cement plugs placed inside casing shall have sufficient volume to fill a minimum of 100' of the casing, or annular void(s) between casings, plus an excess volume sufficient to provide for 50 linear feet of fill above the plug.
 - 4.3 Surface plugs may be no less than 50' in length.
 - 4.4 All cement plugs placed to fill annular void(s) between casing and the formation shall be of sufficient volume to fill a minimum of 100' of the annular space plus 100% excess, calculated using the bit size, or 100' of annular capacity, determined from a caliper log, plus an excess volume sufficient to provide for 50 linear feet of fill above the plug.
 - 4.5 All cement plugs placed to fill an open hole shall be of sufficient volume to fill a minimum of 100' of hole, as calculated from a caliper log, plus an excess volume sufficient to provide for 50 linear feet of fill above the plug. In the absence of a caliper log, an excess of 100% shall be required.
 - 4.6 A cement bond log or other accepted cement evaluation tool is required to be run if one had not been previously ran or cement did not circulate to surface during the original casing cementing job or subsequent cementing jobs.

2

- 5.0 All cement plugs spotted across, or above, any exposed zone(s), when; the wellbore is not full of fluid or the fluid level will not remain static, and in the case of lost circulation or partial returns during cement placement, shall be tested by tagging with the work string.
 - 5.1 The top of any cement plug verified by tagging must be at or above the depth specified in the approved plan, without regard to any excess.
 - 5.2 Testing will not be required for any cement plug that is mechanically contained by use of a bridge plug and/or cement retainer, if casing integrity has been established.
 - 5.3 Any cement plug which is the only isolating medium, for a fresh water interval or a zone containing a prospectively valuable deposit of minerals, shall be tested by tagging.
 - 5.4 If perforations are required below the surface casing shoe, a 30 minute minimum wait time will be required to determine if gas and/or water flows are present. If flow is present, the well will be shut-in for a minimum of one hour and the pressure recorded. Short or long term venting may be necessary to evacuate trapped gas. If only a water flow occurs with no associated gas, shut well in and record the pressures. Contact the Engineer as it may be necessary to change the cement weight and additives.
- 6.0 Before setting any cement plugs the hole needs to be rolled. All wells are to be controlled by means of a fluid that is to be of a weight and consistency necessary to stabilize the wellbore. This fluid shall be left in place as filler between all plugs.
 - 6.1 Drilling mud may be used as the wellbore fluid in open hole plugging operations.
 - 6.2 The wellbore fluid used in cased holes shall be of sufficient weight to balance known pore pressures in all exposed formations.
- 7.0 A blowout preventer and related equipment (BOPE) shall be installed and tested prior to working in a wellbore with any exposed zone(s); (1) that are over pressured, (2) where the pressures are unknown, or (3) known to contain H_2S .
- 8.0 Within 30 days after plugging work is completed, file a Sundry Notice, Subsequent Report of Abandonment (Form 3160-5), five copies, with the Field Manager, Bureau of Land Management, 6251 College Blvd., Suite A, Farmington, NM 87402. The report should show the manner in which the plugging work was carried out, the extent, by depth(s), of cement plugs placed, and the size and location, by depth(s), of casing left in the well. Show date well was plugged.
- 9.0 All permanently abandoned wells are to be marked with a permanent monument as specified in 43 CFR 3162.6(d). Unless otherwise approved.
- 10.0 If this well is located in a Specially Designated Area (SDA), compliance with the appropriate seasonal closure requirements will be necessary.

All of the above are minimum requirements. Failure to comply with the above conditions of approval may result in an assessment for noncompliance and/or a Shut-in Order being issued pursuant to 43 CFR 3163.1. You are further advised that any instructions, orders or decisions issued by the Bureau of Land Management are subject to administrative review pursuant to 43 CFR 3165.3 and appeal pursuant to 43 CFR 3165.4 and 43 CFR 4.700.

(October 2012 Revision)

UNITED STATES DEPARTMENT OF THE INTERIOR BUREAU OF LAND MANAGEMENT FARMINGTON DISTRICT OFFICE

6251 COLLEGE BLVD. FARMINGTON, NEW MEXICO 87402

AFMSS 2 Sundry ID 2677229

Attachment to notice of Intention to Abandon

Well: Schwerdtferger 14

*Fill up wellbore with cement proposal. BLM Geology Report not applicable.

CONDITIONS OF APPROVAL

- 1. Plugging operations authorized are subject to the attached "General Requirements for Permanent Abandonment of Wells on Federal and Indian Lease."
- 2. Farmington Office is to be notified at least 24 hours before the plugging operations commence at (505) 564-7750.

You are also required to place cement excesses per 4.2 and 4.4 of the attached General Requirements.

Office Hours: 7:45 a.m. to 4:30 p.m.

K. Rennick 06/16/2022

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II 811 S. First St., Artesia, NM 88210 Phone:(575) 748-1283 Fax:(575) 748-9720

District III 1000 Rio Brazos Rd., Aztec, NM 87410 Phone:(505) 334-6178 Fax:(505) 334-6170

1220 S. St Francis Dr., Santa Fe, NM 87505 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 S. St Francis Dr. **Santa Fe, NM 87505**

CONDITIONS

Action 118415

CONDITIONS

Operator:	OGRID:
HILCORP ENERGY COMPANY	372171
1111 Travis Street	Action Number:
Houston, TX 77002	118415
	Action Type:
	[C-103] NOI Plug & Abandon (C-103F)

CONDITIONS

Created	Condition Condition	Condition Date
kpickfo	Notify NMOCD 24 Hours Prior to beginning operations	6/24/2022
