

**UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**

RECEIVED

Sundry Notices and Reports on Wells

MAR 07 2012

Farmington Field Office
Bureau of Land Management
Lease Number
SF-078913

1. Type of Well
GAS

6. If Indian, All. or
Tribe Name

2. Name of Operator

7. Unit Agreement Name
Lindrith B Unit

ConocoPhillips

3. Address & Phone No. of Operator

8. Well Name & Number
Lindrith B Unit 15

PO Box 4289, Farmington, NM 87499 (505) 326-9700

9. API Well No.

30-039-22555

4. Location of Well, Footage, Sec., T, R, M

10. Field and Pool
W. Lindrith Gallup DK

Unit O (SWSE), 1157' FSL & 2293' FEL, Section 21, T24N, R3W, NMPM

11. County and State
Rio Arriba, NM

12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Type of Submission

☒ Notice of Intent

Type of Action

☐ Abandonment

☐ Change of Plans

☒ Other ☐ Cathodic

☐ Recompletion

☐ New Construction

☐ Subsequent Report

☐ Plugging

☐ Non-Routine Fracturing

☐ Casing Repair

☐ Water Shut off

☐ Final Abandonment

☐ Altering Casing

☐ Conversion to Injection

13. Describe Proposed or Completed Operations

Attached is a drawing for the placement of the cathodic ground, rectifier and cable for the subject well.

RCVD MAR 9 '12

OIL CONS. DIV.
DIST. 3

14. I hereby certify that the foregoing is true and correct.

Signed

Crystal Tafoya

Crystal Tafoya

Title Staff Regulatory Tech

Date 3/7/2012

(This space for Federal or State Office use)

APPROVED BY

Mark Kelly

Title

**ENVIRONMENTAL
COMPLIANCE TEAM LEAD**

Date

3-8-12


CONDITION OF APPROVAL, if any:

Title 18 U S C Section 1001, makes it a crime for any person knowingly and willfully to make any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction

RECEIVED
A

Lindrith B Unit #15

Section 21, T24N, R3W, N.M.P.M., Rio Arriba County, NM

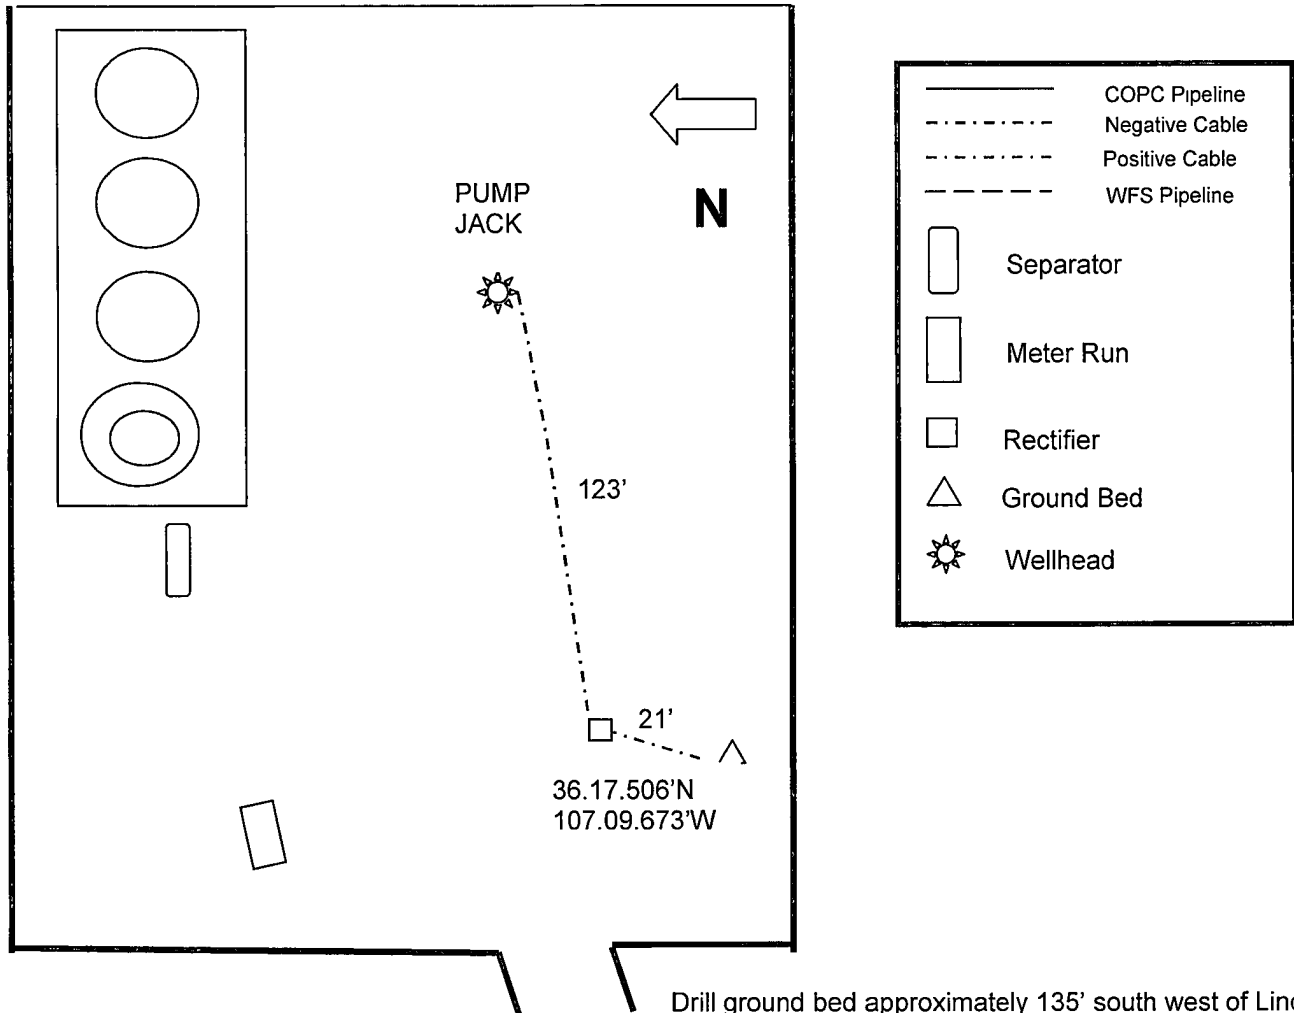

Drill ground bed approximately 135' south west of Lindrith B Unit #15 well head at staked location. Install solar CP at staked location. Install cable to new ground bed and to Lindrith B Unit #15 well head at lengths below.

Lindrith B Unit #15:

Negative: 123'

Positive: 21'

Total Ditch: 144'
