

NMDCD Rec'd 2-6-18

Chaco 2206 2H 226H
API # 30-043-21169




Location				Surface:	Spud Date:	Elevation:
SHL: 1686' FNL 328' FEL	Sec: 2	Twnshp: 22N	Rge: 6W Unit: H	Lat: 36.1696739	3/3/2014	6896' GR
BHL: 1540' FNL & 231' FWL	Sec:2	Twnshp: 22N	Rge: 6W Unit: E	Long: -107.4300613	Completion: 6/16/2014	County San Juan
				Pool Name: Lybrook Gallup	First Delivery: 7/7/2014	KB 14.5"
				Wellbore Updated: 2/1/2018		

Rods	Length
1.25" Polish Rod	36
1"X4' Pony rod	4
1"X8" Pony rod	8
17- 1" Slick rods	425
69-1" guided rods	1725
31-7/8" guided rods	775
70-7/8" slick rods	1750
10-7/8" guided rods	250
24-1" guided rods	600
2-1/2" X 1.5" x 30'x31' x 33' pump w/ max stk 335' weatherford	33
1.25" X 19' dip tube	19
Enercat tool x 7'	7

	MD	TVD
Ojo Alamo	1288'	1280'
Kirtland	1546'	1534'
Pictured Cliffs	1861'	1845'
Lewis	1977'	1960'
Chacra	2308'	2284'
Cliffhouse	3404'	3361'
Menefee	3424'	3380'
Pt. Lookout	4157'	4101'
Mancos	4348'	4290'
Gallup	4734'	4675'

Tubing :Landed @ 5666" w/ 175jts of 2-7/8" EUE tubing, 6.5#, J-55, w/ SN @ 5616'.

Tubing	OD	ID	Lngh (ft)	Dpth (ft)
Hanger	7-1/16"	2.441"	0.50	15'
161jts tubing	2-7/8"	2.441"	5183.52	5198.52'
Weatherford TAC	5.4375"	2.441"	2.36	5200.88'
13 jts tubing	2-7/8"	2.441"	415.30	5616.18'
SN 2.28	3.125"	2.280"	1.07	5616.25'
Sand Screen	3.1875"	2.441"	8.33	5624.58'
Pin X Pin EUE NPL	3.125"	2.441"	0.15	5624.73'
Sand Screen	3.1875"	2.441"	8.33	5633.06'
1 jt tubing	2-7/8"	2.441"	32.46	5665.52'
Purge Valve	3.630"	2.441"	0.74	5666.26'

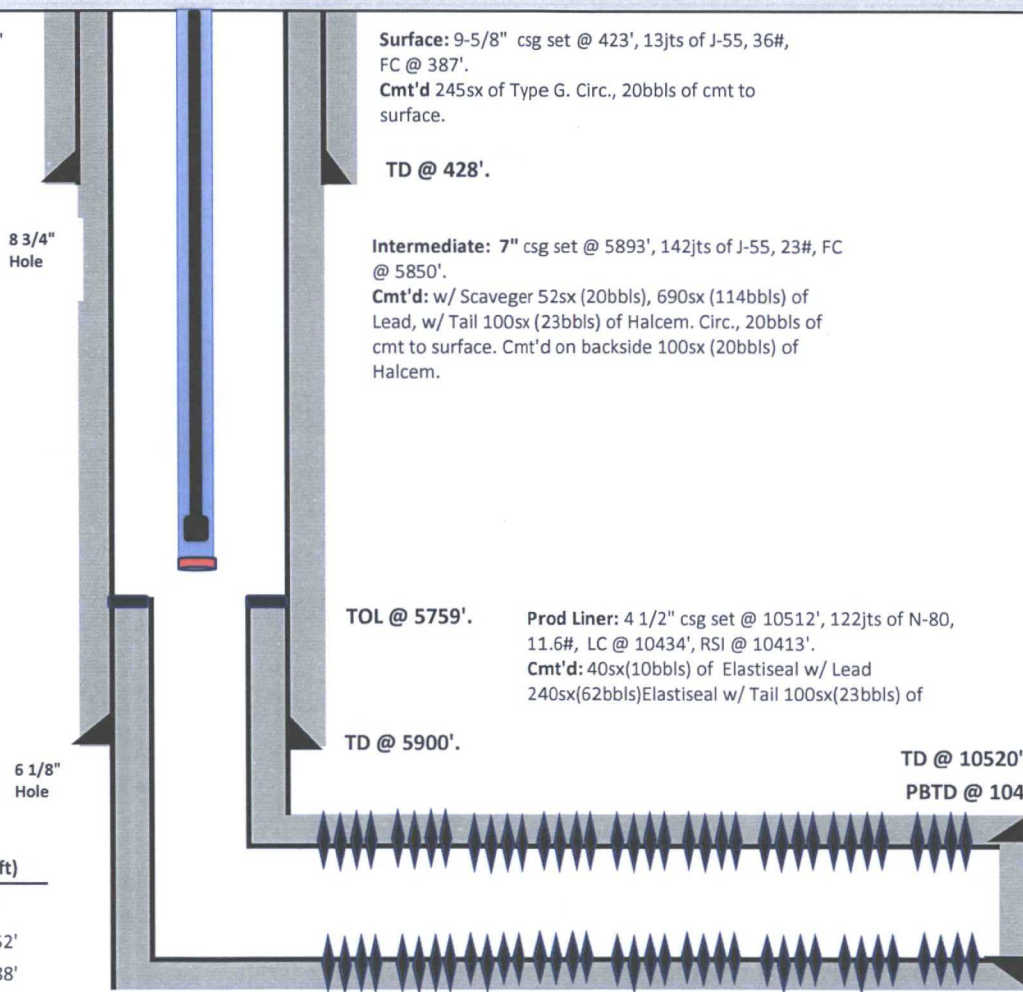

Surface: 9-5/8" csg set @ 423', 13jts of J-55, 36#, FC @ 387'.
Cmt'd 245sx of Type G. Circ., 20bbbs of cmt to surface.

TD @ 428'.

Intermediate: 7" csg set @ 5893', 142jts of J-55, 23#, FC @ 5850'.

Cmt'd: w/ Scavenger 52sx (20bbbs), 690sx (114bbbs) of Lead, w/ Tail 100sx (23bbbs) of Halcem. Circ., 20bbbs of cmt to surface. Cmt'd on backside 100sx (20bbbs) of Halcem.

TOL @ 5759'.

Prod Liner: 4 1/2" csg set @ 10512', 122jts of N-80, 11.6#, LC @ 10434', RSI @ 10413'.

Cmt'd: 40sx(10bbbs) of Elastiseal w/ Lead 240sx(62bbbs)Elastiseal w/ Tail 100sx(23bbbs) of

TD @ 5900'.

TD @ 10520'.

PBTD @ 10434'.

Perf'd w/ 4SPF, 0.40" diameter @ 5898'- 10413' w/ 330 total holes.

Frac'd w/ 14 stages of 20/40 sand of 2,990,426# @ 5658' - 11518'.

PV
