

2 = 30-045-10178
17 = 30-045-23432
200 = 30-045-26949

3545

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL INC. Location: Unit G Sec. 35 Twp 31 Rng 10

Name of Well/Wells or Pipeline Serviced ATLANTIC C #2, #17, #200
cps 2091w

Elevation 6401' Completion Date 7/18/74 Total Depth 520' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 240'

Depths gas encountered: N/A

Type & amount of coke breeze used: N/A

Depths anodes placed: 475', 410', 395', 370', 360', 350', 290', 280', 270', 255'

Depths vent pipes placed: N/A

Vent pipe perforations: 300'

Remarks gb #2

RECEIVED
MAY 31 1991
OIL CON. DIV.
DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL-CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Drilling Log (Attach Hereto) ☐

logged

Completion Date **7-18-74**

Well Name Atlantic #2		Location NE 35-31-10		CPS No. 379W 2091	
Type & Size Bit Used 6 3/4				Work Order No. 52249	
Anode Hole Depth 520	Total Drilling Rig Time	Total Lbs. Coke Used	Lost Circulation Mat'l Used	No. Sacks Mud Used	
Anode Depth					
# 1 475	# 2 410	# 3 395	# 4 370	# 5 360	# 6 350
# 7 290	# 8 280	# 9 27	# 10 255		
Anode Output (Amps)					
# 1 3.5	# 2 2.2	# 3 2.1	# 4 4.3	# 5 3.6	# 6 3.0
# 7 4.1	# 8 4.0	# 9 3.7	# 10 4.2		
Anode Depth					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Anode Output (Amps)					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Total Circuit Resistance				No. 8 C.P. Cable Used	No. 2 C.P. Cable Used
Volts 11.2	Amps 14.0	Ohms 0.8		180	

Remarks: **Driller said water at 240' - Start injection at 60' -**


Vent Perforated 300'
Pump Coke to Surface

\$3,509.00
72.00 Cable
\$3,481.00
139.24 TAX
\$3,620.24 TOTAL

All Construction Completed

Amels
(Signature)

GROUND BED LAYOUT SKETCH

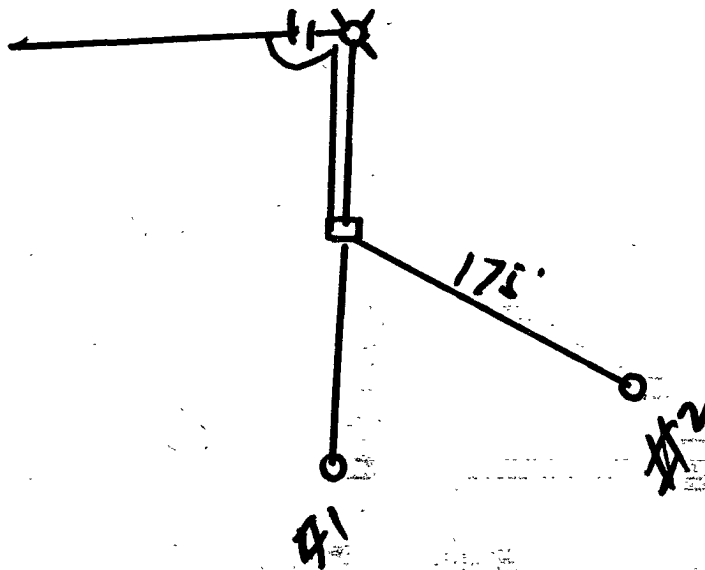

STORM WATER WELL DRILLING INC.

WATER WELL DRILLING

PHONE (303) 278-9505

CALL 1-838-4821

County

Injection at 60
Water at 240

Helper
