

submitted in lieu of Form 3160-5

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Sundry Notices and Reports on Wells

1. Type of Well
GAS

2. Name of Operator
MERIDIAN OIL

3. Address & Phone No. of Operator
PO Box 4289, Farmington, NM 87499 (505) 326-9700

4. Location of Well, Footage, Sec., T, R, M
1785'FSL, 1850'FEL Sec.18, T-26-N, R-3-W, NMPM

5. Lease Number
Jic.Contract 98
6. If Indian, All. or
Tribe Name
Jicarilla Apache
7. Unit Agreement Name
8. Well Name & Number
Jicarilla 98 #12
9. API Well No.
10. Field and Pool
Tapacitos Pic.Cliffs/
Blanco Mesa Verde
11. County and State
Rio Arriba Co, NM

12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Type of Submission

☐ Notice of Intent
☐ Subsequent Report
☐ Final Abandonment

Type of Action

☐ Abandonment
☐ Recompletion
☐ Plugging Back
☐ Casing Repair
☐ Altering Casing
☐ Other -
☐ Change of Plans
☐ New Construction
☐ Non-Routine Fracturing
☐ Water Shut off
☐ Conversion to Injection

13. Describe Proposed or Completed Operations

Per phone conversation with Robert Kent and at his request, the 8 5/8" surface casing will be pressure tested to 2000 psi. A test plug will be set at the bottom of the 8 5/8" csg and a pump truck will be used to pressure test the casing, pipe rams and blind rams to 2000 psi for 30 minutes.

Note: revision of BOP diagrams per BLM recommendation is attached.

14. I hereby certify that the foregoing is true and correct.


Signed Shirley Mondy Title Regulatory Affairs Date 8/16/93

(This space for Federal Office use)
APPROVED BY SHIRLEY MONDY Title AREA MANAGER
CONDITION OF APPROVAL, if any: Acting Date AUG 26 1993

NMOCD

MERIDIAN OIL INC.

BOP Configuration 2M psi SYSTEM

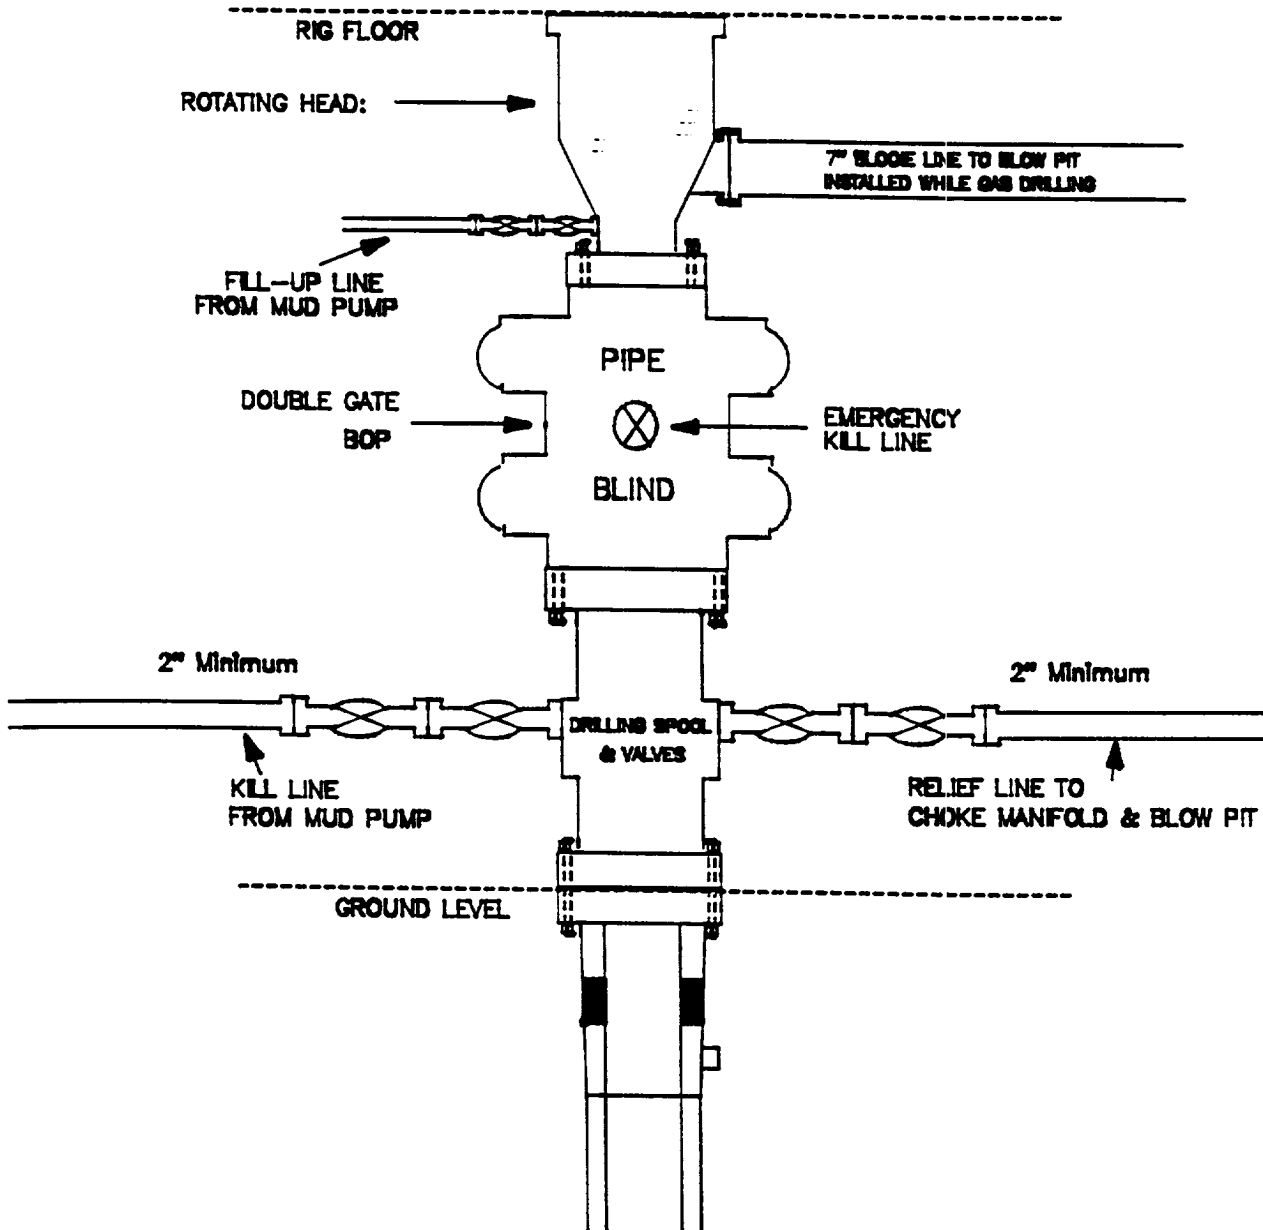


11" Bore, 2000psi minimum working pressure double gate BOP to be equipped with blind and pipe rams. A Schaffer Type 50 or equivalent rotating head to be installed on the top of the BOP. All equipment is 2000psi working pressure/or greater.

Figure #1

MERIDIAN OIL INC.


BOP Configuration
2M psi SYSTEM

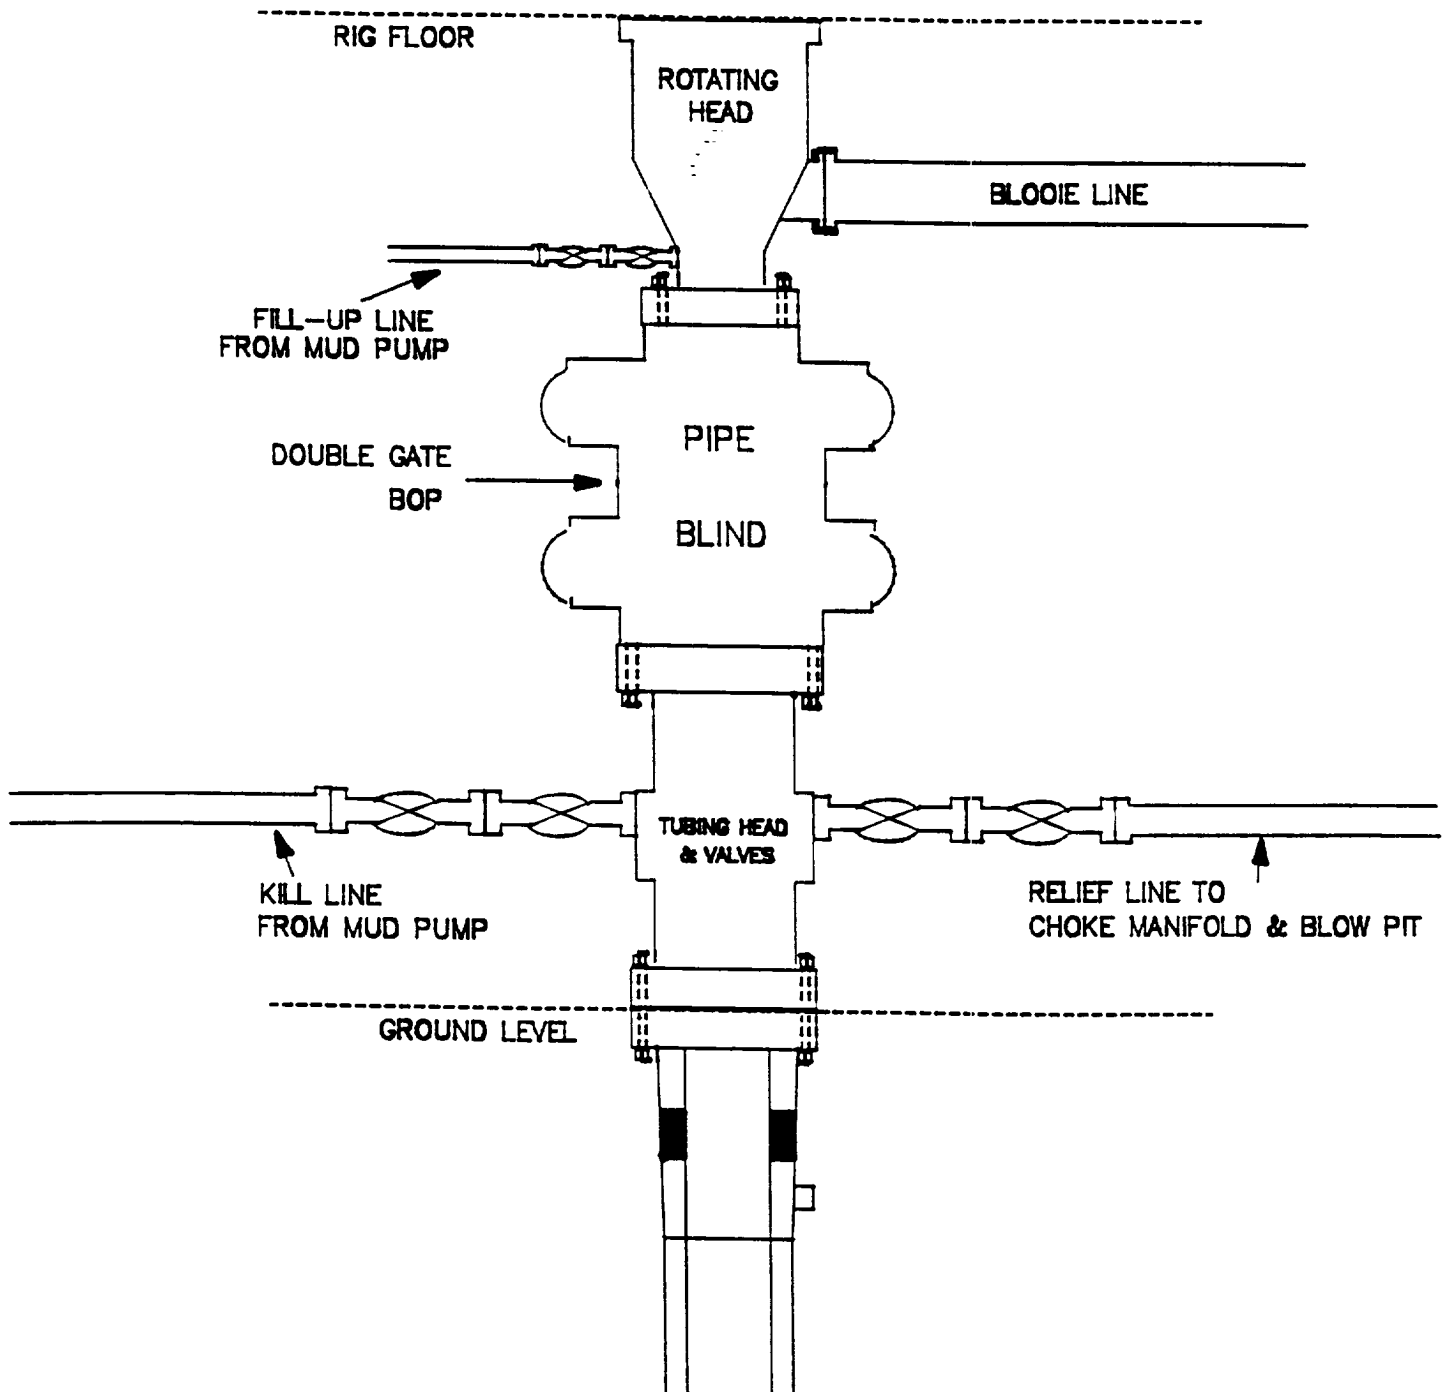

Minimum BOP installation for Completion operations. 7 1/16" Bore (6" Nominal), 3000psi minimum working pressure double gate BOP to be equipped with blind and pipe rams.

Figure #2

MERIDIAN OIL INC.
Choke Manifold Configuration
2M psi SYSTEM

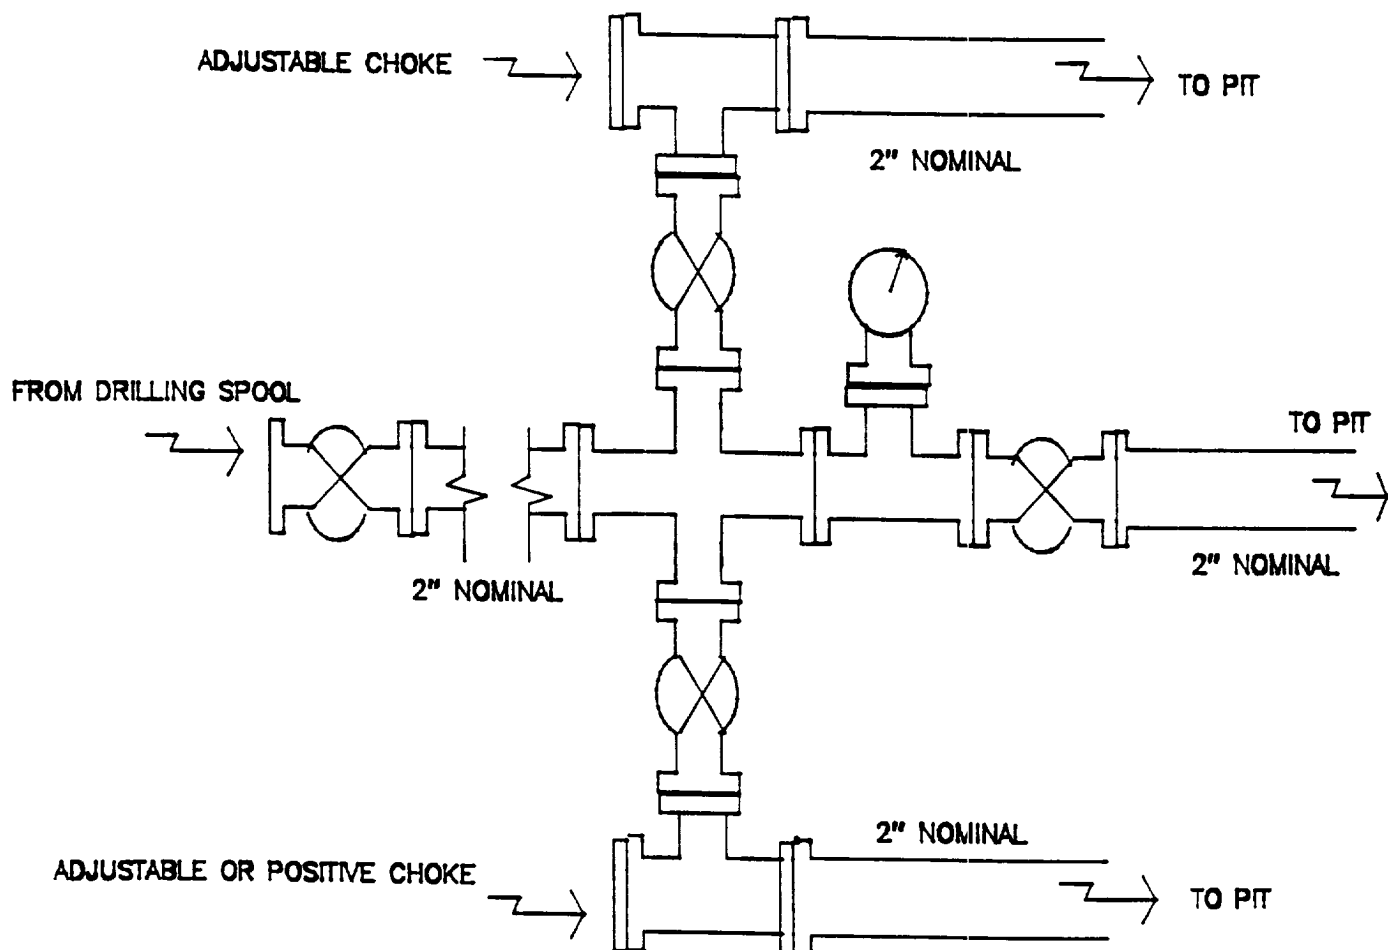

Minimum choke manifold installation from surface to Total Depth.
2" minimum, 2000psi working pressure equipment with two chokes.

Figure #3
