


TEXAS PACIFIC COAL & OIL COMPANY
STATE "AC" #1
UNIT F, 660' FSL & 1,980' FWL
SECTION 15, T10S-R36E
LEA COUNTY, NEW MEXICO

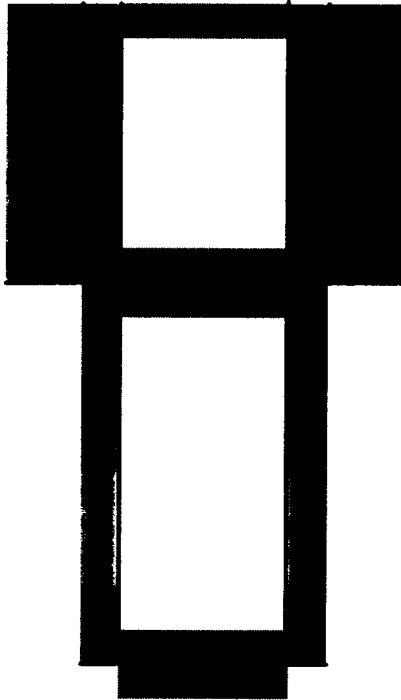


Set 10 sack cement plug at surface.

Set 100' cement plug @ 333'.

13 3/8" casing set @ 360' with 350 sacks of cement
Hole size: 17" - TOC @ surface by circ.

9 5/8" casing set @ 4,270' with 1600 sacks of cement
Hole size: 11" - TOC @ surface by circ.

Set 100' cement plug at 4,259'.



Cut off 7" casing @ 4,500'. Spot 100' cement plug at top of cutoff.

Set CIBP @ 12,000' with 35' cement on top.

Original total depth - 12,341'. 7" casing set
@ 12,253' with 200 sacks of cement.
Completed 12,274' - 12,286'

