

District I1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720**District II**811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720**District III**1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170**District IV**1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form C-101
August 1, 2011

Permit 287003

APPLICATION FOR PERMIT TO DRILL, RE-ENTER, DEEPEN, PLUGBACK, OR ADD A ZONE

1. Operator Name and Address COG OPERATING LLC 600 W Illinois Ave Midland, TX 79701		2. OGRID Number 229137
		3. API Number 30-015-47510
4. Property Code 329721	5. Property Name Myox 4 28 State Com	6. Well No. 706H

7. Surface Location

UL - Lot L	Section 4	Township 26S	Range 28E	Lot Idn L	Feet From 2397	N/S Line S	Feet From 1260	E/W Line W	County Eddy
---------------	--------------	-----------------	--------------	--------------	-------------------	---------------	-------------------	---------------	----------------

8. Proposed Bottom Hole Location

UL - Lot D	Section 28	Township 25S	Range 28E	Lot Idn D	Feet From 50	N/S Line N	Feet From 415	E/W Line W	County Eddy
---------------	---------------	-----------------	--------------	--------------	-----------------	---------------	------------------	---------------	----------------

9. Pool Information

WILDCAT;WOLFCAMP GAS (ABOLISHED)	97489
----------------------------------	-------

Additional Well Information

11. Work Type New Well	12. Well Type OIL	13. Cable/Rotary	14. Lease Type State	15. Ground Level Elevation 2997
16. Multiple N	17. Proposed Depth 22648	18. Formation Wolfcamp	19. Contractor	20. Spud Date 10/13/2020
Depth to Ground water		Distance from nearest fresh water well		Distance to nearest surface water

☒ We will be using a closed-loop system in lieu of lined pits**21. Proposed Casing and Cement Program**

Type	Hole Size	Casing Size	Casing Weight/ft	Setting Depth	Sacks of Cement	Estimated TOC
Surf	14.75	10.75	45.5	600	450	0
Int1	9.875	7.625	29.7	9500	850	0
Prod	6.75	5.5	20	22648	1500	9000

Casing/Cement Program: Additional Comments

Drill 14-3/4" hole to ~600' w/ fresh water. Run 10-3/4" 45.5# J-55 BTC casing to TD and cement to surface in one stage. Drill 9-7/8" hole to ~9,500' with cut brine emulsion. Run 7-5/8 29.7# L-80 BTC to TD and cement to surface in single stage. Drill 6-3/4" vertical hole, curve & lateral to 22,648' with OBM. Run 5-1/2" 20# P110 BTC casing from TD to surface and cement to 9000' in one stage.

22. Proposed Blowout Prevention Program

Type	Working Pressure	Test Pressure	Manufacturer
Double Ram	5000	5000	Cameron

23. I hereby certify that the information given above is true and complete to the best of my knowledge and belief. I further certify I have complied with 19.15.14.9 (A) NMAC ☒ and/or 19.15.14.9 (B) NMAC ☒ if applicable.		OIL CONSERVATION DIVISION	
Signature:			
Printed Name:	Electronically filed by Diane Kuykendall	Approved By:	Scott Cox
Title:	Production Accounting Director	Title:	Petroleum Engineer Supervisor
Email Address:	dkuykendall@concho.com	Approved Date:	10/5/2020
Date:	9/28/2020	Phone:	432-685-4372
		Expiration Date: 10/5/2022	
Conditions of Approval Attached			

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

1 API Number 30-015-	2 Pool Code 98220	3 Pool Name Purple Sage Wildcat; Wolfcamp
4 Property Code	5 Property Name MYOX 4 28 STATE COM	6 Well Number 706H
7 OGRID No. 229137	8 Operator Name COG OPERATING LLC	9 Elevation 2997'

" Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
L	4	26-S	28-E		2397'	SOUTH	1260'	WEST	EDDY

" Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
D	28	25-S	28-E		50'	NORTH	415'	WEST	EDDY

12 Dedicated Acres 800	13 Joint or Infill	14 Consolidation Code	15 Order No.
----------------------------------	--------------------	-----------------------	--------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

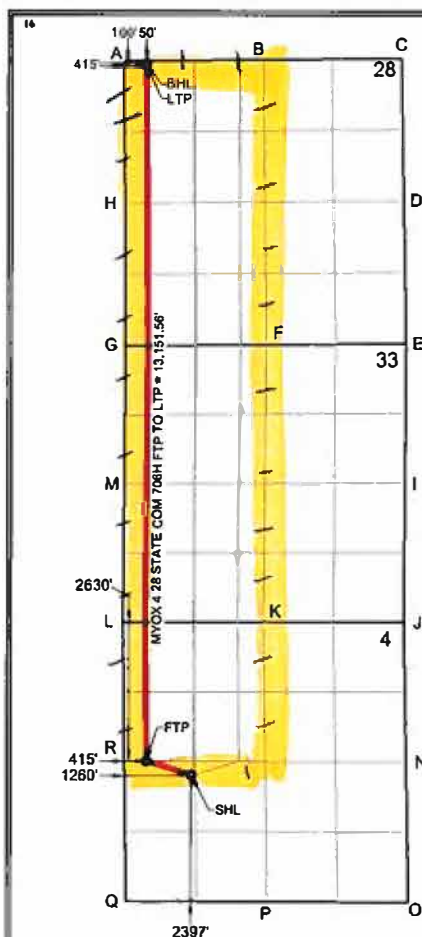

**CORNER DATA
NEW MEXICO EAST - NAD 83**

- A - FOUND IRON PIPE W/ BRASS CAP
N:403146.89' E:613348.71'
- B - CALCULATED CORNER
N:403170.35' E:615984.15'
- C - FOUND IRON PIPE W/ BRASS CAP
N:403208.82' E:618594.32'
- D - FOUND IRON PIPE W/ BRASS CAP
N:400508.73' E:618649.12'
- E - FOUND IRON PIPE W/ BRASS CAP
N:397808.19' E:618708.10'
- F - FOUND IRON PIPE W/ BRASS CAP
N:397781.72' E:616048.82'
- G - FOUND DISTURBED IRON ROD NO CAP
N:397757.72' E:613392.35'
- H - FOUND IRON PIPE W/ BRASS CAP
N:400451.94' E:613369.78'
- I - FOUND IRON PIPE W/ BRASS CAP
N:395170.25' E:618689.77'
- J - FOUND IRON PIPE W/ BRASS CAP
N:392534.13' E:618672.01'
- K - FOUND IRON PIPE W/ BRASS CAP
N:392531.80' E:616012.57'
- L - FOUND IRON PIPE W/ BRASS CAP
N:392529.06' E:613351.46'
- M - FOUND IRON PIPE W/ BRASS CAP
N:395141.98' E:613371.66'
- N - CALCULATED CORNER
N:389881.51' E:618722.69'
- O - FOUND IRON ROD NO CAP
N:387228.88' E:618773.38'
- P - CALCULATED CORNER
N:387234.29' E:616099.89'
- Q - CALCULATED CORNER
N:387239.69' E:613426.41'
- R - FOUND IRON ROD NO CAP
N:389887.40' E:613383.37'

**LAST TAKE POINT (LTP)
NEW MEXICO EAST - NAD 83**
X=613764.47
Y=403050.56
LAT.= 32.0784924° N
LONG.= 104.09941500° W
100' FNL 415' FWL
SECTION 28

**BOTTOM HOLE LOCATION (BHL)
NEW MEXICO EAST - NAD 83**
X=613764.08
Y=403100.56
LAT.= 32.10788669° N
LONG.= 104.09941592° W
50' FNL 415' FWL
SECTION 28

**SURFACE HOLE LOCATION (SHL)
NEW MEXICO EAST - NAD 83**
X=614648.08
Y=389634.80
LAT.= 32.07096423° N
LONG.= 104.09665632° W
2397' FSL 1260' FWL
SECTION 4

**FIRST TAKE POINT (FTP)
NEW MEXICO EAST - NAD 83**
X=613798.25
Y=389899.52
LAT.= 32.07169759° N
LONG.= 104.09939803° W
2630' FNL 415' FWL
SECTION 4

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Mayte Reyes 9-24-2020
Signature Date

Mayte Reyes

Printed Name

mreyes1@concho.com

E-mail Address

" SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date of Survey

Signature and Seal of Professional Surveyor

GARRETT J. SMELKER
NEW MEXICO
25036
08/13/2020
PROFESSIONAL SURVEYOR

Certificate Number

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

GAS CAPTURE PLAN

Date: 10/5/2020

☒ Original

Operator & OGRID No.: [229137] COG OPERATING LLC

☐ Amended - Reason for
Amendment:

This Gas Capture Plan outlines actions to be taken by the Operator to reduce well/production facility flaring/venting for new completion (new drill, recomplete to new zone, re-frac) activity.

Note: Form C-129 must be submitted and approved prior to exceeding 60 days allowed by Rule (Subsection A of 19.15.18.12 NMAC).

Well(s)/Production Facility – Name of facility

The well(s) that will be located at the production facility are shown in the table below.

Well Name	API	Well Location (ULSTR)	Footages	Expected MCF/D	Flared or Vented	Comments
Myox 4 28 State Com #706H	30-015- 47510	L-4-26S- 28E	2397S 1260W	5776	None	It will require additional line to connect to the facility but the amount is unknown currently. Processing Plant Location: Sec 35, Blk 57, T2S, Culberson County, TX

Gathering System and Pipeline Notification

Well(s) will be connected to a production facility after flowback operations are complete, if gas transporter system is in place. The gas produced from production facility is dedicated to ETC Texas Pipeline, Ltd. and will be connected to ETC Texas Pipeline, Ltd. Low Pressure gathering system located in Eddy County, New Mexico. It will require 0' of pipeline to connect the facility to Low Pressure gathering system. COG OPERATING LLC provides (periodically) to ETC Texas Pipeline, Ltd. a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future. In addition, COG OPERATING LLC and ETC Texas Pipeline, Ltd. have periodic conference calls to discuss changes to drilling and completion schedules. Gas from these wells will be processed at ETC Texas Pipeline, Ltd. Processing Plant located in Sec. 02, Twn. 26S, Rng. 28E, Eddy County, New Mexico. The actual flow of the gas will be based on compression operating parameters and gathering system pressures.

Flowback Strategy

After the fracture treatment/completion operations, well(s) will be produced to temporary production tanks and gas will be flared or vented. During flowback, the fluids and sand content will be monitored. When the produced fluids contain minimal sand, the wells will be turned to production facilities. Gas sales should start as soon as the wells start flowing through the production facilities, unless there are operational issues on ETC Texas Pipeline, Ltd. system at that time. Based on current information, it is COG OPERATING LLC's belief the system can take this gas upon completion of the well(s).

Safety requirements during cleanout operations from the use of underbalanced air cleanout systems may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

Alternatives to Reduce Flaring

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

- Power Generation – On lease
 - Only a portion of gas is consumed operating the generator, remainder of gas will be flared
- Compressed Natural Gas – On lease
 - Gas flared would be minimal, but might be uneconomical to operate when gas volume declines
- NGL Removal – On lease
 - Plants are expensive, residue gas is still flared, and uneconomical to operate when gas volume declines

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form APD Comments

Permit 287003

PERMIT COMMENTS

Operator Name and Address: COG OPERATING LLC [229137] 600 W Illinois Ave Midland, TX 79701		API Number: 30-015-47510
		Well: Myox 4 28 State Com #706H

Created By	Comment	Comment Date
mreyes4	COG Operating has conducted a review to determine if an H2S contingency plan is required for the above referenced well. We were able to conclude that any potential hazardous volume would be minimal. H2S concentrations of wells in this area from surface to TD are low enough; therefore we do not believe that an H2S Contingency Plan would be necessary.	9/28/2020

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

Form APD Conditions

Permit 287003

PERMIT CONDITIONS OF APPROVAL

Operator Name and Address: COG OPERATING LLC [229137] 600 W Illinois Ave Midland, TX 79701	API Number: 30-015-47510
	Well: Myox 4 28 State Com #706H

OCD Reviewer	Condition
kpickford	Will require a directional survey with the C-104
kpickford	Will require a administrative order for non-standard location prior to placing the well on production.
kpickford	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string
kpickford	Cement is required to circulate on both surface and intermediate1 strings of casing
kpickford	The Operator is to notify NMOCD by sundry (Form C-103) within ten (10) days of the well being spud 2)- Drilling Sundries Form C-103 (Casing and Cement test are to be submitted within 10 days 3)- Completion Reports & Logs are to be submitted within 45 days
kpickford	The Operator is to notify NMOCD by sundry (Form C-103) within ten (10) days of the well being spud
kpickford	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

DELAWARE BASIN WEST

**ATLAS PROSPECT (NM-E)
MYOX 4 28 & 16 ST COM PROJECT
MYOX 4 28 ST COM #706H**

OWB

Plan: PWP1

Standard Survey Report

20 August, 2020

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Project	ATLAS PROSPECT (NM-E)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Well	MYOX 4 28 ST COM #706H				
Well Position	+N/-S	0.0 usft	Northing:	389,577.13 usft	Latitude: 32° 4' 15.028 N
	+E/-W	0.0 usft	Easting:	573,463.62 usft	Longitude: 104° 5' 46.203 W
Position Uncertainty		3.0 usft	Wellhead Elevation:	usft	Ground Level: 2,997.0 usft

Wellbore	OWB				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	7/15/2020	6.88	59.71	47,446.70401768

Design	PWP1				
Audit Notes:					
Version:	Phase:	PLAN	Tie On Depth:	0.0	
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	356.25	

Survey Tool Program	Date	8/20/2020			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.0	8,698.4	PWP1 (OWB)	Standard Keeper 104	Standard Wireline Keeper ver 1.0.4	
8,698.4	22,648.9	PWP1 (OWB)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction	

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00	
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00	
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00	
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00	
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00	
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00	
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00	
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00	

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
5,100.0	0.00	0.00	5,100.0	0.0	0.0	0.0	0.00	0.00	0.00
5,200.0	0.00	0.00	5,200.0	0.0	0.0	0.0	0.00	0.00	0.00
5,300.0	0.00	0.00	5,300.0	0.0	0.0	0.0	0.00	0.00	0.00
5,400.0	0.00	0.00	5,400.0	0.0	0.0	0.0	0.00	0.00	0.00
5,500.0	0.00	0.00	5,500.0	0.0	0.0	0.0	0.00	0.00	0.00
Start Build 2.00									
5,600.0	2.00	260.00	5,600.0	-0.3	-1.7	-0.2	2.00	2.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,700.0	4.00	260.00	5,699.8	-1.2	-6.9	-0.8	2.00	2.00	0.00
5,750.0	5.00	260.00	5,749.7	-1.9	-10.7	-1.2	2.00	2.00	0.00
Start 2948.4 hold at 5750.0 MD									
5,800.0	5.00	260.00	5,799.5	-2.6	-15.0	-1.7	0.00	0.00	0.00
5,900.0	5.00	260.00	5,899.1	-4.2	-23.6	-2.6	0.00	0.00	0.00
6,000.0	5.00	260.00	5,998.7	-5.7	-32.2	-3.6	0.00	0.00	0.00
6,100.0	5.00	260.00	6,098.4	-7.2	-40.8	-4.5	0.00	0.00	0.00
6,200.0	5.00	260.00	6,198.0	-8.7	-49.4	-5.5	0.00	0.00	0.00
6,300.0	5.00	260.00	6,297.6	-10.2	-57.9	-6.4	0.00	0.00	0.00
6,400.0	5.00	260.00	6,397.2	-11.7	-66.5	-7.3	0.00	0.00	0.00
6,500.0	5.00	260.00	6,496.8	-13.2	-75.1	-8.3	0.00	0.00	0.00
6,600.0	5.00	260.00	6,596.4	-14.8	-83.7	-9.2	0.00	0.00	0.00
6,700.0	5.00	260.00	6,696.1	-16.3	-92.3	-10.2	0.00	0.00	0.00
6,800.0	5.00	260.00	6,795.7	-17.8	-100.9	-11.1	0.00	0.00	0.00
6,900.0	5.00	260.00	6,895.3	-19.3	-109.4	-12.1	0.00	0.00	0.00
7,000.0	5.00	260.00	6,994.9	-20.8	-118.0	-13.0	0.00	0.00	0.00
7,100.0	5.00	260.00	7,094.5	-22.3	-126.6	-14.0	0.00	0.00	0.00
7,200.0	5.00	260.00	7,194.2	-23.8	-135.2	-14.9	0.00	0.00	0.00
7,300.0	5.00	260.00	7,293.8	-25.4	-143.8	-15.9	0.00	0.00	0.00
7,400.0	5.00	260.00	7,393.4	-26.9	-152.4	-16.8	0.00	0.00	0.00
7,500.0	5.00	260.00	7,493.0	-28.4	-160.9	-17.8	0.00	0.00	0.00
7,600.0	5.00	260.00	7,592.6	-29.9	-169.5	-18.7	0.00	0.00	0.00
7,700.0	5.00	260.00	7,692.3	-31.4	-178.1	-19.7	0.00	0.00	0.00
7,800.0	5.00	260.00	7,791.9	-32.9	-186.7	-20.6	0.00	0.00	0.00
7,900.0	5.00	260.00	7,891.5	-34.4	-195.3	-21.6	0.00	0.00	0.00
8,000.0	5.00	260.00	7,991.1	-35.9	-203.9	-22.5	0.00	0.00	0.00
8,100.0	5.00	260.00	8,090.7	-37.5	-212.4	-23.5	0.00	0.00	0.00
8,200.0	5.00	260.00	8,190.4	-39.0	-221.0	-24.4	0.00	0.00	0.00
8,300.0	5.00	260.00	8,290.0	-40.5	-229.6	-25.4	0.00	0.00	0.00
8,400.0	5.00	260.00	8,389.6	-42.0	-238.2	-26.3	0.00	0.00	0.00
8,500.0	5.00	260.00	8,489.2	-43.5	-246.8	-27.3	0.00	0.00	0.00
8,600.0	5.00	260.00	8,588.8	-45.0	-255.4	-28.2	0.00	0.00	0.00
8,698.4	5.00	260.00	8,686.9	-46.5	-263.8	-29.1	0.00	0.00	0.00
Start DLS 10.00 TFO 73.87									
8,700.0	5.05	261.71	8,688.5	-46.5	-263.9	-29.2	10.00	2.92	109.24
8,800.0	12.50	311.53	8,787.3	-40.0	-276.4	-21.8	10.00	7.45	49.82
8,900.0	22.05	321.84	8,882.7	-18.0	-296.2	1.4	10.00	9.56	10.31
9,000.0	31.88	326.04	8,971.8	18.8	-322.6	39.8	10.00	9.82	4.21
9,100.0	41.78	328.41	9,051.7	69.2	-354.9	92.3	10.00	9.90	2.37
9,200.0	51.71	330.00	9,120.2	131.7	-392.0	157.1	10.00	9.93	1.59
9,300.0	61.66	331.21	9,175.0	204.4	-432.9	232.3	10.00	9.95	1.21
9,400.0	71.62	332.21	9,214.6	285.2	-476.4	315.8	10.00	9.96	1.00
9,500.0	81.58	333.09	9,237.8	371.5	-521.0	404.8	10.00	9.96	0.89
9,580.1	89.56	333.77	9,244.0	442.8	-556.7	478.3	10.00	9.96	0.84

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
Start DLS 2.00 TFO 90.10									
9,600.0	89.56	334.17	9,244.1	460.7	-565.4	496.8	2.00	0.00	2.00
9,700.0	89.56	336.17	9,244.9	551.5	-607.4	590.1	2.00	0.00	2.00
9,800.0	89.55	338.17	9,245.7	643.6	-646.2	684.6	2.00	0.00	2.00
9,900.0	89.55	340.17	9,246.4	737.1	-681.8	780.1	2.00	0.00	2.00
10,000.0	89.55	342.17	9,247.2	831.7	-714.0	876.7	2.00	0.00	2.00
10,100.0	89.55	344.17	9,248.0	927.4	-743.0	974.1	2.00	0.00	2.00
10,200.0	89.55	346.17	9,248.8	1,024.1	-768.6	1,072.2	2.00	0.00	2.00
10,300.0	89.55	348.17	9,249.6	1,121.6	-790.8	1,171.0	2.00	0.00	2.00
10,400.0	89.55	350.17	9,250.4	1,219.8	-809.6	1,270.2	2.00	0.00	2.00
10,500.0	89.55	352.17	9,251.2	1,318.6	-824.9	1,369.8	2.00	0.00	2.00
10,600.0	89.55	354.17	9,251.9	1,417.9	-836.8	1,469.6	2.00	0.00	2.00
10,700.0	89.56	356.17	9,252.7	1,517.5	-845.3	1,569.6	2.00	0.00	2.00
10,800.0	89.56	358.17	9,253.5	1,617.4	-850.2	1,669.6	2.00	0.00	2.00
10,868.5	89.56	359.54	9,254.0	1,685.8	-851.6	1,738.0	2.00	0.00	2.00
Start 1209.7 hold at 10868.5 MD									
10,900.0	89.56	359.54	9,254.3	1,717.4	-851.8	1,769.5	0.00	0.00	0.00
11,000.0	89.56	359.54	9,255.0	1,817.4	-852.6	1,869.3	0.00	0.00	0.00
11,100.0	89.56	359.54	9,255.8	1,917.4	-853.4	1,969.1	0.00	0.00	0.00
11,200.0	89.56	359.54	9,256.6	2,017.3	-854.2	2,069.0	0.00	0.00	0.00
11,300.0	89.56	359.54	9,257.3	2,117.3	-855.0	2,168.8	0.00	0.00	0.00
11,400.0	89.56	359.54	9,258.1	2,217.3	-855.9	2,268.6	0.00	0.00	0.00
11,500.0	89.56	359.54	9,258.9	2,317.3	-856.7	2,368.5	0.00	0.00	0.00
11,600.0	89.56	359.54	9,259.6	2,417.3	-857.5	2,468.3	0.00	0.00	0.00
11,700.0	89.56	359.54	9,260.4	2,517.3	-858.3	2,568.1	0.00	0.00	0.00
11,800.0	89.56	359.54	9,261.2	2,617.3	-859.1	2,668.0	0.00	0.00	0.00
11,900.0	89.56	359.54	9,261.9	2,717.3	-859.9	2,767.8	0.00	0.00	0.00
12,000.0	89.56	359.54	9,262.7	2,817.3	-860.7	2,867.6	0.00	0.00	0.00
12,078.2	89.56	359.54	9,263.3	2,895.5	-861.3	2,945.7	0.00	0.00	0.00
Start DLS 2.00 TFO 89.86									
12,100.0	89.56	359.97	9,263.5	2,917.3	-861.4	2,967.4	2.00	0.00	2.00
12,112.8	89.56	0.23	9,263.6	2,930.1	-861.4	2,980.2	2.00	0.01	2.00
Start 5196.8 hold at 12112.8 MD									
12,200.0	89.56	0.23	9,264.2	3,017.3	-861.0	3,067.2	0.00	0.00	0.00
12,300.0	89.56	0.23	9,265.0	3,117.3	-860.6	3,167.0	0.00	0.00	0.00
12,400.0	89.56	0.23	9,265.8	3,217.3	-860.2	3,266.7	0.00	0.00	0.00
12,500.0	89.56	0.23	9,266.5	3,317.3	-859.8	3,366.5	0.00	0.00	0.00
12,600.0	89.56	0.23	9,267.3	3,417.3	-859.4	3,466.2	0.00	0.00	0.00
12,700.0	89.56	0.23	9,268.1	3,517.3	-859.0	3,566.0	0.00	0.00	0.00
12,800.0	89.56	0.23	9,268.8	3,617.3	-858.6	3,665.7	0.00	0.00	0.00
12,900.0	89.56	0.23	9,269.6	3,717.3	-858.2	3,765.5	0.00	0.00	0.00
13,000.0	89.56	0.23	9,270.3	3,817.3	-857.8	3,865.2	0.00	0.00	0.00
13,100.0	89.56	0.23	9,271.1	3,917.3	-857.4	3,965.0	0.00	0.00	0.00
13,200.0	89.56	0.23	9,271.9	4,017.3	-857.0	4,064.8	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,300.0	89.56	0.23	9,272.6	4,117.2	-856.6	4,164.5	0.00	0.00	0.00
13,400.0	89.56	0.23	9,273.4	4,217.2	-856.2	4,264.3	0.00	0.00	0.00
13,500.0	89.56	0.23	9,274.2	4,317.2	-855.8	4,364.0	0.00	0.00	0.00
13,600.0	89.56	0.23	9,274.9	4,417.2	-855.4	4,463.8	0.00	0.00	0.00
13,700.0	89.56	0.23	9,275.7	4,517.2	-855.0	4,563.5	0.00	0.00	0.00
13,800.0	89.56	0.23	9,276.5	4,617.2	-854.6	4,663.3	0.00	0.00	0.00
13,900.0	89.56	0.23	9,277.2	4,717.2	-854.2	4,763.0	0.00	0.00	0.00
14,000.0	89.56	0.23	9,278.0	4,817.2	-853.8	4,862.8	0.00	0.00	0.00
14,100.0	89.56	0.23	9,278.8	4,917.2	-853.4	4,962.6	0.00	0.00	0.00
14,200.0	89.56	0.23	9,279.5	5,017.2	-853.0	5,062.3	0.00	0.00	0.00
14,300.0	89.56	0.23	9,280.3	5,117.2	-852.6	5,162.1	0.00	0.00	0.00
14,400.0	89.56	0.23	9,281.1	5,217.2	-852.2	5,261.8	0.00	0.00	0.00
14,500.0	89.56	0.23	9,281.8	5,317.2	-851.8	5,361.6	0.00	0.00	0.00
14,600.0	89.56	0.23	9,282.6	5,417.2	-851.4	5,461.3	0.00	0.00	0.00
14,700.0	89.56	0.23	9,283.3	5,517.2	-851.0	5,561.1	0.00	0.00	0.00
14,800.0	89.56	0.23	9,284.1	5,617.2	-850.6	5,660.8	0.00	0.00	0.00
14,900.0	89.56	0.23	9,284.9	5,717.2	-850.2	5,760.6	0.00	0.00	0.00
15,000.0	89.56	0.23	9,285.6	5,817.2	-849.8	5,860.3	0.00	0.00	0.00
15,100.0	89.56	0.23	9,286.4	5,917.2	-849.4	5,960.1	0.00	0.00	0.00
15,200.0	89.56	0.23	9,287.2	6,017.2	-849.0	6,059.9	0.00	0.00	0.00
15,300.0	89.56	0.23	9,287.9	6,117.2	-848.6	6,159.6	0.00	0.00	0.00
15,400.0	89.56	0.23	9,288.7	6,217.2	-848.2	6,259.4	0.00	0.00	0.00
15,500.0	89.56	0.23	9,289.5	6,317.2	-847.8	6,359.1	0.00	0.00	0.00
15,600.0	89.56	0.23	9,290.2	6,417.2	-847.4	6,458.9	0.00	0.00	0.00
15,700.0	89.56	0.23	9,291.0	6,517.2	-847.0	6,558.6	0.00	0.00	0.00
15,800.0	89.56	0.23	9,291.8	6,617.2	-846.6	6,658.4	0.00	0.00	0.00
15,900.0	89.56	0.23	9,292.5	6,717.2	-846.2	6,758.1	0.00	0.00	0.00
16,000.0	89.56	0.23	9,293.3	6,817.1	-845.8	6,857.9	0.00	0.00	0.00
16,100.0	89.56	0.23	9,294.1	6,917.1	-845.4	6,957.7	0.00	0.00	0.00
16,200.0	89.56	0.23	9,294.8	7,017.1	-845.0	7,057.4	0.00	0.00	0.00
16,300.0	89.56	0.23	9,295.6	7,117.1	-844.6	7,157.2	0.00	0.00	0.00
16,400.0	89.56	0.23	9,296.3	7,217.1	-844.2	7,256.9	0.00	0.00	0.00
16,500.0	89.56	0.23	9,297.1	7,317.1	-843.8	7,356.7	0.00	0.00	0.00
16,600.0	89.56	0.23	9,297.9	7,417.1	-843.4	7,456.4	0.00	0.00	0.00
16,700.0	89.56	0.23	9,298.6	7,517.1	-843.0	7,556.2	0.00	0.00	0.00
16,800.0	89.56	0.23	9,299.4	7,617.1	-842.6	7,655.9	0.00	0.00	0.00
16,900.0	89.56	0.23	9,300.2	7,717.1	-842.2	7,755.7	0.00	0.00	0.00
17,000.0	89.56	0.23	9,300.9	7,817.1	-841.8	7,855.5	0.00	0.00	0.00
17,100.0	89.56	0.23	9,301.7	7,917.1	-841.4	7,955.2	0.00	0.00	0.00
17,200.0	89.56	0.23	9,302.5	8,017.1	-841.0	8,055.0	0.00	0.00	0.00
17,300.0	89.56	0.23	9,303.2	8,117.1	-840.6	8,154.7	0.00	0.00	0.00
17,309.6	89.56	0.23	9,303.3	8,126.7	-840.5	8,164.3	0.00	0.00	0.00
Start DLS 2.00 TFO -89.89									

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,344.4	89.56	359.53	9,303.6	8,161.5	-840.6	8,199.0	2.00	0.00	-2.00
Start 5304.6 hold at 17344.4 MD									
17,400.0	89.56	359.53	9,304.0	8,217.1	-841.1	8,254.5	0.00	0.00	0.00
17,500.0	89.56	359.53	9,304.8	8,317.1	-841.9	8,354.4	0.00	0.00	0.00
17,600.0	89.56	359.53	9,305.5	8,417.1	-842.7	8,454.2	0.00	0.00	0.00
17,700.0	89.56	359.53	9,306.3	8,517.1	-843.5	8,554.0	0.00	0.00	0.00
17,800.0	89.56	359.53	9,307.0	8,617.1	-844.3	8,653.9	0.00	0.00	0.00
17,900.0	89.56	359.53	9,307.8	8,717.1	-845.1	8,753.7	0.00	0.00	0.00
18,000.0	89.56	359.53	9,308.6	8,817.1	-845.9	8,853.5	0.00	0.00	0.00
18,100.0	89.56	359.53	9,309.3	8,917.1	-846.7	8,953.4	0.00	0.00	0.00
18,200.0	89.56	359.53	9,310.1	9,017.0	-847.6	9,053.2	0.00	0.00	0.00
18,300.0	89.56	359.53	9,310.8	9,117.0	-848.4	9,153.0	0.00	0.00	0.00
18,400.0	89.56	359.53	9,311.6	9,217.0	-849.2	9,252.9	0.00	0.00	0.00
18,500.0	89.56	359.53	9,312.4	9,317.0	-850.0	9,352.7	0.00	0.00	0.00
18,600.0	89.56	359.53	9,313.1	9,417.0	-850.8	9,452.5	0.00	0.00	0.00
18,700.0	89.56	359.53	9,313.9	9,517.0	-851.6	9,552.4	0.00	0.00	0.00
18,800.0	89.56	359.53	9,314.7	9,617.0	-852.4	9,652.2	0.00	0.00	0.00
18,900.0	89.56	359.53	9,315.4	9,717.0	-853.2	9,752.0	0.00	0.00	0.00
19,000.0	89.56	359.53	9,316.2	9,817.0	-854.1	9,851.9	0.00	0.00	0.00
19,100.0	89.56	359.53	9,316.9	9,917.0	-854.9	9,951.7	0.00	0.00	0.00
19,200.0	89.56	359.53	9,317.7	10,017.0	-855.7	10,051.5	0.00	0.00	0.00
19,300.0	89.56	359.53	9,318.5	10,117.0	-856.5	10,151.3	0.00	0.00	0.00
19,400.0	89.56	359.53	9,319.2	10,217.0	-857.3	10,251.2	0.00	0.00	0.00
19,500.0	89.56	359.53	9,320.0	10,317.0	-858.1	10,351.0	0.00	0.00	0.00
19,600.0	89.56	359.53	9,320.8	10,417.0	-858.9	10,450.8	0.00	0.00	0.00
19,700.0	89.56	359.53	9,321.5	10,517.0	-859.7	10,550.7	0.00	0.00	0.00
19,800.0	89.56	359.53	9,322.3	10,616.9	-860.6	10,650.5	0.00	0.00	0.00
19,900.0	89.56	359.53	9,323.0	10,716.9	-861.4	10,750.3	0.00	0.00	0.00
20,000.0	89.56	359.53	9,323.8	10,816.9	-862.2	10,850.2	0.00	0.00	0.00
20,100.0	89.56	359.53	9,324.6	10,916.9	-863.0	10,950.0	0.00	0.00	0.00
20,200.0	89.56	359.53	9,325.3	11,016.9	-863.8	11,049.8	0.00	0.00	0.00
20,300.0	89.56	359.53	9,326.1	11,116.9	-864.6	11,149.7	0.00	0.00	0.00
20,400.0	89.56	359.53	9,326.9	11,216.9	-865.4	11,249.5	0.00	0.00	0.00
20,500.0	89.56	359.53	9,327.6	11,316.9	-866.2	11,349.3	0.00	0.00	0.00
20,600.0	89.56	359.53	9,328.4	11,416.9	-867.1	11,449.2	0.00	0.00	0.00
20,700.0	89.56	359.53	9,329.1	11,516.9	-867.9	11,549.0	0.00	0.00	0.00
20,800.0	89.56	359.53	9,329.9	11,616.9	-868.7	11,648.8	0.00	0.00	0.00
20,900.0	89.56	359.53	9,330.7	11,716.9	-869.5	11,748.7	0.00	0.00	0.00
21,000.0	89.56	359.53	9,331.4	11,816.9	-870.3	11,848.5	0.00	0.00	0.00
21,100.0	89.56	359.53	9,332.2	11,916.9	-871.1	11,948.3	0.00	0.00	0.00
21,200.0	89.56	359.53	9,333.0	12,016.9	-871.9	12,048.2	0.00	0.00	0.00
21,300.0	89.56	359.53	9,333.7	12,116.9	-872.7	12,148.0	0.00	0.00	0.00
21,400.0	89.56	359.53	9,334.5	12,216.8	-873.6	12,247.8	0.00	0.00	0.00
21,500.0	89.56	359.53	9,335.2	12,316.8	-874.4	12,347.7	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
21,600.0	89.56	359.53	9,336.0	12,416.8	-875.2	12,447.5	0.00	0.00	0.00
21,700.0	89.56	359.53	9,336.8	12,516.8	-876.0	12,547.3	0.00	0.00	0.00
21,800.0	89.56	359.53	9,337.5	12,616.8	-876.8	12,647.2	0.00	0.00	0.00
21,900.0	89.56	359.53	9,338.3	12,716.8	-877.6	12,747.0	0.00	0.00	0.00
22,000.0	89.56	359.53	9,339.1	12,816.8	-878.4	12,846.8	0.00	0.00	0.00
22,100.0	89.56	359.53	9,339.8	12,916.8	-879.2	12,946.7	0.00	0.00	0.00
22,200.0	89.56	359.53	9,340.6	13,016.8	-880.1	13,046.5	0.00	0.00	0.00
22,300.0	89.56	359.53	9,341.3	13,116.8	-880.9	13,146.3	0.00	0.00	0.00
22,400.0	89.56	359.53	9,342.1	13,216.8	-881.7	13,246.2	0.00	0.00	0.00
22,500.0	89.56	359.53	9,342.9	13,316.8	-882.5	13,346.0	0.00	0.00	0.00
22,600.0	89.56	359.53	9,343.6	13,416.8	-883.3	13,445.8	0.00	0.00	0.00
22,648.9	89.56	359.53	9,344.0	13,465.7	-883.7	13,494.7	0.00	0.00	0.00
TD at 22648.9									

Design Targets

Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
FTP (MYOX 4 28 ST C - plan misses target center by 341.6usft at 9552.1usft MD (9243.1 TVD, 417.8 N, -544.3 E) - Circle (radius 50.0)	0.00	0.00	9,244.0	264.9	-849.8	389,842.06	572,613.83	32° 4' 17.668 N	104° 5' 56.073 W
T1 (MYOX 4 28 ST C - plan hits target center - Rectangle (sides W100.0 H2,995.0 D20.0)	-0.44	179.54	9,263.3	2,895.5	-861.3	392,472.60	572,602.30	32° 4' 43.702 N	104° 5' 56.141 W
T2 (MYOX 4 28 ST C - plan hits target center - Rectangle (sides W100.0 H5,224.0 D20.0)	-0.44	180.23	9,303.3	8,126.7	-840.5	397,703.83	572,623.09	32° 5' 35.472 N	104° 5' 55.767 W
PBHL (MYOX 4 28 ST - plan hits target center - Rectangle (sides W100.0 H5,340.0 D20.0)	-0.44	179.53	9,344.0	13,465.7	-883.7	403,042.84	572,579.92	32° 6' 28.311 N	104° 5' 56.134 W
LTP (MYOX 4 28 ST C - plan misses target center by 0.4usft at 22598.9usft MD (9343.6 TVD, 13415.7 N, -883.3 E) - Point	0.00	0.00	9,344.0	13,415.7	-883.3	402,992.84	572,580.31	32° 6' 27.816 N	104° 5' 56.130 W

Concho Resources LLC


Survey Report

Company:	DELAWARE BASIN WEST	Local Co-ordinate Reference:	Well MYOX 4 28 ST COM #706H
Project:	ATLAS PROSPECT (NM-E)	TVD Reference:	*KB=30' @ 3027.0usft (TBD)
Site:	MYOX 4 28 & 16 ST COM PROJECT	MD Reference:	*KB=30' @ 3027.0usft (TBD)
Well:	MYOX 4 28 ST COM #706H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
5500	5500	0	0	Start Build 2.00
5750	5750	-2	-11	Start 2948.4 hold at 5750.0 MD
8698	8687	-47	-264	Start DLS 10.00 TFO 73.87
9580	9244	443	-557	Start DLS 2.00 TFO 90.10
10,868	9254	1686	-852	Start 1209.7 hold at 10868.5 MD
12,078	9263	2895	-861	Start DLS 2.00 TFO 89.86
12,113	9264	2930	-861	Start 5196.8 hold at 12112.8 MD
17,310	9303	8127	-841	Start DLS 2.00 TFO -89.89
17,344	9304	8161	-841	Start 5304.6 hold at 17344.4 MD
22,649	9344	13,466	-884	TD at 22648.9

Checked By: _____ Approved By: _____ Date: _____

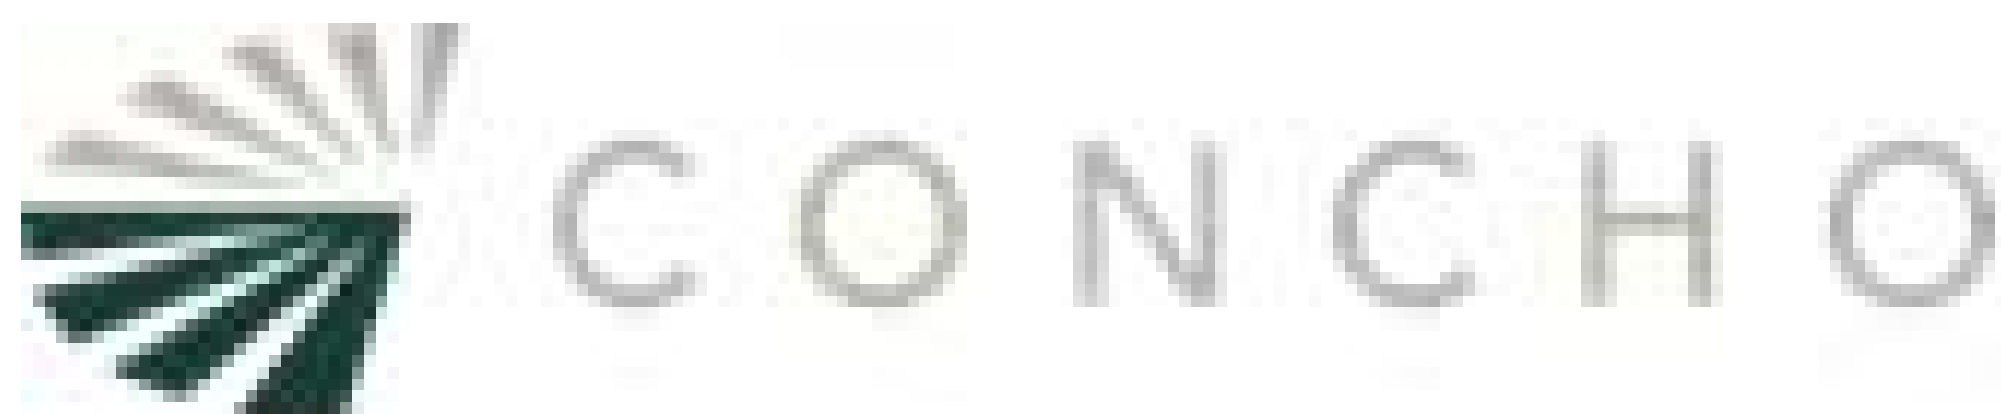



Project: ATLAS PROSPECT (NM-E)
Site: MYOX 4 28 & 16 ST COM PROJECT
Well: MYOX 4 28 ST COM #706H
Wellbore: OWB
Design: PWP1
GL: 2997.0
*KB=30' @ 3027.0usft (TBD)

WELL DETAILS: MYOX 4 28 ST COM #706H

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	389577.13	573463.62	32° 4' 15.028 N	104° 5' 46.203 W





DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
FTP (MYOX 4 28 ST COM #706H)	244.0	264.9	-849.8	389842.06	572613.83	32° 4' 17.668 N	104° 5' 56.073 W
T1 (MYOX 4 28 ST COM #706H)	9263.3	2895.5	-861.3	392472.60	572602.30	32° 4' 43.702 N	104° 5' 56.141 W
T2 (MYOX 4 28 ST COM #706H)	9303.3	8126.7	-840.5	397703.83	572623.08	32° 5' 35.472 N	104° 5' 55.767 W
LTP (MYOX 4 28 ST COM #706H)	9344.0	13415.7	-883.3	402992.84	572580.31	32° 6' 27.816 N	104° 5' 56.130 W
PBHL (MYOX 4 28 ST COM #706H)	9344.0	13465.7	-883.7	403042.84	572579.92	32° 6' 28.311 N	104° 5' 56.134 W

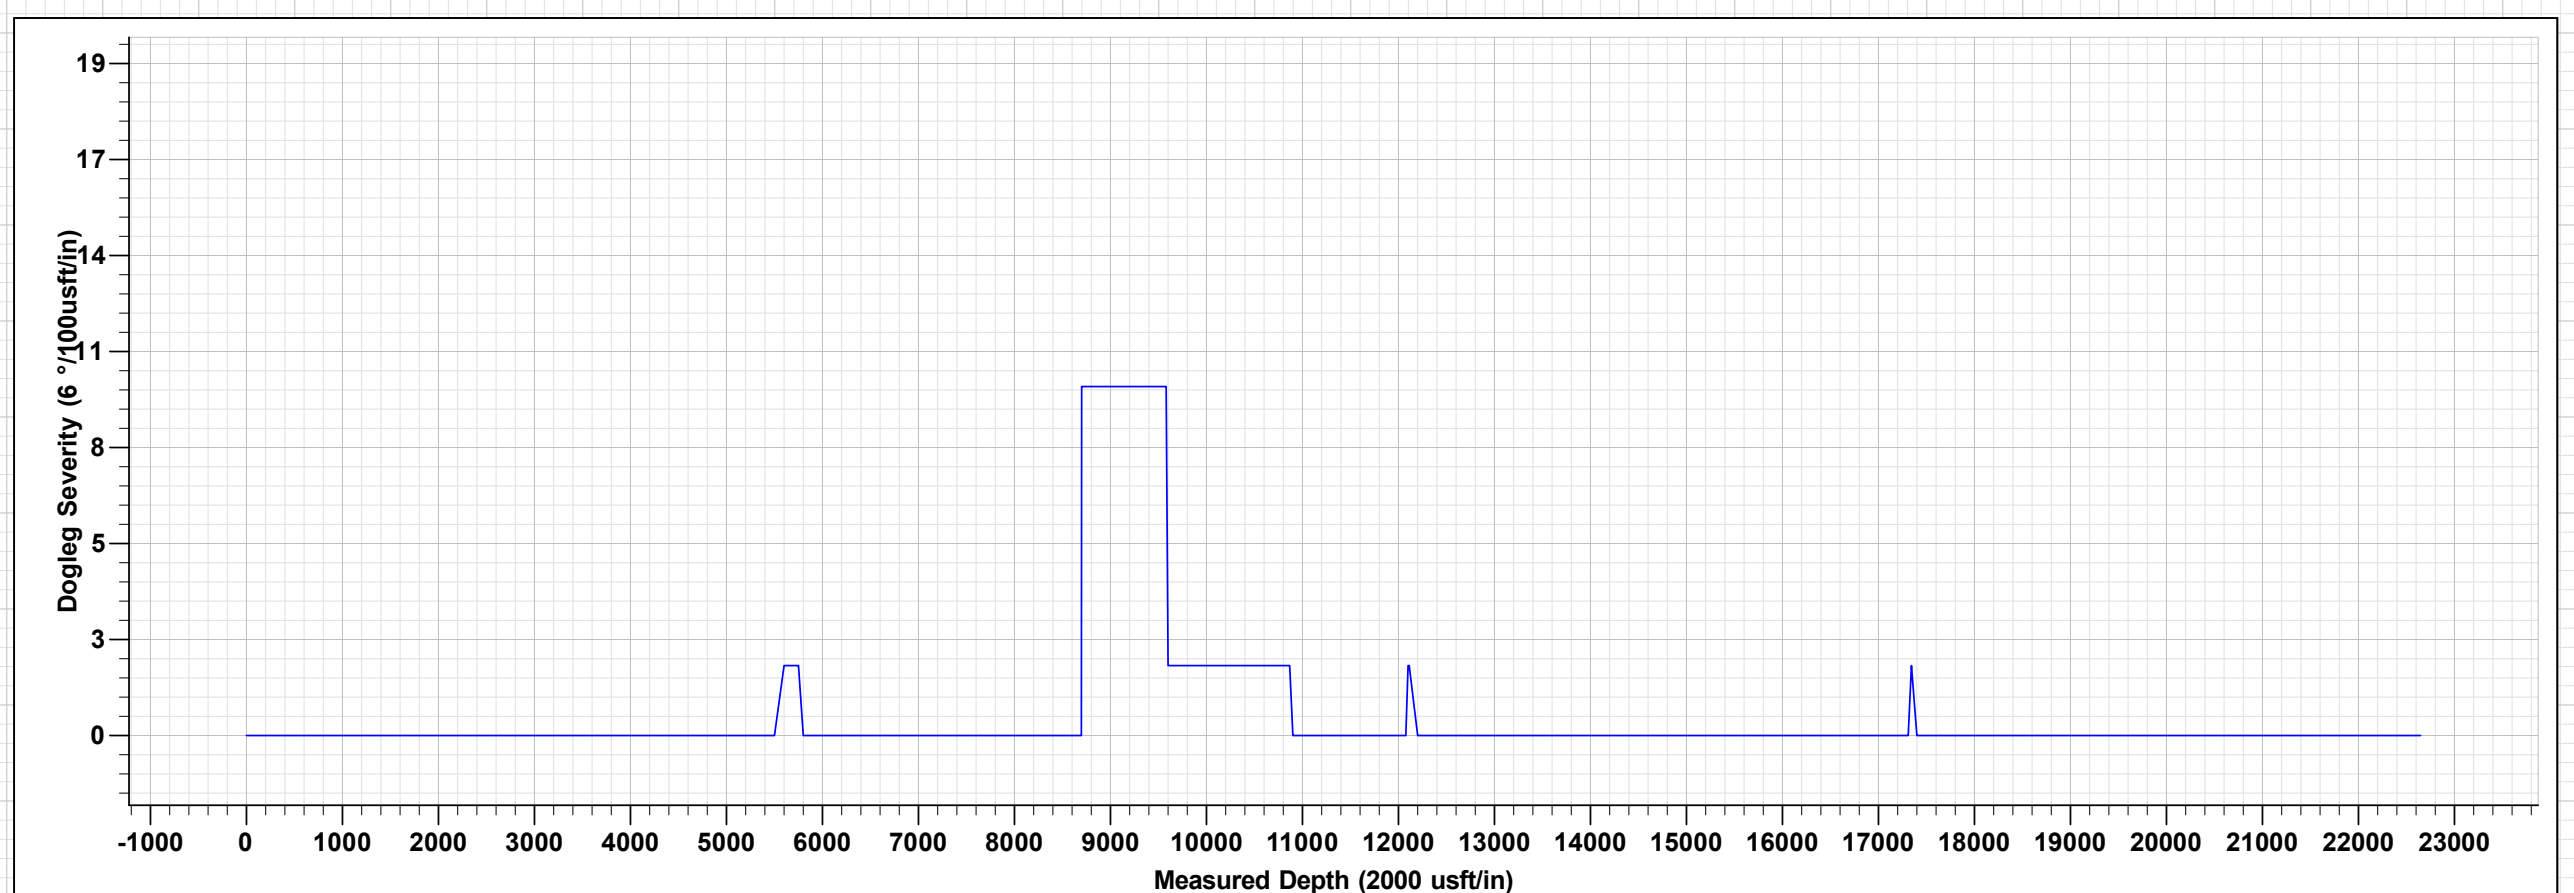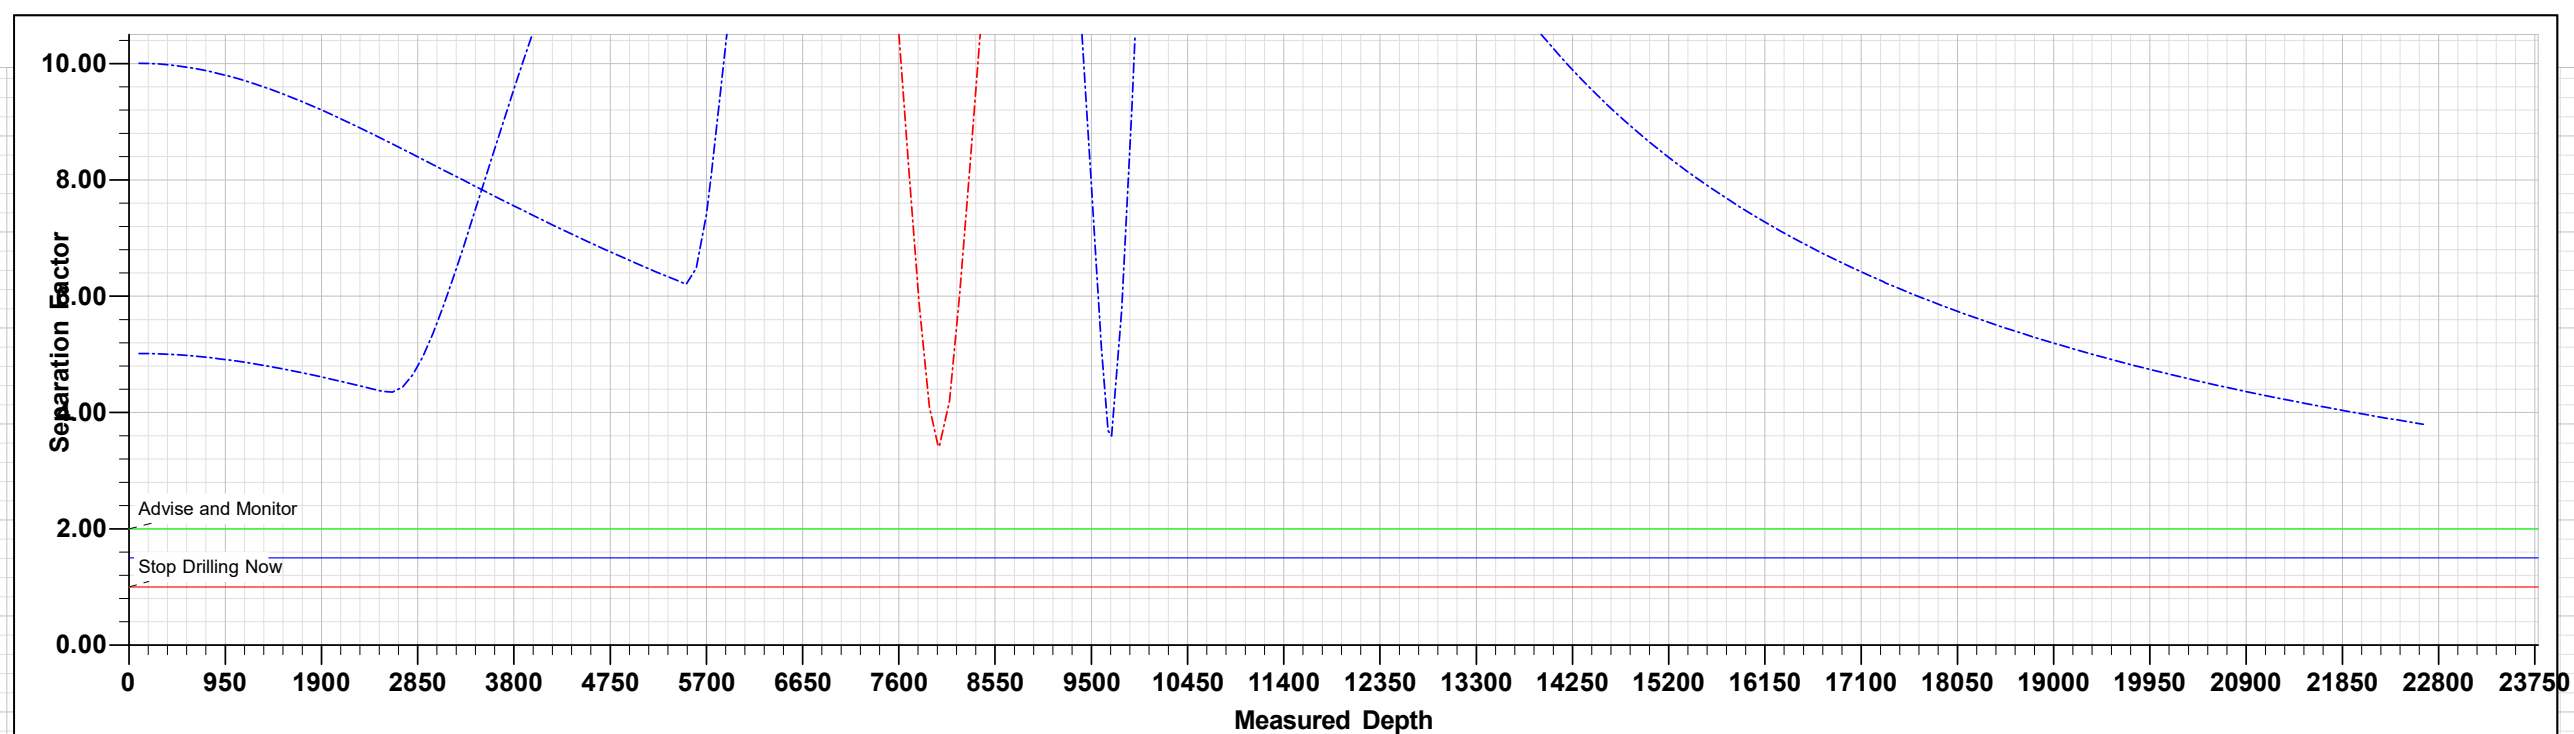

MYOX 4 28 ST COM #706H

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
5500.0	0.00	0.00	5500.0	0.0	0.0	0.00	0.00	0.0	Start Build 2.00
5750.0	5.00	260.00	5749.7	-1.9	-10.7	2.00	260.00	-1.2	Start 2948.4 hold at 5750.0 MD
5698.4	5.00	260.00	5698.9	-46.5	-253.8	0.00	0.00	-29.1	Start DLS 10.00 TFO 73.87
9590.1	89.56	333.77	9244.0	442.8	-556.7	10.00	73.87	478.3	Start DLS 2.00 TFO 90.10
10868.5	89.56	359.54	9254.0	1685.8	-851.6	2.00	90.10	1738.0	Start 1209.7 hold at 10868.5 MD
12078.2	89.56	359.54	9263.3	2895.5	-861.3	0.00	0.00	2945.7	Start DLS 2.00 TFO 89.86
12112.8	89.56	0.23	9263.6	2930.1	-861.4	2.00	89.86	2980.2	Start 5196.8 hold at 12112.8 MD
17309.6	89.56	0.23	9303.3	8126.7	-840.5	0.00	0.00	8164.3	Start DLS 2.00 TFO -89.89
17344.4	89.56	359.53	9303.6	8161.5	-840.6	2.00	-89.89	8199.0	Start 5304.6 hold at 17344.4 MD
22648.9	89.56	359.53	9344.0	13465.7	-883.7	0.00	0.00	13494.7	TD at 22648.9

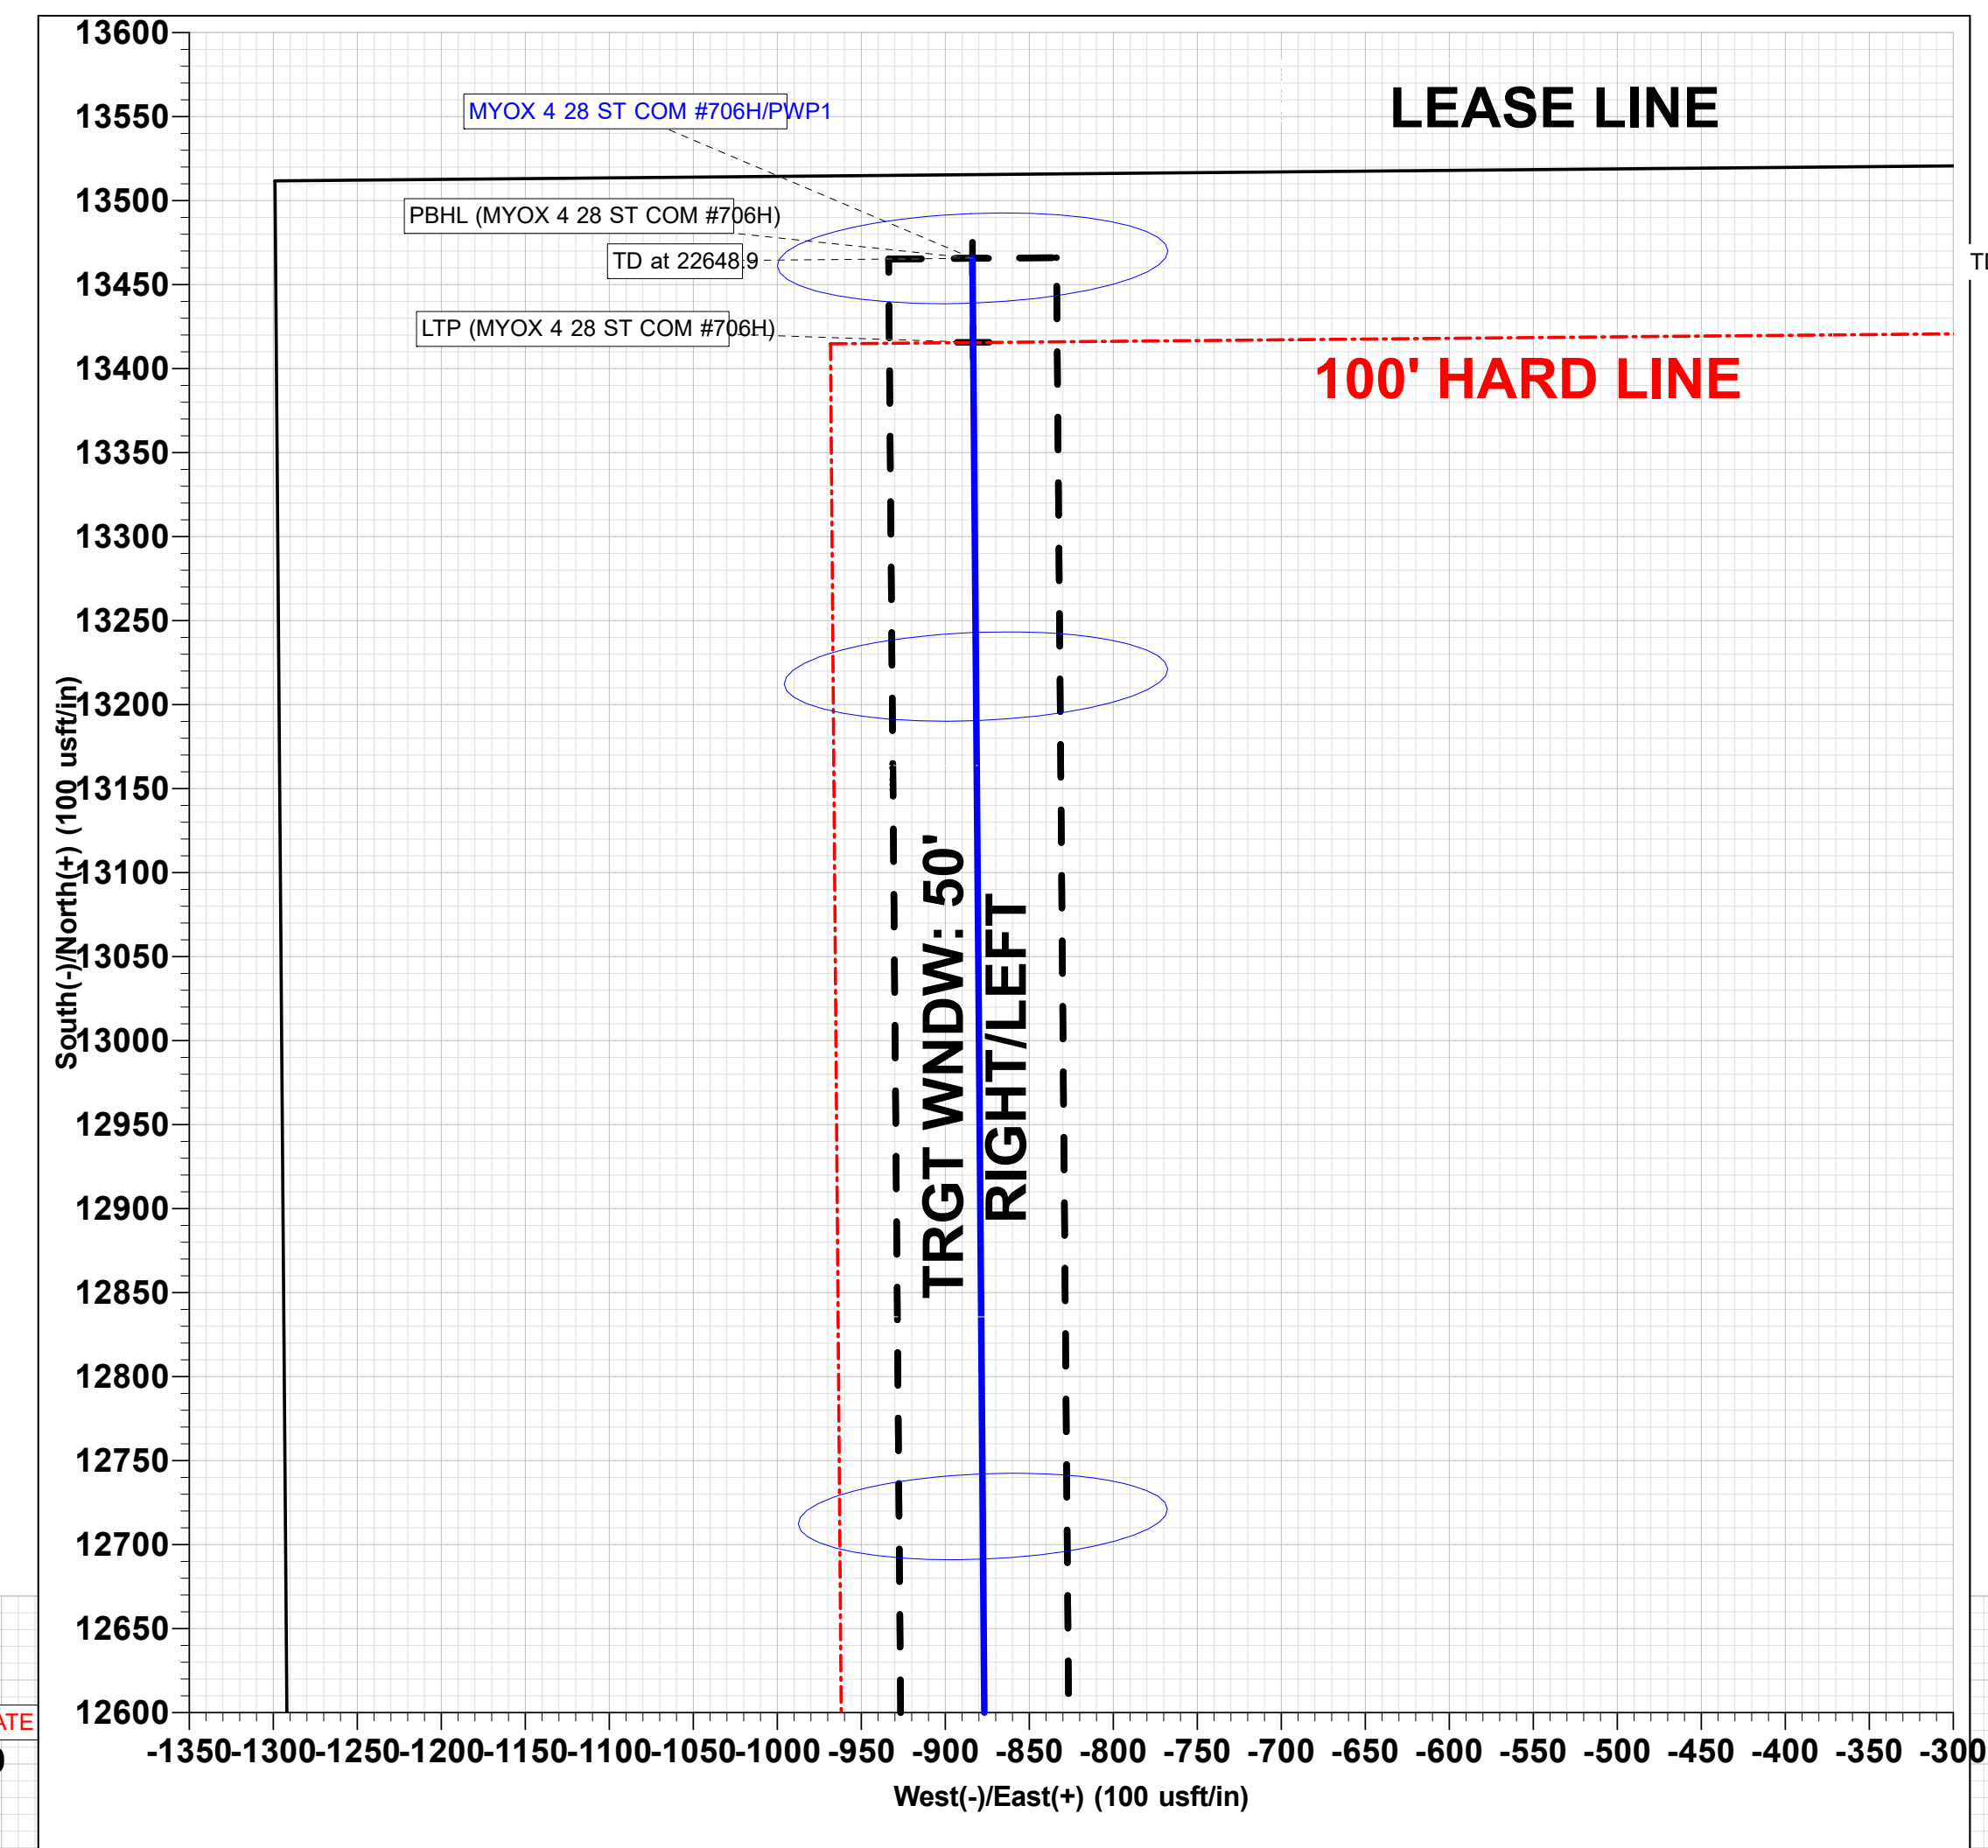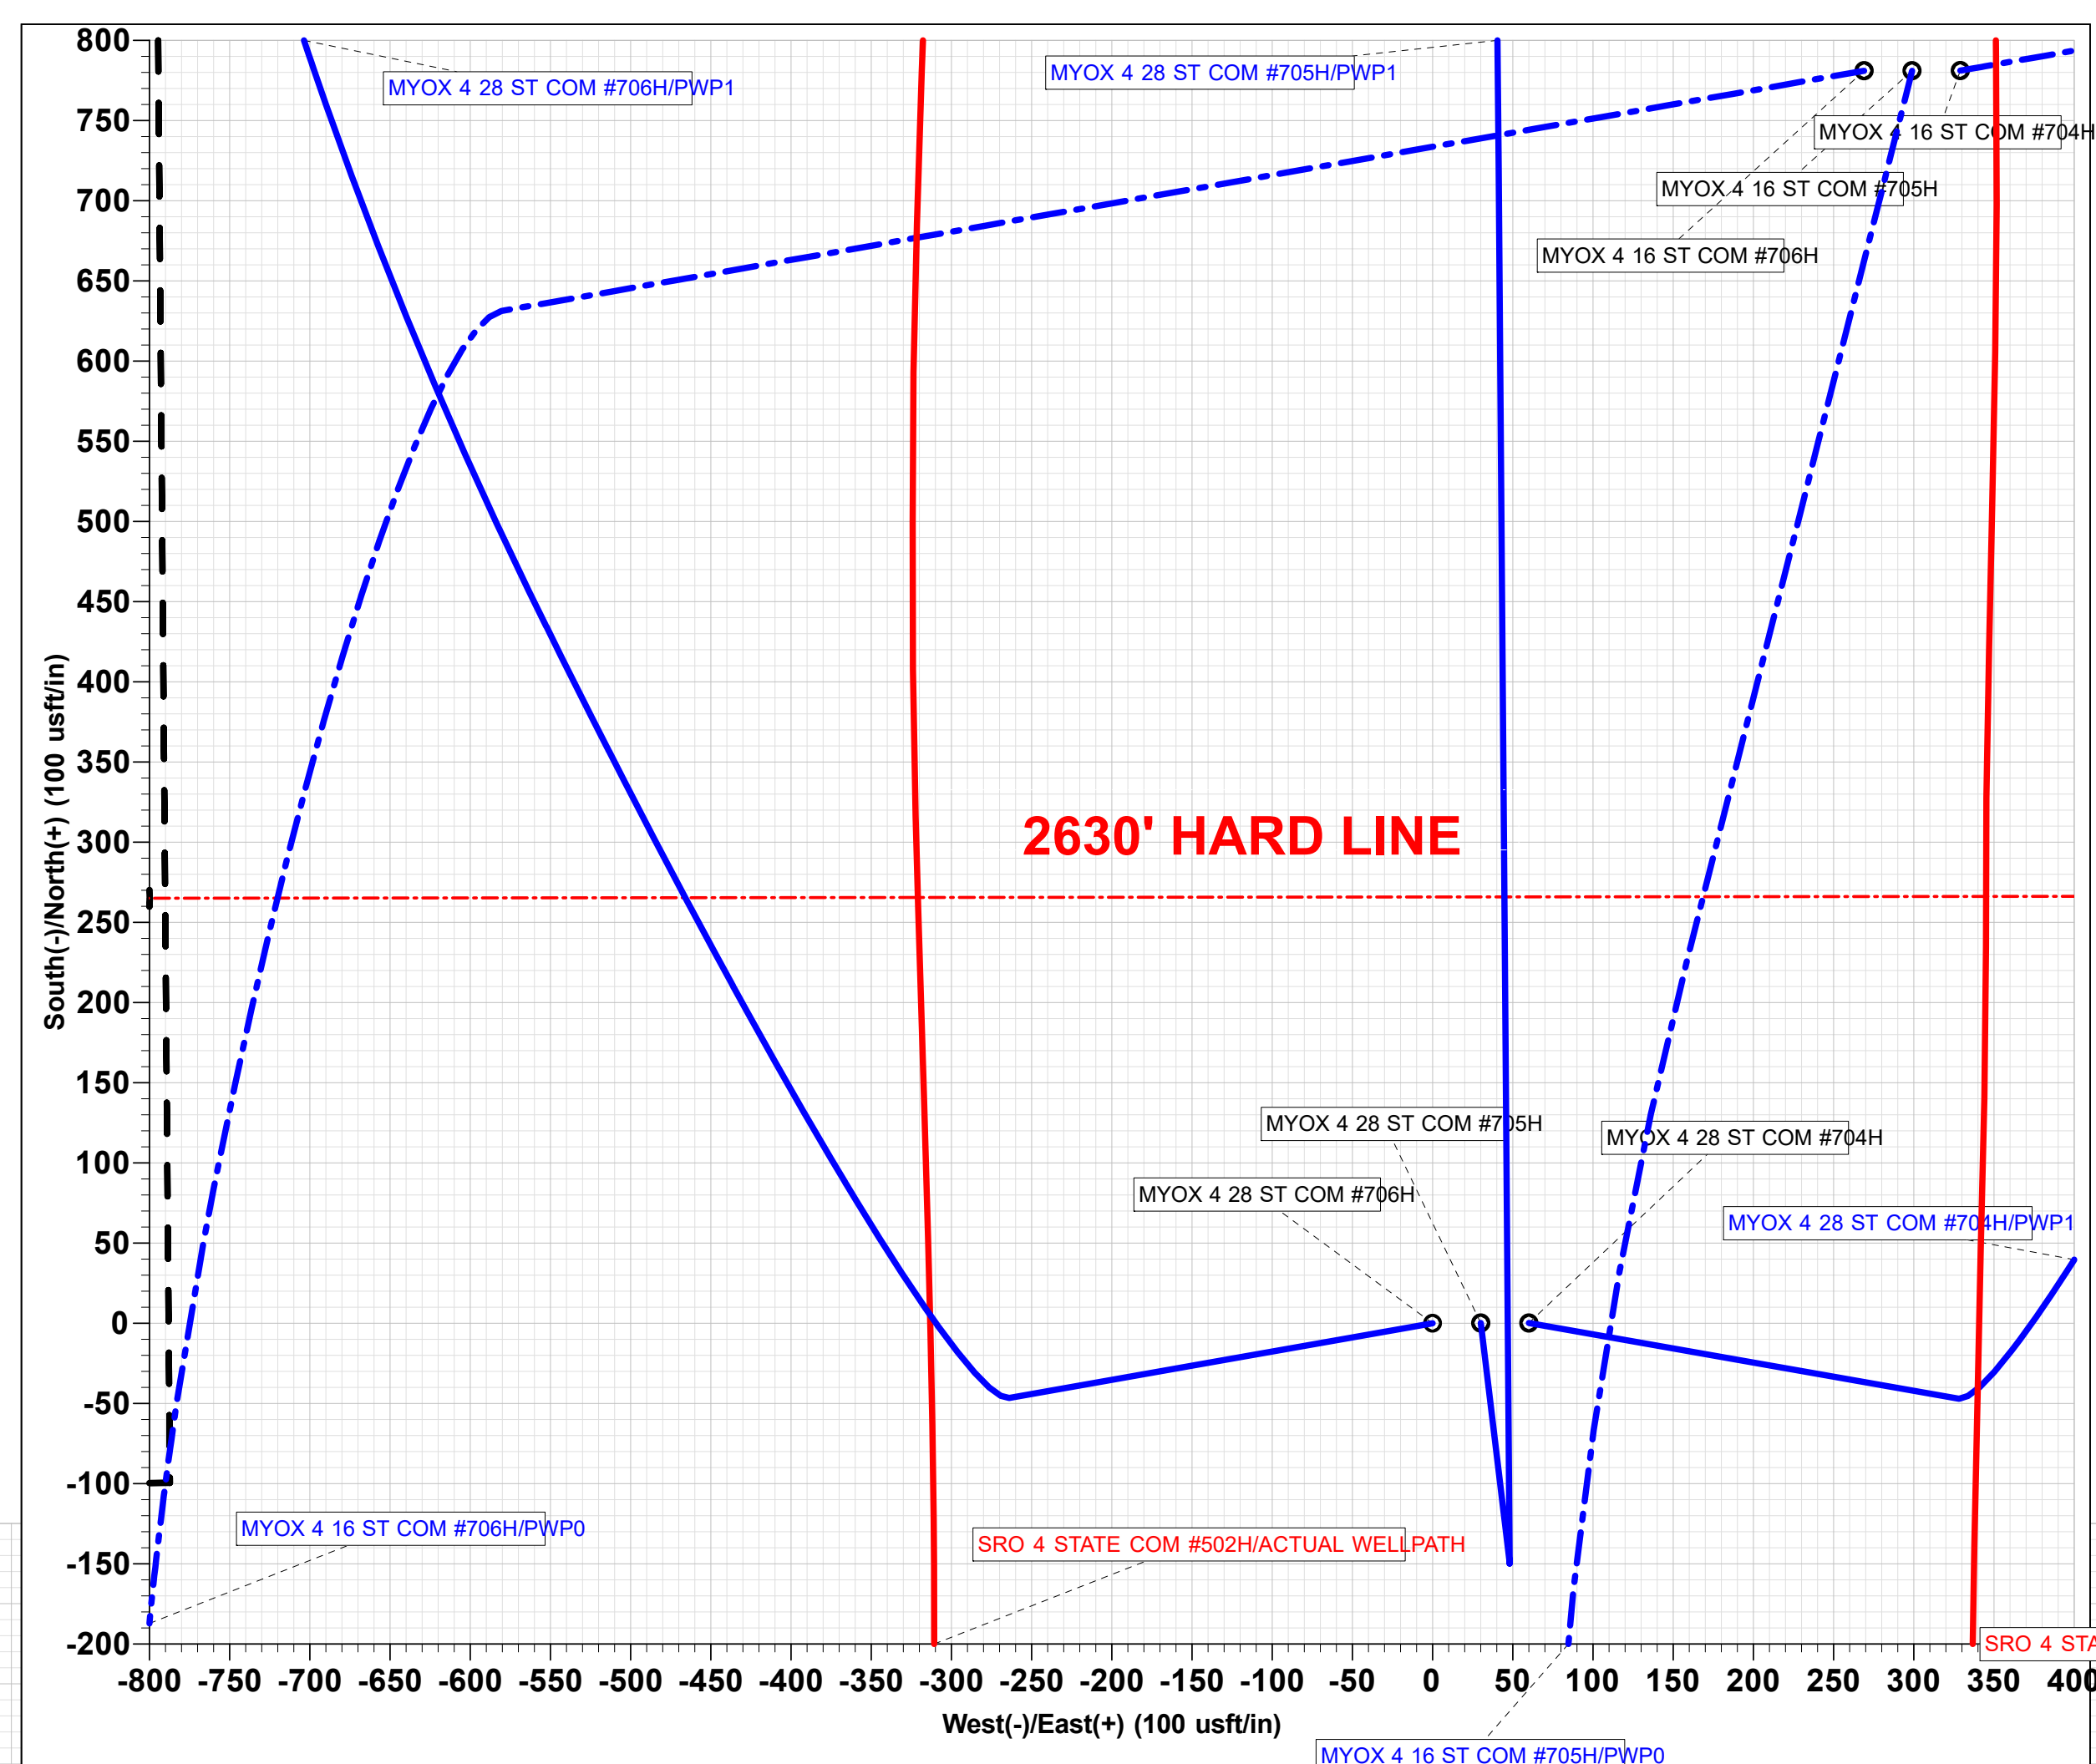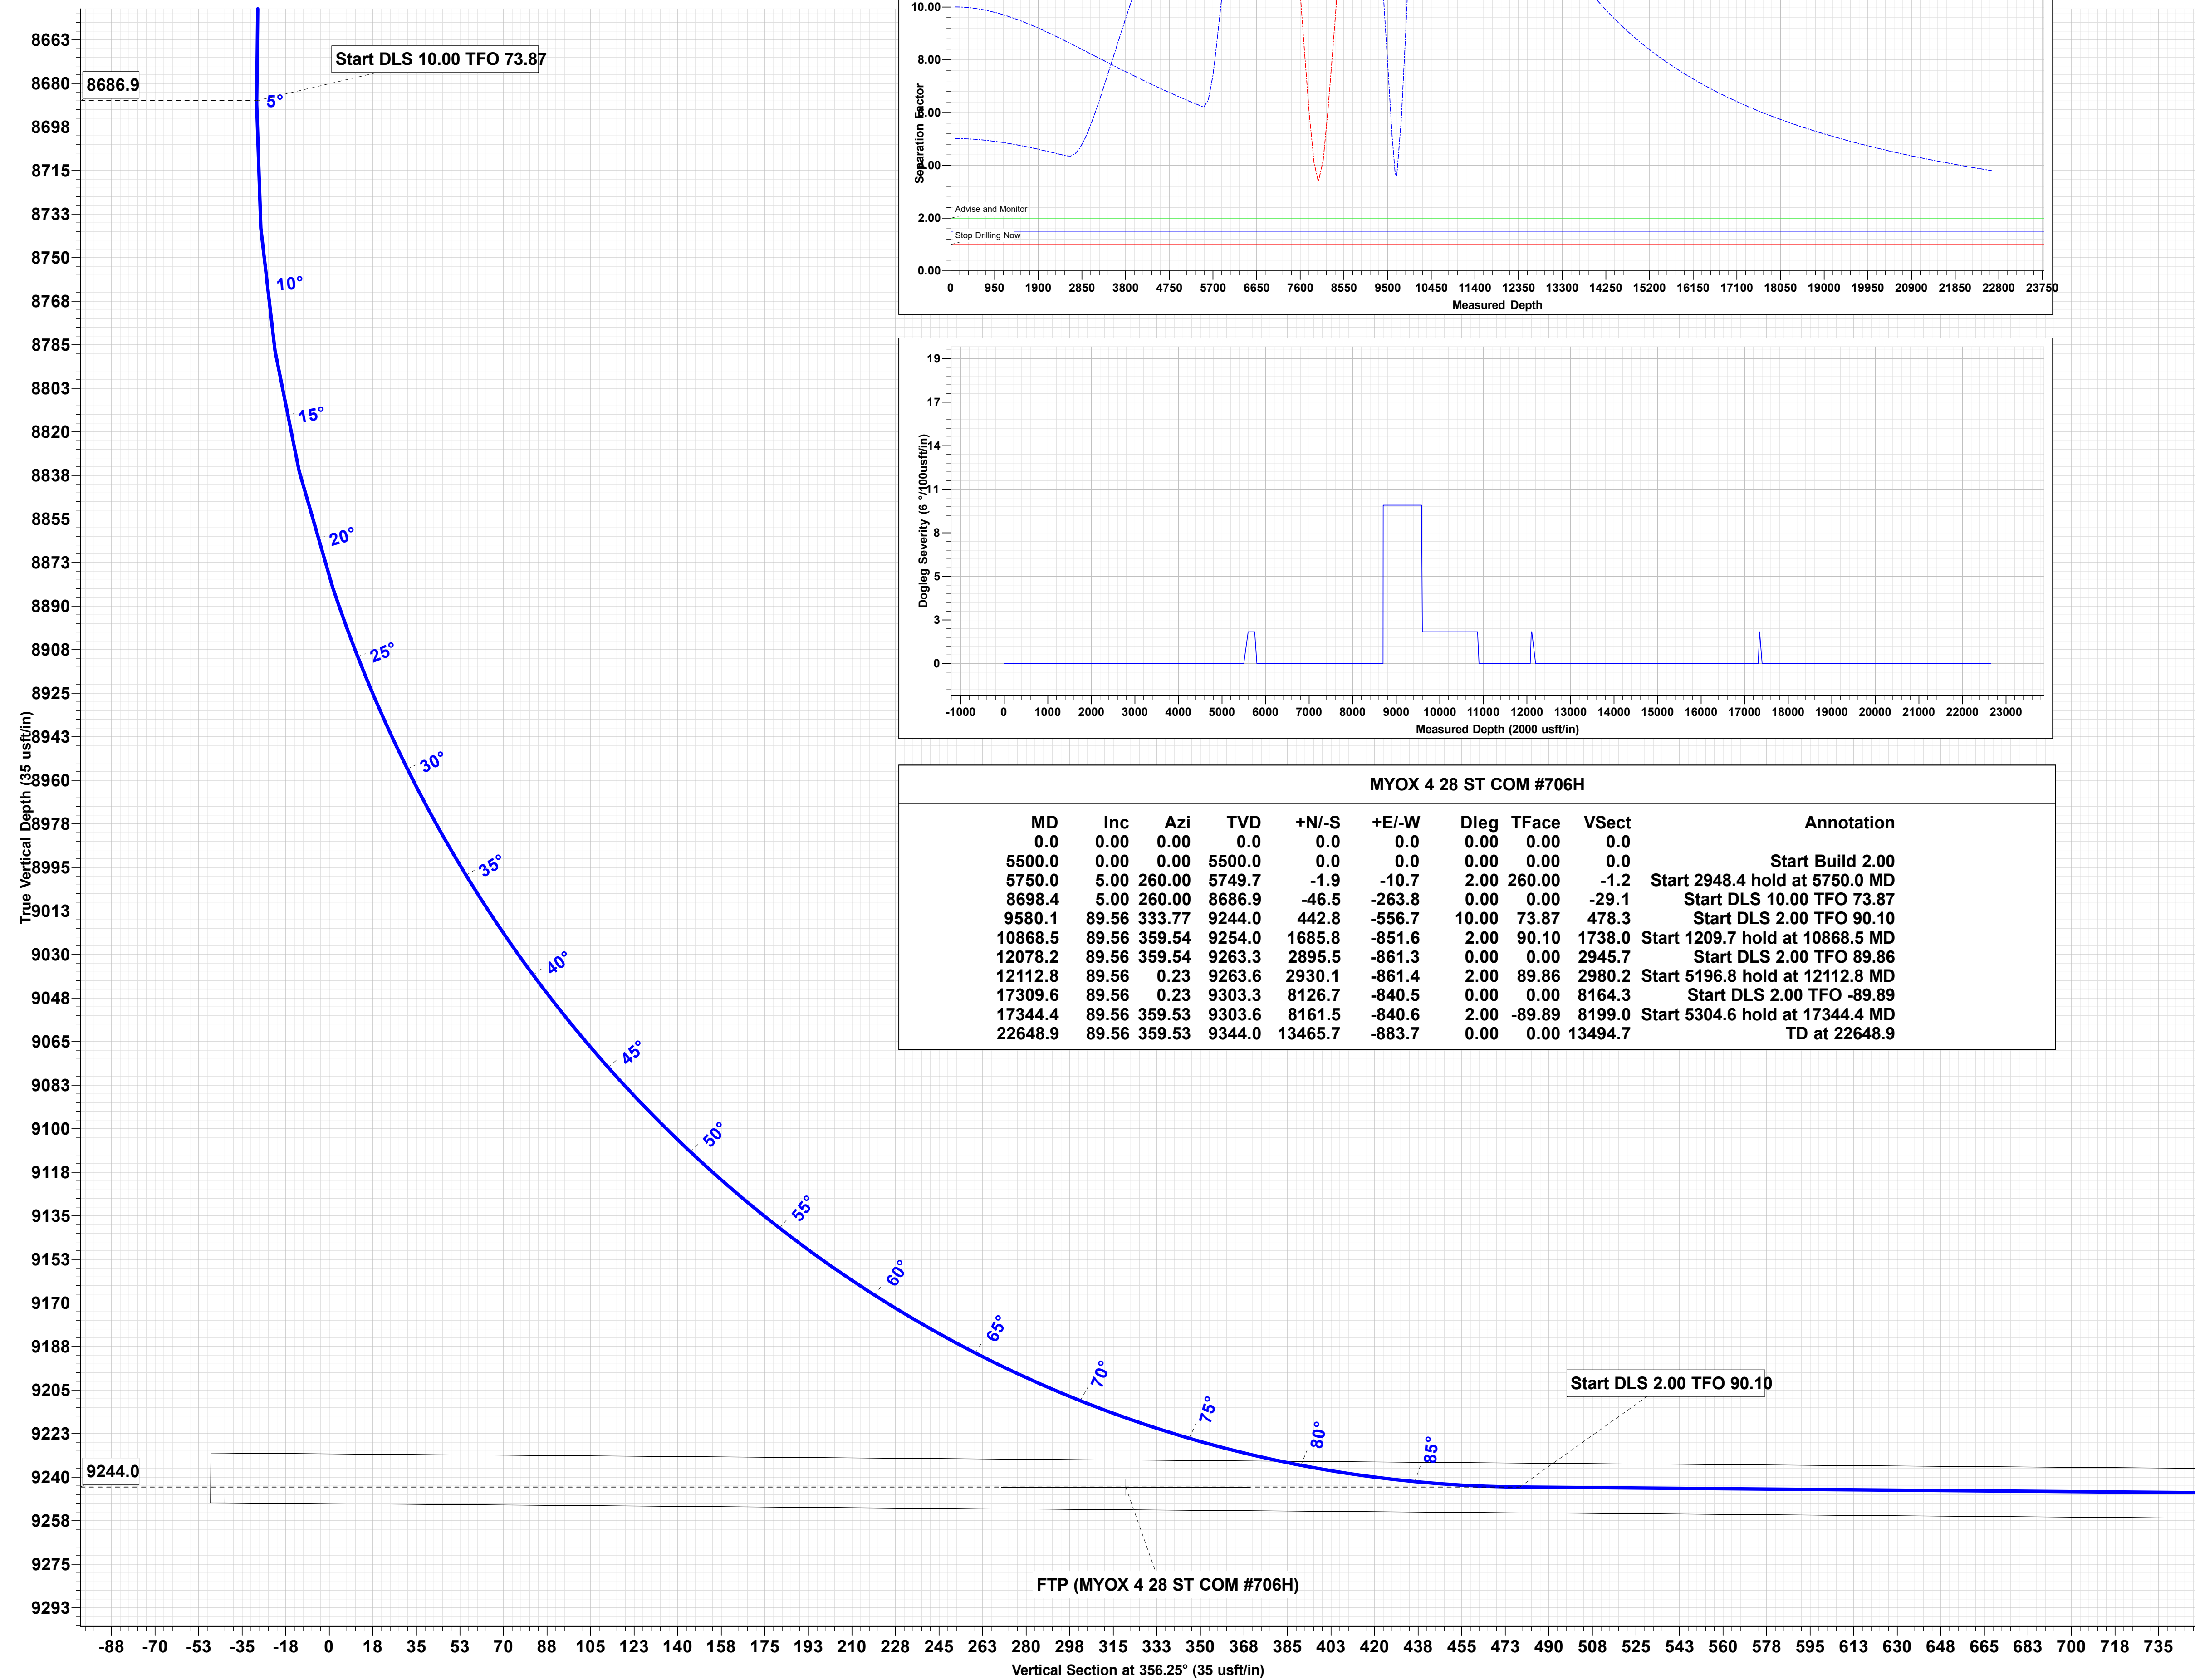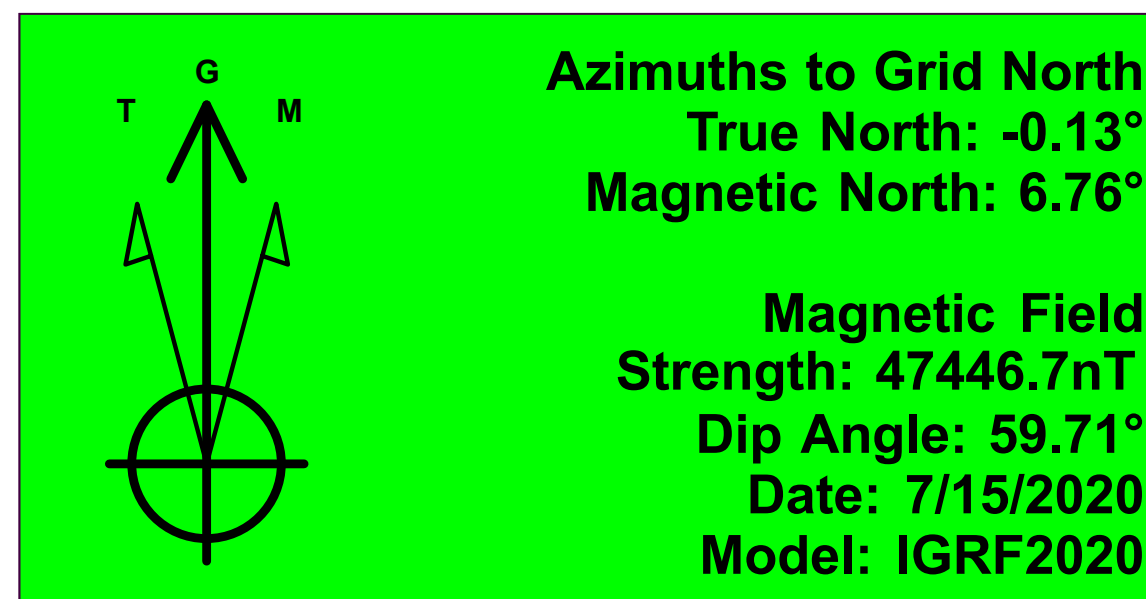

TRGT WNDW: 10' ABOVE/BELOW

