


0-005-60717.

P-35-8-28

Hanayan Petro. Corp.

Twin Lakes San Andres wt. #44.

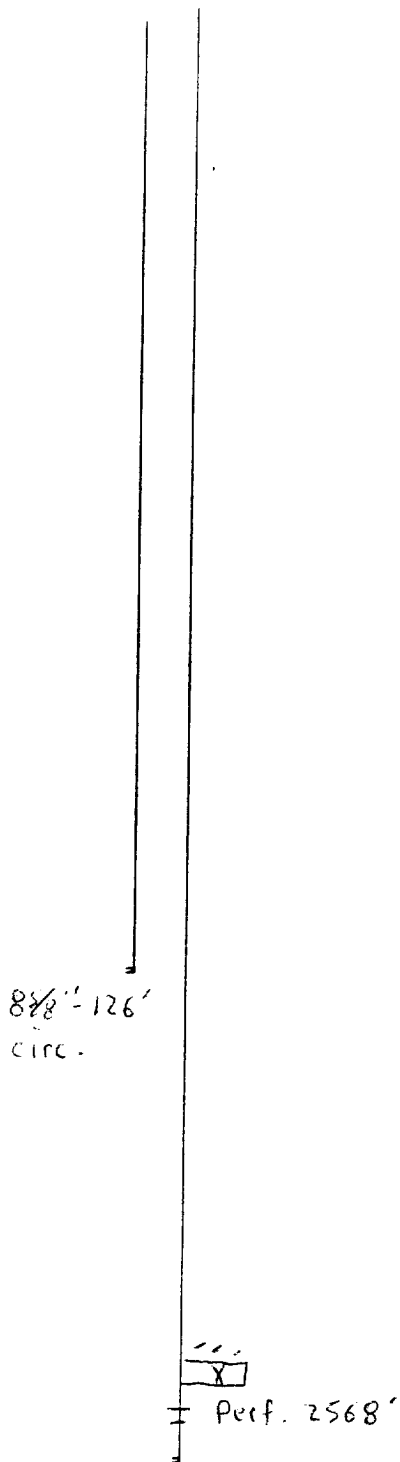

* erect dry hole marker.

* Spot cement from 176' to surface.

* Spot 100' cement Plug 50' in & 50' out 4 1/2" csq. TAL

* Cut & Pull 4 1/2" csq @ 2000'

* Circ. brine gel.

* Run & set CIBP @ 2550' w/ 35' cement.

4 1/2" - 2703'

w/ 125sx

Cal. roc - 1959'
