


DEVON ENERGY CORPORATION

WELLBORE SCHEMATIC

WELL NAME: Pure Federal #2			FIELD: Catclaw Draw (Morrow)			
LOCATION: Section 11, T21S, R25E			COUNTY: EDDY			STATE: NM
ELEVATION: GL=3297' - KB=3316'			SPUD DATE: 12/2/80		COMP DATE: 1/27/81	
API#: 30-015-23510		PREPARED BY: W. M. Frank			DATE: 12/30/97	
TUBULARS	DEPTH	SIZE	WEIGHT	GRADE	THREAD	HOLE SIZE
CASING:	0' - 450'	13 3/8"	61 & 54.5	K-55	ST&C	17 1/2"
CASING:	0' - 3,500'	8 5/8"	28	S-80	ST&C	11"
CASING:	0' - 10,552'	5 1/2"	17	L-80		7 7/8"
TUBING:	0' - 9,980'	2 3/8"	4.7	N-80	8 rd	

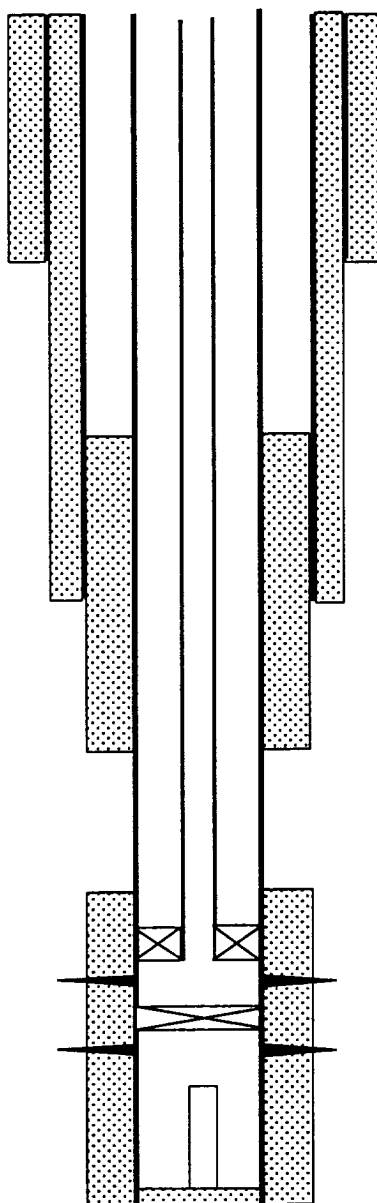

☐ CURRENT

☒ PROPOSED

13 3/8" Casing, Cemented w/564 sxs. Top job cement to surface.

Tubing String Detail:

2 3/8", N-80, 8rd tubing

Baker "EL" On/Off tool w/1.812" ID @ 9,978'

Baker MAX Packer @ 9,980'

8 5/8" casing, Cemented w/1650 sxs. TOC @ surface.

DV tool @ 5,501'. Cemented w/950 sxs cement. TOC @ 1,100' f/Temp. Surve

Morrow Perfs: 10,088 - 98' (2 spf).

Baker Lok-set Packer and "EL" On/Off Tool w/plug in place @ 10,136'

Morrow Perfs: 10,216 - 229', 10,255 - 267' (2 spf).

Approx. 70' of Vann gun believed to have been dropped to PBTD.

PBTD @ 10,464'.

5 1/2" @ 10552'. Casing cemented w/1050 sxs. TOC @ 7,240' f/CBL.

TD @ 10552'
