

FEDERAL LEGG NO. 1

LOCATION: 660'FNL & 2003'FEL, SECT. 27, T22S, R30E, UNIT B.
API NO: 30015047340000
ELEVATIONS: 3309' KB
SPUD DATE: 07-10-53

BASS ENTERPRISES
QUAHADA RIDGE FIELD
EDDY COUNTY, N.M.
DATE: 09-08-93: BEM

PROPOSED WELLBORE INFORMATION

20' 94#/FT, H-40, CSA 426', CMTD
W/400 SX 3% & 300 SX REG. NEAT
CMT CIRC TO SURFACE.

13-3/8" 61# & 68#/FT, CSA 3629'
1ST STAGE CMTD W/950 SX SLO SET
NEAT, 2ND STAGE CMTD W/2400 SX
SLO SET NEAT. CMT CIRC TO SURFACE.

PERF @ 3820'-3860'
PERF @ 3880'-3920'


PERF @ 6082' SQZ W/100 SX
PERF @ 6112'-6118' FRAC'D
PERF @ 6130' SQZ W/100 SX

PERF @ 7188' SQZ W/100 SX
PERF @ 7218'-7226' FRAC'D

PERF @ 7252' SQZ W/100 SX

PERF @ 7426' SQZ W/100 SX
PERF @ 7456'-7460' FRAC'D
PERF @ 7470' SQZ W/100 SX
PERF @ 7500'-7504' FRAC'D
PERF @ 7530' SQZ W/100 SX

9-5/8" 40# & 47#/FT, CSA 9025',
1ST STAGE CMTD W/1060 SX 8% & 200
SX INFERNO, 2ND STAGE CMTD W/1130
SX 8% & 200 SX INFERNO NEAT.

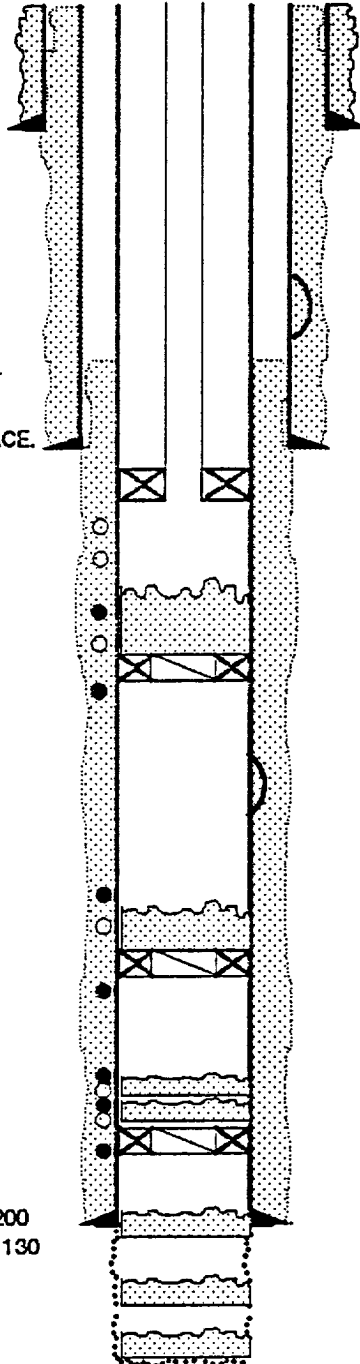

SPOT 150 SX 130' TO SURFACE

RETAINER @ 254'

CENTRALIZERS @ 3578', 4818', 6336',
6368', 7098', 9006'.

DV TOOL @ 2472'

TOC @ 2840' BY TEMP. SVY

2-3/8" 4.7 #/FT, J-55 IPC TBG

BAKER LOK-SET PKR @ 3700'

CMT PLUG W/300 SX @ APPX. 6124' -
5000' APPX.
RETAINER @ 6124'

DV TOOL @ 6352'

CMT PLUG W/30 SX @ 7234' - 7190'
RETAINER @ 7234'

CMT PLUG W/30 SX @ 7463' - 7420'
CMT PLUG W/30 SX @ 7512' - 7468'
RETAINER @ 7518'

CMT PLUG W/100 SX @ 9050' - 8790'

CMT PLUG W/75 SX @ 12625' - 12430'

CMT PLUG W/100 SX @ 15845' - 15590'
TD @ 15845'
