

RICKS EXPLORATION INC.


CACTUS 16 STATE #1

SECTION 16-24S-31E

EDDY COUNTY, NM

SPUD DATE: 6/17/92

Proposed TA

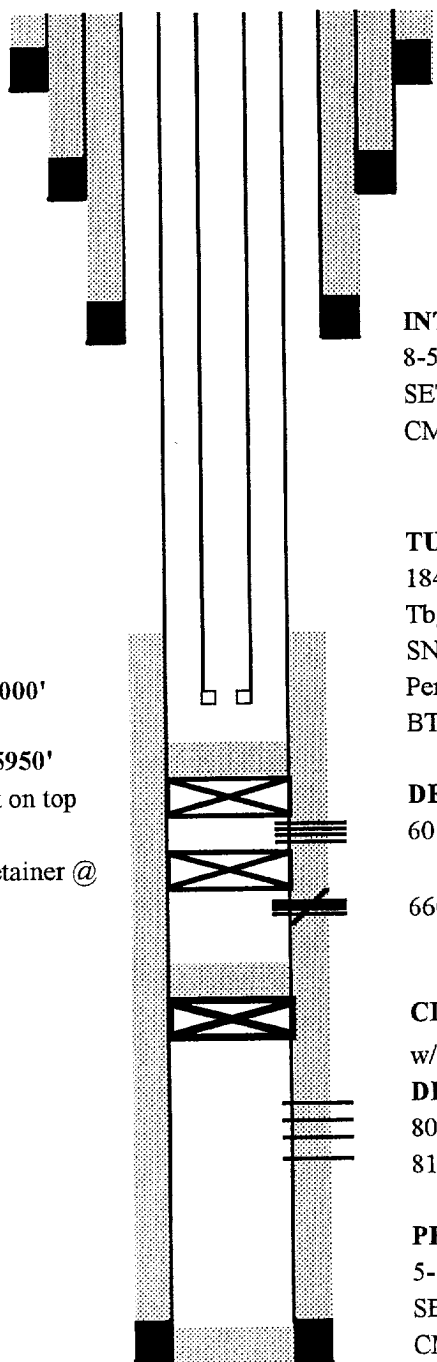

45' - 20" CONDUCTOR

GL: 3492'

DF:

KB: 3507'

SURFACE CASING:

13-5/8" 54# SET @ 626'

CMT w/ 470sx

INTERMEDIATE CASING:

8-5/8" 24# & 32#

SET @ 4250'

CMT w/ 1450 sx

TUBING:

184 jts 2-7/8" 6.5# N80 8rd

Tbg Anchor @ 5981 in 15K tension.

SN @ 6079'

Perf Sub 6080'

BTM of Mud Anchor @ 6114'

DELAWARE PERFORATIONS

6015 - 6020 4spf (8/95)

6600' 4 holes (Squeezed w/900 sx)

CIBP @ 7950' (7/95)

w/ 35' cmt on top

DELAWARE PERFORATIONS

8053' - 8089' 1/spf (36 holes - 7/92)

8165' - 68'; 8191' - 96'; 8224' - 28' 1 spf (15 holes - 10/92)

PRODUCTION CASING:

5-1/2" 15.5# & 17#

SET @ 8450'

CMT w/ 250 sx

RODS

142 - 3/4" N97 Rods

99 - 7/8" N97 Rods

1 - 8' X 7/8" Pony Rod

1-1/4" Rod

TOC @ 4000'

(Calc)

CIBP @ 5950'

w/ 35' cmt on top

Cement retainer @

6490'

PBTD: 7915'

10/18/01 BJR

TD: 8450'
