

RECEIVED

SEP 19 2011

submitted in lieu of Form 3160-5
UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Sundry Notices and Reports on Wells

Farmington Field Office
Bureau of Land Management

1. Type of Well
GAS

2. Name of Operator



3. Address & Phone No. of Operator

PO Box 4289, Farmington, NM 87499 (505) 326-9700

4. Location of Well, Footage, Sec., T, R, M

Surface: Unit M (SWSW), 1225' FSL & 1095' FWL, Section 32, T26N, R3W, NMPM
BH: Unit N (SESW), 1104' FSL & 1901' FWL, Section 32, T26N, R3W, NMPM


- 5. Lease Number
Jicarilla Contract 100
6. If Indian, All. or
Tribe Name
Jicarilla Apache
7. Unit Agreement Name

8. Well Name & Number
Jicarilla D 22Y

9. API Well No.
30-039-30837

10. Field and Pool
Blanco MV

11. County and State
Rio Arriba, NM



12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Table with 4 columns: Type of Submission, Type of Action, Change of Plans, Other - Cathodic. Includes options like Notice of Intent, Subsequent Report, Abandonment, etc.

13. Describe Proposed or Completed Operations

Attached is a drawing for the placement of the cathodic ground, rectifier and cable for the subject well.

14. I hereby certify that the foregoing is true and correct.

Signed Denise Journey Title Staff Regulatory Technician Date 9-19-11

(This space for Federal or State Office use)

APPROVED BY Title ACCEPTED FOR RECORD

CONDITION OF APPROVAL, if any:

Title 18 U S C Section 1001, makes it a crime for any person knowingly and willfully to make any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction

SEP 20 2011


FARMINGTON FIELD OFFICE BY MK

NMOCD

Handwritten initials 'PK'

Jicarilla D 22Y

Section 32, T26N, R3W, N.M.P.M., Rio Arriba County, NM

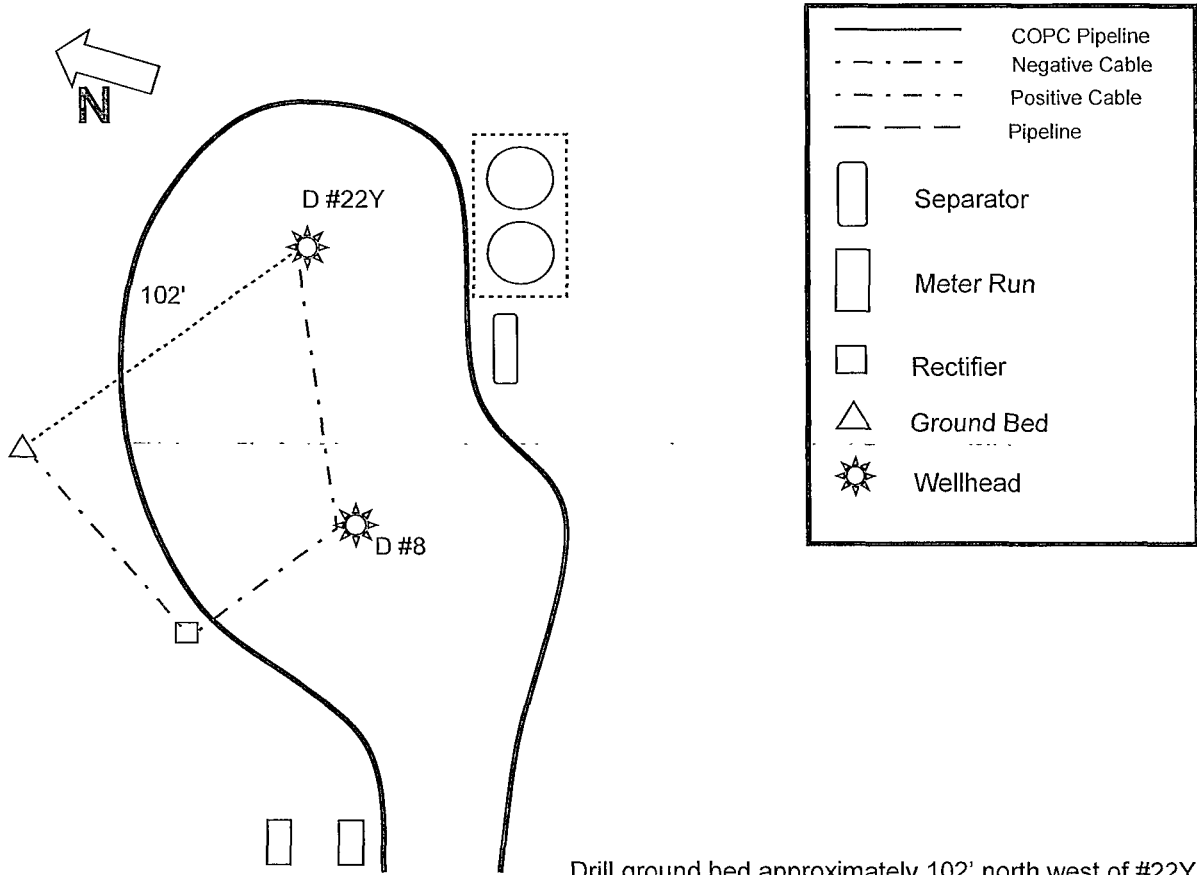

Drill ground bed approximately 102' north west of #22Y wellhead at staked location. Install single well solar unit, and install cables to new ground bed and #22Y and #8 wellheads at lengths below.

#22Y Cables:

Negative: 135'

Positive: 75'

#8 Cables:

Negative: 30'

Total Ditch: 210'
