

**UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**

RECEIVED**SEP 19 2011**

Sundry Notices and Reports on Wells

Farmington Field Office
Bureau of Land Management

1. Type of Well
GAS

2. Name of Operator

ConocoPhillips

3. Address & Phone No. of Operator

PO Box 4289, Farmington, NM 87499 (505) 326-9700

4. Location of Well, Footage, Sec., T, R, M

Unit L (NWSW), 1750' FSL & 1045' FWL, Section 15, T29N, R5W, NMPM

5. Lease Number
SF-080069

6. If Indian, All. or
Tribe Name

7. Unit Agreement Name
San Juan 29-5 Unit

8. Well Name & Number
San Juan 29-5 Unit 235

9. API Well No.

30-039-30879

10. Field and Pool
Basin FC/Gobernador PC

11. County and State
Rio Arriba, NM

12. CHECK APPROPRIATE BOX TO INDICATE NATURE OF NOTICE, REPORT, OTHER DATA

Type of Submission

Type of Action

☐ Notice of Intent☐ Abandonment☐ Change of Plans☒ Other -☐ Cathodic☒ Subsequent Report☐ Recompletion☐ New Construction☐ Plugging☐ Non-Routine Fracturing☐ Final Abandonment☐ Casing Repair☐ Water Shut off☐ Altering Casing☐ Conversion to Injection**13. Describe Proposed or Completed Operations**

Attached is a drawing for the placement of the cathodic ground, rectifier and cable for the subject well.

14. I hereby certify that the foregoing is true and correct.

Signed

Denise Journey

Denise Journey

Title Staff Regulatory Technician

Date 9-19-11

(This space for Federal or State Office use)

APPROVED BY

Title

ACCEPTED FOR RECORD


CONDITION OF APPROVAL, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction

SEP 20 2011**NMOCD****FARMINGTON FIELD OFFICE**
BY *mk**PC*

San Juan 29-5 #235

Section 15, T29N, R5W, N.M.P.M., Rio Arriba County, NM

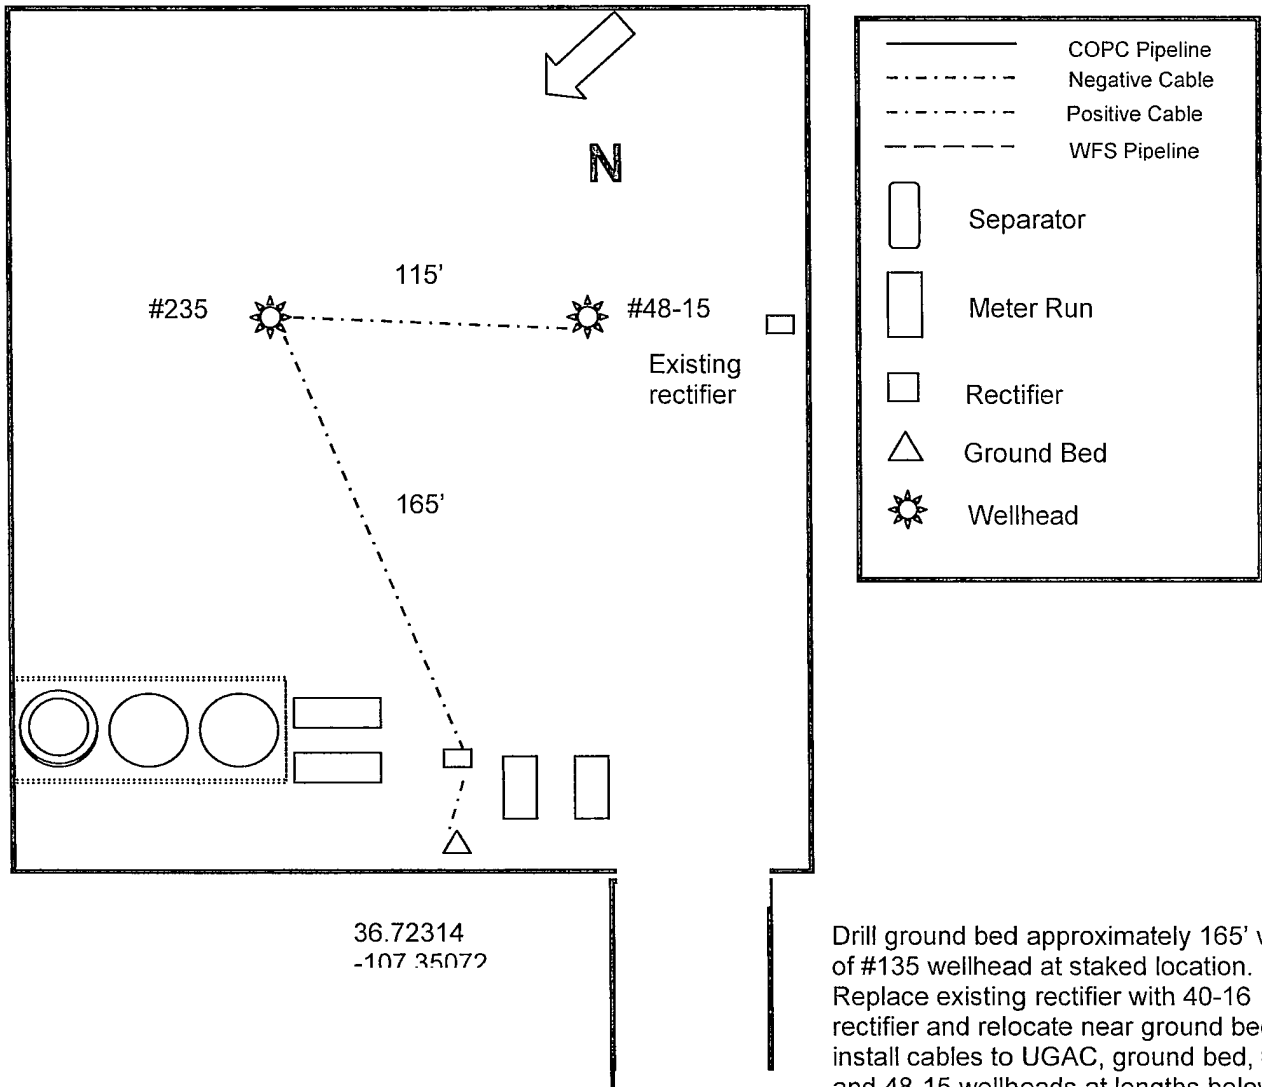

Drill ground bed approximately 165' west of #135 wellhead at staked location. Replace existing rectifier with 40-16 rectifier and relocate near ground bed and install cables to UGAC, ground bed, #235 and 48-15 wellheads at lengths below:

#235 Cables:

Negative: 470'

Positive: 110'

Total Ditch: 480'
