

RECEIVED

Form 3160-5
(August 2007)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

MAY 18 2016

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

Farmington Field Office
Bureau of Land Management
Serial No. **NM-020499**

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other		6. If Indian, Allottee or Tribe Name
2. Name of Operator ConocoPhillips Company		7. If Unit of CA/Agreement, Name and/or No.
3a. Address PO Box 4289, Farmington, NM 87499		8. Well Name and No. Ohio 1E
3b. Phone No. (include area code) (505) 326-9700		9. API Well No. 30-045-24406
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) Surface Unit G (SWNE), 1740' FNL & 1800' FEL, Sec. 22, T28N, R11W		10. Field and Pool or Exploratory Area Basin Dakota
		11. Country or Parish, State San Juan New Mexico

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input checked="" type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once Testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

The subject well is part of the proposed Mangum SRC 1C P&A program agreed to with the NMOCD. The attached revised procedure replaces the procedure filed with the P&A NOI submitted on 3/30/2016.

Notify NMOCD 24 hrs prior to beginning operations

OIL CONS. DIV DIST. 3
JUN 01 2016

BLM'S APPROVAL OR ACCEPTANCE OF THIS ACTION DOES NOT RELIEVE THE LESSEE AND OPERATOR FROM OBTAINING ANY OTHER AUTHORIZATION REQUIRED FOR OPERATIONS ON FEDERAL AND INDIAN LANDS

SEE ATTACHED FOR CONDITIONS OF APPROVAL

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed) Dollie L. Busse		Title Regulatory Technician
Signature	Date 5/16/16	

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by	Title PE	Date 5/31/16
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office FFO	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instruction on page 2)

NMOCD

Handwritten initials and marks in the bottom right corner.

ConocoPhillips
OHIO 1E
Expense - P&A

Lat 36° 39' 0.472" N

Long 107° 59' 15.936" W

PROCEDURE

This project requires the use of a steel tank to handle waste fluids circulated from the well and cement wash up.

Prior to commencing abandonment operations, ensure that the bradenhead valve is dug out and properly plumbed to the surface. Record the casing, intermediate and bradenhead pressures with an appropriately ranged gauge. Contact the Engineer if bradenhead pressure is present (per Exhibit "A-3").

1. Hold pre-job safety meeting. Comply with all NMOCD, BLM, and COP safety and environmental regulations. Test rig anchors prior to moving in rig. Before RU, run slickline to remove downhole equipment. If an obstruction is found, set a locking-3-slip-stop in the tubing.

2. MIRU workover rig. Check casing, tubing, and bradenhead pressures and record them in WellView. If there is pressure on the BH, contact the Wells Engineer (per Exhibit "A-3").

3. Remove existing piping on casing valve. RU blow lines from casing valves and begin blowing down casing pressure. Kill well as necessary. Ensure well is dead or on a vacuum.

4. ND wellhead and NU BOPE. Pressure and function test BOP to 250 psi low and 1000 psi over SICP high to a maximum of 2000 psi held and charted for 10 minutes per COP Well Control Manual. PU and remove tubing hanger.

5. TOOH with tubing (per pertinent data sheet).

Tubing size: 2-3/8" 4.7# J-55 EUE

Set Depth: 6,103'

KB: 12'

6. PU 3-3/4" bit and watermelon mill and round trip as deep as possible above top perforation at 5,985'.

7. PU 4-1/2" CR on tubing, and set at 5,935'. Pressure test tubing to 1000 psi. Sting out of CR. Load hole, and pressure test casing to 800 psi. If casing does not test, spot or tag subsequent plugs as appropriate. POOH with tubing.

8. RU wireline and run CBL with 500 psi on casing from CR at 5,935' to surface to identify TOC. Adjust plugs as necessary for new TOC. *Email log copy to Wells Engineer, Troy Salyers (BLM) at tsalyers@blm.gov, and Brandon Powell (NMOCD) at brandon.powell@state.nm.us upon completion of logging operations.*

All cement volumes use 100% excess outside pipe and 50' excess inside pipe. The stabilizing wellbore fluid will be 8.3 ppg, sufficient to balance all exposed formation pressures. All cement will be ASTM Class B mixed at 15.6 ppg with a 1.18 ct/sk yield.

9. Plug 1 (Perforations, Dakota, and Graneros formation tops, 5835-5935', 12 sacks Class B cement)

Mix 12 sx Class B cement and spot a balanced plug inside the casing to cover the perforations, Dakota, and Graneros tops. POOH.

10. Roll the hole with water and ensure that the wellbore is in a stabilized condition with no flow of gas and/or water before spotting the next plug. If flow occurs, the fluid weight must be increased until a stabilized condition is established (per Exhibit "A-3").

11. Plug 2 (Gallup formation top, 5050-5150', 51 sacks Class B cement)

RIH and perforate 3 squeeze holes at 5,150'. Establish injection rate into squeeze holes. RIH with a 4-1/2" CR and set at 5,109'. Mix 51 sx Class B cement. Squeeze 39 sx outside the casing, leaving 12 sx inside the casing to cover the Gallup top. PUH.

12. Plug 3 (Mancos formation top, 4180-4280', 12 sacks Class B cement)

Mix 12 sx Class B cement and spot a balanced plug inside the casing to cover the Mancos top. POOH.

13. Plug 4 (Mesaverde, Pictured Cliffs, and Fruitland formation tops, 1080-1672', 277 sacks Class B cement)

RIH and perforate 3 squeeze holes at 1,672'. Establish injection rate into squeeze holes. RIH with a 4-1/2" CR and set at 1,622'. Mix 277 sx Class B cement. Squeeze 229 sx outside the casing, leaving 48 sx inside the casing to cover the Mesaverde, Pictured Cliffs, and Fruitland tops. POOH.

14. Cease operations for 30 minutes allowing the bradenhead to be observed for pressure build. Record pressures with crystal gauge for accuracy. If pressures are observed, notify Wells Engineer and Production Engineering for path-forward discussion with NMOCD (per Exhibit "A-3").

Continued on next page

ConocoPhillips
OHIO 1E
Expense - P&A

Lat 36° 39' 0.472" N

Long 107° 59' 15.936" W

PROCEDURE (continued)

15. Plug 5 (Kirtland and Ojo Alamo formation tops, and surface plug, 0-602', 196 sacks Class B cement)

RU WL and perforate 4 big hole charge (if available) squeeze holes at 602'. TOO H and RD wireline. **Observe well for 30 minutes per BLM regulations.** RU pump, close blind rams and establish circulation out bradenhead with water. Circulate BH clean. TIH with 4-1/2" CR and set at 552'. Mix 151 sx Class B cement and squeeze until good cement returns to surface out BH valve. Shut BH valve and squeeze to max 200 psi. Sting out of CR and reverse circulate cement out of tubing. TOO H and LD stinger. TIH with open ended tubing to 552'. Mix 45 sx Class B cement and pump inside plug. TOO H and LD Tubing. SI well and WOC.

16. Nipple down BOP and cut off casing below the casing flange. Install P&A marker with cement to comply with regulations. RDMO.

Exhibit "A-3"

To Final Agreement - Withdrawal of Notice of Violation (3-15-02)
dated May 4, 2016 from ConocoPhillips Company to NMOCD

Updated Abandonment Procedures


The following procedural changes will be required for the P&A Program:

- 1) Prior to commencing abandonment operations, ensure that the bradenhead valve is dug out and properly plumbed to the surface. Record the casing, intermediate and bradenhead pressures with an appropriately ranged gauge. Contact the Engineer if bradenhead pressure is present. After the last set of completion perforations are abandoned with cement, roll the hole with water and ensure that the wellbore is in a stabilized condition with no flow of gas and/or water before spotting the next plug. If flow occurs, the fluid weight must be increased until a stabilized condition is established.
- 2) Following the plug over the Fruitland Formation Top, and prior to the plug over the Kirtland and Ojo Alamo Tops:
 - a. Operations will cease for 30 minutes allowing the Bradenhead to be observed for pressure build.
 - b. Pressures will be recorded with a crystal gauge for accuracy.
 - c. If pressures are observed, notify Wells Engineer and Production Engineering for path-forward discussion with NMOCD.
- 3) Within 24 hours of the abandonment and after two weeks, BLM will check for the presence of gas at the base of the dry hole marker and at the weep hole. Note ambient weather conditions when recording the results. If gas is detected, contact the Engineer.
- 4) If a Cathodic Protection well is on the well pad, check for the presence of gas at the vent cap. If gas is present, record results in AFMSS and contact the Engineer.


Note: when checking any sample point for the presence of gas, please be prepared for the possibility of anomalous pressure and the H₂S gas.

District NORTH	Field Name DK	API / UWI 3004524406	County SAN JUAN	State/Province NEW MEXICO
Original Spud Date 12/3/1980	Surface Legal Location 022-028N-011W-G	East/West Distance (ft) 1,800.00	East/West Reference FEL	North/South Distance (ft) 1,740.00
North/South Reference FNL				

Vertical - Original Hole, 3/1/2016 10:00:44 AM

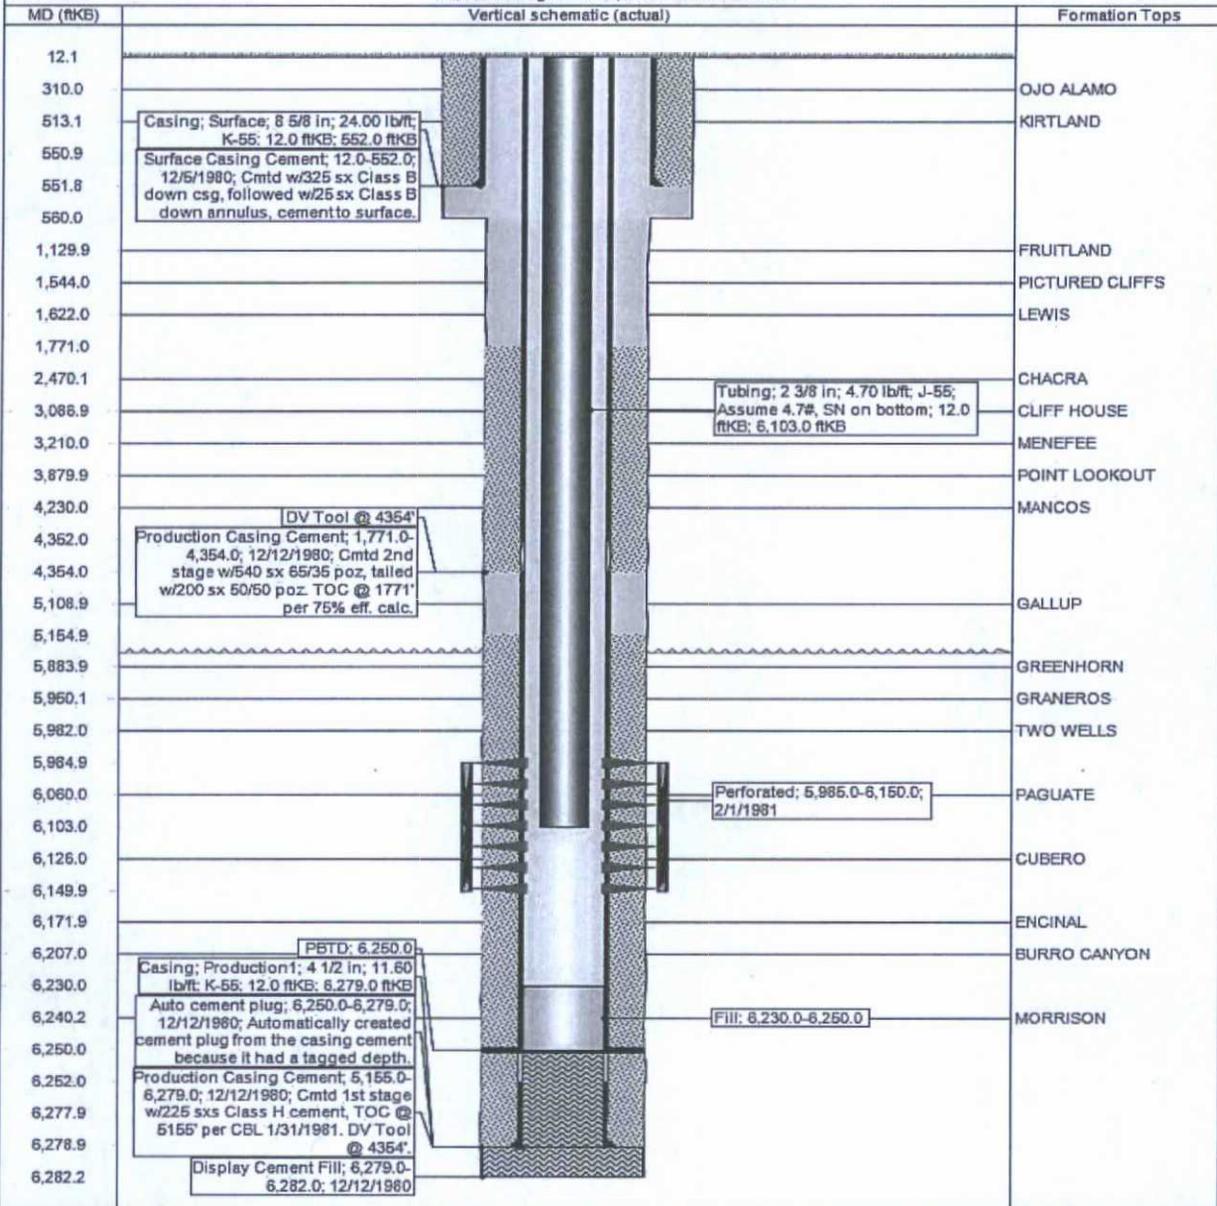

District NORTH	Field Name DK	API / UWI 3004624406	County SAN JUAN	State/Province NEW MEXICO
Original Spud Date 12/3/1980	Surface Legal Location 022-028N-011W-G	East/West Distance (R) 1,800.00	East/West Reference FEL	North/South Distance (R) 1,740.00
			North/South Reference FNL	

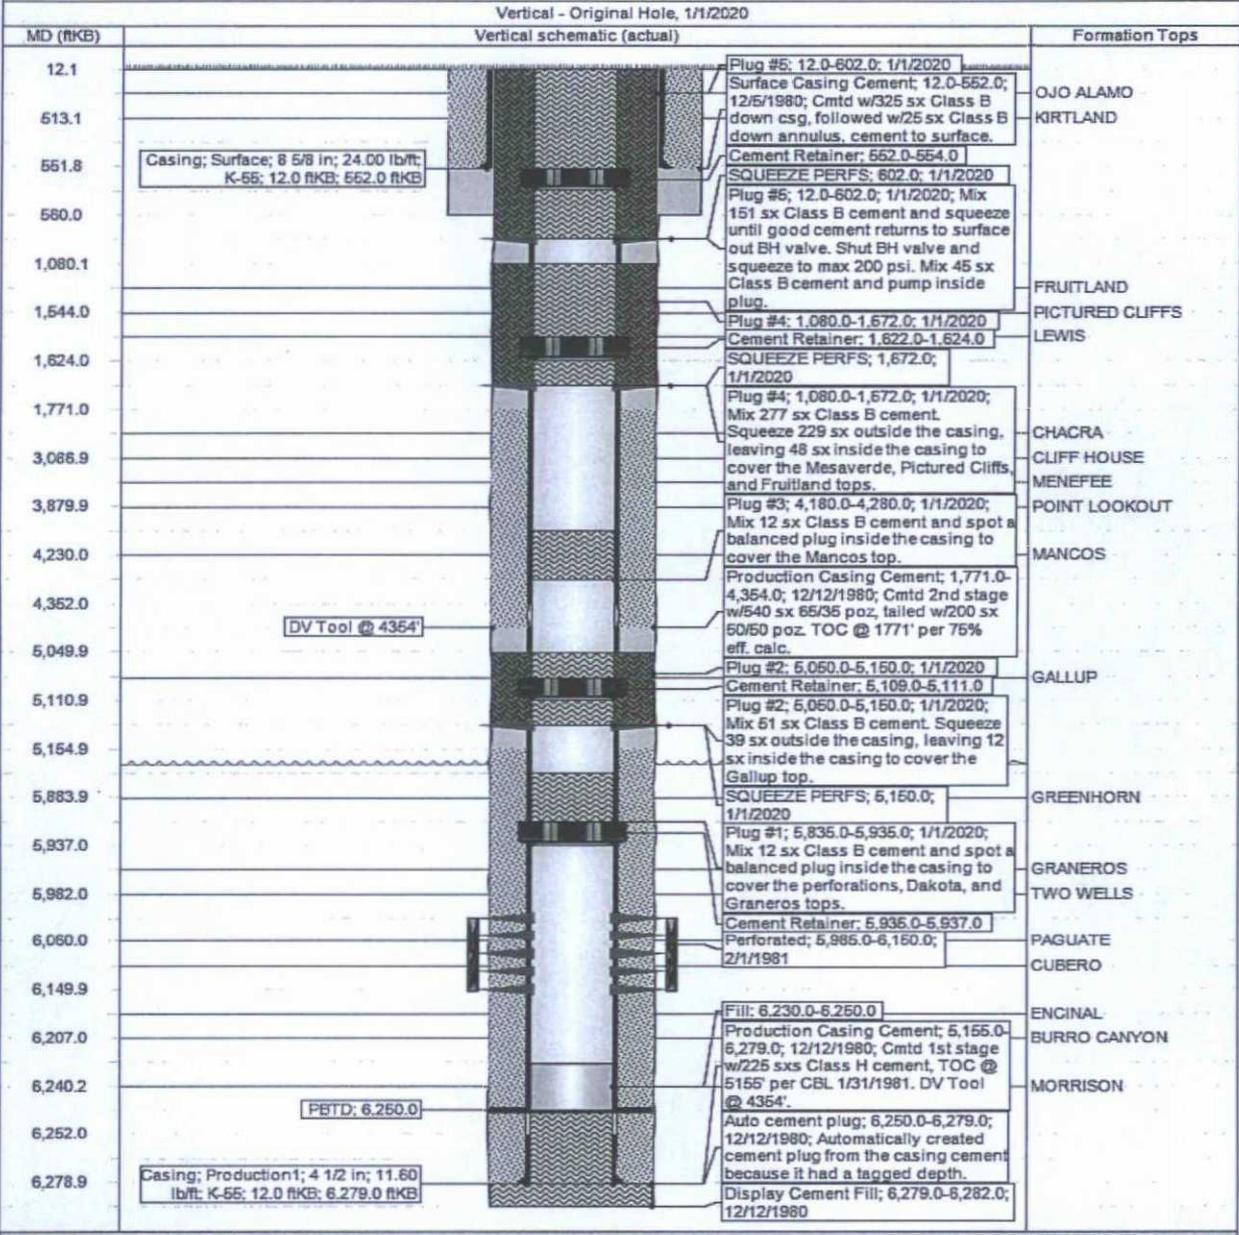

UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
FARMINGTON DISTRICT OFFICE
6251 COLLEGE BLVD.
FARMINGTON, NEW MEXICO 87402

Attachment to notice of
Intention to Abandon:

Re: Permanent Abandonment
Well: Ohio 1E

CONDITIONS OF APPROVAL

1. Plugging operations authorized are subject to the attached "General Requirements for Permanent Abandonment of Wells on Federal and Indian Lease."

2. Farmington Office is to be notified at least 24 hours before the plugging operations commence (505) 564-7750.

3. The following modifications to your plugging program are to be made:

- a) Bring the top of plug #3 to 4160 ft. to cover the Mancos top. BLM picks top of Mancos at 4210 ft. Adjust cement volume accordingly.
- b) Set a cement plug (3101-3001) ft. to cover the Mesaverde top. BLM picks top of Cliff House at 3051 ft.
- c) Set plug #4 (1589-1185) ft. inside/outside to cover the Pictured Cliffs and Fruitland tops. BLM picks top of Pictured Cliffs at 1539 ft. BLM picks top of Fruitland at 1235 ft.

Operator will run CBL from CR @ 5,935 ft. to surface to verify cement top. Submit the electronic copy of the log for verification to the following addresses: jwsavage@blm.gov
Brandon.Powell@state.nm.us

You are also required to place cement excesses per 4.2 and 4.4 of the attached General Requirements.

Office Hours: 7:45 a.m. to 4:30 p.m.
