

E

749 4 30-045-200 89
1A- 30-045-211663

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SW Sec. 4 Twp 30 Rng 9

Name of Well/Wells or Pipeline Serviced RIDDLE #1A, #4
cps 1048w

Elevation 6229' Completion Date 7/19/76 Total Depth 333' Land Type* N/A

Casing, Sizes, Types & Depths N/A

If Casing is cemented, show amounts & types used N/A

If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 80'

Depths gas encountered: N/A

Type & amount of coke breeze used: 4900 lbs.

Depths anodes placed: 310', 300', 290', 275', 265', 255', 245', 205', 125', 115'

Depths vent pipes placed: N/A

Vent pipe perforations: 240'

Remarks: gb #1

RECEIVED
MAY 31 1991
OIL CON. DIV.
DIST. 3

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Log 19-76

Drilling Log (Attach Hereto) ☐ #4

Completion Date **7-19-76**

Well Name Riddle #1 A		Location SW 4-30-9		CPS No. 1048 W	
Type & Size Bit Used 6 3/4				Work Order No. 57009	
Anode Hole Depth Log 333	Total Drilling Rig Time	Total Loss Coke Used 4900	Lost Circulation Mat'l Used	No. Sacks Mud Used	
Anode Depth					
# 1 310	# 2 300	# 3 290	# 4 275	# 5 265	# 6 255
# 7 245	# 8 205	# 9 125	# 10 115		
Anode Output (Amps)					
# 1 4.0	# 2 3.4	# 3 3.5	# 4 3.0	# 5 3.0	# 6 2.9
# 7 2.6	# 8 2.5	# 9 3.3	# 10 4.		
Anode Depth					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Anode Output (Amps)					
# 11	# 12	# 13	# 14	# 15	# 16
# 17	# 18	# 19	# 20		
Total Circuit Resistance		No. 8 C.P. Cable Used		No. 2 C.P. Cable Used	
Volts 12.07	Amps 15.2	Ohms 0.78	33		

Remarks: **Wet at 80' Driller Said Blew water out at 100 Water Next A.M. at 106'**

Vent Perforated 240'
Slurry 49 Coke

2248.50

79.44 cable

113.96 Seal Water

170.00 Anodes

(51.00) credit

2560.90

102.44 Tax

2663.34


294.00 Labor

194.50 Rent

213.40 Slurry

2965.24

GROUND BED LAYOUT SKETCH

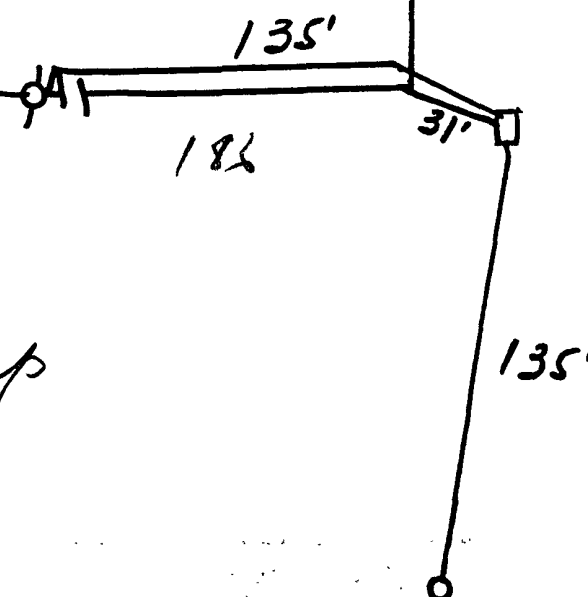

All Construction Completed

Amels
(Signature)

