

894

59-30-039-07400
137-30-039-20052

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator MERIDIAN OIL Location: Unit SW Sec. 14 Twp 28 Rng 6
Name of Well/Wells or Pipeline Serviced SAN JUAN 28-6 UNIT #59, #137
cps 115lw
Elevation 6458' Completion Date 8/15/77 Total Depth 325' Land Type* N/A
Casing, Sizes, Types & Depths N/A
If Casing is cemented, show amounts & types used N/A
If Cement or Bentonite Plugs have been placed, show depths & amounts used
N/A
Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 105' - 120'
Depths gas encountered: N/A
Type & amount of coke breeze used: 32 SACKS
Depths anodes placed: 290', 280', 270', 260', 250', 240', 185', 175', 165', 140'
Depths vent pipes placed: 295'
Vent pipe perforations: 200'
Remarks: gb #1

RECEIVED
MAY 31 1991
OIL CON. DIV. 1
DIST. 2

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.

WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

Drilling Log (Attach Hereto). ☐

Completion Date **8-15-77**


Well Name SAN JUAN 28-6 UNIT #59		Location SW 14-28-6		CPS No. 1151W	
Type & Size Bit Used 6 3/4"		Total Drilling Rig Time 325-312		Work Order No. 157-54523-19	
Anode Hole Depth 325-312		Total Lbs. Coke Used 32		No. Sacks Mud Used 137-54526.19	
Anode Depth		Anode Output (Amps)		Anode Depth	
#1 290	#2 280	#3 270	#4 260	#5 250	#6 240
#7 185	#8 175	#9 165	#10 140		
#11	#12	#13	#14	#15	#16
#17	#18	#19	#20		
Total Circuit Resistance		No. 8 C.P. Cable Used		No. 2 C.P. Cable Used	
Volts 11.6		Amps 12.2		Ohms 0.95	

Remarks: **Static #59 600' NW = 0.76, Static #137 600' NE = 0.76**
Installed 10-2"x2"x48" Graphite Anodes. Driller said
MAKING WATER between 105' & 120'. Blew water after 30 minutes.
Perforated 200' of 1" PVC Vent Pipe. Installed 295' of 1" PVC Vent Pipe
Slurried 32 sacks of coke.
Installed 60V 30A Rectifier. Stub Pole

All Construction Completed

Lott & Knight
(Signature)

GROUND BED LAYOUT SKETCH

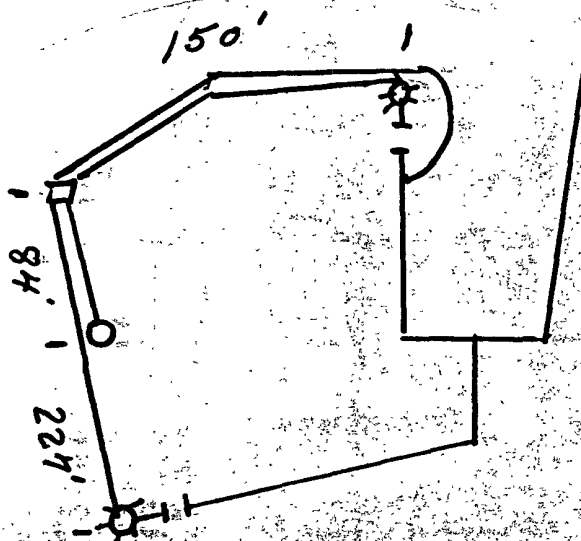

DISTRIBUTION:

- WHITE - Division Corrosion Office
- YELLOW - Area Corrosion Office
- PINK - Originator File

6458

DAILY DRILLING REPORT

[illegible]

SIGNED: Toolpusher

____ Company Supervisor
