

52 - 30-039-06986

113 - 30-039-06985

DATA SHEET FOR DEEP GROUND BED CATHODIC PROTECTION WELLS
NORTHWESTERN NEW MEXICO
(Submit 3 copies to OCD Aztec Office)

Operator Union Oil Company of California Location: Unit Sec. 20 Twp 27N Rng 6WName of Well/Wells or Pipeline Serviced Rincon Unit 52 PC and Rincon 113 MVElevation 6589' Completion Date 11/4/1965 Total Depth 260' Land Type* FCasing, Sizes, Types & Depths NoneIf Casing is cemented, show amounts & types used none


If Cement or Bentonite Plugs have been placed, show depths & amounts used
 None

Depths & thickness of water zones with description of water when possible:
Fresh, Clear, Salty, Sulphur, Etc. 80' deep

Depths gas encountered: NAType & amount of coke breeze used: 3335 lbsDepths anodes placed: 142'Depths vent pipes placed: 142'Vent pipe perforations: ?Remarks: El Paso Natural Gas was operator at time this ground bed was installed.This was the first ground bed installed.

If any of the above data is unavailable, please indicate so. Copies of all logs, including Drillers Log, Water Analyses & Well Bore Schematics should be submitted when available. Unplugged abandoned wells are to be included.

*Land Type may be shown: F-Federal; I-Indian; S-State; P-Fee.
If Federal or Indian, add Lease Number.



WELL CASING
CATHODIC PROTECTION CONSTRUCTION REPORT
DAILY LOG

12-130'-4 $\frac{3}{4}$ " Drop-#9

Date 11-9-65

Well Name RINCON #52, #113 & 175				CPS No. 690W			
Location NE 20-27-6				Work Order No. 184 53421 } -50-20			
Anode Hole Depth 260	Total Drilling Rig Time 20 Hrs.	Type & Size Bit Used 20192 = 150		No. Sacks of Cement Used 54265			
No. Sacks Lost Circulation Mat'l Used 0		Anode Depth		2 Mud			
		#1 130	#2 105	#3 99	#4 93	#5 87	#6 136
Total Lbs. Coke Used 3335		#1 230	#2 224	#3 218	#4 148	#5 142	#6 136
Total Circuit Resistance		Anode Output (Volts)					
Volts 12.3 Amps 11.8 Ohms 1.04		#1 2.5	#2 2.8	#3 2.6	#4 3.5	#5 3.6	#6 3.7
No. Ft. Surface Cable Conduit 1109							


Drilling Log (Attach Hereto). ☐

Remarks: Static #175 600' N = .70 #113 600' S = .70 #52 600' SE = .70
3/4" Plastic Hose to #10 Anode = 103' - 41bs Chemical
Install 45V 30A (3NEG) Good All Rect. Ser. 65C6645

All Construction Completed

Darrells
(Signature)

GROUND BED LAYOUT SKETCH

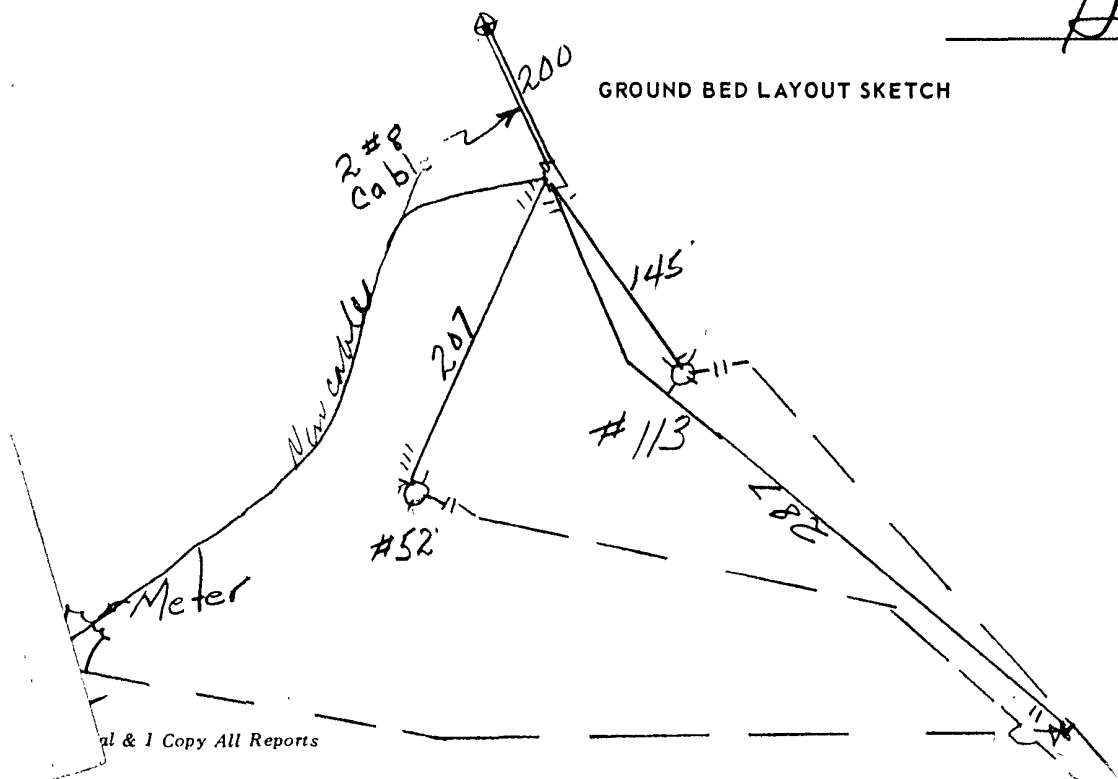

283' #8 WIRE

