

District I
1625 N. French Dr., Hobbs, NM 88240

State of New Mexico
Energy, Minerals & Natural Resources

Form C-104
Revised August 1, 2011

District II
811 S. First St., Artesia, NM 88210

District III
1000 Rio Brazos Rd., Aztec, NM 87410

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit one copy to appropriate District Office

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT

¹ Operator name and Address OXY USA INC. P.O. BOX 50250 MIDLAND, TX 79710		² OGRID Number: 16696
		³ Reason for Filing Code/ Effective Date: RT - 09/12/2022
⁴ API Number 30 - 025-48025	⁵ Pool Name WC-025 G-09 S223219D; Wolfcamp	⁶ Pool Code 98296
⁷ Property Code: 332928	⁸ Property Name: DR PI FEDERAL UNIT 18-7 IPP	⁹ Well Number: 34H

II. ¹⁰ Surface Location

Ul or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South Line	Feet from the	East/West line	County
O	18	22S	32E		170	SOUTH	1430	EAST	LEA

¹¹ Bottom Hole Location

FTP- 134' FSL 1445' FEL LTP- 294' FNL 1308' FEL

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	7	22S	32E		88	NORTH	1282	EAST	LEA
¹² Lse Code F	¹³ Producing Method Code : F		¹⁴ Gas Connection Date: TBD		¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
237722	CENTURION PIPELINE L.P.	O
248749	DCP MIDSTREAM, LP	G

IV. Well Completion Data

²¹ Spud Date 02/02/22	²² Ready Date 09/12/2022	²³ TD 22647'M 12034'V	²⁴ PBTD 22545'M 12036'V	²⁵ Perforations 12253-22439'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	³⁰ Sacks Cement
17-1/2"		13-3/8"		948'	1140
9-7/8"		7-5/8"		10770'	2050
6-3/4"		5-1/2"		22570'	904

V. Well Test Data

³¹ Date New Oil	³² Gas Delivery Date	³³ Test Date	³⁴ Test Length	³⁵ Tbg. Pressure	³⁶ Csg. Pressure
³⁷ Choke Size	³⁸ Oil	³⁹ Water	⁴⁰ Gas		⁴¹ Test Method

⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief.

Signature: 

Printed name: JANA MENDIOLA

Title: SR. REGULATORY ANALYST

E-mail Address:
Janalyn_mendiola@oxy.com

Date: 09/11/2022 Phone: 432-685-5936

OIL CONSERVATION DIVISION

Approved by:

PATRICIA MARTINEZ

Title: PETROLEUM SPECIALIST

Approval Date: 12/7/2022

RT EXPIRES 12/12/2022

1625 N. French Dr., Hobbs, NM 88240
 Phone: (575) 393-6161 Fax: (575) 393-0720
District II
 811 S. First St., Artesia, NM 88210
 Phone: (575) 748-1283 Fax: (575) 748-9720
District III
 1000 Rio Brazos Road, Aztec, NM 87410
 Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
 1220 S. St. Francis Dr., Santa Fe, NM 87505
 Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
 Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
 1220 South St. Francis Dr.
 Santa Fe, NM 87505

Revised August 1, 2011
 Submit one copy to appropriate
 District Office

☒ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION AS-DRILLED PLAT

¹ API Number 30-025-48025	² Pool Code 98296	³ Pool Name WC-025 G-09 S223219D; WOLFCAMP
⁴ Property Code 332928	Property Name DR PI FEDERAL UNIT 18-7 IPP	
⁷ OGRID No. 16696	⁸ Operator Name OXY USA INC.	⁶ Well Number 34H
		⁹ Elevation 3664'



¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
O	18	22S	32E		170	SOUTH	1430	EAST	LEA
¹¹ Bottom Hole Location If Different From Surface									
UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	7	22S	32E		88	NORTH	1282	EAST	LEA
¹² Dedicated Acres 640.0	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.						

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

	CORNER COORDINATES NAD 83, SPCS NM EAST A - X: 735137.95' / Y: 512036.21' B - X: 735157.00' / Y: 509399.20' C - X: 735175.20' / Y: 506758.05' D - X: 735193.40' / Y: 504116.89' E - X: 732552.19' / Y: 504086.41' F - X: 732516.41' / Y: 509369.02' G - X: 732476.29' / Y: 514647.62' H - X: 735118.90' / Y: 514673.22' CORNER COORDINATES NAD 27, SPCS NM EAST A - X: 693955.77' / Y: 511975.57' B - X: 693974.74' / Y: 509338.63' C - X: 693992.87' / Y: 506697.55' D - X: 694010.99' / Y: 504056.48' E - X: 691369.80' / Y: 504025.99' F - X: 691334.17' / Y: 509308.45' G - X: 691294.20' / Y: 514587.11' H - X: 693936.79' / Y: 514612.51' BOTTOM HOLE LOCATION 88' FNL 1282' FEL, SECTION 7 22647' MEASURED DEPTH IN FEET NAD 83, SPCS NM EAST X: 733837.16' / Y: 514572.72' LAT: 32.41308345N / LON: 103.70953512W NAD 27, SPCS NM EAST X: 692655.06' / Y: 514512.01' LAT: 32.41296083N / LON: 103.70904588W LAST TAKE POINT 294' FNL 1308' FEL, SECTION 7 22439' MEASURED DEPTH IN FEET NAD 83, SPCS NM EAST X: 733813.07' / Y: 514366.15' LAT: 32.41251604N / LON: 103.70961708W NAD 27, SPCS NM EAST X: 692630.96' / Y: 514305.44' LAT: 32.41239342N / LON: 103.70912786W FIRST TAKE POINT 134' FSL 1445' FEL, SECTION 18 12253' MEASURED DEPTH IN FEET NAD 83, SPCS NM EAST X: 733747.77' / Y: 504234.67' LAT: 32.38466903N / LON: 103.71002006W NAD 27, SPCS NM EAST X: 692565.37' / Y: 504174.24' LAT: 32.38454628N / LON: 103.70953190W KICK OFF POINT 252' FNL 1403' FEL, SECTION 19 11525' MEASURED DEPTH IN FEET NAD 83, SPCS NM EAST X: 733791.95' / Y: 503848.61' LAT: 32.38360715N / LON: 103.70988423W NAD 27, SPCS NM EAST X: 692609.54' / Y: 503788.19' LAT: 32.38348440N / LON: 103.70939611W SURFACE HOLE LOCATION 170' FSL 1430' FEL, SECTION 18 NAD 83, SPCS NM EAST X: 733762.25' / Y: 504270.47' LAT: 32.38476719N / LON: 103.70997247W NAD 27, SPCS NM EAST X: 692579.85' / Y: 504210.04' LAT: 32.38464444N / LON: 103.70948431W	¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division. Signature: Date: 09/11/22 Printed Name: JANA MENDIOLA E-mail Address: janalyn_mendiola@oxy.com ¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well surface location shown on this plat was plotted from field notes of the as-staked surveys made by me or under my supervision, and that the same is true and correct to the best of my belief. Data used for underground measurements were provided by others for reference only and does not constitute field measurements performed by R-Squared Global. SEPTEMBER 8, 2022 Date of Survey Signature and Seal of Professional Surveyor: Certificate Number: DAVID W. MYERS
--	---	---

Distances/areas relative to NAD 83 Combined Scale Factor: 0.999776382 Convergence Angle: 00°20'34.08"

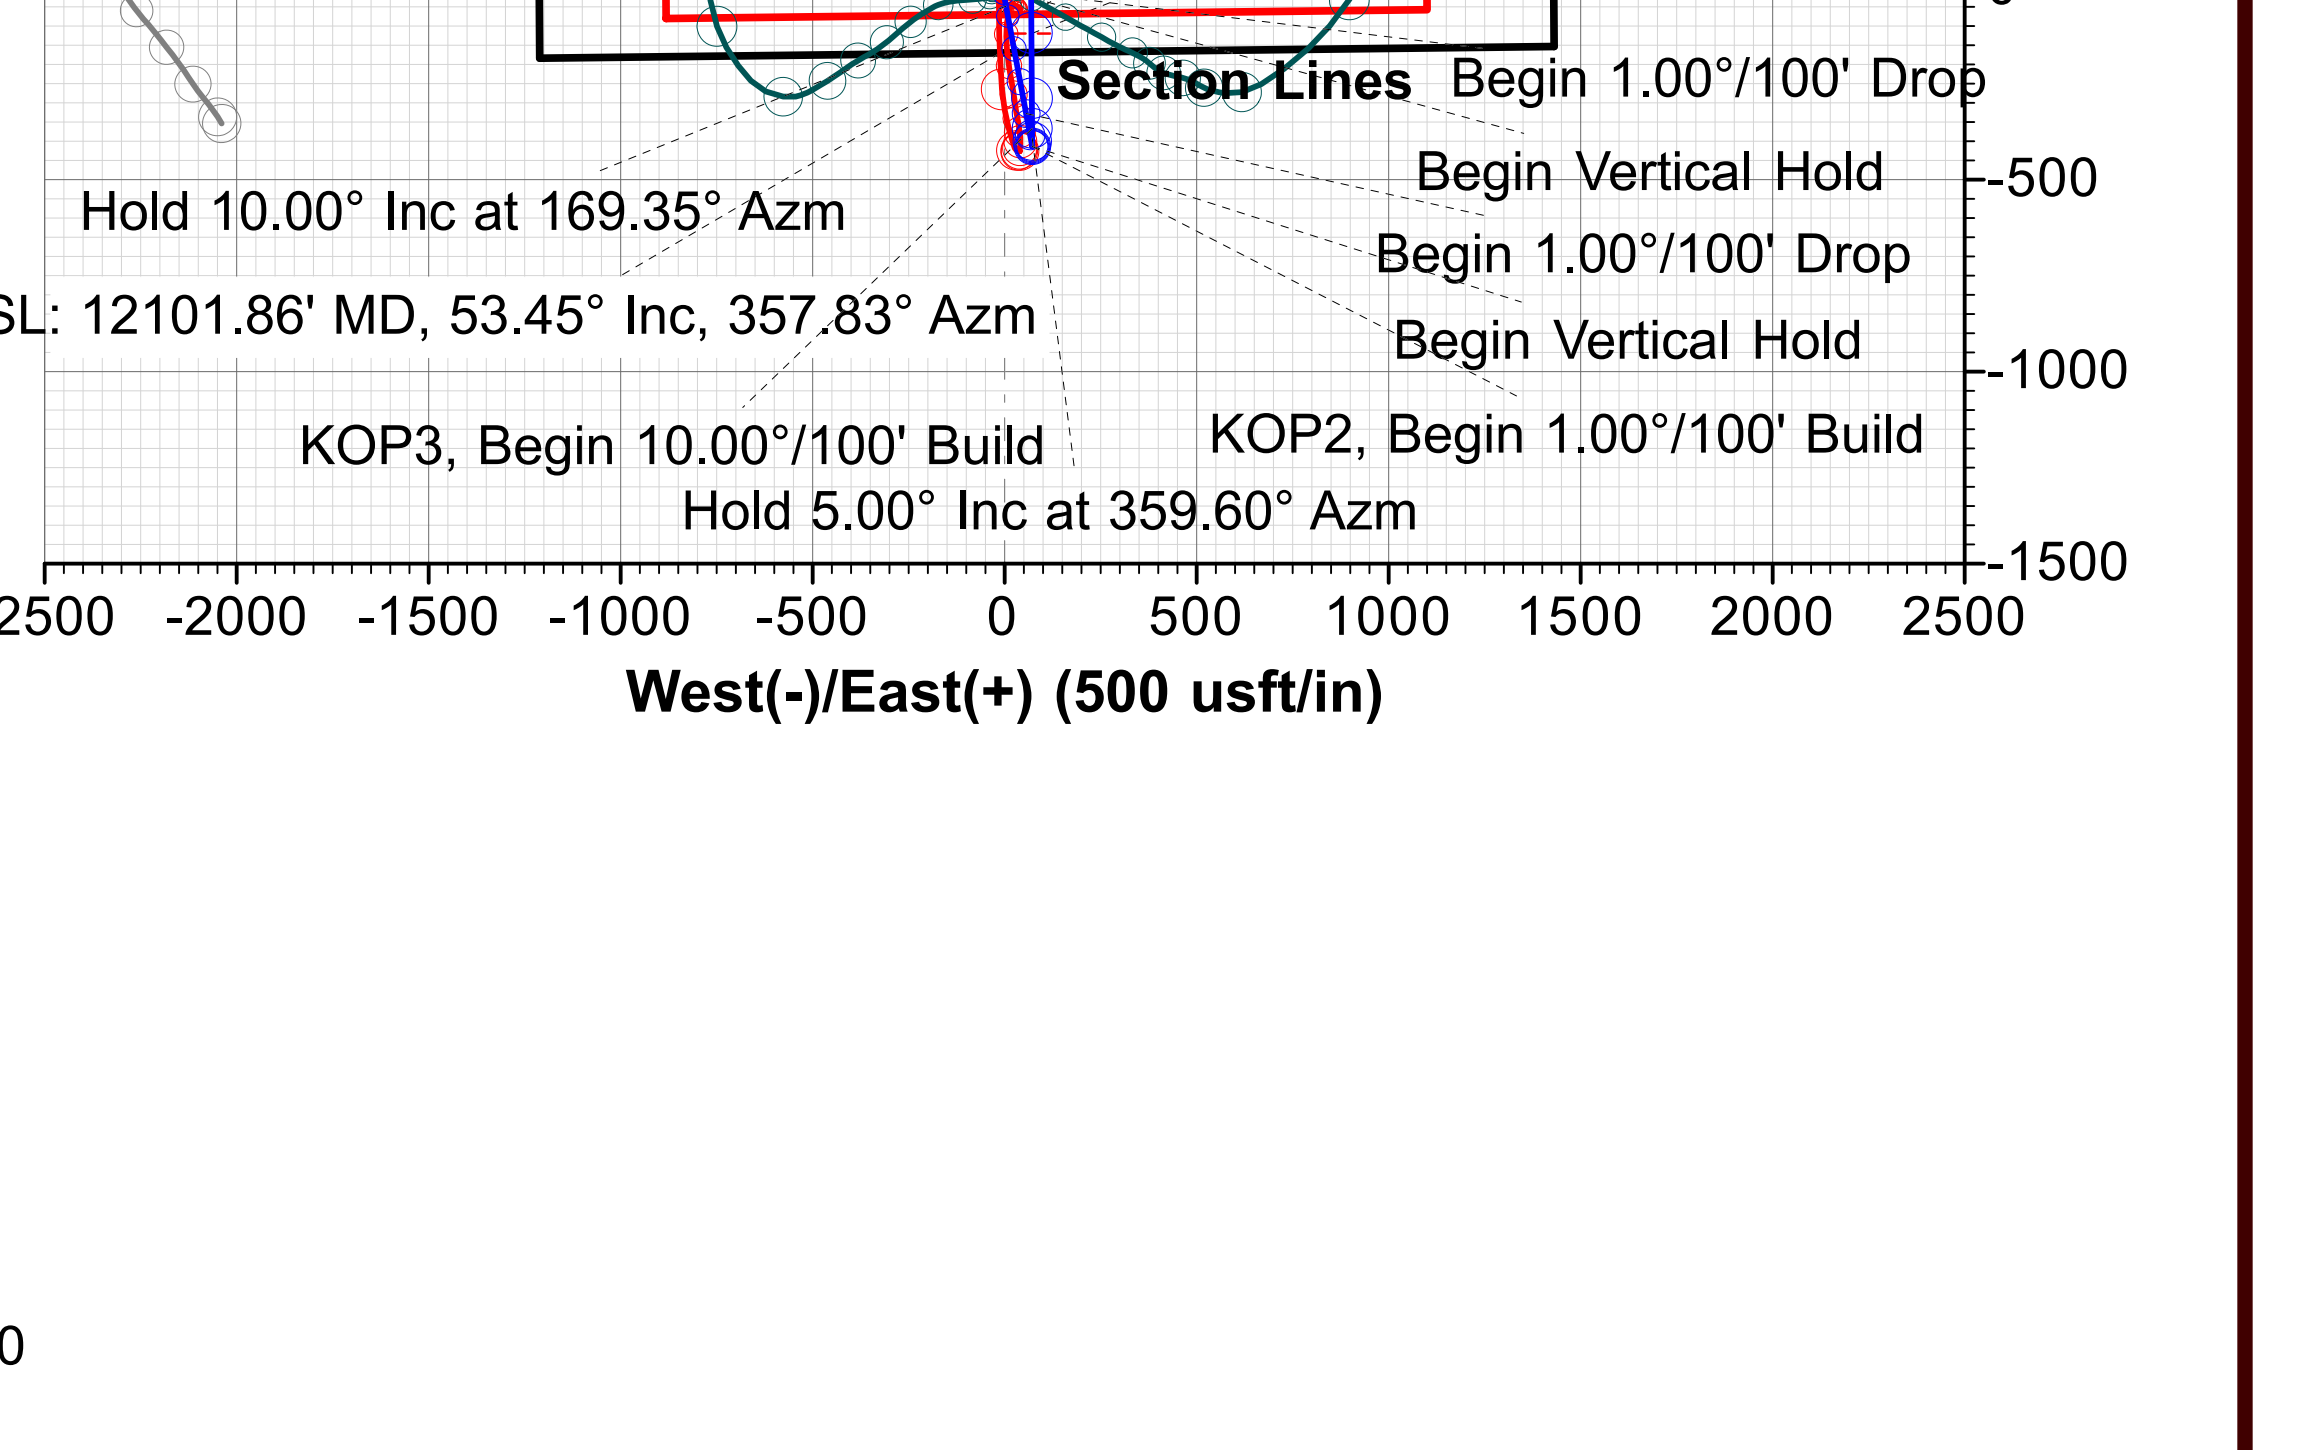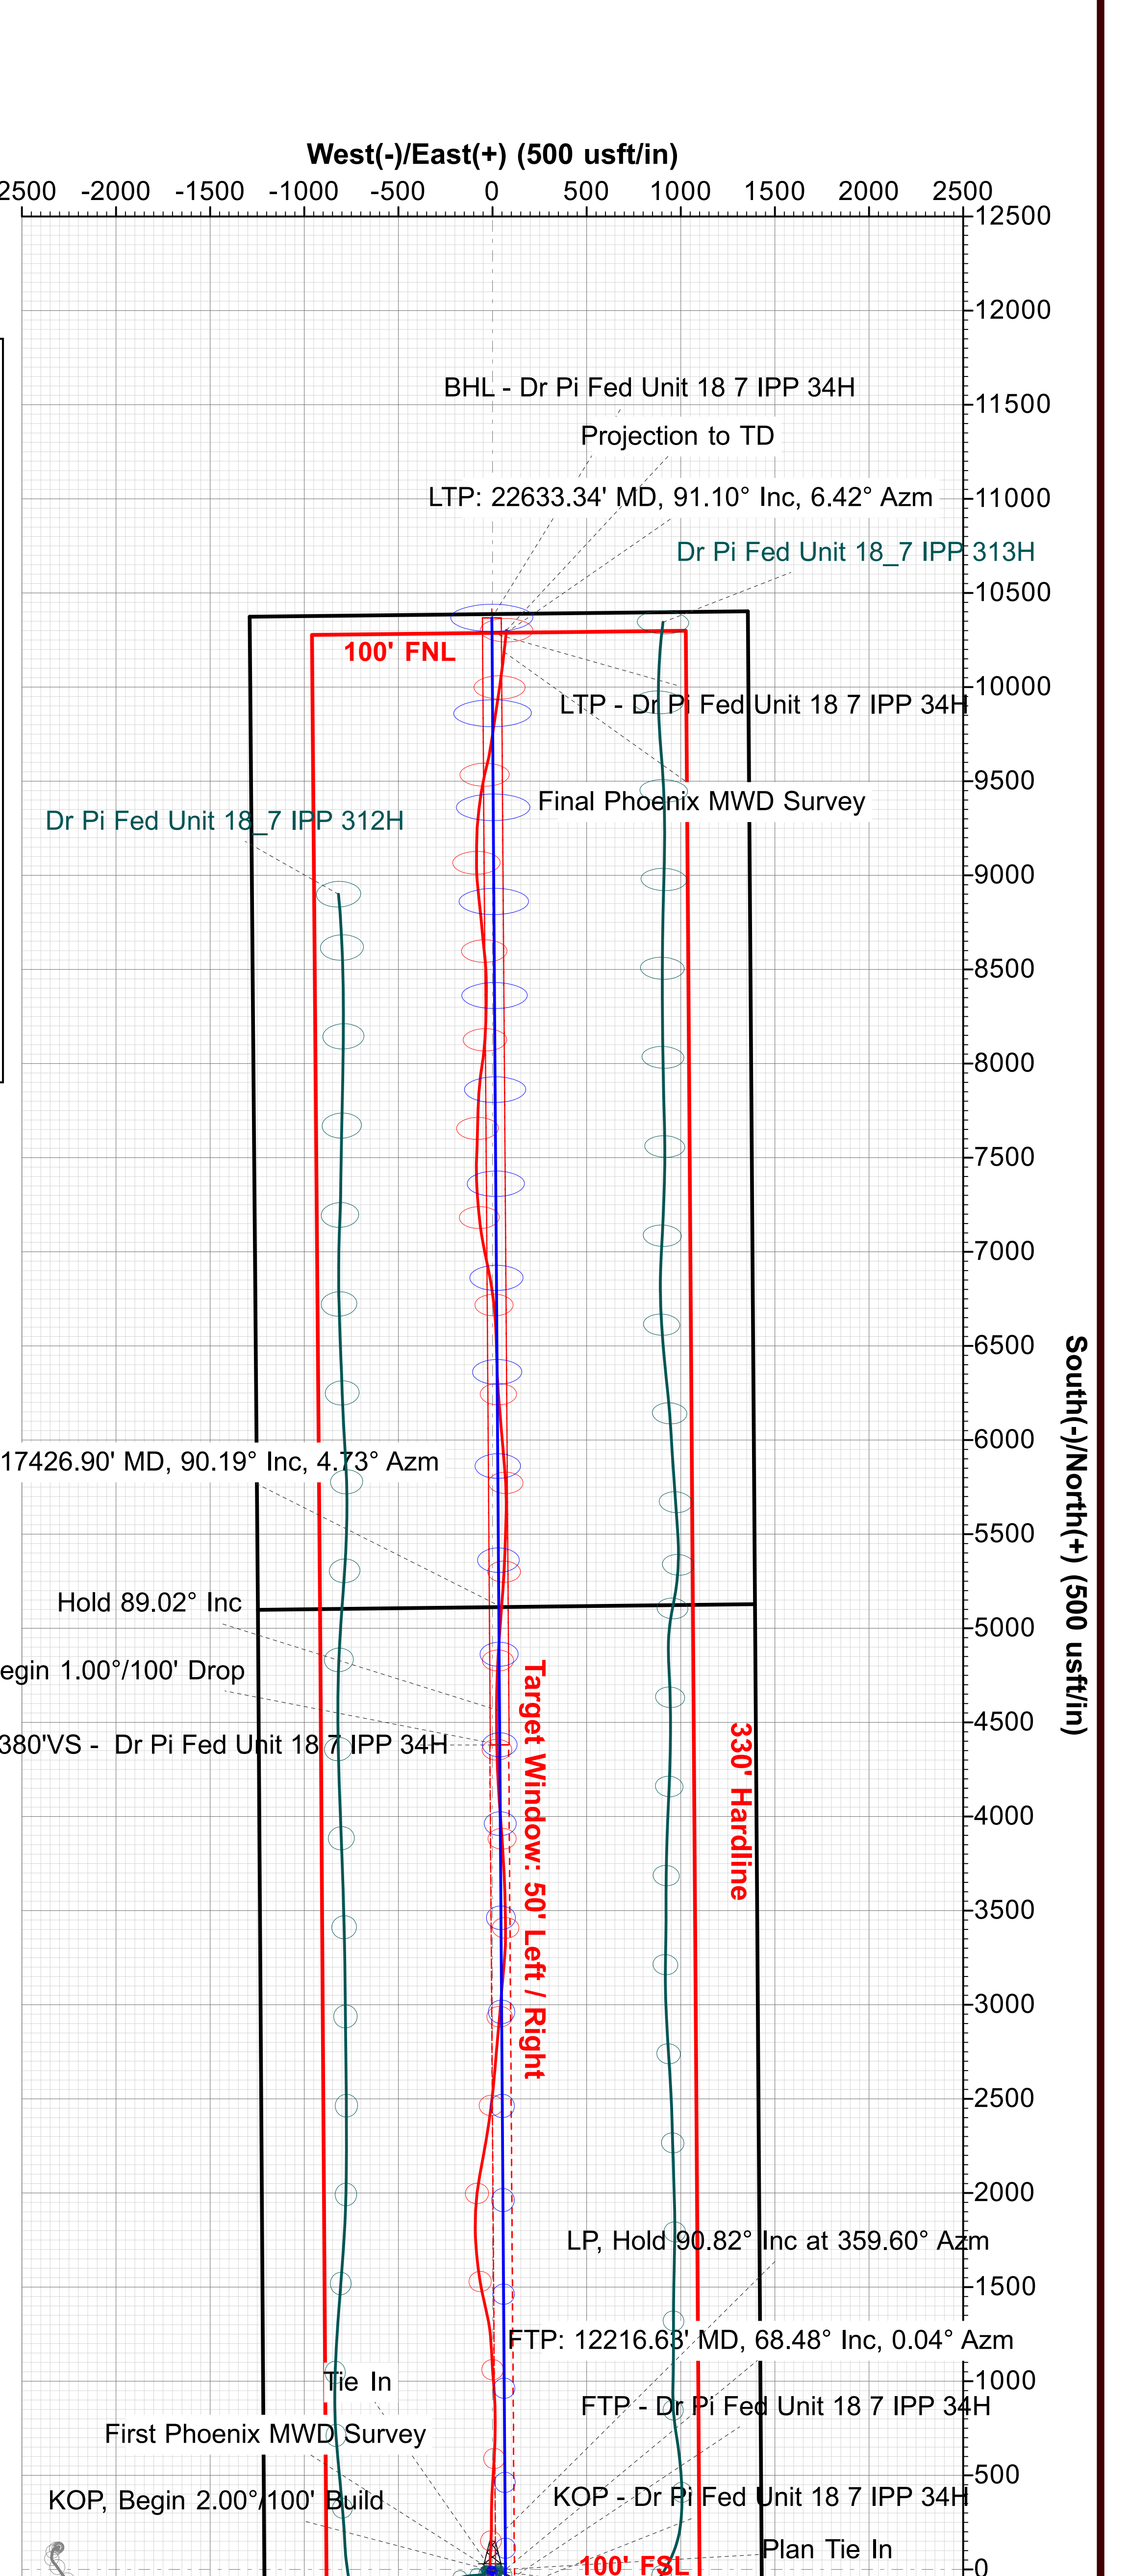



OXY USA INC.

Lea County, NM (NAD83-NME)

Dr Pi Fed Unit 18 7 IPP

Dr Pi Fed Unit 18_7 IPP 34H

OH / 69896

Design: Surveys (H&P 466)

Standard Survey Report

04 August, 2022



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Project	Lea County, NM (NAD83-NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Dr Pi Fed Unit 18 7 IPP		
Site Position:		Northing:	504,270.47 usft
From:	Map	Easting:	733,762.25 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 23' 5.161892 N
		Longitude:	103° 42' 35.900893 W
		Grid Convergence:	0.334 °

Well	Dr Pi Fed Unit 18_7 IPP 34H		
Well Position	+N/-S	0.00 usft	Northing: 504,270.47 usft
	+E/-W	0.00 usft	Easting: 733,762.25 usft
Position Uncertainty	1.00 usft	Wellhead Elevation:	usft
		Latitude:	32° 23' 5.161892 N
		Longitude:	103° 42' 35.900893 W
		Ground Level:	3,663.60 usft

Wellbore	OH / 69896		
Magnetics	Model Name	Sample Date	Declination (°)
	IFR	7/11/2022	6.720
			Dip Angle (°) 60.146
			Field Strength (nT) 47,837.90000000

Design	Surveys (H&P 466)		
Audit Notes:			
Version:	1.0	Phase:	ACTUAL
		Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)
	0.00	0.00	0.00
			Direction (°) 359.98

Survey Program	Date	8/4/2022		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
25.00	936.09	Gyrodata Gyro Surveys (OH / 69896)	GYD_G003_GC+DROP+	Gyrodata Stationary Tool drop on BHA on open h
1,003.00	22,647.00	Phoenix MWD Surveys - SQC R6 (OH / 69	SQC_C705a_MWD+IFR1	OWSG MWD + IFR1 + Sag + FDIR Correction

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25.00	0.00	0.00	25.00	0.00	0.00	0.00	0.00	0.00	0.00
97.25	0.11	163.00	97.25	-0.07	0.02	-0.07	0.15	0.15	0.00
191.52	0.24	135.30	191.52	-0.29	0.19	-0.29	0.16	0.14	-29.38
279.07	0.35	122.90	279.07	-0.57	0.54	-0.57	0.14	0.13	-14.16
373.35	0.06	359.94	373.35	-0.68	0.78	-0.68	0.41	-0.31	-130.42
467.48	0.30	246.02	467.48	-0.73	0.56	-0.73	0.35	0.25	-121.02
561.75	0.58	221.19	561.74	-1.19	0.02	-1.19	0.35	0.30	-26.34
656.10	0.45	220.22	656.09	-1.83	-0.54	-1.83	0.14	-0.14	-1.03
750.00	0.76	251.15	749.99	-2.31	-1.37	-2.31	0.47	0.33	32.94



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
844.98	0.70	225.33	844.96	-2.92	-2.37	-2.92	0.35	-0.06	-27.18
936.09	0.82	212.48	936.06	-3.86	-3.12	-3.86	0.23	0.13	-14.10
Tie In									
1,003.00	1.04	189.70	1,002.96	-4.87	-3.48	-4.87	0.64	0.33	-34.05
First Phoenix MWD Survey									
1,097.00	1.39	181.38	1,096.94	-6.85	-3.65	-6.85	0.42	0.37	-8.85
1,192.00	1.43	180.70	1,191.91	-9.18	-3.69	-9.18	0.05	0.04	-0.72
1,286.00	1.34	174.70	1,285.88	-11.45	-3.61	-11.45	0.18	-0.10	-6.38
1,380.00	1.28	172.71	1,379.86	-13.59	-3.37	-13.59	0.08	-0.06	-2.12
1,475.00	1.14	174.22	1,474.84	-15.58	-3.14	-15.58	0.15	-0.15	1.59
1,569.00	1.03	181.02	1,568.82	-17.35	-3.06	-17.35	0.18	-0.12	7.23
1,664.00	1.11	178.86	1,663.81	-19.13	-3.06	-19.13	0.09	0.08	-2.27
1,758.00	1.11	181.25	1,757.79	-20.95	-3.06	-20.95	0.05	0.00	2.54
1,853.00	1.04	181.15	1,852.77	-22.73	-3.10	-22.73	0.07	-0.07	-0.11
1,948.00	1.11	174.44	1,947.75	-24.51	-3.03	-24.51	0.15	0.07	-7.06
2,042.00	1.15	171.35	2,041.74	-26.35	-2.80	-26.35	0.08	0.04	-3.29
2,137.00	1.22	167.06	2,136.72	-28.28	-2.43	-28.28	0.12	0.07	-4.52
2,232.00	1.25	167.26	2,231.69	-30.27	-1.97	-30.27	0.03	0.03	0.21
2,327.00	1.39	168.76	2,326.67	-32.41	-1.52	-32.41	0.15	0.15	1.58
2,421.00	1.40	166.20	2,420.64	-34.65	-1.02	-34.65	0.07	0.01	-2.72
2,516.00	1.40	165.22	2,515.61	-36.90	-0.45	-36.90	0.03	0.00	-1.03
2,611.00	1.31	161.93	2,610.59	-39.05	0.18	-39.05	0.13	-0.09	-3.46
2,705.00	1.12	154.41	2,704.56	-40.90	0.91	-40.90	0.26	-0.20	-8.00
2,800.00	1.15	146.50	2,799.55	-42.53	1.84	-42.53	0.17	0.03	-8.33
2,895.00	1.11	130.79	2,894.53	-43.93	3.06	-43.93	0.33	-0.04	-16.54
3,085.00	1.15	100.72	3,084.49	-45.49	6.33	-45.49	0.31	0.02	-15.83
3,179.00	1.01	73.26	3,178.48	-45.42	8.05	-45.42	0.56	-0.15	-29.21
3,369.00	0.72	83.23	3,368.45	-44.80	10.84	-44.80	0.17	-0.15	5.25
3,463.00	0.57	91.04	3,462.45	-44.74	11.89	-44.74	0.18	-0.16	8.31
3,653.00	2.07	98.80	3,652.39	-45.28	16.23	-45.29	0.79	0.79	4.08
3,747.00	3.00	107.28	3,746.30	-46.27	20.26	-46.28	1.06	0.99	9.02
3,842.00	3.63	107.49	3,841.14	-47.91	25.50	-47.92	0.66	0.66	0.22
3,936.00	1.46	108.81	3,935.04	-49.19	29.47	-49.20	2.31	-2.31	1.40
4,031.00	0.65	122.24	4,030.03	-49.87	31.07	-49.88	0.89	-0.85	14.14
4,126.00	1.45	121.56	4,125.01	-50.79	32.55	-50.80	0.84	0.84	-0.72
4,220.00	2.31	118.61	4,218.96	-52.32	35.23	-52.33	0.92	0.91	-3.14
4,315.00	2.18	117.03	4,313.88	-54.06	38.52	-54.07	0.15	-0.14	-1.66
4,410.00	1.06	116.69	4,408.84	-55.27	40.91	-55.28	1.18	-1.18	-0.36
4,504.00	0.21	24.45	4,502.84	-55.51	41.76	-55.52	1.16	-0.90	-98.13
4,599.00	0.52	335.95	4,597.84	-54.95	41.66	-54.97	0.43	0.33	-51.05
4,693.00	0.33	322.11	4,691.83	-54.35	41.32	-54.36	0.23	-0.20	-14.72
4,788.00	0.38	324.25	4,786.83	-53.88	40.97	-53.89	0.05	0.05	2.25
4,883.00	0.58	316.24	4,881.83	-53.28	40.45	-53.29	0.22	0.21	-8.43



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,977.00	1.00	308.09	4,975.82	-52.43	39.48	-52.44	0.46	0.45	-8.67
5,072.00	1.01	308.07	5,070.81	-51.40	38.16	-51.41	0.01	0.01	-0.02
5,167.00	0.92	305.86	5,165.79	-50.43	36.89	-50.45	0.10	-0.09	-2.33
5,261.00	0.93	301.39	5,259.78	-49.60	35.62	-49.61	0.08	0.01	-4.76
5,356.00	1.04	298.25	5,354.77	-48.79	34.21	-48.80	0.13	0.12	-3.31
5,451.00	0.96	289.91	5,449.75	-48.11	32.70	-48.12	0.17	-0.08	-8.78
5,545.00	0.94	282.76	5,543.74	-47.67	31.21	-47.68	0.13	-0.02	-7.61
5,640.00	1.02	290.27	5,638.72	-47.20	29.65	-47.21	0.16	0.08	7.91
5,735.00	1.10	292.49	5,733.71	-46.56	28.02	-46.57	0.09	0.08	2.34
5,829.00	1.06	292.71	5,827.69	-45.88	26.38	-45.89	0.04	-0.04	0.23
5,924.00	1.03	293.19	5,922.68	-45.21	24.79	-45.21	0.03	-0.03	0.51
6,019.00	1.13	296.43	6,017.66	-44.45	23.16	-44.46	0.12	0.11	3.41
6,113.00	1.23	298.63	6,111.64	-43.56	21.45	-43.56	0.12	0.11	2.34
6,208.00	1.23	296.08	6,206.62	-42.62	19.64	-42.63	0.06	0.00	-2.68
6,303.00	0.69	255.96	6,301.60	-42.31	18.16	-42.32	0.87	-0.57	-42.23
6,398.00	1.82	203.00	6,396.58	-43.84	17.02	-43.84	1.59	1.19	-55.75
6,493.00	3.07	194.03	6,491.49	-47.69	15.81	-47.70	1.37	1.32	-9.44
6,587.00	4.38	196.08	6,585.29	-53.59	14.21	-53.59	1.40	1.39	2.18
6,682.00	5.31	197.38	6,679.95	-61.27	11.89	-61.27	0.99	0.98	1.37
6,777.00	5.97	189.49	6,774.49	-70.33	9.76	-70.34	1.07	0.69	-8.31
6,871.00	5.52	188.25	6,868.02	-79.63	8.31	-79.63	0.50	-0.48	-1.32
6,966.00	5.43	187.99	6,962.59	-88.60	7.03	-88.61	0.10	-0.09	-0.27
7,061.00	5.42	186.86	7,057.16	-97.51	5.87	-97.51	0.11	-0.01	-1.19
7,155.00	7.02	184.07	7,150.61	-107.65	4.93	-107.65	1.73	1.70	-2.97
7,250.00	8.47	180.21	7,244.74	-120.43	4.49	-120.44	1.62	1.53	-4.06
7,345.00	10.42	175.66	7,338.45	-136.00	5.12	-136.00	2.20	2.05	-4.79
7,439.00	10.89	175.82	7,430.83	-153.33	6.41	-153.33	0.50	0.50	0.17
7,534.00	10.63	174.38	7,524.16	-171.00	7.92	-171.00	0.39	-0.27	-1.52
7,628.00	10.11	173.12	7,616.62	-187.82	9.76	-187.82	0.60	-0.55	-1.34
7,723.00	9.52	172.02	7,710.23	-203.88	11.85	-203.88	0.65	-0.62	-1.16
7,818.00	9.52	171.37	7,803.92	-219.43	14.12	-219.43	0.11	0.00	-0.68
7,913.00	9.13	170.64	7,897.67	-234.63	16.52	-234.64	0.43	-0.41	-0.77
8,007.00	8.89	170.64	7,990.51	-249.16	18.91	-249.16	0.26	-0.26	0.00
8,102.00	8.89	170.90	8,084.37	-263.65	21.27	-263.65	0.04	0.00	0.27
8,197.00	8.72	171.05	8,178.25	-278.01	23.55	-278.01	0.18	-0.18	0.16
8,292.00	8.53	171.74	8,272.17	-292.09	25.68	-292.10	0.23	-0.20	0.73
8,386.00	7.95	171.17	8,365.20	-305.42	27.68	-305.42	0.62	-0.62	-0.61
8,481.00	7.25	169.32	8,459.37	-317.80	29.80	-317.81	0.78	-0.74	-1.95
8,576.00	6.94	169.34	8,553.64	-329.33	31.97	-329.34	0.33	-0.33	0.02
8,671.00	6.37	169.85	8,648.00	-340.16	33.97	-340.17	0.60	-0.60	0.54
8,765.00	5.88	170.01	8,741.46	-350.03	35.72	-350.04	0.52	-0.52	0.17
8,860.00	4.65	171.95	8,836.06	-358.64	37.10	-358.65	1.31	-1.29	2.04
8,955.00	3.62	168.47	8,930.81	-365.39	38.24	-365.40	1.12	-1.08	-3.66
9,049.00	3.45	172.07	9,024.63	-371.10	39.23	-371.11	0.30	-0.18	3.83



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,144.00	3.20	175.02	9,119.47	-376.57	39.85	-376.58	0.32	-0.26	3.11
9,239.00	3.44	175.36	9,214.31	-382.05	40.31	-382.07	0.25	0.25	0.36
9,334.00	3.03	174.25	9,309.16	-387.39	40.79	-387.41	0.44	-0.43	-1.17
9,428.00	3.07	179.14	9,403.03	-392.38	41.08	-392.39	0.28	0.04	5.20
9,523.00	2.43	175.62	9,497.92	-396.93	41.27	-396.95	0.70	-0.67	-3.71
9,618.00	2.30	180.02	9,592.84	-400.85	41.42	-400.86	0.23	-0.14	4.63
9,712.00	2.47	179.95	9,686.75	-404.76	41.43	-404.77	0.18	0.18	-0.07
9,807.00	2.63	185.77	9,781.66	-408.98	41.21	-408.99	0.32	0.17	6.13
9,902.00	2.35	186.40	9,876.57	-413.08	40.77	-413.09	0.30	-0.29	0.66
9,996.00	1.74	187.56	9,970.51	-416.41	40.37	-416.42	0.65	-0.65	1.23
10,091.00	0.91	195.09	10,065.48	-418.57	39.98	-418.58	0.89	-0.87	7.93
10,186.00	0.93	181.44	10,160.47	-420.07	39.77	-420.08	0.23	0.02	-14.37
10,280.00	0.96	175.60	10,254.46	-421.61	39.81	-421.63	0.11	0.03	-6.21
10,375.00	1.00	203.37	10,349.45	-423.17	39.54	-423.18	0.50	0.04	29.23
10,470.00	0.57	193.43	10,444.44	-424.39	39.10	-424.40	0.47	-0.45	-10.46
10,565.00	0.54	186.06	10,539.43	-425.29	38.95	-425.31	0.08	-0.03	-7.76
10,659.00	0.39	187.90	10,633.43	-426.05	38.85	-426.06	0.16	-0.16	1.96
10,714.00	0.34	175.92	10,688.43	-426.40	38.84	-426.41	0.17	-0.09	-21.78
10,831.00	0.63	45.74	10,805.43	-426.30	39.33	-426.31	0.76	0.25	-111.26
10,926.00	0.29	168.96	10,900.42	-426.17	39.75	-426.18	0.87	-0.36	129.71
11,021.00	0.06	310.78	10,995.42	-426.37	39.75	-426.38	0.36	-0.24	149.28
11,115.00	0.70	299.52	11,089.42	-426.06	39.22	-426.07	0.68	0.68	-11.98
11,210.00	0.59	252.87	11,184.42	-425.92	38.24	-425.93	0.55	-0.12	-49.11
11,305.00	0.90	305.85	11,279.41	-425.62	37.17	-425.63	0.76	0.33	55.77
11,400.00	2.00	293.44	11,374.38	-424.53	35.05	-424.54	1.20	1.16	-13.06
11,494.00	2.85	272.78	11,468.29	-423.76	31.21	-423.77	1.28	0.90	-21.98
11,589.00	7.41	338.28	11,562.95	-417.95	26.58	-417.96	7.10	4.80	68.95
11,683.00	17.42	343.41	11,654.64	-398.78	20.30	-398.79	10.70	10.65	5.46
11,778.00	27.07	344.17	11,742.46	-364.28	10.32	-364.28	10.16	10.16	0.80
11,873.00	32.23	350.87	11,825.02	-318.42	0.39	-318.42	6.45	5.43	7.05
11,968.00	37.40	354.00	11,902.99	-264.68	-6.65	-264.68	5.76	5.44	3.29
12,063.00	48.35	358.90	11,972.53	-200.29	-10.36	-200.28	12.04	11.53	5.16
12,101.86	53.45	357.83	11,997.02	-170.15	-11.23	-170.15	13.31	13.13	-2.77
SL: 12101.86' MD, 53.45° Inc, 357.83° Azm									
12,157.00	60.71	356.52	12,026.97	-123.95	-13.53	-123.95	13.31	13.16	-2.37
12,216.63	68.48	0.04	12,052.54	-70.17	-15.10	-70.16	14.08	13.04	5.90
FTP: 12216.63' MD, 68.48° Inc, 0.04° Azm									
12,252.00	73.13	1.94	12,064.16	-36.78	-14.51	-36.77	14.08	13.13	5.38
12,347.00	86.78	1.22	12,080.69	56.51	-11.95	56.51	14.39	14.37	-0.76
12,442.00	90.71	3.78	12,082.77	151.37	-7.81	151.37	4.94	4.14	2.69
12,502.00	90.25	0.71	12,082.27	211.31	-5.46	211.32	5.17	-0.77	-5.12
12,597.00	89.97	359.50	12,082.09	306.31	-5.28	306.31	1.31	-0.29	-1.27
12,691.00	93.61	3.68	12,079.15	400.19	-2.68	400.19	5.89	3.87	4.45

Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
12,786.00	93.37	3.69	12,073.37	494.82	3.41	494.82	0.25	-0.25	0.01
12,881.00	92.79	3.26	12,068.27	589.51	9.16	589.51	0.76	-0.61	-0.45
12,976.00	92.91	1.46	12,063.54	684.31	13.07	684.30	1.90	0.13	-1.89
13,070.00	92.37	0.50	12,059.21	778.19	14.68	778.19	1.17	-0.57	-1.02
13,165.00	92.29	357.93	12,055.35	873.10	13.38	873.09	2.70	-0.08	-2.71
13,260.00	91.81	355.10	12,051.95	967.85	7.60	967.85	3.02	-0.51	-2.98
13,354.00	91.22	356.19	12,049.46	1,061.54	0.47	1,061.54	1.32	-0.63	1.16
13,449.00	90.07	357.39	12,048.39	1,156.39	-4.85	1,156.39	1.75	-1.21	1.26
13,544.00	91.05	354.36	12,047.47	1,251.12	-11.68	1,251.13	3.35	1.03	-3.19
13,639.00	89.90	347.37	12,046.68	1,344.86	-26.75	1,344.86	7.46	-1.21	-7.36
13,733.00	88.53	347.36	12,047.97	1,436.57	-47.31	1,436.58	1.46	-1.46	-0.01
13,828.00	89.52	350.67	12,049.58	1,529.80	-65.41	1,529.82	3.64	1.04	3.48
13,923.00	88.96	353.40	12,050.84	1,623.87	-78.57	1,623.89	2.93	-0.59	2.87
14,017.00	85.03	355.76	12,055.77	1,717.29	-87.44	1,717.32	4.87	-4.18	2.51
14,110.00	83.42	359.74	12,065.13	1,809.73	-91.08	1,809.75	4.60	-1.73	4.28
14,205.00	84.34	2.17	12,075.26	1,904.16	-89.50	1,904.19	2.72	0.97	2.56
14,299.00	87.31	6.81	12,082.11	1,997.59	-82.16	1,997.61	5.85	3.16	4.94
14,394.00	91.52	10.79	12,083.08	2,091.43	-67.63	2,091.45	6.10	4.43	4.19
14,488.00	90.64	9.94	12,081.31	2,183.87	-50.72	2,183.89	1.30	-0.94	-0.90
14,583.00	91.56	9.80	12,079.48	2,277.45	-34.44	2,277.46	0.98	0.97	-0.15
14,678.00	91.73	8.56	12,076.75	2,371.19	-19.29	2,371.20	1.32	0.18	-1.31
14,773.00	92.39	7.15	12,073.34	2,465.24	-6.31	2,465.24	1.64	0.69	-1.48
14,868.00	91.45	5.33	12,070.16	2,559.62	4.00	2,559.61	2.16	-0.99	-1.92
14,962.00	92.22	5.17	12,067.15	2,653.17	12.60	2,653.17	0.84	0.82	-0.17
15,057.00	92.08	4.73	12,063.58	2,747.75	20.79	2,747.75	0.49	-0.15	-0.46
15,152.00	92.33	5.37	12,059.93	2,842.31	29.15	2,842.30	0.72	0.26	0.67
15,247.00	91.79	5.26	12,056.51	2,936.84	37.94	2,936.83	0.58	-0.57	-0.12
15,342.00	90.64	4.06	12,054.50	3,031.50	45.66	3,031.49	1.75	-1.21	-1.26
15,436.00	91.00	5.74	12,053.15	3,125.15	53.69	3,125.13	1.83	0.38	1.79
15,531.00	91.88	4.87	12,050.77	3,219.71	62.47	3,219.69	1.30	0.93	-0.92
15,626.00	90.63	2.43	12,048.68	3,314.48	68.51	3,314.46	2.89	-1.32	-2.57
15,720.00	89.59	358.85	12,048.50	3,408.46	69.56	3,408.44	3.97	-1.11	-3.81
15,815.00	91.14	358.83	12,047.90	3,503.44	67.64	3,503.42	1.63	1.63	-0.02
15,910.00	91.51	358.73	12,045.70	3,598.39	65.62	3,598.37	0.40	0.39	-0.11
16,004.00	91.02	356.96	12,043.63	3,692.30	62.08	3,692.28	1.95	-0.52	-1.88
16,099.00	90.83	356.81	12,042.09	3,787.14	56.92	3,787.13	0.25	-0.20	-0.16
16,194.00	91.03	356.25	12,040.55	3,881.96	51.17	3,881.94	0.63	0.21	-0.59
16,289.00	90.53	355.40	12,039.26	3,976.69	44.26	3,976.68	1.04	-0.53	-0.89
16,384.00	90.13	356.36	12,038.71	4,071.45	37.43	4,071.43	1.09	-0.42	1.01
16,478.00	90.39	356.25	12,038.28	4,165.25	31.37	4,165.24	0.30	0.28	-0.12
16,573.00	90.53	357.82	12,037.52	4,260.12	26.46	4,260.11	1.66	0.15	1.65
16,668.00	90.97	358.75	12,036.28	4,355.06	23.62	4,355.06	1.08	0.46	0.98
16,762.00	90.57	359.65	12,035.01	4,449.05	22.31	4,449.04	1.05	-0.43	0.96
16,857.00	89.74	359.78	12,034.76	4,544.04	21.83	4,544.04	0.88	-0.87	0.14



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
16,952.00	89.59	0.98	12,035.31	4,639.04	22.46	4,639.03	1.27	-0.16	1.26
17,047.00	88.63	2.05	12,036.79	4,733.99	24.97	4,733.98	1.51	-1.01	1.13
17,142.00	90.31	3.17	12,037.67	4,828.88	29.30	4,828.87	2.13	1.77	1.18
17,237.00	90.18	3.58	12,037.26	4,923.72	34.89	4,923.71	0.45	-0.14	0.43
17,331.00	89.55	3.98	12,037.48	5,017.51	41.09	5,017.50	0.79	-0.67	0.43
17,426.00	90.20	4.73	12,037.69	5,112.24	48.30	5,112.22	1.04	0.68	0.79
17,426.90	90.19	4.73	12,037.69	5,113.13	48.38	5,113.12	1.23	-1.13	-0.51
SL: 17426.90' MD, 90.19° Inc, 4.73° Azm									
17,521.00	89.13	4.25	12,038.25	5,206.94	55.74	5,206.92	1.23	-1.13	-0.51
17,615.00	89.78	2.83	12,039.14	5,300.76	61.54	5,300.74	1.66	0.69	-1.51
17,710.00	92.32	2.14	12,037.40	5,395.64	65.66	5,395.62	2.77	2.67	-0.73
17,804.00	93.39	2.23	12,032.72	5,489.46	69.24	5,489.43	1.14	1.14	0.10
17,899.00	94.11	1.43	12,026.50	5,584.20	72.27	5,584.18	1.13	0.76	-0.84
17,993.00	93.62	359.87	12,020.17	5,677.98	73.33	5,677.96	1.74	-0.52	-1.66
18,088.00	91.28	356.62	12,016.11	5,772.83	70.42	5,772.81	4.21	-2.46	-3.42
18,183.00	90.88	355.00	12,014.31	5,867.55	63.48	5,867.53	1.76	-0.42	-1.71
18,277.00	90.70	355.24	12,013.02	5,961.20	55.49	5,961.19	0.32	-0.19	0.26
18,372.00	90.25	354.98	12,012.23	6,055.86	47.39	6,055.84	0.55	-0.47	-0.27
18,467.00	90.51	355.24	12,011.60	6,150.51	39.29	6,150.49	0.39	0.27	0.27
18,561.00	90.34	355.30	12,010.90	6,244.18	31.54	6,244.17	0.19	-0.18	0.06
18,656.00	90.01	357.57	12,010.61	6,338.99	25.63	6,338.99	2.41	-0.35	2.39
18,751.00	90.17	358.79	12,010.46	6,433.94	22.62	6,433.94	1.30	0.17	1.28
18,846.00	90.50	358.50	12,009.91	6,528.92	20.37	6,528.91	0.46	0.35	-0.31
18,940.00	90.56	356.59	12,009.04	6,622.82	16.35	6,622.82	2.03	0.06	-2.03
19,035.00	91.72	353.79	12,007.15	6,717.46	8.38	6,717.45	3.19	1.22	-2.95
19,129.00	91.61	350.86	12,004.42	6,810.56	-4.17	6,810.57	3.12	-0.12	-3.12
19,224.00	89.13	348.24	12,003.80	6,903.97	-21.39	6,903.98	3.80	-2.61	-2.76
19,319.00	87.81	348.65	12,006.34	6,997.01	-40.42	6,997.02	1.45	-1.39	0.43
19,414.00	81.98	350.48	12,014.79	7,090.02	-57.55	7,090.04	6.43	-6.14	1.93
19,508.00	81.60	354.37	12,028.22	7,182.23	-69.82	7,182.25	4.12	-0.40	4.14
19,603.00	85.66	355.48	12,038.76	7,276.25	-78.16	7,276.28	4.43	4.27	1.17
19,698.00	86.44	356.96	12,045.30	7,370.82	-84.41	7,370.84	1.76	0.82	1.56
19,793.00	91.56	2.17	12,046.96	7,465.74	-85.13	7,465.76	7.69	5.39	5.48
19,888.00	89.46	1.81	12,046.11	7,560.67	-81.83	7,560.69	2.24	-2.21	-0.38
19,983.00	89.26	1.09	12,047.18	7,655.63	-79.42	7,655.66	0.79	-0.21	-0.76
20,078.00	90.51	2.31	12,047.37	7,750.59	-76.61	7,750.61	1.84	1.32	1.28
20,172.00	90.80	2.88	12,046.29	7,844.48	-72.35	7,844.50	0.68	0.31	0.61
20,267.00	91.78	8.80	12,044.15	7,938.92	-62.69	7,938.94	6.31	1.03	6.23
20,361.00	90.35	7.74	12,042.40	8,031.93	-49.17	8,031.94	1.89	-1.52	-1.13
20,456.00	89.81	3.63	12,042.27	8,126.44	-39.77	8,126.45	4.36	-0.57	-4.33
20,550.00	90.60	2.17	12,041.93	8,220.31	-35.01	8,220.32	1.77	0.84	-1.55
20,645.00	89.97	0.67	12,041.46	8,315.28	-32.66	8,315.29	1.71	-0.66	-1.58
20,739.00	90.08	359.78	12,041.42	8,409.28	-32.29	8,409.29	0.95	0.12	-0.95



Phoenix Survey Report



Company:	OXY USA INC.	Local Co-ordinate Reference:	Well Dr Pi Fed Unit 18_7 IPP 34H
Project:	Lea County, NM (NAD83-NME)	TVD Reference:	RKB @ 3688.60usft (H&P 466)
Site:	Dr Pi Fed Unit 18 7 IPP	MD Reference:	RKB @ 3688.60usft (H&P 466)
Well:	Dr Pi Fed Unit 18_7 IPP 34H	North Reference:	Grid
Wellbore:	OH / 69896	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (H&P 466)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
20,834.00	89.95	356.44	12,041.40	8,504.21	-35.42	8,504.22	3.52	-0.14	-3.52
20,928.00	89.68	353.45	12,041.70	8,597.84	-43.70	8,597.85	3.19	-0.29	-3.18
21,022.00	90.07	354.93	12,041.90	8,691.35	-53.22	8,691.37	1.63	0.41	1.57
21,116.00	90.48	353.98	12,041.45	8,784.91	-62.30	8,784.93	1.10	0.44	-1.01
21,210.00	89.85	353.90	12,041.18	8,878.38	-72.22	8,878.40	0.68	-0.67	-0.09
21,304.00	89.86	355.05	12,041.42	8,971.94	-81.27	8,971.97	1.22	0.01	1.22
21,399.00	92.51	0.68	12,039.45	9,066.81	-84.81	9,066.84	6.55	2.79	5.93
21,493.00	88.54	0.20	12,038.59	9,160.78	-84.09	9,160.81	4.25	-4.22	-0.51
21,587.00	89.59	3.40	12,040.13	9,254.71	-81.14	9,254.74	3.58	1.12	3.40
21,681.00	90.14	7.57	12,040.35	9,348.26	-72.15	9,348.28	4.47	0.59	4.44
21,775.00	89.16	7.69	12,040.92	9,441.43	-59.67	9,441.44	1.05	-1.04	0.13
21,870.00	90.52	14.10	12,041.19	9,534.66	-41.73	9,534.67	6.90	1.43	6.75
21,964.00	90.31	12.69	12,040.51	9,626.10	-19.95	9,626.11	1.52	-0.22	-1.50
22,058.00	90.18	7.31	12,040.11	9,718.64	-3.64	9,718.64	5.73	-0.14	-5.72
22,152.00	91.22	8.95	12,038.96	9,811.68	9.66	9,811.68	2.07	1.11	1.74
22,246.00	90.77	8.81	12,037.33	9,904.54	24.16	9,904.53	0.50	-0.48	-0.15
22,341.00	90.04	7.77	12,036.65	9,998.54	37.86	9,998.53	1.34	-0.77	-1.09
22,436.00	89.46	7.47	12,037.07	10,092.70	50.46	10,092.69	0.69	-0.61	-0.32
22,531.00	91.10	6.42	12,036.60	10,187.00	61.94	10,186.98	2.05	1.73	-1.11
Final Phoenix MWD Survey									
22,633.34	91.10	6.42	12,034.64	10,288.68	73.39	10,288.66	0.00	0.00	0.00
LTP: 22633.34' MD, 91.10° Inc, 6.42° Azm									
22,647.00	91.10	6.42	12,034.38	10,302.25	74.91	10,302.23	0.00	0.00	0.00
Projection to TD									

Checked By: _____ Approved By: _____ Date: _____

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 142182

ACKNOWLEDGMENTS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 142182
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 142182

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 142182
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	RT EXPIRES 12/12/2022.	12/7/2022
