


TIME	P S I @ 1745 FEET	TIME	P S I @ 1745 FEET
10:25 A.M.	660 GAUGE REACHED 1745'	1:00 P.M.	513 OPEN CHOKE 32/64
10:50 A.M.	660 OPEN CHOKE 12/64	1:15	448
11:00	627	1:30	440
11:15	624	1:45 P.M.	437 END 4TH RATE
11:30 A.M.	621 END 1ST RATE	2:10 P.M.	WELL SHUT-IN
11:30 A.M.	621 OPEN CHOKE 18/64		636 GAUGE OUT, END TEST
11:45 A.M.	578		
12:00 NOON	575	TEST DATE:	DECEMBER 28, 1972
12:15 P.M.	572 END 2ND RATE	TEST DEPTH:	1745 FEET
12:15 P.M.	572 OPEN CHOKE 24/64	ELEMENT NO.:	18948-N
12:30	522	RANGE:	0-3700 P S I
12:45	516	CLOCK NO.:	11782
1:00 P.M.	513 END 3RD RATE	RANGE:	0-24 HOUR

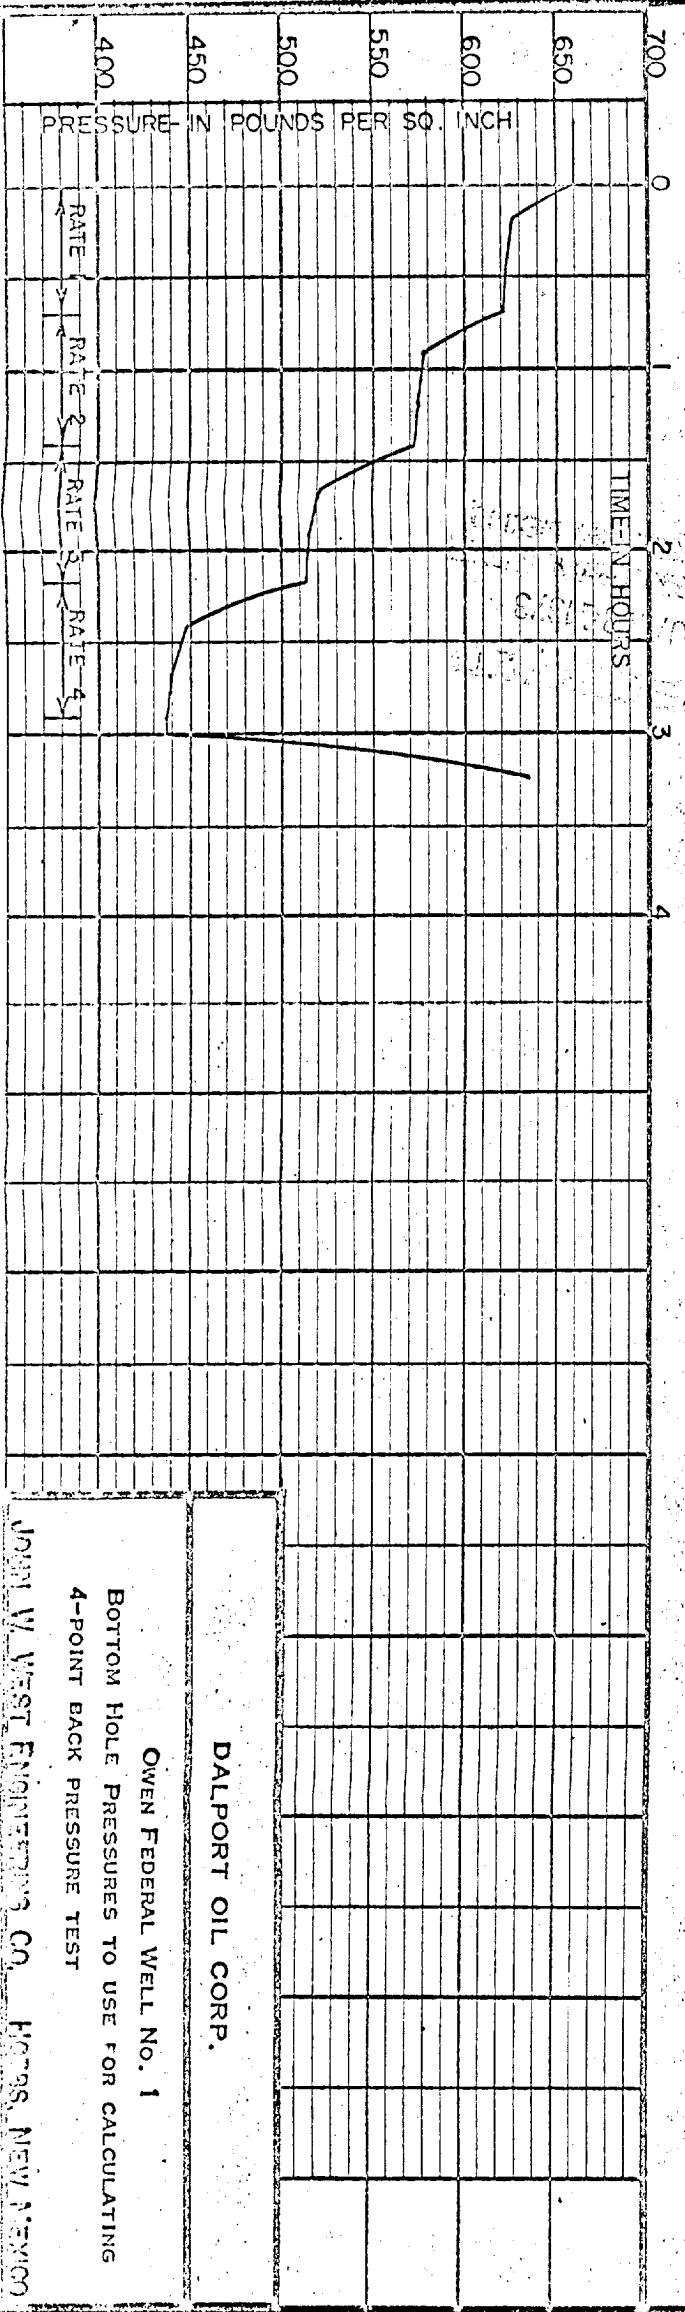

DALPORT OIL CORP.

OWEN FEDERAL WELL No. 1

BOTTOM HOLE PRESSURES TO USE FOR CALCULATING
4-POINT BACK PRESSURE TEST

JOHN V. WEST ENGINEERING CO. HOUSTON, NEW MEXICO
 Date: 1-15-73 Drawn by: M.C.T. Scale: AS SHOWN
