

OCD - HOBBS  
10/02/2020  
RECEIVED

FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No.
1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		7. If Unit or CA Agreement, Name and No.
		8. Lease Name and Well No.  <b>[328302]</b>
2. Name of Operator <b>[372043]</b>		9. API Well No. <b>30-025-47832</b>
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory <b>[98098]</b>
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
		13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification.  |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM.            |

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**GCP Rec 10/02/2020**

**SL**

(Continued on page 2)

**APPROVED WITH CONDITIONS**  
**Approval Date: 09/29/2020**

**Kz**  
**10/19/2020**

\*(Instructions on page 2)

## INSTRUCTIONS

**GENERAL:** This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

**ITEM I:** If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

**ITEM 4:** Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

**ITEM 14:** Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

**ITEMS 15 AND 18:** If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

**ITEM 22:** Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

**ITEM 24:** If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

## NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48( d) provide that you be furnished the following information in connection with information required by this application.

**AUTHORITY:** 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

**PRINCIPAL PURPOSES:** The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

**ROUTINE USE:** Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

**EFFECT OF NOT PROVIDING INFORMATION:** Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

**BURDEN HOURS STATEMENT:** Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

## **Additional Operator Remarks**

### **Location of Well**

0. SHL: SWSE / 629 FSL / 2085 FEL / TWSP: 24S / RANGE: 35E / SECTION: 27 / LAT: 32.1829697 / LONG: -103.3535768 ( TVD: 0 feet, MD: 0 feet )

PPP: SWSE / 1320 FSL / 2310 FEL / TWSP: 24S / RANGE: 35E / SECTION: 34 / LAT: 32.170396 / LONG: -103.354324 ( TVD: 12267 feet, MD: 15905 feet )

PPP: NWNE / 324 FNL / 2276 FEL / TWSP: 24S / RANGE: 35E / SECTION: 34 / LAT: 32.1803603 / LONG: -103.3541941 ( TVD: 12135 feet, MD: 12250 feet )

BHL: SWNE / 2638 FSL / 2310 FEL / TWSP: 25S / RANGE: 35E / SECTION: 3 / LAT: 32.1593879 / LONG: -103.3543112 ( TVD: 12282 feet, MD: 19905 feet )

### **BLM Point of Contact**

Name: TYLER HILL

Title: LIE

Phone: (575) 234-5972

Email: tjhill@blm.gov

**Review and Appeal Rights**

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

**PECOS DISTRICT  
SURFACE USE  
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	Tap Rock Operating LLC
LEASE NO.:	NMNM138890, NMNM138895, NMNM101608
COUNTY:	Lea

**Wells:**

Well Pad 1

Mulva Fed Com 133H

Surface Hole Location: 629' FSL & 2060' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2639' FSL & 990' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 137H

Surface Hole Location: 604' FSL & 2085' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 2640' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 213H

Surface Hole Location: 629' FSL & 2085' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 2310' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 216H

Surface Hole Location: 604' FSL & 2060' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2639' FSL & 1650' FEL, Section 3, T. 25 S, R 35 E.

Well Pad 2

Man Hands Fed Com 113H

Surface Hole Location: 321' FNL & 1984' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1980' FEL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 133H

Surface Hole Location: 346' FNL & 2089' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1980' FEL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 136H

Surface Hole Location: 321' FNL & 2064' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1320' FEL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 213H

Surface Hole Location: 321' FNL & 2089' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 2310' FEL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 216H

Surface Hole Location: 346' FNL & 2064' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1650' FEL, Section 22, T. 24 S, R 35 E.

Mulva Fed Com 113H

Surface Hole Location: 346' FNL & 1984' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 2639' FSL & 1980' FEL, Section 3, T. 25 S, R 35 E.

Well Pad 3

Mulva Fed Com 114H

Surface Hole Location: 210' FSL & 661' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2640' FSL & 660' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 134H

Surface Hole Location: 235' FSL & 741' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2640' FSL & 660' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 136H

Surface Hole Location: 210' FSL & 766' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2640' FSL & 660' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 214H

Surface Hole Location: 335' FSL & 766' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2640' FSL & 660' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 218H

Surface Hole Location: 210' FSL & 741' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2640' FSL & 660' FEL, Section 3, T. 25 S, R 35 E.

Man Hands Fed Com 114H

Surface Hole Location: 235' FSL & 661' FEL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 660' FEL, Section 22, T. 24 S, R 35 E.

Well Pad 4

Man Hands Fed Com 134H

Surface Hole Location: 265' FSL & 766' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FSL & 660' FEL, Section 22, T. 25 S, R 35 E.

Man Hands Fed Com 214H

Surface Hole Location: 240' FSL & 766' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FSL & 9900' FEL, Section 22, T. 25 S, R 35 E.

Man Hands Fed Com 218H

Surface Hole Location: 265' FSL & 741' FEL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FSL & 337' FEL, Section 22, T. 25 S, R 35 E.

Well Pad 5

Mulva Fed Com 112H

Surface Hole Location: 210' FSL & 2126' FWL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 1980' FEL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 132H

Surface Hole Location: 235' FSL & 2046' FWL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 1980' FWL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 135H

Surface Hole Location: 210' FSL & 2021' FWL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 1325' FWL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 212H

Surface Hole Location: 235' FSL & 2021' FWL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 1652' FWL, Section 3, T. 25 S, R 35 E.

Mulva Fed Com 217H

Surface Hole Location: 210' FSL & 2046' FWL, Section 27, T. 24 S., R. 35 E.

Bottom Hole Location: 2638' FSL & 2310' FWL, Section 3, T. 25 S, R 35 E.

Man Hands Fed Com 112H

Surface Hole Location: 235' FSL & 2126' FWL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FSL & 1980' FWL, Section 22, T. 24 S, R 35 E.

Well Pad 6

Man Hands Fed Com 132H

Surface Hole Location: 265' FNL & 2126' FWL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1980' FWL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 137H

Surface Hole Location: 240' FNL & 2126' FWL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 2640' FWL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 212H

Surface Hole Location: 240' FNL & 2126' FWL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 1650' FWL, Section 22, T. 24 S, R 35 E.

Man Hands Fed Com 217H

Surface Hole Location: 236' FNL & 2126' FWL, Section 34, T. 24 S., R. 35 E.

Bottom Hole Location: 30' FNL & 2310' FWL, Section 22, T. 24 S, R 35 E.

**TABLE OF CONTENTS**

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
  - Watershed
  - Range
  - VRM IV
- ☐ **Construction**
  - Notification
  - Topsoil
  - Closed Loop System
  - Federal Mineral Material Pits
  - Well Pads
  - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
  - Well Structures & Facilities
  - Pipelines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

## **I. GENERAL PROVISIONS**

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

## **II. PERMIT EXPIRATION**

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

## **III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES**

Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See information below discussing NAGPRA.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."



Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

#### **IV. NOXIOUS WEEDS**

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

#### **SPECIAL REQUIREMENT(S)**

##### **Watershed:**

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The topsoil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

##### **TANK BATTERY:**

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

##### **BURIED/SURFACE LINE(S):**

When crossing ephemeral drainages the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons should be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences should be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars should be placed within the ROW to divert and dissipate surface runoff. A pipeline access road is not permitted to cross these ephemeral drainages. Traffic should be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present.

The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

**TEMPORARY USE FRESH WATER FRAC LINE(S):**

Once the temporary use exceeds the timeline of 180 days and/or with a 90 day extension status; further analysis will be required if the applicant pursues to turn the temporary ROW into a permanent ROW.

**Range:**

**Cattleguards**

Where a permanent cattlegaurd is approved, an appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

**Fence Requirement**

Where entry granted across a fence line, the fence must be braced and tied off on both sides of the passageway prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

**Livestock Watering Requirement**

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

**VRM IV:**

Above-ground structures including meter housing that are not subject to safety requirements are painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

**V. CONSTRUCTION**

**A. NOTIFICATION**

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

**B. TOPSOIL**

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim

reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

#### **C. CLOSED LOOP SYSTEM**

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

#### **D. FEDERAL MINERAL MATERIALS PIT**

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

#### **E. WELL PAD SURFACING**

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

#### **F. EXCLOSURE FENCING (CELLARS & PITS)**

##### **Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

#### **G. ON LEASE ACCESS ROADS**

##### **Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

##### **Surfacing**

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

### **Crowning**

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

### **Ditching**

Ditching shall be required on both sides of the road.


### **Turnouts**

Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

### **Drainage**

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outsloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

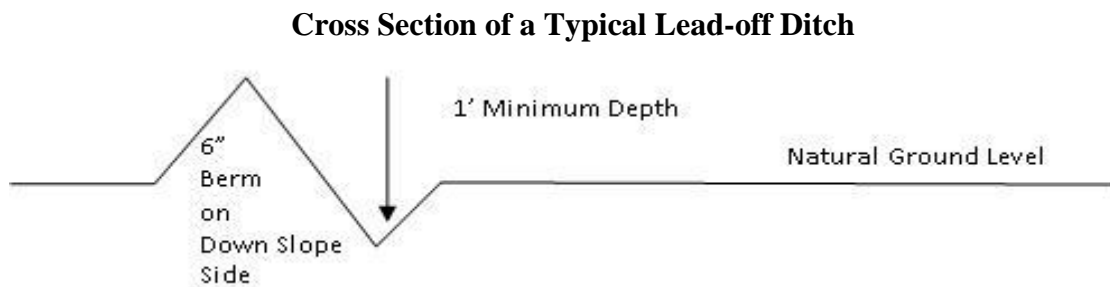

All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

### **Formula for Spacing Interval of Lead-off Ditches**

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

### **Cattle guards**

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

**Fence Requirement**

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

**Public Access**

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

### Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes



Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

## **VI. PRODUCTION (POST DRILLING)**

### **A. WELL STRUCTURES & FACILITIES**

#### **Placement of Production Facilities**

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

#### **Exclosure Netting (Open-top Tanks)**

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

#### **Chemical and Fuel Secondary Containment and Exclosure Screening**

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

#### **Open-Vent Exhaust Stack Exclosures**

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

#### **Containment Structures**

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

#### **Painting Requirement**

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

## B. PIPELINES

- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.
- Special restoration stipulations or realignment may be required at such intersections, if any.
- A leak detection plan **will be submitted to the BLM Carlsbad Field Office for approval** prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.
- All spills or leaks will be reported to the BLM immediately for their immediate and proper treatment.

### CONDITIONS OF APPROVAL FOR TEMPORARY FRESHWATER PIPELINES

Subject to the terms and conditions which are shown below, is hereby approved:

- Surface pipelines 6.5 inch to 16 inch OD may be in place for no more than 180 days not including installation. In accordance with your request, this 180 day period is requested to begin 9/22/2020.
- Surface pipeline will be in operation for no more than 180 days; a maximum of seven (7) days authorized for installation of the lay flat poly line prior to operation.
- Surface pipelines larger than 6.5 inch to-16-inch OD may be in place for no more than 180 days from date of authorization; 5/1/2018, unless a SF-299 is submitted within 30 days of this decision expiring requesting a long term buried fresh water pipeline, and processing of the SF-299 is not yet complete at the end of 30 days, in which case the line(s) may be left in place until a decision is made on the SF-299.
- All lines will be removed when no longer in use.
- Width of authorized use is 15-feet.
- No blading and/or earthwork will be allowed in order to place the pipeline except burying the line under crossings.
- The pipeline will be buried under all intersecting routes, including BLM-designated trails and access roads into caliche pits, rancher watering stations, etc. All such buried crossings will be removed when the pipeline is removed, unless otherwise approved by the Authorized Officer. Pipelines larger than 6.5-inch OD may utilize other crossing methodologies (but any fill placed over pipeline must be brought in from off-site).
- Pipeline crossings of fences should be avoided where possible. If a crossing is necessary, contact fence owner [usually the grazing permittee] prior to installation, and install by threading pipeline under the lowest wire of the fence; pipeline should never cross on top of any fence wires.



- The pipeline shall stay within 10 feet maximum of existing disturbance (e.g. lease road, pipeline right-of-way etc.); placement should be within 5 feet whenever possible.
- Placement of pumps or other high-maintenance equipment shall be installed along maintained lease roads.
- Gas or diesel pumps, generators, or compressors shall be placed on visqueen matting [or 20 mil plastic] and in a containment structure capable of containing all potentially released fuels. Containments must be protected against wildlife deaths in accordance with oilfield best management practices.
- Due to potential damage to natural resources, no work is allowed during inclement weather.
- Pipeline will be marked with your company's name and contact number, at beginning and ending points, at all public-road crossings, and at intervals not exceeding every 0.6 mile, unless otherwise approved by the Authorized Officer.
- Should unforeseen damage occur to resources, BLM will require reclamation of the impacted land.
- No water may be released into the environment without BLM consent.
- Placement of surface pipelines along or under public roadways may require permits from the road authority.
- This authorization is limited to lands under BLM jurisdiction. If your proposed pipeline crosses lands under private ownership or under other agency jurisdiction, you are responsible for obtaining all necessary permits and approvals from those parties.

#### BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C.6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.

6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.

7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:

- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
- Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
- The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)

8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.

9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the

owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- |  |  |
|--|--|
| <input type="checkbox"/> seed mixture 1            | <input type="checkbox"/> seed mixture 3          |
| <input checked="" type="checkbox"/> seed mixture 2 | <input type="checkbox"/> seed mixture 4          |
| <input type="checkbox"/> seed mixture 2/LPC        | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 17 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

17. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

18. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

19. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

20. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

#### STANDARD STIPULATIONS FOR SURFACE INSTALLED PIPELINES

**A copy of the Grant and attachments, including stipulations, survey plat(s) and/or map(s), shall be on location during construction. BLM personnel may request to review a copy of your permit during construction to ensure compliance with all stipulations.**

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, Holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC § 2601 *et seq.* (1982) with regard to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant (see 40 CFR, Part 702-799 and in particular, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193). Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the Authorized Officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. Holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. § 9601, *et seq.* or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, *et seq.*) on the Right-of-Way (unless the release or threatened release is wholly unrelated to activity of the Right-of-Way Holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way Holder on the Right-of-Way. This provision applies without regard to whether a release is caused by Holder, its agent, or unrelated third parties.
4. Holder shall be liable for damage or injury to the United States to the extent provided by 43 CFR Sec. 2883.1-4. Holder shall be held to a standard of strict liability for damage or injury to the United States resulting from pipe rupture, fire, or spills caused or substantially aggravated by any of the following within the right-of-way or permit area:
  - a. Activities of Holder including, but not limited to: construction, operation, maintenance, and termination of the facility;
  - b. Activities of other parties including, but not limited to:
    - (1) Land clearing
    - (2) Earth-disturbing and earth-moving work
    - (3) Blasting
    - (4) Vandalism and sabotage;

c. Acts of God.

The maximum limitation for such strict liability damages shall not exceed one million dollars (\$1,000,000) for any one event, and any liability in excess of such amount shall be determined by the ordinary rules of negligence of the jurisdiction in which the damage or injury occurred.

This section shall not impose strict liability for damage or injury resulting primarily from an act of war or from the negligent acts or omissions of the United States.

5. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil, salt water, or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil, salt water, or other pollutant, wherever found, shall be the responsibility of Holder, regardless of fault. Upon failure of Holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he/she deems necessary to control and clean up the discharge and restore the area, including, where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of Holder. Such action by the Authorized Officer shall not relieve Holder of any responsibility as provided herein.

6. All construction and maintenance activity shall be confined to the authorized right-of-way width of 30 feet. If the pipeline route follows an existing road or buried pipeline right-of-way, the surface pipeline shall be installed no farther than 10 feet from the edge of the road or buried pipeline right-of-way. If existing surface pipelines prevent this distance, the proposed surface pipeline shall be installed immediately adjacent to the outer surface pipeline. All construction and maintenance activity shall be confined to existing roads or right-of-ways.

7. No blading or clearing of any vegetation shall be allowed unless approved in writing by the Authorized Officer.

8. Holder shall install the pipeline on the surface in such a manner that will minimize suspension of the pipeline across low areas in the terrain. In hummocky or dune areas, the pipeline shall be "snaked" around hummocks and dunes rather than suspended across these features.

9. The pipeline shall be buried with a minimum of 6 inches under all roads, "two-tracks," and trails. Burial of the pipe will continue for 20 feet on each side of each crossing. The condition of the road, upon completion of construction, shall be returned to at least its former state with no bumps or dips remaining in the road surface.

10. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. Excluding the pipe, all above-ground structures not subject to safety requirement shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be a color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2; designated by the Rocky Mountain Five State Interagency Committee.

13. The pipeline will be identified by signs at the point of origin and completion of the right-of-way

and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. Signs will be maintained in a legible condition for the life of the pipeline.

14. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway.

15. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 16 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

16. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

17. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

18. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, powerline corridor, and adjacent land affected by the establishment of

weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

19. Surface pipelines shall be less than or equal to 4 inches and a working pressure below 125 psi.

## **VII. INTERIM RECLAMATION**

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

## **VIII. FINAL ABANDONMENT & RECLAMATION**

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.



### **Seed Mixture 2, for Sandy Sites**

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)\* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed\* per acre:

#### **Species**

	<u>lb/acre</u>
Sand dropseed ( <i>Sporobolus cryptandrus</i> )	1.0
Sand love grass ( <i>Eragrostis trichodes</i> )	1.0
Plains bristlegrass ( <i>Setaria macrostachya</i> )	2.0

\*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

# PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

<b>OPERATOR'S NAME:</b>	Tap Rock Operating LLC
<b>WELL NAME &amp; NO.:</b>	Mulva Fed Com 213H
<b>LOCATION:</b>	Sec 27-24S-35E-NMP
<b>COUNTY:</b>	Eddy County, New Mexico

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

## A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

## B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately 550 feet (a minimum of 70 feet (Eddy County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours

after bringing cement to surface or 500 pounds compressive strength, whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

**Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
  - Cement to surface. If cement does not circulate see B.1.a, c-d above.
3. The minimum required fill of cement behind the **7-5/8** inch intermediate casing is:
  - Cement should tie-back at least 3
  - 00 feet into previous casing string. Operator shall provide method of verification.
4. The minimum required fill of cement behind the **5-1/2** inch production casing is:
  - Cement should tie-back at least **50 feet** on top of Capitan Reef top. If cement does not circulate see B.1.a, c-d above.

**C. PRESSURE CONTROL**

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

## D. SPECIAL REQUIREMENT (S)

### **Communitization Agreement**

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,  
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)  
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.

- Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
  - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
  3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

#### A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

**B. PRESSURE CONTROL**

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
  - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
  - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
  - c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
  - d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
  - e. The results of the test shall be reported to the appropriate BLM office.

- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

#### C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.


#### D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



# LOCATION & ELEVATION VERIFICATION MAP

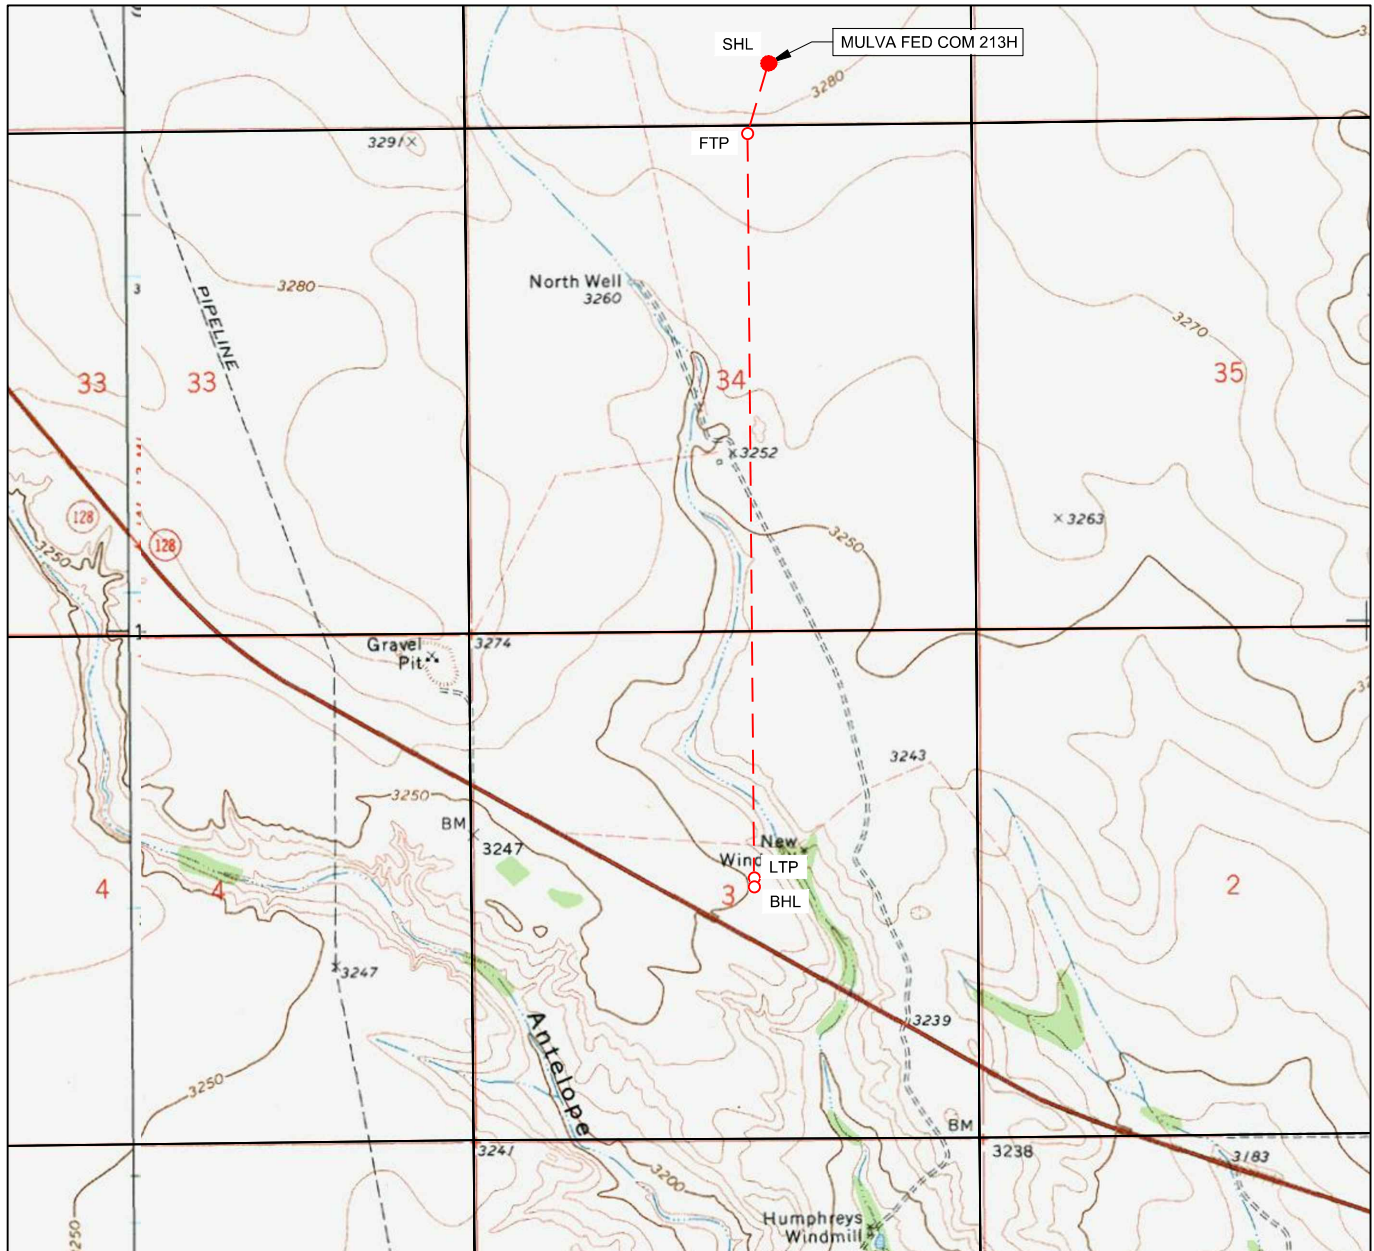

LEASE NAME & WELL NO.: MULVA FED COM 213H

SECTION 27 TWP 24-S RGE 35-E SURVEY N.M.P.M.  
 COUNTY LEA STATE NM ELEVATION 3285'  
 DESCRIPTION 629' FSL & 2085' FEL

LATITUDE N 32.1829697 LONGITUDE W 103.3535768



SCALE: 1" = 2000'  
 0' 1000' 2000'

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.


ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



**TOPOGRAPHIC**  
 LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
 WWW.TOPOGRAPHIC.COM

# EXHIBIT 2 VICINITY MAP

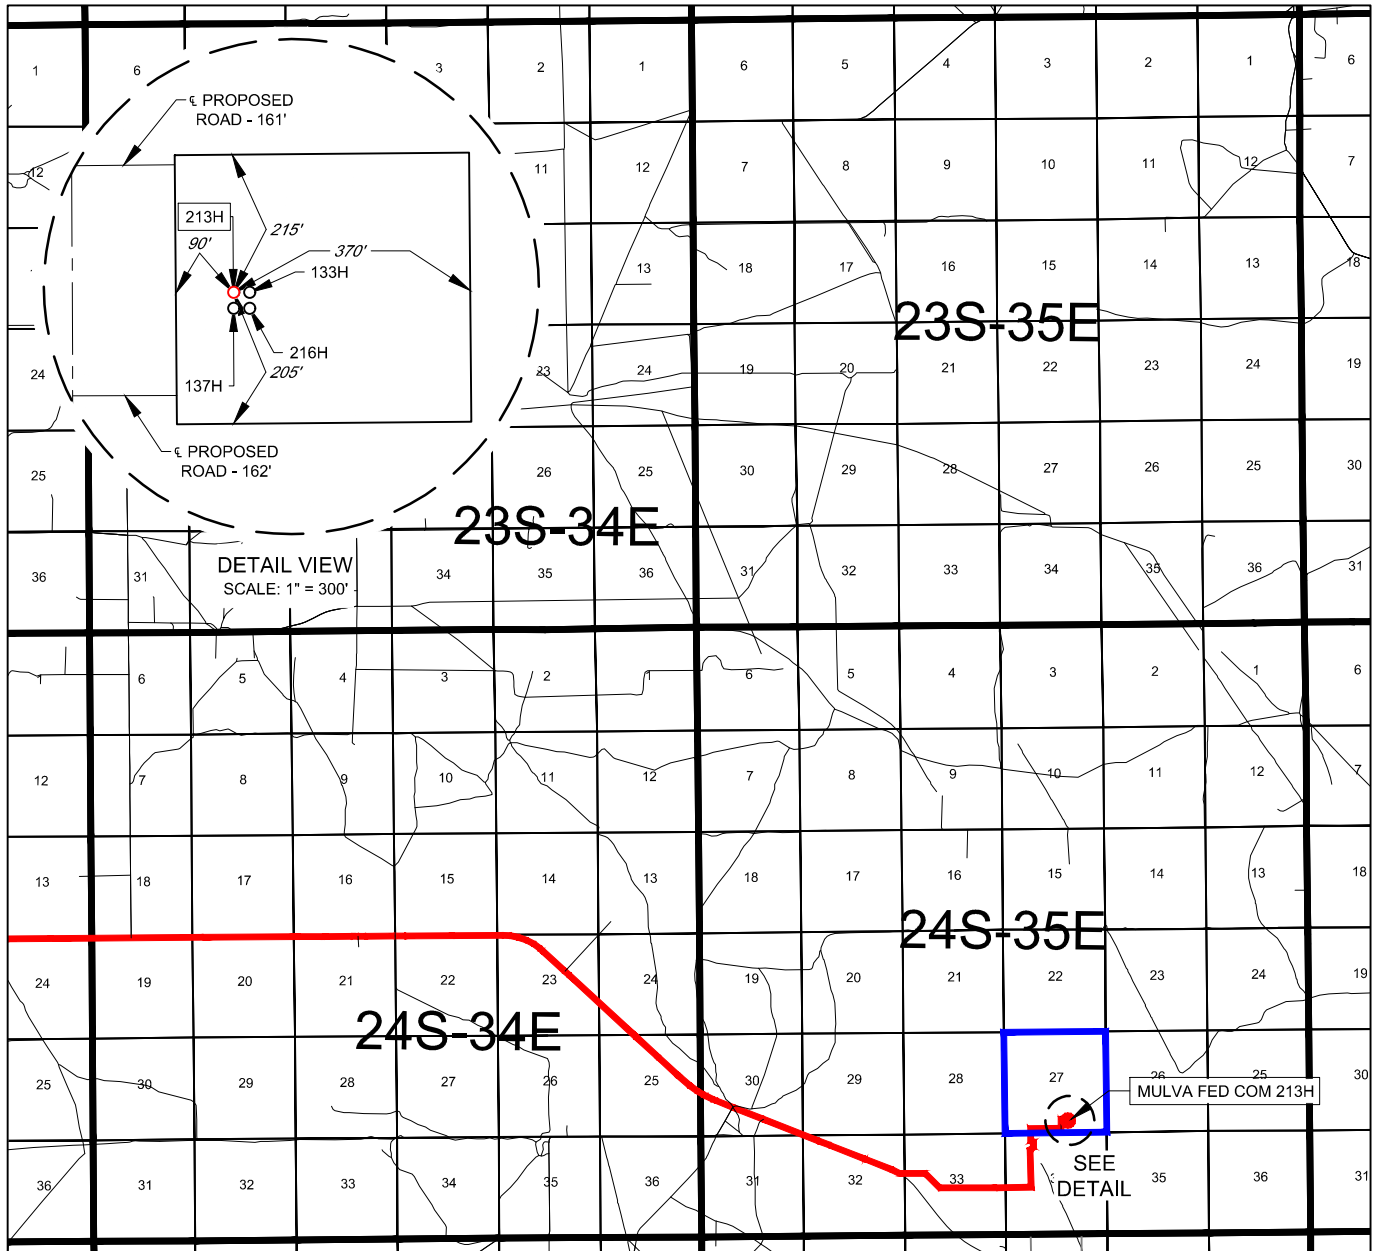

LEASE NAME & WELL NO.: MULVA FED COM 213H

SECTION 27 TWP 24-S RGE 35-E SURVEY N.M.P.M.  
 COUNTY LEA STATE NM  
 DESCRIPTION 629' FSL & 2085' FEL

## DISTANCE & DIRECTION

FROM INT. OF NM-128 & DELAWARE BASIN RD., GO EAST ON NM-128  
 ±9.7 MILES, THENCE NORTHEAST (LEFT) ON A LEASE RD. ±3.1 MILES,  
 THENCE NORTH (LEFT) ON A PROPOSED RD. ±162 FEET TO A POINT  
 ±184 FEET SOUTHWEST OF THE LOCATION.

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



SCALE: 1" = 10000'

0' 5000' 10000'




**TOPOGRAPHIC**  
 LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
 WWW.TOPOGRAPHIC.COM



## EXHIBIT 2A

SECTION 27, TOWNSHIP 24-S, RANGE 35-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

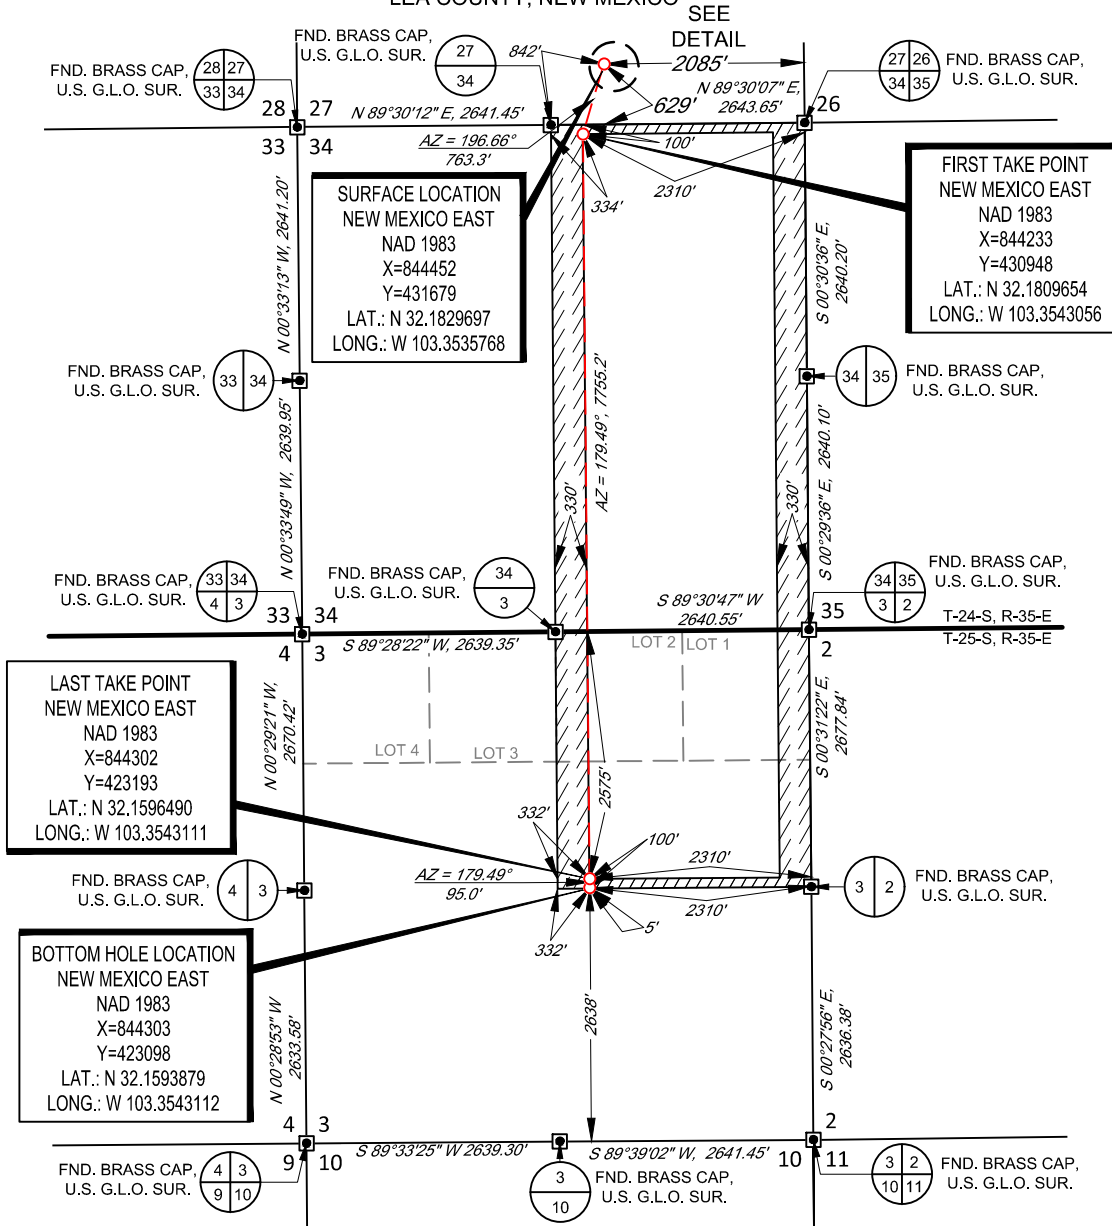

DETAIL VIEW  
SCALE: 1" = 300'

LEASE NAME & WELL NO.: \_\_\_\_\_ MULVA FED COM 213H

SECTION 27 TWP 24-S RGE 35-E SURVEY N.M.P.M.  
COUNTY LEA STATE NM  
DESCRIPTION 629' FSL & 2085' FEL

DISTANCE & DIRECTION  
FROM INT. OF NM-128 & DELAWARE BASIN RD., GO EAST ON NM-128  
±9.7 MILES, THENCE NORTHEAST (LEFT) ON A LEASE RD. ±3.1 MILES,  
THENCE NORTH (LEFT) ON A PROPOSED RD. ±162 FEET TO A POINT  
±184 FEET SOUTHWEST OF THE LOCATION.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID  
BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY  
FEET.

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND  
UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF  
SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC THIS CERTIFICATION IS MADE AND  
LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS  
NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.



John Trevor Carnegie, P.S. No. 11401




**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM


# EXHIBIT 2B



SECTION 27, TOWNSHIP 24-S, RANGE 35-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

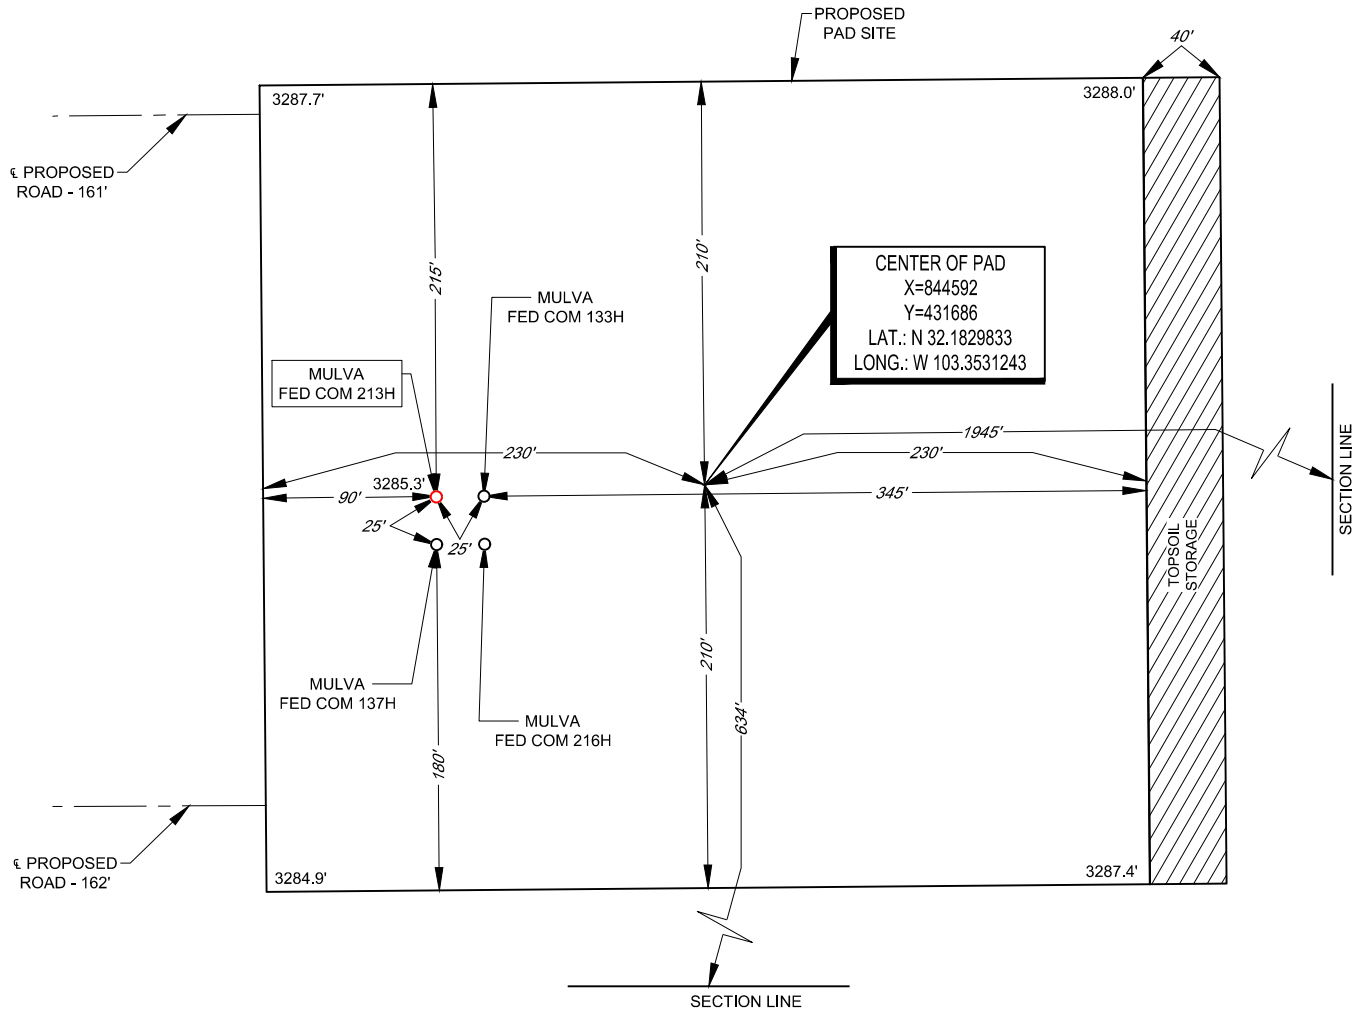

LEASE NAME & WELL NO.: MULVA FED COM 213H  
213H LATITUDE N 32.1829697 213H LONGITUDE W 103.3535768  
CENTER OF PAD IS 634' FSL & 1945' FEL




John Trevor Carnegie, P.S. No. 11401

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET, ELEVATIONS USED ARE NAVD88, OBTAINED THROUGH AN OPUS SOLUTION.

THIS PROPOSED PAD SITE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ORIGINAL DOCUMENT SIZE: 8.5" X 11"



**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM



Drilling Operations Plan  
Mulva Fed Com 213H  
Tap Rock Operating, LLC  
SHL 629' FSL & 2085' FEL, Sec. 27  
BHL 2638' FSL & 2310' FEL, Sec. 3  
Surface- T. 24S, R. 35E Lea County, NM  
BHL- T. 25S, R. 35E Lea County, NM

Elevation above Sea Level: 3285'

## **DRILLING PROGRAM**

### **1. Estimated Tops**

Formation	TVD	MD	Lithologies	Bearing
Quaternary Deposits	0	0	Surface	None
Rustler Anhydrite	970	970		Salt
Salado	1350	1350	Salt	Salt
Base Salt	4750	4765		Salt
Lamar	5260	5279	Limestone	None
Bell Canyon	5265	5284	Sandstone	Hydrocarbons
Cherry Canyon	6150	6176	Sandstone	Hydrocarbons
Brushy Canyon	7610	7647	Sandstone	Hydrocarbons
Bone Spring	8915	8960	Limestone	Hydrocarbons
1st Bone Spring	10120	10165	Sandstone	Hydrocarbons
2nd Bone Spring	10315	10360	Sandstone	Hydrocarbons
3rd Bone Spring	11225	11270	Sandstone	Hydrocarbons
3rd BS W Sand	12065	12147	Sandstone	Hydrocarbons
KOP	11682	11727	Sandstone	Hydrocarbons
Wolfcamp	12135	12250	Shale	Hydrocarbons
TD	12282	19905	Shale	Hydrocarbons

### **2. Notable Zones**

Wolfcamp is the formation target.

### **3. Pressure Control**

Pressure Control Equipment (See Schematics):

A 15,000', 10,000 psi BOP stack consisting of 3 rams with 2 pipe rams, 1 blind ram, and 1 annular preventer will be used below surface casing to TD. See attachments for BOP and choke manifold diagrams. Also present will be an accumulator that meets the requirements of Onshore Order #2 for the pressure rating of the BOP stack. A rotating head will also be installed as needed. BOP will be inspected and operated as recommended in Onshore Order #2. A top drive check valve and sub equipped with a full opening valve sized to fit the drill pipe and collars will be available on the rig floor in the open position. The wellhead will be a multi-bowl speed head.





Drilling Operations Plan  
Mulva Fed Com 213H  
Tap Rock Operating, LLC  
SHL 629' FSL & 2085' FEL, Sec. 27  
BHL 2638' FSL & 2310' FEL, Sec. 3  
Surface- T. 24S, R. 35E Lea County, NM  
BHL- T. 25S, R. 35E Lea County, NM

BOP Test procedure will be as follows:

After surface casing is set and the BOP is nipped up, the BOP pressure tests will be made with a third party tester to 250 psi low, 5000 psi high, and the annular preventer will be tested to 2,500 psi. The BOP will be tested in this manner after nipple-up if any break of the stack occurs. Before drilling out from 7.625" casing shoe, the BOP pressure tests will be made with a third party tester to 250 psi low, 10,000 psi high, and the annular preventer will be tested to 5,000 psi. The BOP will be tested in this manner if passage of allotted time occurs.

Variance Requests:

Tap Rock requests a variance to run a multi-bowl speed head for setting the Intermediate 1, Intermediate 2, and Production Strings. Tap Rock requests a variance to drill this well using a co-flex line between the BOP and choke manifold. Certification for proposed co-flex hose is attached. The hose is not required by the manufacturer to be anchored. In the event the specific hose is not available, one of equal or higher rating will be used. Tap Rock requests a variance to have the option of batch drilling this well with other wells on the same pad. In the event that this well is batch drilled, after drilling surface, 1<sup>st</sup> intermediate, and 2<sup>nd</sup> intermediate hole sections and cementing 2<sup>nd</sup> intermediate casing, a 10M dry hole cap with bleed off valve will be installed. The rig will then walk to another well on the pad. When the rig returns to this well and BOPs are installed, the operator will perform a full BOP test. Tap Rock requests a variance to run 7-5/8" BTC casing inside 9-5/8" BTC casing will be less than the 0.422" stand off regulation. Through conversations with BLM representatives, Tap Rock has received approval for this design as long as the 7-5/8" flush casing was run throughout the entire 300' cement tie back section between 9-5/8" and 7-5/8" casing. Tap Rock requests a variance to use a 5000 psi annular BOP on a 10M BOP stack. The annular will be tested to 250 psi low and 5000 psi high.

Tap Rock requests approval to possibly utilize a spudder rig to drill and set casing for the surface interval on this well. The spudder rig will be possibly utilized in order to reduce cost and save time. The wellhead will be installed and tested as soon as the surface casing is cut off per the existing COAs. A blind flange with the same pressure rating as the wellhead will be installed on the well. Once the spudder rig is removed, Tap Rock will secure the wellhead area by placing a guard rail around the cellar. Pressure will be monitored and a means for intervention will be maintained while the drilling rig is not over the well. Spudder rig operations are expected to take 2-3 days per well. Three wells on the pad will have surface casing set by the spudder rig as a part of this operation. The BLM will be notified 24 hours prior to commencing spudder rig operations. Within 90 days of the departure of the spudder rig, drilling operations will recommence on these wells. This rig will have a BOP stack equal or greater to the pressure rating required in the COAs. The BLM will be notified 24 hours before the larger rig moves on the pre-set wells. Tap Rock will have supervision on the spudder rig to ensure compliance with all BLM and NMOCD regulations.



Drilling Operations Plan  
 Mulva Fed Com 213H  
 Tap Rock Operating, LLC  
 SHL 629' FSL & 2085' FEL, Sec. 27  
 BHL 2638' FSL & 2310' FEL, Sec. 3  
 Surface- T. 24S, R. 35E Lea County, NM  
 BHL- T. 25S, R. 35E Lea County, NM

#### 4. Casing & Cement

All Casing will be new.

Name	Hole Size	Casing Size	Standard	Tapered	Top MD	Bottom MD	Top TVD	BTM TVD	Grade	Weight	Thread	Collapse	Burst	Tension
Surface	17 1/2	13 3/8	API	No	0	1045	0	1045	J-55	54.5	BUTT	1.13	1.15	1.6
1st Intermediate	12 1/4	9 5/8	API	No	0	5299	0	5280	J-55	40	BUTT	1.13	1.15	1.6
2nd Intermediate	8 3/4	7 5/8	API	No	0	4999	0	4980	P-110	29.7	BUTT	1.13	1.15	1.6
2nd Intermediate	8 3/4	7 5/8	NON API	Yes	4999	11627	4980	11582	P-110	29.7	W-513	1.13	1.15	1.6
Production	6 3/4	5 1/2	NON API	No	0	11427	0	11382	P-110	20	TXP	1.13	1.15	1.6
Production	6 3/4	5	NON API	Yes	11427	19905	11382	12282	P-110	18	W-521	1.13	1.15	1.6

Name	Type	Top MD	Sacks	Yield	Cu. Ft	Weight	Excess	Cement	Additives
Surface	Tail	0	1075	1.35	1452	14.8	100%	C	5% NCI + LCM
1st Intermediate	Lead	0	1005	2.18	2190	12.7	65%	C	Bentonite + 1% CaCL <sub>2</sub> + 8% NaCl + LCM
	Tail	4239	412	1.33	548	14.8	65%	C	5% NaCl + LCM
2nd Intermediate	Lead	4999	344	2.22	763	11.5	35%	TXI	Fluid Loss + Dispersant + Retarder + LCM
	Tail	10627	99	1.37	136	13.2	35%	H	Fluid Loss + Dispersant + Retarder + LCM
Production	Tail	10927	1058	1.19	1259	15.8	25%	H	Fluid Loss + Dispersant + Retarder + LCM

#### 5. Mud Program

Name	Top	Bottom	Type	Mud Weight	Visc	Fluid Loss
Surface	0	1045	FW Spud Mud	8.30	28	NC
Intermediate	1045	5299	Brine Water	10.00	30-32	NC
Intermediate 2	5299	11627	FW/Cut Brine	9.00	30-32	NC
Production	11627	19905	Oil Base Mud	11.50	50-70	<10

Electronic Pason mud monitor system complying with Onshore Order 1 will be used. All necessary mud products (e. g., barite, cedar bark) for weight addition and fluid loss control will always be on site. Mud program is subject to change due to hole conditions. A closed loop system will be used.

#### 6. Cores, Tests, & Logs

- Electric Logging Program: No open-hole logs are planned at this time for the pilot hole.
- GR will be collected while drilling through the MWD tools from 9.625" casing shoe to TD.
- A 2-person mud logging program will be used from 9.625" casing shoe to TD.
- No DSTs or cores are planned at this time.
- CBL w/ CCL from as far as gravity will let it fall to TOC.



Drilling Operations Plan  
Mulva Fed Com 213H  
Tap Rock Operating, LLC  
SHL 629' FSL & 2085' FEL, Sec. 27  
BHL 2638' FSL & 2310' FEL, Sec. 3  
Surface- T. 24S, R. 35E Lea County, NM  
BHL- T. 25S, R. 35E Lea County, NM

## **7. Down Hole Conditions**

No abnormal pressure or temperature is expected. Maximum expected bottom hole pressure is  $\approx 7,345$  psi. Expected bottom hole temperature is  $\approx 170^{\circ}$  F.

Tap Rock does not anticipate that there will be enough H<sub>2</sub>S from the surface to the Wolfcamp formations to meet the BLM's Onshore Order 6 requirements for the submission of an "H<sub>2</sub>S Drilling Operation Plan" or "Public Protection Plan" for drilling and completing this well. Tap Rock has an H<sub>2</sub>S safety package on all wells and an "H<sub>2</sub>S Drilling Operations Plan" is attached. Adequate flare lines will be installed off the mud/gas separator where gas may be safely flared. All personnel will be familiar with all aspects of safe operation of equipment being used.

## **8. Other Information**


Road and location construction will begin after BLM approval of APD. Anticipated spud date as soon as approved. Drilling expected to take 30 days. If production casing is run an additional 60 days will be required to complete and construct surface facilities.







Drilling Operations Plan  
 Mulva Fed Com 213H  
 Tap Rock Operating, LLC  
 SHL 629' FSL & 2085' FEL, Sec. 27  
 BHL 2638' FSL & 2310' FEL, Sec. 3  
 Surface- T. 24S, R. 35E Lea County, NM  
 BHL- T. 25S, R. 35E Lea County, NM

10,000 psi BOP Stack

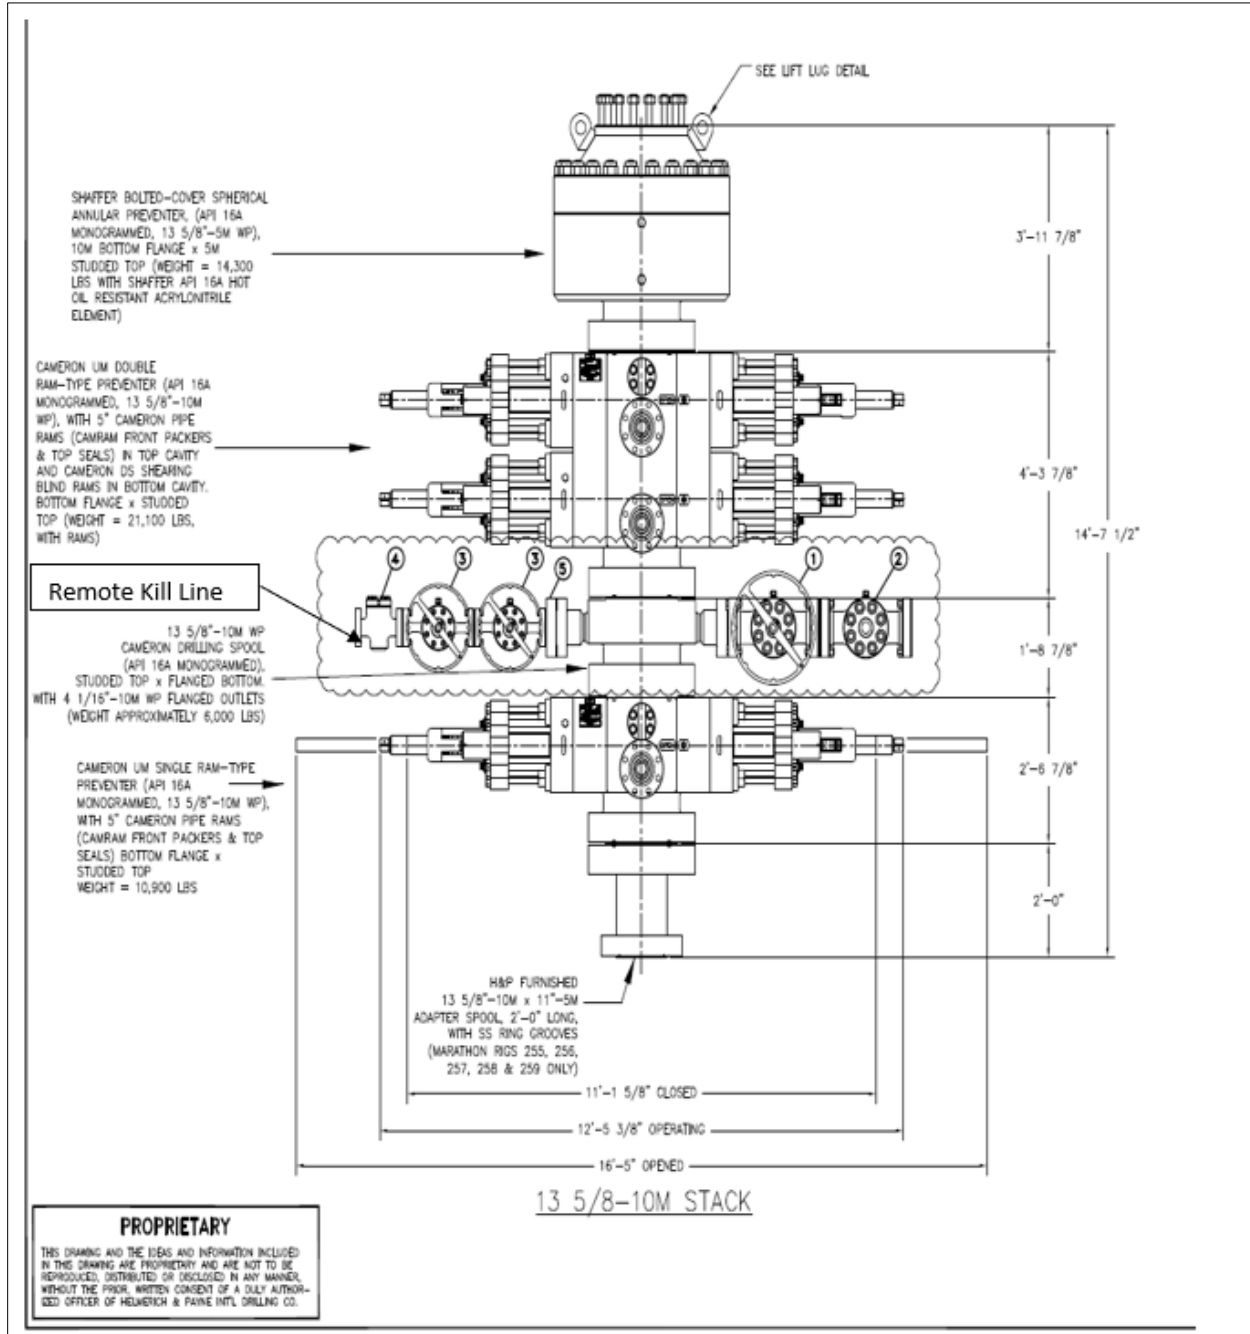







Drilling Operations Plan  
Mulva Fed Com 213H  
Tap Rock Operating, LLC  
SHL 629' FSL & 2085' FEL, Sec. 27  
BHL 2638' FSL & 2310' FEL, Sec. 3  
Surface- T. 24S, R. 35E Lea County, NM  
BHL- T. 25S, R. 35E Lea County, NM

Multi-bowl Wellhead

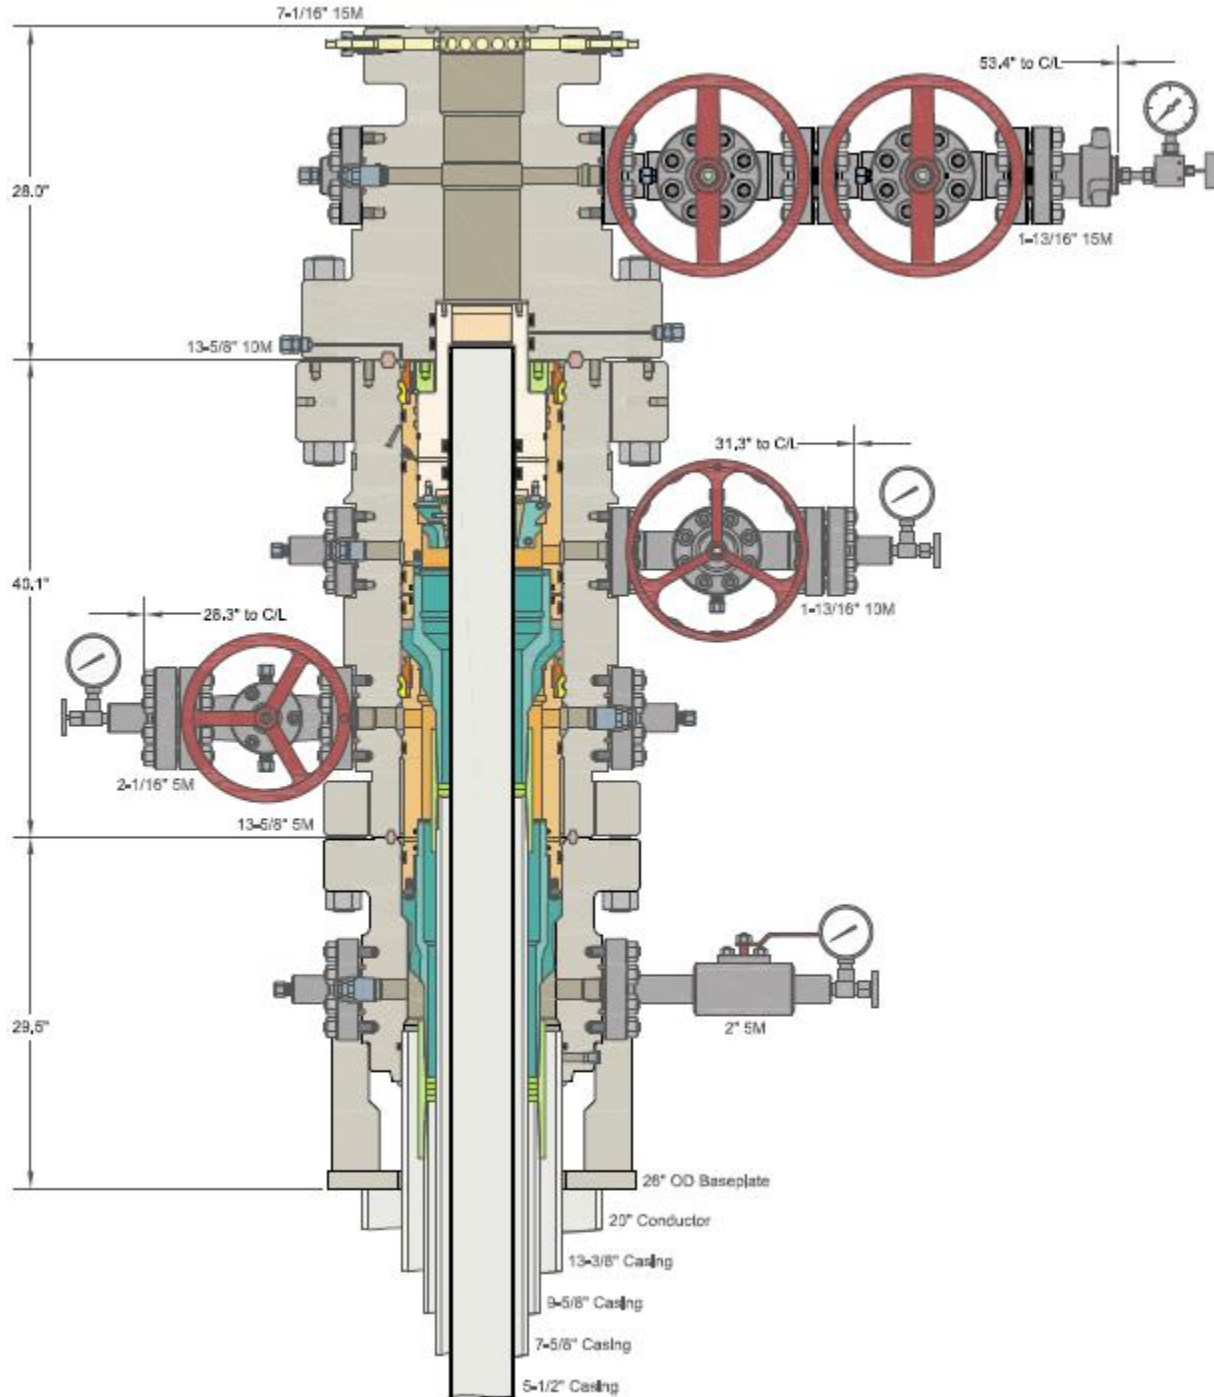

[illegible]



# **Tap Rock Resources, LLC**

**Lea County, NM (NAD 83 NME)  
(Mulva Fed) Sec-27\_T-24-S\_R-35-E  
Mulva Fed Com #213H**

**OWB**

**Plan: Plan #2**

## **Standard Planning Report**

**24 July, 2020**



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

<b>Project</b>	Lea County, NM (NAD 83 NME)		
<b>Map System:</b>	US State Plane 1983	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	North American Datum 1983		
<b>Map Zone:</b>	New Mexico Eastern Zone		

<b>Site</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E		
<b>Site Position:</b>		<b>Northing:</b>	431,446.00 usft
<b>From:</b>	Map	<b>Easting:</b>	841,909.00 usft
<b>Position Uncertainty:</b>	0.0 usft	<b>Slot Radius:</b>	13-3/16 "
		<b>Latitude:</b>	32° 10' 56.609 N
		<b>Longitude:</b>	103° 21' 42.490 W
		<b>Grid Convergence:</b>	0.52 °

<b>Well</b>	Mulva Fed Com #213H		
<b>Well Position</b>	<b>+N/-S</b>	233.0 usft	<b>Northing:</b> 431,679.00 usft
	<b>+E/-W</b>	2,543.0 usft	<b>Easting:</b> 844,452.00 usft
<b>Position Uncertainty</b>	0.0 usft	<b>Wellhead Elevation:</b>	<b>Latitude:</b> 32° 10' 58.686 N
			<b>Longitude:</b> 103° 21' 12.878 W
			<b>Ground Level:</b> 3,285.0 usft

<b>Wellbore</b>	OWB				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	IGRF2015	01/08/20	6.57	60.02	47,673.84061064

<b>Design</b>	Plan #2			
<b>Audit Notes:</b>				
<b>Version:</b>	<b>Phase:</b>	PLAN	<b>Tie On Depth:</b>	0.0
<b>Vertical Section:</b>	<b>Depth From (TVD) (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Direction (°)</b>
	0.0	0.0	0.0	179.49

<b>Plan Survey Tool Program</b>	<b>Date</b>	07/24/20		
<b>Depth From (usft)</b>	<b>Depth To (usft)</b>	<b>Survey (Wellbore)</b>	<b>Tool Name</b>	<b>Remarks</b>
1	0.0	19,905.4 Plan #2 (OWB)	MWD	
			OWSG MWD - Standard	

<b>Plan Sections</b>										
<b>Measured Depth (usft)</b>	<b>Inclination (°)</b>	<b>Azimuth (°)</b>	<b>Vertical Depth (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Dogleg Rate (°/100usft)</b>	<b>Build Rate (°/100usft)</b>	<b>Turn Rate (°/100usft)</b>	<b>TFO (°)</b>	<b>Target</b>
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,850.1	7.00	193.83	2,849.2	-20.7	-5.1	2.00	2.00	0.00	193.83	
8,675.1	7.00	193.83	8,630.8	-710.3	-174.9	0.00	0.00	0.00	0.00	
9,025.2	0.00	0.00	8,980.0	-731.0	-180.0	2.00	-2.00	0.00	180.00	
11,727.2	0.00	0.00	11,682.0	-731.0	-180.0	0.00	0.00	0.00	0.00	
12,625.1	89.79	182.90	12,255.0	-1,301.1	-208.9	10.00	10.00	0.00	182.90	
12,795.6	89.79	179.49	12,255.6	-1,471.6	-212.4	2.00	0.00	-2.00	-90.05	
19,905.4	89.79	179.49	12,282.0	-8,581.0	-149.0	0.00	0.00	0.00	0.00	PBHL (Mulva Fed C



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
970.0	0.00	0.00	970.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>Rustler Anhydrite</b>									
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,350.0	0.00	0.00	1,350.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>Top Salt</b>									
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
<b>NUDGE - Build 2.00</b>									
2,600.0	2.00	193.83	2,600.0	-1.7	-0.4	1.7	2.00	2.00	0.00
2,700.0	4.00	193.83	2,699.8	-6.8	-1.7	6.8	2.00	2.00	0.00
2,800.0	6.00	193.83	2,799.5	-15.2	-3.8	15.2	2.00	2.00	0.00
2,850.1	7.00	193.83	2,849.2	-20.7	-5.1	20.7	2.00	2.00	0.00
<b>HOLD - 5825.0 at 2850.1 MD</b>									
2,900.0	7.00	193.83	2,898.8	-26.7	-6.6	26.6	0.00	0.00	0.00
3,000.0	7.00	193.83	2,998.0	-38.5	-9.5	38.4	0.00	0.00	0.00
3,100.0	7.00	193.83	3,097.3	-50.3	-12.4	50.2	0.00	0.00	0.00
3,200.0	7.00	193.83	3,196.5	-62.2	-15.3	62.0	0.00	0.00	0.00
3,300.0	7.00	193.83	3,295.8	-74.0	-18.2	73.8	0.00	0.00	0.00
3,400.0	7.00	193.83	3,395.0	-85.8	-21.1	85.6	0.00	0.00	0.00
3,500.0	7.00	193.83	3,494.3	-97.7	-24.1	97.5	0.00	0.00	0.00
3,600.0	7.00	193.83	3,593.5	-109.5	-27.0	109.3	0.00	0.00	0.00
3,700.0	7.00	193.83	3,692.8	-121.3	-29.9	121.1	0.00	0.00	0.00
3,800.0	7.00	193.83	3,792.0	-133.2	-32.8	132.9	0.00	0.00	0.00
3,900.0	7.00	193.83	3,891.3	-145.0	-35.7	144.7	0.00	0.00	0.00
4,000.0	7.00	193.83	3,990.6	-156.9	-38.6	156.5	0.00	0.00	0.00
4,100.0	7.00	193.83	4,089.8	-168.7	-41.5	168.3	0.00	0.00	0.00
4,200.0	7.00	193.83	4,189.1	-180.5	-44.5	180.1	0.00	0.00	0.00
4,300.0	7.00	193.83	4,288.3	-192.4	-47.4	191.9	0.00	0.00	0.00
4,400.0	7.00	193.83	4,387.6	-204.2	-50.3	203.8	0.00	0.00	0.00
4,500.0	7.00	193.83	4,486.8	-216.0	-53.2	215.6	0.00	0.00	0.00
4,600.0	7.00	193.83	4,586.1	-227.9	-56.1	227.4	0.00	0.00	0.00



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,700.0	7.00	193.83	4,685.3	-239.7	-59.0	239.2	0.00	0.00	0.00
4,765.2	7.00	193.83	4,750.0	-247.4	-60.9	246.9	0.00	0.00	0.00
<b>Base Salt</b>									
4,800.0	7.00	193.83	4,784.6	-251.6	-61.9	251.0	0.00	0.00	0.00
4,900.0	7.00	193.83	4,883.8	-263.4	-64.9	262.8	0.00	0.00	0.00
5,000.0	7.00	193.83	4,983.1	-275.2	-67.8	274.6	0.00	0.00	0.00
5,100.0	7.00	193.83	5,082.3	-287.1	-70.7	286.4	0.00	0.00	0.00
5,200.0	7.00	193.83	5,181.6	-298.9	-73.6	298.2	0.00	0.00	0.00
5,273.9	7.00	193.83	5,255.0	-307.7	-75.8	307.0	0.00	0.00	0.00
<b>Delaware Mountain Gp</b>									
5,279.0	7.00	193.83	5,260.0	-308.3	-75.9	307.6	0.00	0.00	0.00
<b>Lamar</b>									
5,284.0	7.00	193.83	5,265.0	-308.9	-76.1	308.2	0.00	0.00	0.00
<b>Bell Canyon</b>									
5,289.1	7.00	193.83	5,270.0	-309.4	-76.2	308.8	0.00	0.00	0.00
<b>Ramsey Sand</b>									
5,300.0	7.00	193.83	5,280.9	-310.7	-76.5	310.0	0.00	0.00	0.00
5,400.0	7.00	193.83	5,380.1	-322.6	-79.4	321.9	0.00	0.00	0.00
5,500.0	7.00	193.83	5,479.4	-334.4	-82.3	333.7	0.00	0.00	0.00
5,600.0	7.00	193.83	5,578.6	-346.3	-85.3	345.5	0.00	0.00	0.00
5,700.0	7.00	193.83	5,677.9	-358.1	-88.2	357.3	0.00	0.00	0.00
5,800.0	7.00	193.83	5,777.1	-369.9	-91.1	369.1	0.00	0.00	0.00
5,900.0	7.00	193.83	5,876.4	-381.8	-94.0	380.9	0.00	0.00	0.00
6,000.0	7.00	193.83	5,975.6	-393.6	-96.9	392.7	0.00	0.00	0.00
6,100.0	7.00	193.83	6,074.9	-405.4	-99.8	404.5	0.00	0.00	0.00
6,175.7	7.00	193.83	6,150.0	-414.4	-102.0	413.5	0.00	0.00	0.00
<b>Cherry Canyon</b>									
6,200.0	7.00	193.83	6,174.1	-417.3	-102.7	416.3	0.00	0.00	0.00
6,300.0	7.00	193.83	6,273.4	-429.1	-105.7	428.2	0.00	0.00	0.00
6,400.0	7.00	193.83	6,372.7	-441.0	-108.6	440.0	0.00	0.00	0.00
6,500.0	7.00	193.83	6,471.9	-452.8	-111.5	451.8	0.00	0.00	0.00
6,600.0	7.00	193.83	6,571.2	-464.6	-114.4	463.6	0.00	0.00	0.00
6,700.0	7.00	193.83	6,670.4	-476.5	-117.3	475.4	0.00	0.00	0.00
6,800.0	7.00	193.83	6,769.7	-488.3	-120.2	487.2	0.00	0.00	0.00
6,900.0	7.00	193.83	6,868.9	-500.1	-123.2	499.0	0.00	0.00	0.00
7,000.0	7.00	193.83	6,968.2	-512.0	-126.1	510.8	0.00	0.00	0.00
7,100.0	7.00	193.83	7,067.4	-523.8	-129.0	522.6	0.00	0.00	0.00
7,200.0	7.00	193.83	7,166.7	-535.6	-131.9	534.5	0.00	0.00	0.00
7,300.0	7.00	193.83	7,265.9	-547.5	-134.8	546.3	0.00	0.00	0.00
7,400.0	7.00	193.83	7,365.2	-559.3	-137.7	558.1	0.00	0.00	0.00
7,500.0	7.00	193.83	7,464.4	-571.2	-140.6	569.9	0.00	0.00	0.00
7,600.0	7.00	193.83	7,563.7	-583.0	-143.6	581.7	0.00	0.00	0.00
7,646.6	7.00	193.83	7,610.0	-588.5	-144.9	587.2	0.00	0.00	0.00
<b>Brushy Canyon</b>									
7,700.0	7.00	193.83	7,663.0	-594.8	-146.5	593.5	0.00	0.00	0.00
7,800.0	7.00	193.83	7,762.2	-606.7	-149.4	605.3	0.00	0.00	0.00
7,900.0	7.00	193.83	7,861.5	-618.5	-152.3	617.1	0.00	0.00	0.00
8,000.0	7.00	193.83	7,960.7	-630.3	-155.2	628.9	0.00	0.00	0.00
8,100.0	7.00	193.83	8,060.0	-642.2	-158.1	640.7	0.00	0.00	0.00
8,200.0	7.00	193.83	8,159.2	-654.0	-161.0	652.6	0.00	0.00	0.00
8,300.0	7.00	193.83	8,258.5	-665.9	-164.0	664.4	0.00	0.00	0.00
8,400.0	7.00	193.83	8,357.7	-677.7	-166.9	676.2	0.00	0.00	0.00
8,500.0	7.00	193.83	8,457.0	-689.5	-169.8	688.0	0.00	0.00	0.00



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,600.0	7.00	193.83	8,556.2	-701.4	-172.7	699.8	0.00	0.00	0.00
8,675.1	7.00	193.83	8,630.8	-710.3	-174.9	708.7	0.00	0.00	0.00
<b>DROP - -2.00</b>									
8,700.0	6.50	193.83	8,655.5	-713.1	-175.6	711.5	2.00	-2.00	0.00
8,800.0	4.50	193.83	8,755.0	-722.4	-177.9	720.8	2.00	-2.00	0.00
8,900.0	2.50	193.83	8,854.9	-728.3	-179.3	726.7	2.00	-2.00	0.00
8,960.2	1.30	193.83	8,915.0	-730.3	-179.8	728.7	2.00	-2.00	0.00
<b>Bone Spring Lime</b>									
9,000.0	0.50	193.83	8,954.8	-730.9	-180.0	729.3	2.00	-2.00	0.00
9,010.2	0.30	193.83	8,965.0	-731.0	-180.0	729.3	2.00	-2.00	0.00
<b>Upper Avalon</b>									
9,025.2	0.00	0.00	8,980.0	-731.0	-180.0	729.4	2.00	-2.00	0.00
<b>HOLD - 2702.0 at 9025.2 MD</b>									
9,100.0	0.00	0.00	9,054.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,200.0	0.00	0.00	9,154.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,250.2	0.00	0.00	9,205.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>Middle Avalon</b>									
9,300.0	0.00	0.00	9,254.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,400.0	0.00	0.00	9,354.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,500.0	0.00	0.00	9,454.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,600.0	0.00	0.00	9,554.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,685.2	0.00	0.00	9,640.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>Lower Avalon</b>									
9,700.0	0.00	0.00	9,654.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,800.0	0.00	0.00	9,754.8	-731.0	-180.0	729.4	0.00	0.00	0.00
9,900.0	0.00	0.00	9,854.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,000.0	0.00	0.00	9,954.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,100.0	0.00	0.00	10,054.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,165.2	0.00	0.00	10,120.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>1st Bone Spring Sand</b>									
10,200.0	0.00	0.00	10,154.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,300.0	0.00	0.00	10,254.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,360.2	0.00	0.00	10,315.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>2nd Bone Spring Carb</b>									
10,400.0	0.00	0.00	10,354.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,500.0	0.00	0.00	10,454.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,600.0	0.00	0.00	10,554.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,700.0	0.00	0.00	10,654.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,715.2	0.00	0.00	10,670.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>2nd Bone Spring Sand</b>									
10,800.0	0.00	0.00	10,754.8	-731.0	-180.0	729.4	0.00	0.00	0.00
10,900.0	0.00	0.00	10,854.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,000.0	0.00	0.00	10,954.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,100.0	0.00	0.00	11,054.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,200.0	0.00	0.00	11,154.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,270.2	0.00	0.00	11,225.0	-731.0	-180.0	729.4	0.00	0.00	0.00
<b>3rd Bone Spring Carb</b>									
11,300.0	0.00	0.00	11,254.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,400.0	0.00	0.00	11,354.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,500.0	0.00	0.00	11,454.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,600.0	0.00	0.00	11,554.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,700.0	0.00	0.00	11,654.8	-731.0	-180.0	729.4	0.00	0.00	0.00
11,727.2	0.00	0.00	11,682.0	-731.0	-180.0	729.4	0.00	0.00	0.00



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mulva Fed Com #213H
Company:	Tap Rock Resources, LLC	TVD Reference:	KB @ 3311.0usft
Project:	Lea County, NM (NAD 83 NME)	MD Reference:	KB @ 3311.0usft
Site:	(Mulva Fed) Sec-27_T-24-S_R-35-E	North Reference:	Grid
Well:	Mulva Fed Com #213H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	Plan #2		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
KOP - Build 10.00									
11,750.0	2.28	182.90	11,704.8	-731.5	-180.0	729.8	10.00	10.00	0.00
11,800.0	7.28	182.90	11,754.6	-735.6	-180.2	734.0	10.00	10.00	0.00
11,850.0	12.28	182.90	11,803.9	-744.1	-180.7	742.5	10.00	10.00	0.00
11,900.0	17.28	182.90	11,852.2	-756.8	-181.3	755.2	10.00	10.00	0.00
11,950.0	22.28	182.90	11,899.2	-773.7	-182.2	772.1	10.00	10.00	0.00
12,000.0	27.28	182.90	11,944.6	-794.7	-183.2	793.0	10.00	10.00	0.00
12,023.2	29.60	182.90	11,965.0	-805.7	-183.8	804.0	10.00	10.00	0.00
3rd Bone Spring Sand									
12,050.0	32.28	182.90	11,988.0	-819.4	-184.5	817.8	10.00	10.00	0.00
12,100.0	37.28	182.90	12,029.1	-847.9	-185.9	846.2	10.00	10.00	0.00
12,146.7	41.95	182.90	12,065.0	-877.6	-187.4	875.9	10.00	10.00	0.00
3rd BS W Sand									
12,150.0	42.28	182.90	12,067.5	-879.9	-187.5	878.2	10.00	10.00	0.00
12,200.0	47.28	182.90	12,102.9	-915.0	-189.3	913.3	10.00	10.00	0.00
12,249.6	52.24	182.90	12,135.0	-952.9	-191.2	951.1	10.00	10.00	0.00
Wolfcamp A X Sand									
12,250.0	52.28	182.90	12,135.2	-953.1	-191.3	951.4	10.00	10.00	0.00
12,300.0	57.28	182.90	12,164.0	-993.9	-193.3	992.2	10.00	10.00	0.00
12,301.8	57.46	182.90	12,165.0	-995.4	-193.4	993.7	10.00	10.00	0.00
Wolfcamp A Y Sand									
12,350.0	62.28	182.90	12,189.2	-1,037.1	-195.5	1,035.3	10.00	10.00	0.00
12,400.0	67.28	182.90	12,210.5	-1,082.2	-197.8	1,080.4	10.00	10.00	0.00
12,441.1	71.39	182.90	12,225.0	-1,120.6	-199.7	1,118.8	10.00	10.00	0.00
Wolfcamp A Lower									
12,450.0	72.28	182.90	12,227.8	-1,129.1	-200.2	1,127.2	10.00	10.00	0.00
12,500.0	77.28	182.90	12,240.9	-1,177.2	-202.6	1,175.4	10.00	10.00	0.00
12,550.0	82.28	182.90	12,249.8	-1,226.4	-205.1	1,224.5	10.00	10.00	0.00
12,600.0	87.28	182.90	12,254.3	-1,276.1	-207.6	1,274.2	10.00	10.00	0.00
12,625.1	89.79	182.90	12,255.0	-1,301.1	-208.9	1,299.2	10.00	10.00	0.00
EOC/TRN - DLS 2.00 TFO -90.05									
12,700.0	89.79	181.40	12,255.2	-1,376.0	-211.7	1,374.0	2.00	0.00	-2.00
12,795.6	89.79	179.49	12,255.6	-1,471.6	-212.4	1,469.7	2.00	0.00	-2.00
Start 7109.7 hold at 12795.6 MD									
12,800.0	89.79	179.49	12,255.6	-1,476.0	-212.4	1,474.0	0.00	0.00	0.00
12,900.0	89.79	179.49	12,256.0	-1,576.0	-211.5	1,574.0	0.00	0.00	0.00
13,000.0	89.79	179.49	12,256.3	-1,676.0	-210.6	1,674.0	0.00	0.00	0.00
13,100.0	89.79	179.49	12,256.7	-1,776.0	-209.7	1,774.0	0.00	0.00	0.00
13,200.0	89.79	179.49	12,257.1	-1,876.0	-208.8	1,874.0	0.00	0.00	0.00
13,300.0	89.79	179.49	12,257.5	-1,976.0	-207.9	1,974.0	0.00	0.00	0.00
13,400.0	89.79	179.49	12,257.8	-2,075.9	-207.0	2,074.0	0.00	0.00	0.00
13,500.0	89.79	179.49	12,258.2	-2,175.9	-206.2	2,174.0	0.00	0.00	0.00
13,600.0	89.79	179.49	12,258.6	-2,275.9	-205.3	2,274.0	0.00	0.00	0.00
13,700.0	89.79	179.49	12,258.9	-2,375.9	-204.4	2,374.0	0.00	0.00	0.00
13,800.0	89.79	179.49	12,259.3	-2,475.9	-203.5	2,474.0	0.00	0.00	0.00
13,900.0	89.79	179.49	12,259.7	-2,575.9	-202.6	2,574.0	0.00	0.00	0.00
14,000.0	89.79	179.49	12,260.1	-2,675.9	-201.7	2,674.0	0.00	0.00	0.00
14,100.0	89.79	179.49	12,260.4	-2,775.9	-200.8	2,774.0	0.00	0.00	0.00
14,200.0	89.79	179.49	12,260.8	-2,875.9	-199.9	2,874.0	0.00	0.00	0.00
14,300.0	89.79	179.49	12,261.2	-2,975.9	-199.0	2,974.0	0.00	0.00	0.00
14,400.0	89.79	179.49	12,261.5	-3,075.9	-198.1	3,074.0	0.00	0.00	0.00
14,500.0	89.79	179.49	12,261.9	-3,175.9	-197.2	3,174.0	0.00	0.00	0.00
14,600.0	89.79	179.49	12,262.3	-3,275.9	-196.3	3,274.0	0.00	0.00	0.00



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,700.0	89.79	179.49	12,262.7	-3,375.9	-195.4	3,374.0	0.00	0.00	0.00
14,800.0	89.79	179.49	12,263.0	-3,475.9	-194.6	3,474.0	0.00	0.00	0.00
14,900.0	89.79	179.49	12,263.4	-3,575.9	-193.7	3,574.0	0.00	0.00	0.00
15,000.0	89.79	179.49	12,263.8	-3,675.9	-192.8	3,674.0	0.00	0.00	0.00
15,100.0	89.79	179.49	12,264.1	-3,775.9	-191.9	3,774.0	0.00	0.00	0.00
15,200.0	89.79	179.49	12,264.5	-3,875.9	-191.0	3,874.0	0.00	0.00	0.00
15,300.0	89.79	179.49	12,264.9	-3,975.9	-190.1	3,974.0	0.00	0.00	0.00
15,400.0	89.79	179.49	12,265.3	-4,075.9	-189.2	4,074.0	0.00	0.00	0.00
15,500.0	89.79	179.49	12,265.6	-4,175.9	-188.3	4,174.0	0.00	0.00	0.00
15,600.0	89.79	179.49	12,266.0	-4,275.8	-187.4	4,274.0	0.00	0.00	0.00
15,700.0	89.79	179.49	12,266.4	-4,375.8	-186.5	4,374.0	0.00	0.00	0.00
15,800.0	89.79	179.49	12,266.7	-4,475.8	-185.6	4,474.0	0.00	0.00	0.00
15,900.0	89.79	179.49	12,267.1	-4,575.8	-184.7	4,574.0	0.00	0.00	0.00
16,000.0	89.79	179.49	12,267.5	-4,675.8	-183.8	4,674.0	0.00	0.00	0.00
16,100.0	89.79	179.49	12,267.9	-4,775.8	-183.0	4,774.0	0.00	0.00	0.00
16,200.0	89.79	179.49	12,268.2	-4,875.8	-182.1	4,874.0	0.00	0.00	0.00
16,300.0	89.79	179.49	12,268.6	-4,975.8	-181.2	4,974.0	0.00	0.00	0.00
16,400.0	89.79	179.49	12,269.0	-5,075.8	-180.3	5,074.0	0.00	0.00	0.00
16,500.0	89.79	179.49	12,269.3	-5,175.8	-179.4	5,174.0	0.00	0.00	0.00
16,600.0	89.79	179.49	12,269.7	-5,275.8	-178.5	5,274.0	0.00	0.00	0.00
16,700.0	89.79	179.49	12,270.1	-5,375.8	-177.6	5,374.0	0.00	0.00	0.00
16,800.0	89.79	179.49	12,270.5	-5,475.8	-176.7	5,474.0	0.00	0.00	0.00
16,900.0	89.79	179.49	12,270.8	-5,575.8	-175.8	5,574.0	0.00	0.00	0.00
17,000.0	89.79	179.49	12,271.2	-5,675.8	-174.9	5,674.0	0.00	0.00	0.00
17,100.0	89.79	179.49	12,271.6	-5,775.8	-174.0	5,774.0	0.00	0.00	0.00
17,200.0	89.79	179.49	12,271.9	-5,875.8	-173.1	5,874.0	0.00	0.00	0.00
17,300.0	89.79	179.49	12,272.3	-5,975.8	-172.2	5,974.0	0.00	0.00	0.00
17,400.0	89.79	179.49	12,272.7	-6,075.8	-171.4	6,074.0	0.00	0.00	0.00
17,500.0	89.79	179.49	12,273.1	-6,175.8	-170.5	6,174.0	0.00	0.00	0.00
17,600.0	89.79	179.49	12,273.4	-6,275.8	-169.6	6,274.0	0.00	0.00	0.00
17,700.0	89.79	179.49	12,273.8	-6,375.7	-168.7	6,374.0	0.00	0.00	0.00
17,800.0	89.79	179.49	12,274.2	-6,475.7	-167.8	6,474.0	0.00	0.00	0.00
17,900.0	89.79	179.49	12,274.5	-6,575.7	-166.9	6,574.0	0.00	0.00	0.00
18,000.0	89.79	179.49	12,274.9	-6,675.7	-166.0	6,674.0	0.00	0.00	0.00
18,100.0	89.79	179.49	12,275.3	-6,775.7	-165.1	6,774.0	0.00	0.00	0.00
18,200.0	89.79	179.49	12,275.7	-6,875.7	-164.2	6,874.0	0.00	0.00	0.00
18,300.0	89.79	179.49	12,276.0	-6,975.7	-163.3	6,974.0	0.00	0.00	0.00
18,400.0	89.79	179.49	12,276.4	-7,075.7	-162.4	7,074.0	0.00	0.00	0.00
18,500.0	89.79	179.49	12,276.8	-7,175.7	-161.5	7,174.0	0.00	0.00	0.00
18,600.0	89.79	179.49	12,277.1	-7,275.7	-160.6	7,274.0	0.00	0.00	0.00
18,700.0	89.79	179.49	12,277.5	-7,375.7	-159.8	7,374.0	0.00	0.00	0.00
18,800.0	89.79	179.49	12,277.9	-7,475.7	-158.9	7,474.0	0.00	0.00	0.00
18,900.0	89.79	179.49	12,278.3	-7,575.7	-158.0	7,574.0	0.00	0.00	0.00
19,000.0	89.79	179.49	12,278.6	-7,675.7	-157.1	7,674.0	0.00	0.00	0.00
19,100.0	89.79	179.49	12,279.0	-7,775.7	-156.2	7,774.0	0.00	0.00	0.00
19,200.0	89.79	179.49	12,279.4	-7,875.7	-155.3	7,874.0	0.00	0.00	0.00
19,300.0	89.79	179.49	12,279.8	-7,975.7	-154.4	7,974.0	0.00	0.00	0.00
19,400.0	89.79	179.49	12,280.1	-8,075.7	-153.5	8,074.0	0.00	0.00	0.00
19,500.0	89.79	179.49	12,280.5	-8,175.7	-152.6	8,174.0	0.00	0.00	0.00
19,600.0	89.79	179.49	12,280.9	-8,275.7	-151.7	8,274.0	0.00	0.00	0.00
19,700.0	89.79	179.49	12,281.2	-8,375.7	-150.8	8,374.0	0.00	0.00	0.00
19,800.0	89.79	179.49	12,281.6	-8,475.6	-149.9	8,474.0	0.00	0.00	0.00
19,905.4	89.79	179.49	12,282.0	-8,581.0	-149.0	8,579.3	0.00	0.00	0.00

<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
TD at 19905.4									

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
FTP (Mulva Fed Com - hit/miss target - Shape - Point)	0.00	0.00	12,255.0	-731.0	-219.0	430,948.00	844,233.00	32° 10' 51.473 N	103° 21' 15.503 W
- plan misses target center by 239.2usft at 12179.5usft MD (12088.8 TVD, -900.2 N, -188.6 E)									
LTP (Mulva Fed Com - plan misses target center by 10.4usft at 19800.0usft MD (12281.6 TVD, -8475.6 N, -149.9 E) - Point)	0.00	0.00	12,282.0	-8,486.0	-150.0	423,193.00	844,302.00	32° 9' 34.733 N	103° 21' 15.521 W
PBHL (Mulva Fed Cor - plan hits target center - Rectangle (sides W100.0 H7,851.0 D30.0)	0.21	179.49	12,282.0	-8,581.0	-149.0	423,098.00	844,303.00	32° 9' 33.793 N	103° 21' 15.520 W

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
970.0	970.0	Rustler Anhydrite				
1,350.0	1,350.0	Top Salt				
4,765.2	4,750.0	Base Salt				
5,273.9	5,255.0	Delaware Mountain Gp				
5,279.0	5,260.0	Lamar				
5,284.0	5,265.0	Bell Canyon				
5,289.1	5,270.0	Ramsey Sand				
6,175.7	6,150.0	Cherry Canyon				
7,646.6	7,610.0	Brushy Canyon				
8,960.2	8,915.0	Bone Spring Lime				
9,010.2	8,965.0	Upper Avalon				
9,250.2	9,205.0	Middle Avalon				
9,685.2	9,640.0	Lower Avalon				
10,165.2	10,120.0	1st Bone Spring Sand				
10,360.2	10,315.0	2nd Bone Spring Carb				
10,715.2	10,670.0	2nd Bone Spring Sand				
11,270.2	11,225.0	3rd Bone Spring Carb				
12,023.2	11,965.0	3rd Bone Spring Sand				
12,146.7	12,065.0	3rd BS W Sand				
12,249.6	12,135.0	Wolfcamp A X Sand				
12,301.8	12,165.0	Wolfcamp A Y Sand				
12,441.1	12,225.0	Wolfcamp A Lower				



<b>Database:</b>	EDM 5000.15 Single User Db	<b>Local Co-ordinate Reference:</b>	Well Mulva Fed Com #213H
<b>Company:</b>	Tap Rock Resources, LLC	<b>TVD Reference:</b>	KB @ 3311.0usft
<b>Project:</b>	Lea County, NM (NAD 83 NME)	<b>MD Reference:</b>	KB @ 3311.0usft
<b>Site:</b>	(Mulva Fed) Sec-27_T-24-S_R-35-E	<b>North Reference:</b>	Grid
<b>Well:</b>	Mulva Fed Com #213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	OWB		
<b>Design:</b>	Plan #2		

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2,500.0	2,500.0	0.0	0.0	NUDGE - Build 2.00
2,850.1	2,849.2	-20.7	-5.1	HOLD - 5825.0 at 2850.1 MD
8,675.1	8,630.8	-710.3	-174.9	DROP - -2.00
9,025.2	8,980.0	-731.0	-180.0	HOLD - 2702.0 at 9025.2 MD
11,727.2	11,682.0	-731.0	-180.0	KOP - Build 10.00
12,625.1	12,255.0	-1,301.1	-208.9	EOC/TRN - DLS 2.00 TFO -90.05
12,795.6	12,255.6	-1,471.6	-212.4	Start 7109.7 hold at 12795.6 MD
19,905.4	12,282.0	-8,581.0	-149.0	TD at 19905.4



## Hydrogen Sulfide Drilling

### Operations Plan

#### Tap Rock Resources

##### 1 H2S safety instructions to the following:

- Characteristics of H2S
- Physical effects and hazards
- Principal and operation of H2S detectors, warning system and briefing areas
- Evacuation procedures, routes and first aid
- Proper use of safety equipment & life support systems
- Essential personnel meeting medical evaluation criteria will receive additional training on the proper use of 30min pressure demand air packs

##### 2 H2S Detection and Alarm Systems:

- H2S sensor/detectors to be located on the drilling rig floor, in the base of the sub structure / cellar area, on the mud pits in the shale shaker area. Additional H2S detectors may be placed as deemed necessary
- An audio alarm system will be installed on the derrick floor and in the doghouse

##### 3 Windssocks and / Wind Streamers:

- Windssocks at mud pit area should be high enough to be visible
- Windssock on the rig floor and / top of doghouse should be high enough to be visible

##### 4 Condition Flags and Signs:

- Warning sign on access road to location
- Flags to be displayed on sign at entrance to location
  - Green Flag – Normal Safe Operation Condition
  - Yellow Flag – Potential Pressure and Danger
  - Red Flag – Danger (H2S present in dangerous concentrations) Only H2S trained personnel admitted on location

##### 5 Well Control Equipment:

- See Drilling Operations Plan Schematics

##### 6 Communication:

- While working under masks chalkboards will be used for communications
- Hand signals will be used where chalk board is inappropriate
- Two way radio will be used to communicate off location in case of emergency help is required. In most cases cellular telephones will be available at most drilling foreman's trailer or living quarters.



7 Drilling Stem Testing:

- No DST cores are planned at this time

8 Drilling contractor supervisor will be required to be familiar with the effects H<sub>2</sub>S has on tubulars good and other mechanical equipment


9 If H<sub>2</sub>S is encountered, mud system will be altered if necessary to maintain control of formation. A mud gas separator will be brought into service along with H<sub>2</sub>S scavengers if necessary

11 Emergency Contacts

<b>Emergency Contacts</b>		
Carlsbad Police Department	575.887.7551	911
Carlsbad Medical Center	575.887.4100	911
Eddy County Fire Service	575.628.5450	911
Eddy County Sherriff	575.887.7551	911
Lea County Fire Service	575.391.2983	911
Lea County Sherriff	575.396.3611	911
Jal Police Department	575.395.2121	911
Jal Fire Department	575.395.2221	911
Tap Rock Resources	720.772.5090	

H2S Diagram  
Mulva W2E2 Pad  
Tap Rock Operating, LLC  
27-24S-35E  
Lea County, NM

- N  
↑
- Briefing Area
  - Current Well
  - △ Flare Stack
  - ◇ H2S Monitor
  - 🚩 Wind Indicator
  - Mud Gas Separator

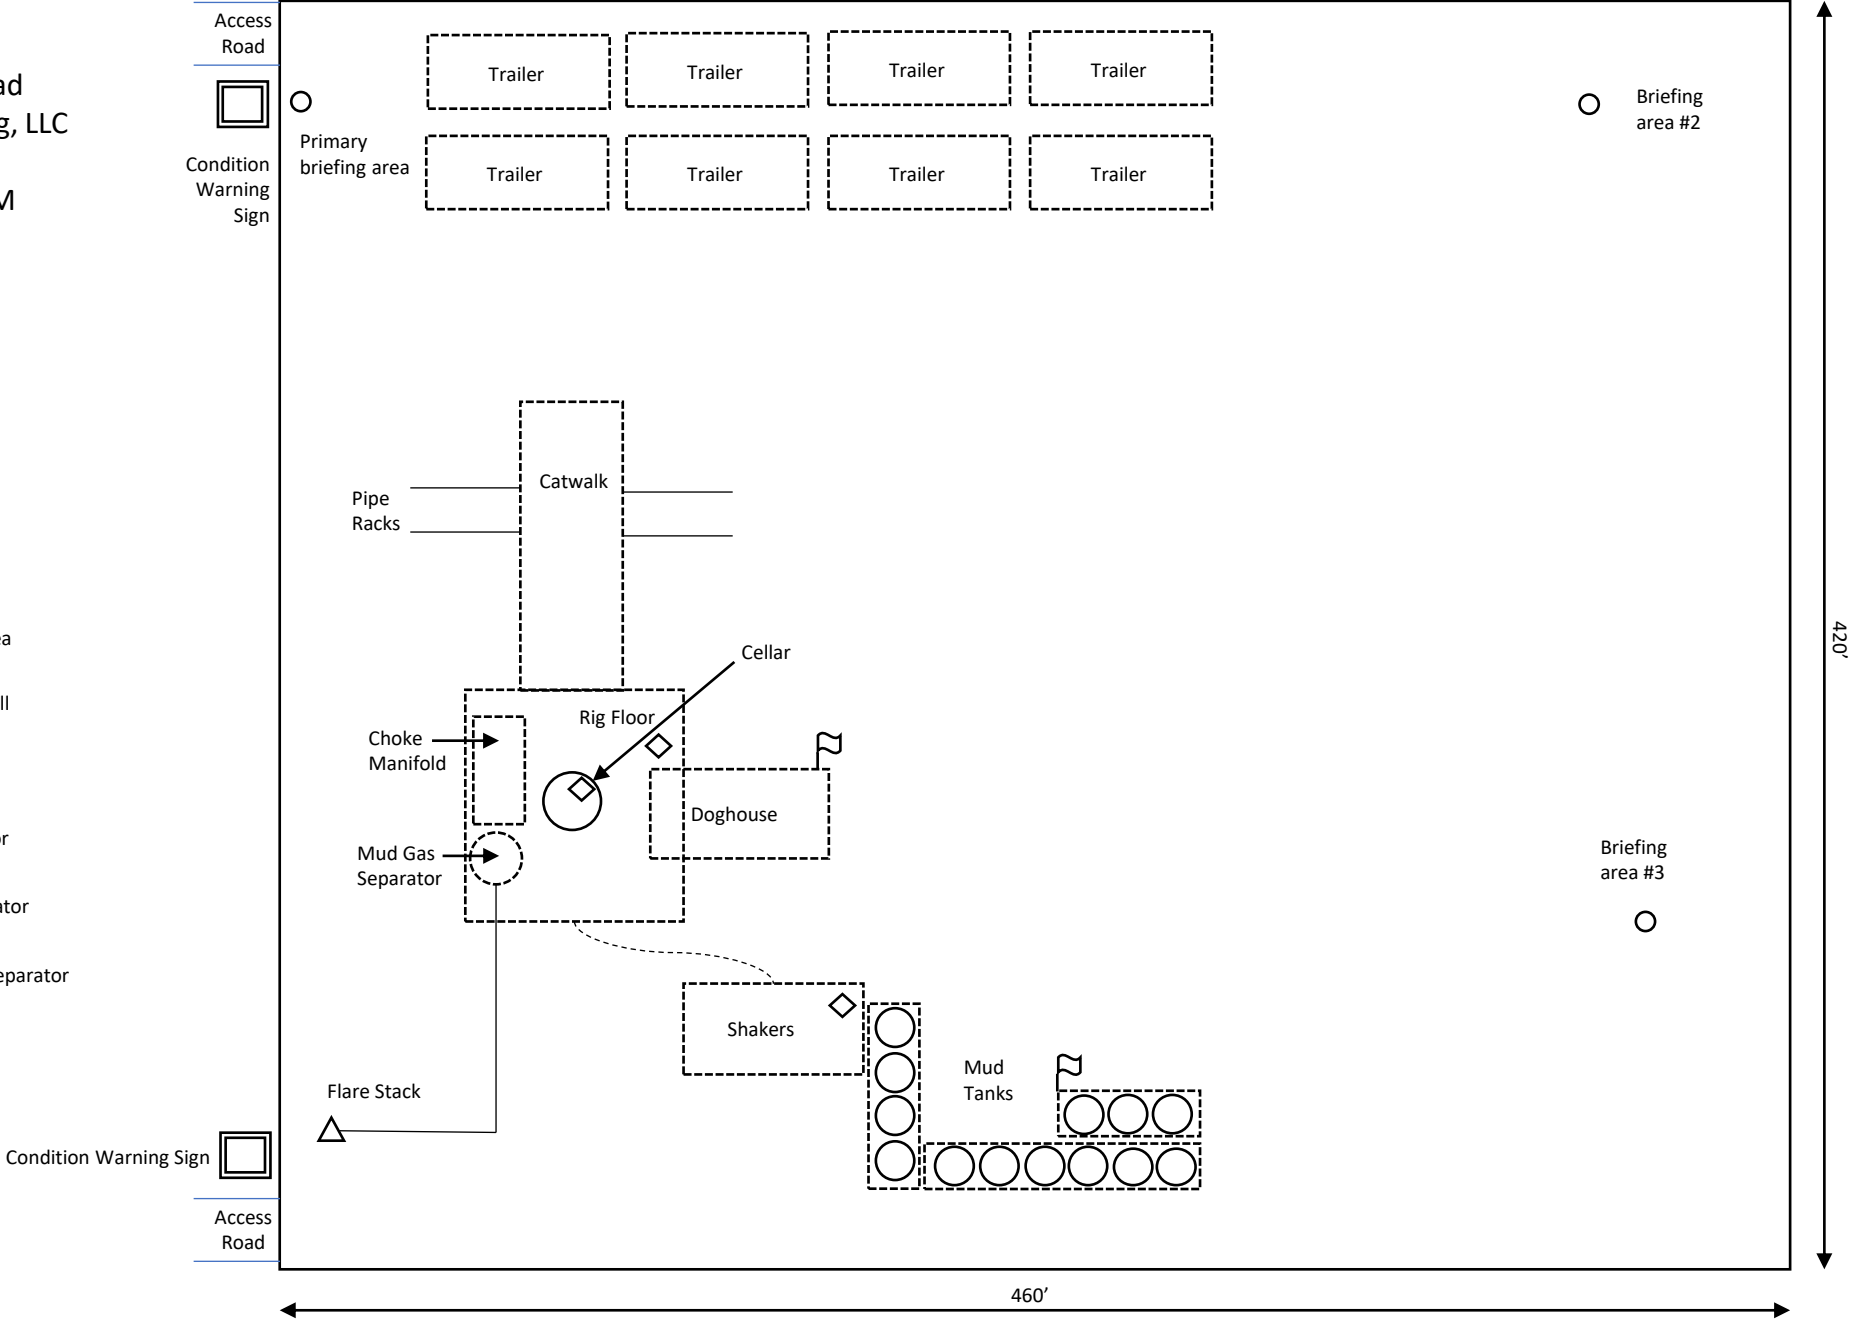




# Tap Rock Operating, LLC

Mulva W2E2 Pad  
H2S Contingency Plan:  
Radius Map

Section 27, Township 24S, Range 35E  
Lea County, New Mexico


 Pad Center Point



NAD 1983 New Mexico State Plane East  
FIPS 3001 Feet



Prepared by Permits West, Inc., February 7, 2020  
for Tap Rock Operating, LLC

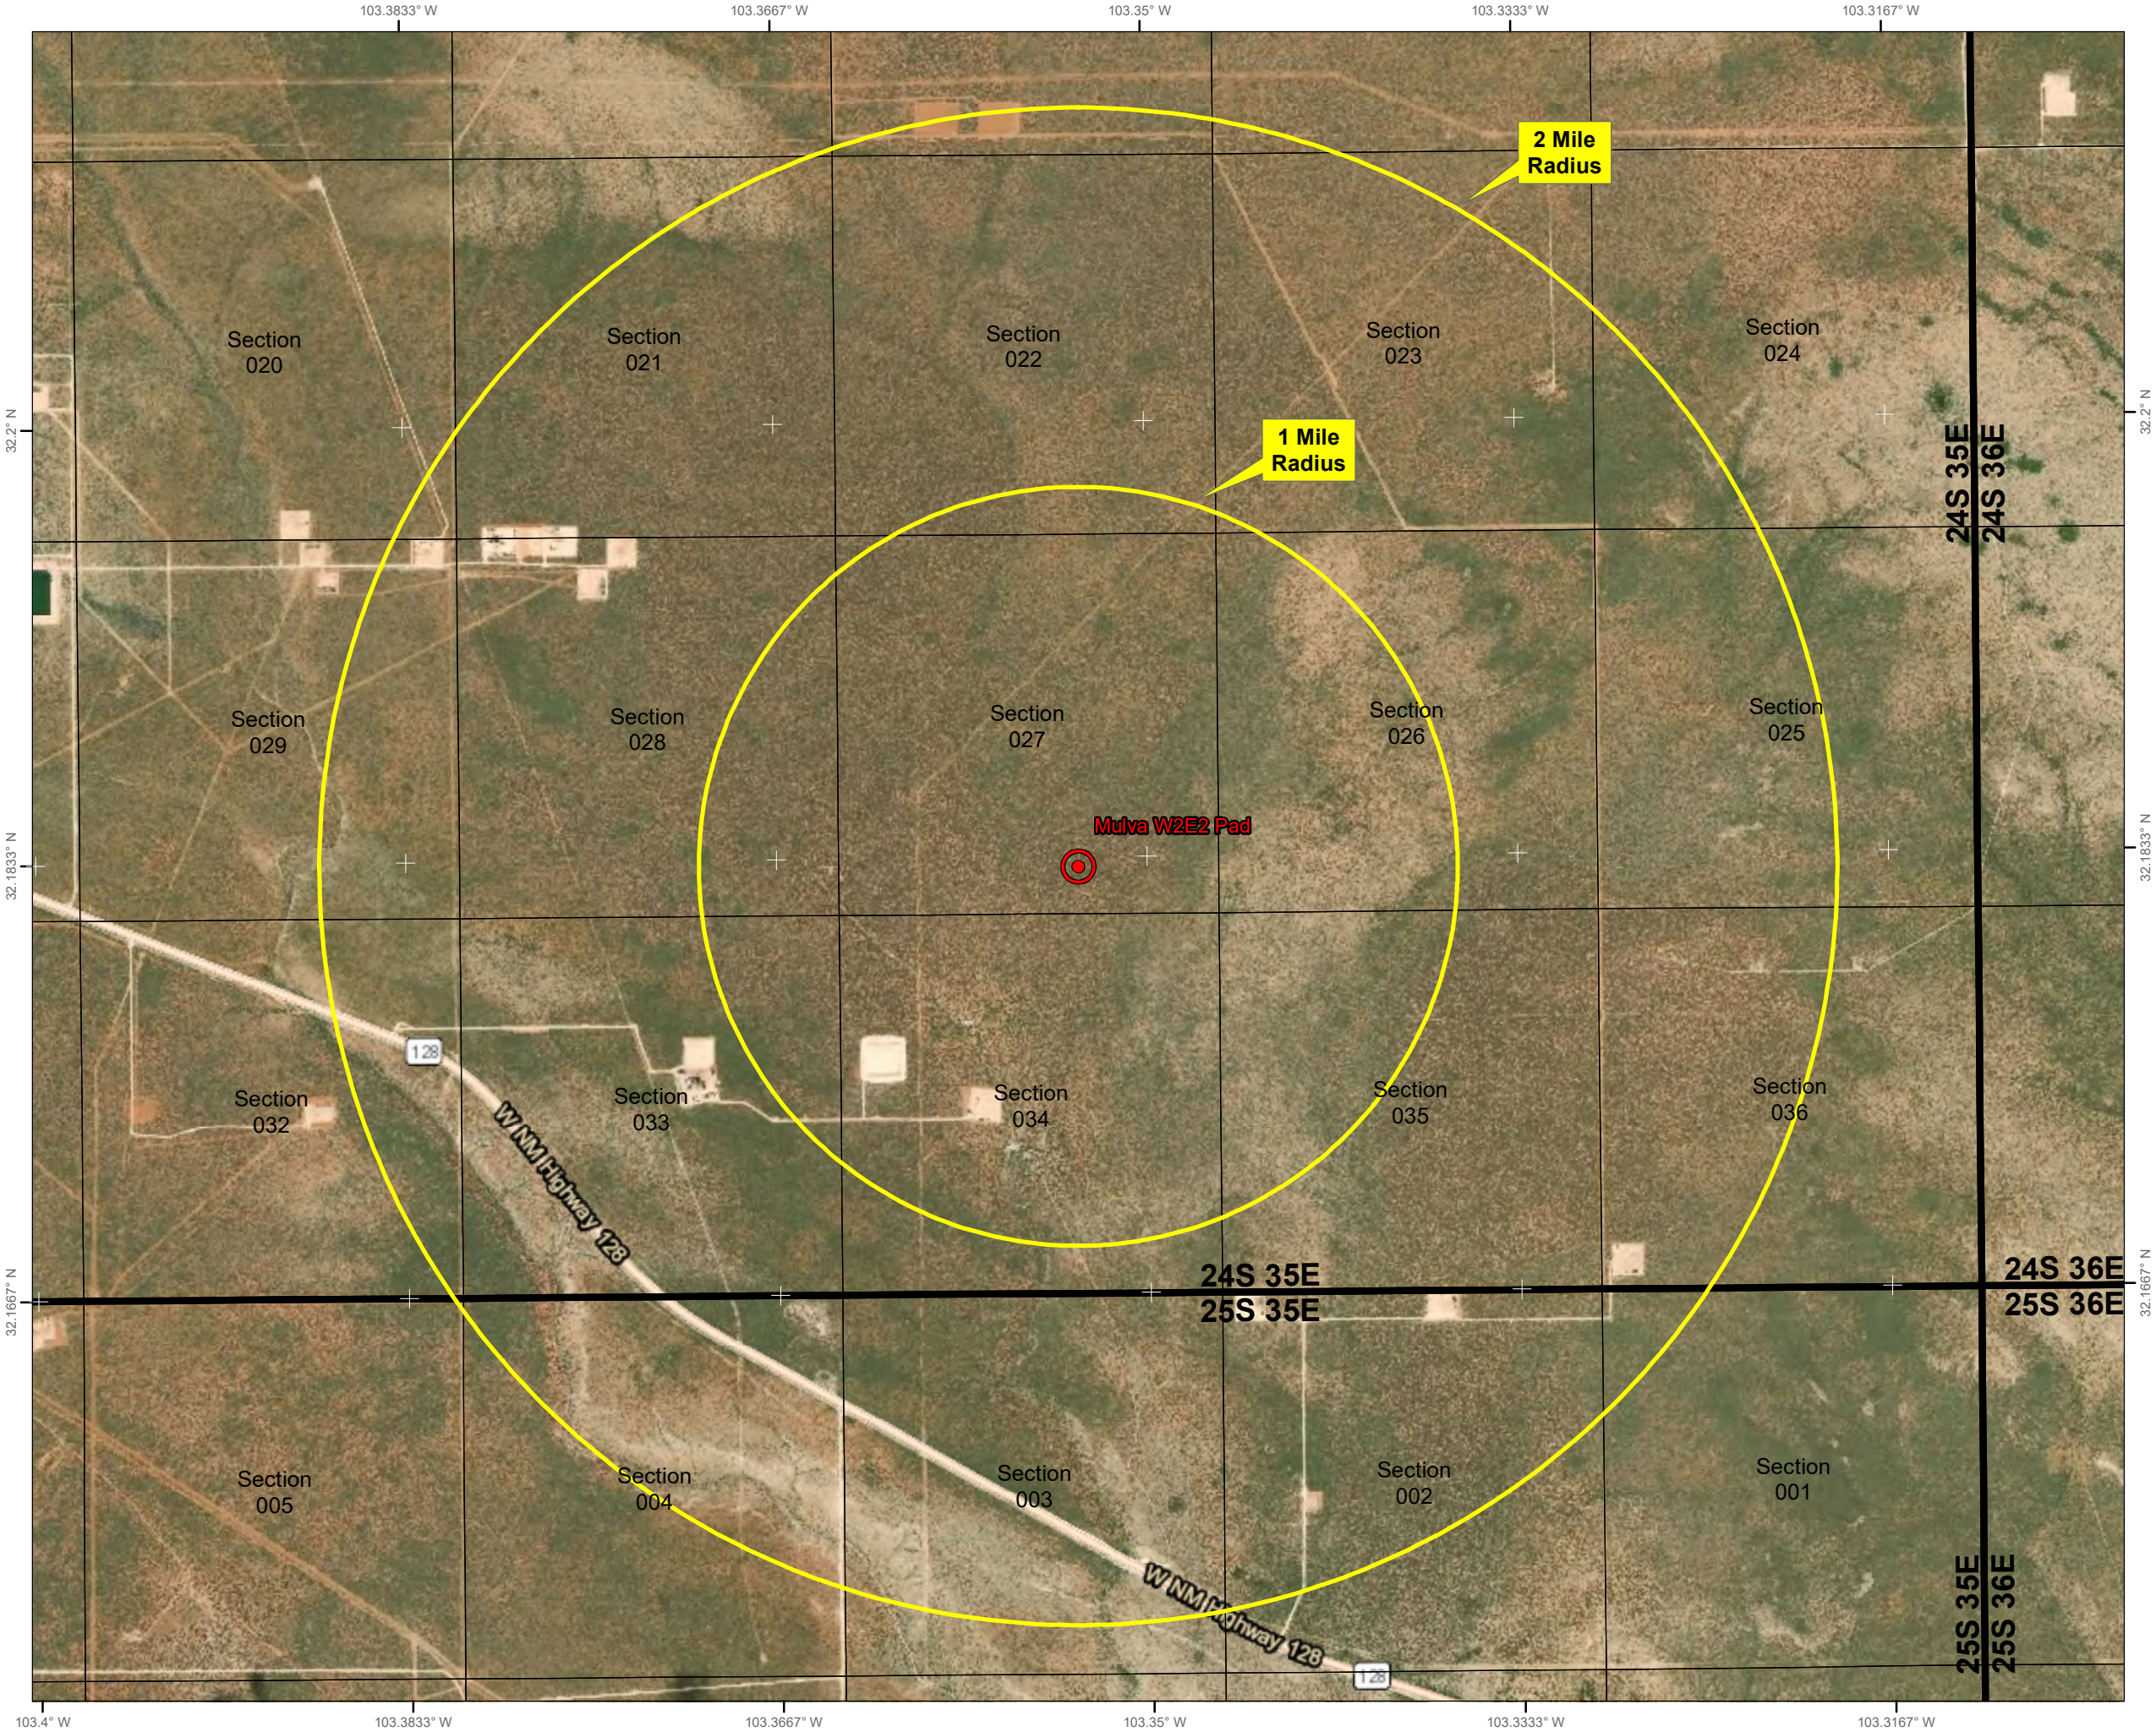





District I  
1625 N. French Dr., Hobbs, NM 88240  
District II  
811 S. First St., Artesia, NM 88210  
District III  
1000 Rio Brazos Road, Aztec, NM 87410  
District IV  
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico  
Energy, Minerals and Natural Resources Department  
Oil Conservation Division  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

Submit Original  
to Appropriate  
District Office

**OCD – HOBBS**  
**10/02/2020**  
**RECEIVED**

## **GAS CAPTURE PLAN**

Date: 1/16/2019

☒ Original

Operator & OGRID No.: 372043

☐ Amended - Reason for Amendment: \_\_\_\_\_

This Gas Capture Plan outlines actions to be taken by the Operator to reduce well/production facility flaring/venting for new completion (new drill, recomple to new zone, re-frac) activity.

*Note: Form C-129 must be submitted and approved prior to exceeding 60 days allowed by Rule (Subsection A of 19.15.18.12 NMAC).*

### **Well(s)/Production Facility – Name of facility**

The well(s) that will be located at the production facility are shown in the table below.

Well Name	API	Well Location (ULSTR)	Footages	Expected MCF/D	Flared or Vented	Comments
MULVA FED COM #213	30-025-47832	O SEC 27 T24S R35E	629' FSL 2085' FEL	+/- 8000	21 days	Gas will be flared for ~21 days during flowback before being turned to the TB. Time est. depends on sales connect and well cleanup.

### **Gathering System and Pipeline Notification**

Well(s) will be connected to a production facility after flowback operations are complete, if gas transporter system is in place. The gas produced from production facility should be connected to Lucid Energy Group, LLC and will be connected to Lucid Energy Group LLC's low/high pressure gathering system located in Eddy County, New Mexico. It will require approximately 2500' of pipeline to connect the facility to low/high pressure gathering system. Tap Rock Operating, LLC provides (periodically) to Lucid Energy Group, LLC a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future. In addition, Tap Rock Operating, LLC and Lucid Energy Group, LLC have periodic conference calls to discuss changes to drilling and completion schedules. Gas from these wells will be Processed at Lucid Energy Group, LLC 's Red Hills processing facility located in Lea County, New Mexico, and, although unanticipated, any issues with downstream facilities could cause flaring at the wellhead. The actual flow of the gas will be based on compression operating parameters and gathering system pressures.

### **Flowback Strategy**

After the fracture treatment/completion operations, well(s) will be produced to temporary production tanks and gas will be flared or vented. During flowback, the fluids and sand content will be monitored. When the produced fluids contain minimal sand, the wells will be turned to production facilities. Gas sales should start as soon as the wells start flowing through the production facilities, unless there are operational issues on Lucid's system at that time. Based on current information, it is Tap Rock Operating, LLC's belief the system can take this gas upon completion of the well(s).

Safety requirements during cleanout operations from the use of underbalanced air cleanout systems may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

### **Alternatives to Reduce Flaring**

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

- Power Generation – On lease
  - Only a portion of gas is consumed operating the generator, remainder of gas will be flared

- Compressed Natural Gas – On lease
  - Gas flared would be minimal, but might be uneconomical to operate when gas volume declines
- NGL Removal – On lease
  - Plants are expensive, residue gas is still flared, and uneconomical to operate when gas volume declines
