




Tubing Summary

Well Name SALADO DRAW WE 23 FED P7 004H	Lease SD 23 FED P7	Field Name JENNINGS	Business Unit Mid-Continent	
Ground Elevation (ft) 3,165.00	Original RKB Elevation (ft) 3,197.60	Current RKB Elevation 3,197.60, 3/28/2016	Mud Line Elevation (ft)	Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)	

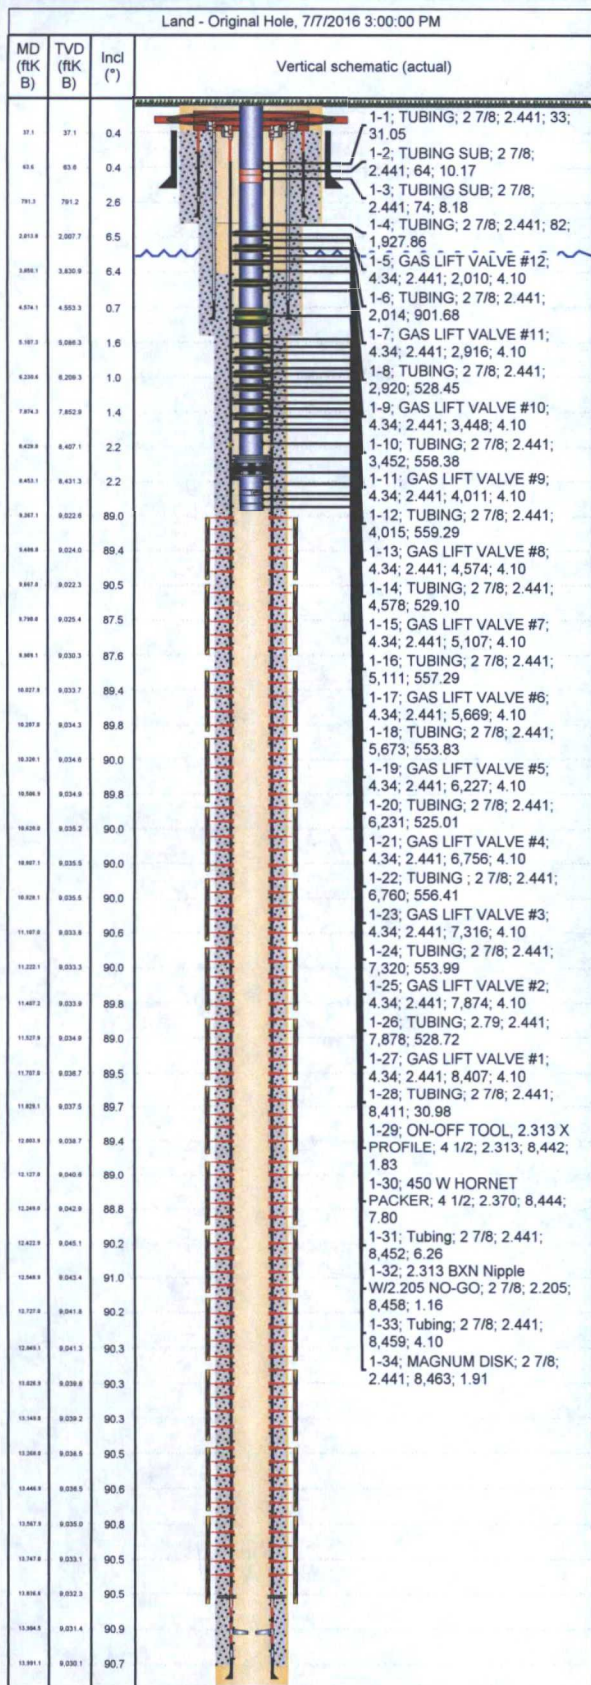


Tubing Strings										
Tubing Description TUBING		Planned Run? N		Set Depth (MD) (ftKB) 8,465.2			Set Depth (TVD) (ftKB) 8,443.4			
Run Date 7/7/2016		Run Job Complete, 6/12/2016 06:00		Pull Date			Pull Job			
Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Btm (ftKB)	
1	TUBING	2 7/8	2.441	6.50	L-80	8RD	31.05	32.6	63.6	
1	TUBING SUB	2 7/8	2.441	6.50	L-80	8RD	10.17	63.6	73.8	
1	TUBING SUB	2 7/8	2.441	6.50	L-80	8RD	8.18	73.8	82.0	
62	TUBING	2 7/8	2.441	6.50	L-80	8RD	1,927.86	82.0	2,009.8	
1	GAS LIFT VALVE #12	4.335	2.441			8RD	4.10	2,009.8	2,013.9	
17	TUBING	2 7/8	2.441	6.50	L-80	8RD	901.68	2,013.9	2,915.6	
1	GAS LIFT VALVE #11	4.335	2.441			8RD	4.10	2,915.6	2,919.7	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	528.45	2,919.7	3,448.1	
1	GAS LIFT VALVE #10	4.335	2.441			8RD	4.10	3,448.1	3,452.2	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	558.38	3,452.2	4,010.6	
1	GAS LIFT VALVE #9	4.335	2.441			8RD	4.10	4,010.6	4,014.7	
17	TUBING	2 7/8	2.441	6.50	L-80	8RD	559.29	4,014.7	4,574.0	
1	GAS LIFT VALVE #8	4.335	2.441			8RD	4.10	4,574.0	4,578.1	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	529.10	4,578.1	5,107.2	
1	GAS LIFT VALVE #7	4.335	2.441			8RD	4.10	5,107.2	5,111.3	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	557.29	5,111.3	5,668.6	
1	GAS LIFT VALVE #6	4.335	2.441			8RD	4.10	5,668.6	5,672.7	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	553.83	5,672.7	6,226.5	
1	GAS LIFT VALVE #5	4.335	2.441			8RD	4.10	6,226.5	6,230.6	
17	TUBING	2 7/8	2.441	6.50	L-80	8RD	525.01	6,230.6	6,755.6	
1	GAS LIFT VALVE #4	4.335	2.441			8RD	4.10	6,755.6	6,759.7	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	556.41	6,759.7	7,316.2	
1	GAS LIFT VALVE #3	4.335	2.441			8RD	4.10	7,316.2	7,320.3	
18	TUBING	2 7/8	2.441	6.50	L-80	8RD	553.99	7,320.3	7,874.2	
1	GAS LIFT VALVE #2	4.335	2.441			8TRD	4.10	7,874.2	7,878.3	
17	TUBING	2.785	2.441	6.50	L-80	8RD	528.72	7,878.3	8,407.1	
1	GAS LIFT VALVE #1	4.335	2.441			8RD	4.10	8,407.1	8,411.2	
1	TUBING	2 7/8	2.441	6.50	L-80	8RD	30.98	8,411.2	8,442.1	
1	ON-OFF TOOL, 2.313 X PROFILE	4 1/2	2.313			8RD	1.83	8,442.1	8,444.0	
1	450 W HORNET PACKER	4 1/2	2.370			8RD	7.80	8,444.0	8,451.8	
1	Tubing	2 7/8	2.441	6.50	L-80	8RD	6.26	8,451.8	8,458.0	
1	2.313 BXN Nipple W/2.205 NO-GO	2 7/8	2.205			8RD	1.16	8,458.0	8,459.2	



Tubing Summary

Well Name SALADO DRAW WE 23 FED P7 004H	Lease SD 23 FED P7	Field Name JENNINGS	Business Unit Mid-Continent	
Ground Elevation (ft) 3,165.00	Original RKB Elevation (ft) 3,197.60	Current RKB Elevation 3,197.60, 3/28/2016	Mud Line Elevation (ft)	Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)	

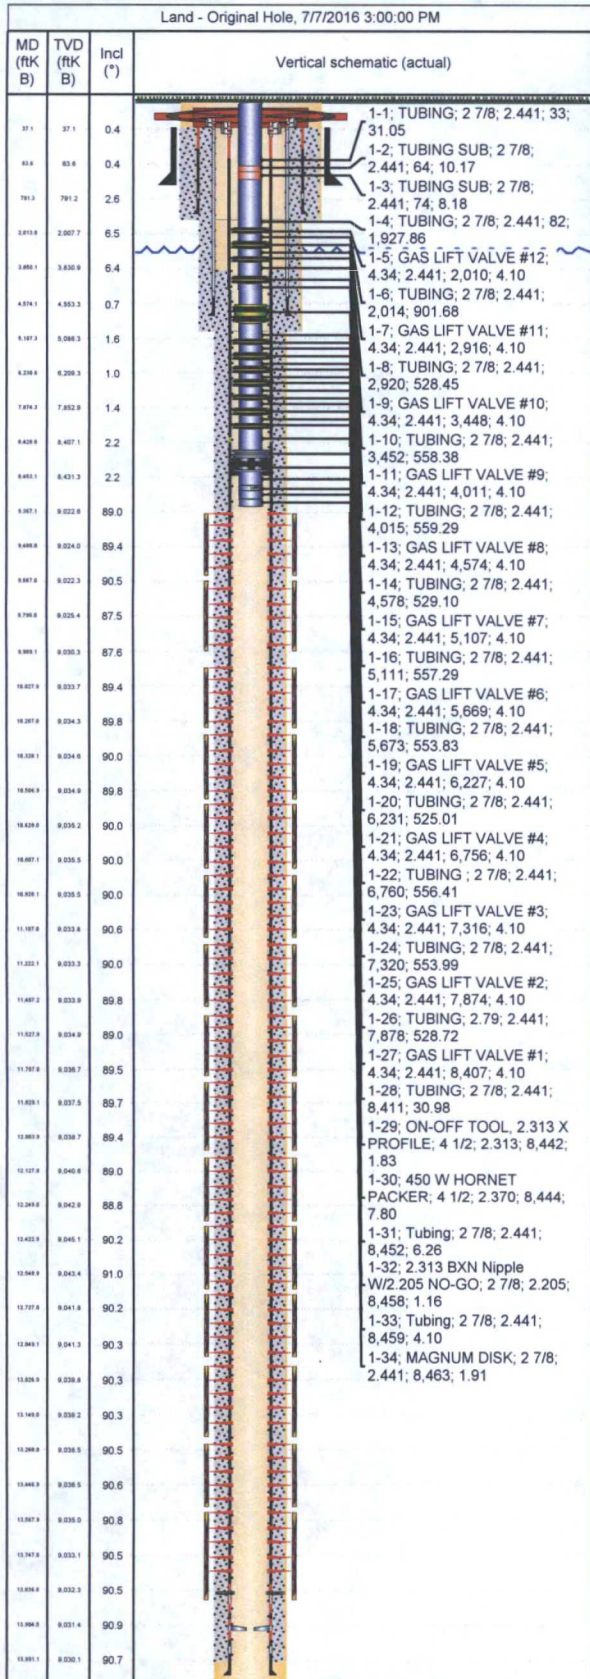

Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Btm (ftKB)
1	Tubing	2 7/8	2.441	6.50	L-80	8RD	4.10	8,459.2	8,463.3
1	MAGNUM DISK	2 7/8	2.441			8RD	1.91	8,463.3	8,465.2

Rod Strings			
Rod Description	Planned Run?	Set Depth (ftKB)	Set Depth (TVD) (ftKB)
Run Date	Run Job	Pull Date	Pull Job

Rod Components							
Jts	Item Des	OD (in)	Grade	Model	Len (ft)	Top (ftKB)	Btm (ftKB)
