




Tubing Summary

Well Name SALADO DRAW WE 14 FED P7 004H	Lease SD 14 FED P7	Field Name JENNINGS	Business Unit Mid-Continent	
Ground Elevation (ft) 3,165.00	Original RKB Elevation (ft) 3,197.60	Current RKB Elevation 3,197.60, 3/28/2016	Mud Line Elevation (ft)	Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)	

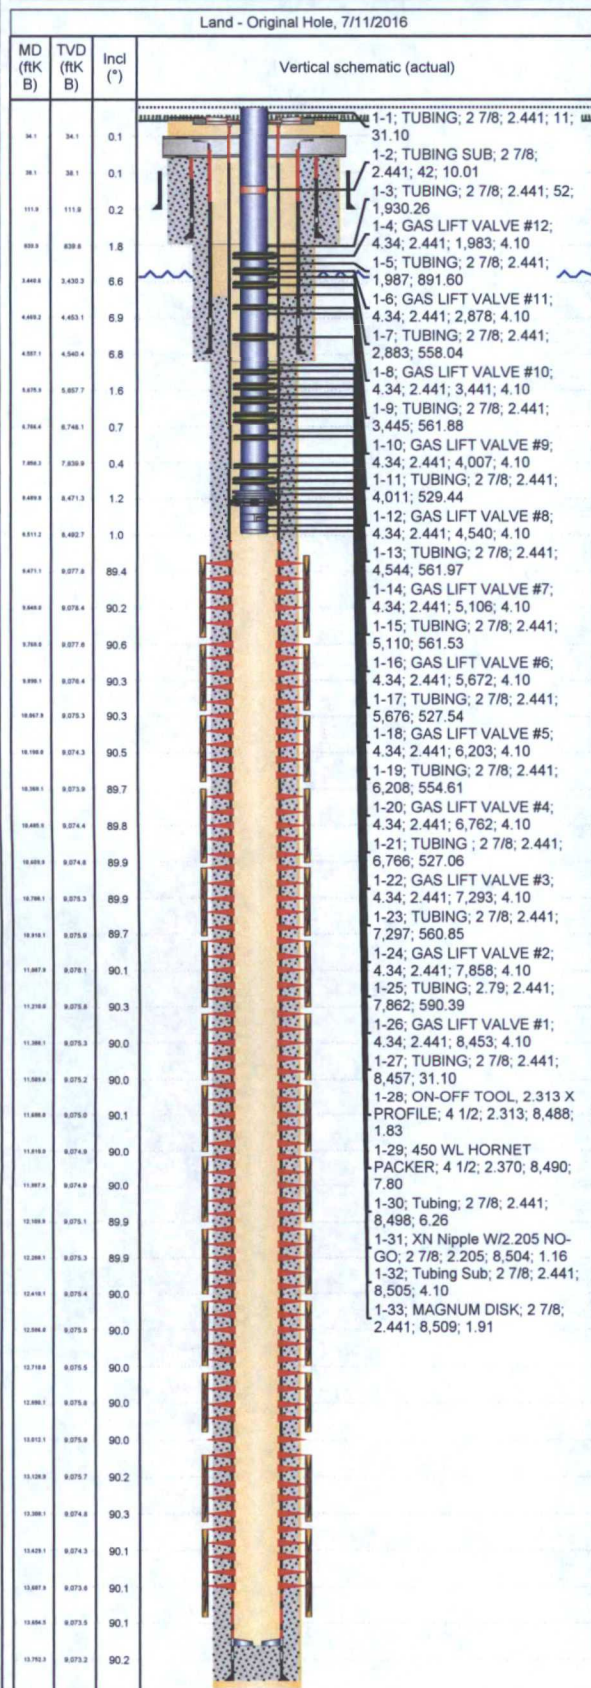

Tubing Strings									
Tubing Description Tubing - Production		Planned Run? N		Set Depth (MD) (ftKB) 8,511.0		Set Depth (TVD) (ftKB) 8,492.5			
Run Date 7/11/2016		Run Job Complete, 6/12/2016 06:00		Pull Date		Pull Job			
Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Btm (ftKB)
1	TUBING	2 7/8	2,441	6.50	L-80	8RD	31.10	11.4	42.5
1	TUBING SUB	2 7/8	2,441	6.50	L-80	8RD	10.01	42.5	52.5
62	TUBING	2 7/8	2,441	6.50	L-80	8RD	1,930.26	52.5	1,982.7
1	GAS LIFT VALVE #12	4.335	2,441			8RD	4.10	1,982.7	1,986.8
29	TUBING	2 7/8	2,441	6.50	L-80	8RD	891.60	1,986.8	2,878.4
1	GAS LIFT VALVE #11	4.335	2,441			8RD	4.10	2,878.4	2,882.5
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	558.04	2,882.5	3,440.6
1	GAS LIFT VALVE #10	4.335	2,441			8RD	4.10	3,440.6	3,444.7
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	561.88	3,444.7	4,006.6
1	GAS LIFT VALVE #9	4.335	2,441			8RD	4.10	4,006.6	4,010.7
17	TUBING	2 7/8	2,441	6.50	L-80	8RD	529.44	4,010.7	4,540.1
1	GAS LIFT VALVE #8	4.335	2,441			8RD	4.10	4,540.1	4,544.2
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	561.97	4,544.2	5,106.2
1	GAS LIFT VALVE #7	4.335	2,441			8RD	4.10	5,106.2	5,110.3
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	561.53	5,110.3	5,671.8
1	GAS LIFT VALVE #6	4.335	2,441			8RD	4.10	5,671.8	5,675.9
17	TUBING	2 7/8	2,441	6.50	L-80	8RD	527.54	5,675.9	6,203.4
1	GAS LIFT VALVE #5	4.335	2,441			8RD	4.10	6,203.4	6,207.5
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	554.61	6,207.5	6,762.1
1	GAS LIFT VALVE #4	4.335	2,441			8RD	4.10	6,762.1	6,766.2
17	TUBING	2 7/8	2,441	6.50	L-80	8RD	527.06	6,766.2	7,293.3
1	GAS LIFT VALVE #3	4.335	2,441			8RD	4.10	7,293.3	7,297.4
18	TUBING	2 7/8	2,441	6.50	L-80	8RD	560.85	7,297.4	7,858.3
1	GAS LIFT VALVE #2	4.335	2,441			8TRD	4.10	7,858.3	7,862.4
19	TUBING	2.785	2,441	6.50	L-80	8RD	590.39	7,862.4	8,452.7
1	GAS LIFT VALVE #1	4.335	2,441			8RD	4.10	8,452.7	8,456.8
1	TUBING	2 7/8	2,441	6.50	L-80	8RD	31.10	8,456.8	8,487.9
1	ON-OFF TOOL, 2.313 X PROFILE	4 1/2	2,313			8RD	1.83	8,487.9	8,489.8
1	450 WL HORNET PACKER	4 1/2	2,370			8RD	7.80	8,489.8	8,497.6
1	Tubing	2 7/8	2,441	6.50	L-80	8RD	6.26	8,497.6	8,503.8
1	XN Nipple W/2.205 NO-GO	2 7/8	2,205			8RD	1.16	8,503.8	8,505.0
1	Tubing Sub	2 7/8	2,441	6.50	L-80	8RD	4.10	8,505.0	8,509.1
1	MAGNUM DISK	2 7/8	2,441			8RD	1.91	8,509.1	8,511.0



Tubing Summary

Well Name SALADO DRAW WE 14 FED P7 004H	Lease SD 14 FED P7	Field Name JENNINGS	Business Unit Mid-Continent	
Ground Elevation (ft) 3,165.00	Original RKB Elevation (ft) 3,197.60	Current RKB Elevation 3,197.60, 3/28/2016	Mud Line Elevation (ft)	Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)	

Land - Original Hole, 7/11/2016				Vertical schematic (actual)	
MD (ftK B)	TVD (ftK B)	Incl (°)			
36.1	34.1	0.1			1-1; TUBING; 2 7/8; 2.441; 11; 31.10
36.1	36.1	0.1			1-2; TUBING SUB; 2 7/8; 2.441; 42; 10.01
111.9	111.9	0.2			1-3; TUBING; 2 7/8; 2.441; 52; 1,930.26
808.9	808.8	1.8			1-4; GAS LIFT VALVE #12; 4.34; 2.441; 1,983; 4.10
848.8	843.3	6.6			1-5; TUBING; 2 7/8; 2.441; 1,987; 891.60
848.2	843.1	6.9			1-6; GAS LIFT VALVE #11; 4.34; 2.441; 2,878; 4.10
4387.1	4340.4	6.8			1-7; TUBING; 2 7/8; 2.441; 2,883; 558.04
8475.9	8387.7	1.6			1-8; GAS LIFT VALVE #10; 4.34; 2.441; 3,441; 4.10
8788.6	8748.1	0.7			1-9; TUBING; 2 7/8; 2.441; 3,445; 561.88
7888.3	7838.9	0.4			1-10; GAS LIFT VALVE #9; 4.34; 2.441; 4,007; 4.10
8488.9	8471.3	1.2			1-11; TUBING; 2 7/8; 2.441; 4,011; 529.44
8511.2	8492.7	1.0			1-12; GAS LIFT VALVE #8; 4.34; 2.441; 4,540; 4.10
8471.1	8377.8	89.4			1-13; TUBING; 2 7/8; 2.441; 4,544; 561.97
8488.9	8378.4	90.2			1-14; GAS LIFT VALVE #7; 4.34; 2.441; 5,106; 4.10
8788.6	8377.8	90.6			1-15; TUBING; 2 7/8; 2.441; 5,110; 561.53
9088.1	8378.4	90.3			1-16; GAS LIFT VALVE #6; 4.34; 2.441; 5,672; 4.10
10387.8	8378.3	90.3			1-17; TUBING; 2 7/8; 2.441; 5,676; 527.54
10188.8	8374.3	90.5			1-18; GAS LIFT VALVE #5; 4.34; 2.441; 6,203; 4.10
10388.1	8373.9	89.7			1-19; TUBING; 2 7/8; 2.441; 6,208; 554.61
10488.9	8374.4	89.8			1-20; GAS LIFT VALVE #4; 4.34; 2.441; 6,762; 4.10
10488.9	8374.6	89.9			1-21; TUBING; 2 7/8; 2.441; 6,766; 527.06
10788.1	8373.3	89.9			1-22; GAS LIFT VALVE #3; 4.34; 2.441; 7,293; 4.10
10818.1	8375.9	89.7			1-23; TUBING; 2 7/8; 2.441; 7,297; 560.85
11387.8	8376.1	90.1			1-24; GAS LIFT VALVE #2; 4.34; 2.441; 7,858; 4.10
11218.8	8375.8	90.3			1-25; TUBING; 2 7/8; 2.441; 7,862; 590.39
11388.1	8376.3	90.0			1-26; GAS LIFT VALVE #1; 4.34; 2.441; 8,453; 4.10
11588.9	8375.2	90.0			1-27; TUBING; 2 7/8; 2.441; 8,457; 31.10
11688.0	8375.0	90.1			1-28; ON-OFF TOOL, 2.313 X PROFILE; 4 1/2; 2.313; 8,488; 1.83
11818.8	8374.9	90.0			1-29; 450 WL HORNET PACKER; 4 1/2; 2.370; 8,490; 7.80
12188.8	8375.1	89.9			1-30; Tubing; 2 7/8; 2.441; 8,498; 6.26
12388.1	8376.3	89.9			1-31; XN Nipple W/2.205 NO-GO; 2 7/8; 2.205; 8,504; 1.16
12418.1	8376.4	90.0			1-32; Tubing Sub; 2 7/8; 2.441; 8,505; 4.10
12888.8	8375.9	90.0			1-33; MAGNUM DISK; 2 7/8; 2.441; 8,509; 1.91
12718.9	8375.9	90.0			
12888.1	8376.8	90.0			
13018.1	8375.9	90.0			
13138.8	8375.7	90.2			
13288.1	8374.8	90.3			
13428.1	8374.3	90.1			
13687.8	8373.8	90.1			
13888.9	8373.5	90.1			
13782.8	8373.2	90.2			

Rod Strings			
Rod Description	Planned Run?	Set Depth (ftKB)	Set Depth (TVD) (ftKB)
Run Date	Run Job	Pull Date	Pull Job

Rod Components							
Jts	Item Des	OD (in)	Grade	Model	Len (ft)	Top (ftKB)	Btm (ftKB)
