




Tubing Summary

Well Name SALADO DRAW EA 19 FED P6 006H	Lease Salado Draw EA 19 Fed P6	Field Name WILDCAT (HOBBS)	Business Unit Mid-Continent
Ground Elevation (ft) 3,205.00	Original RKB Elevation (ft) 3,237.60	Current RKB Elevation 3,237.60, 12/15/2015	Mud Line Elevation (ft) Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)

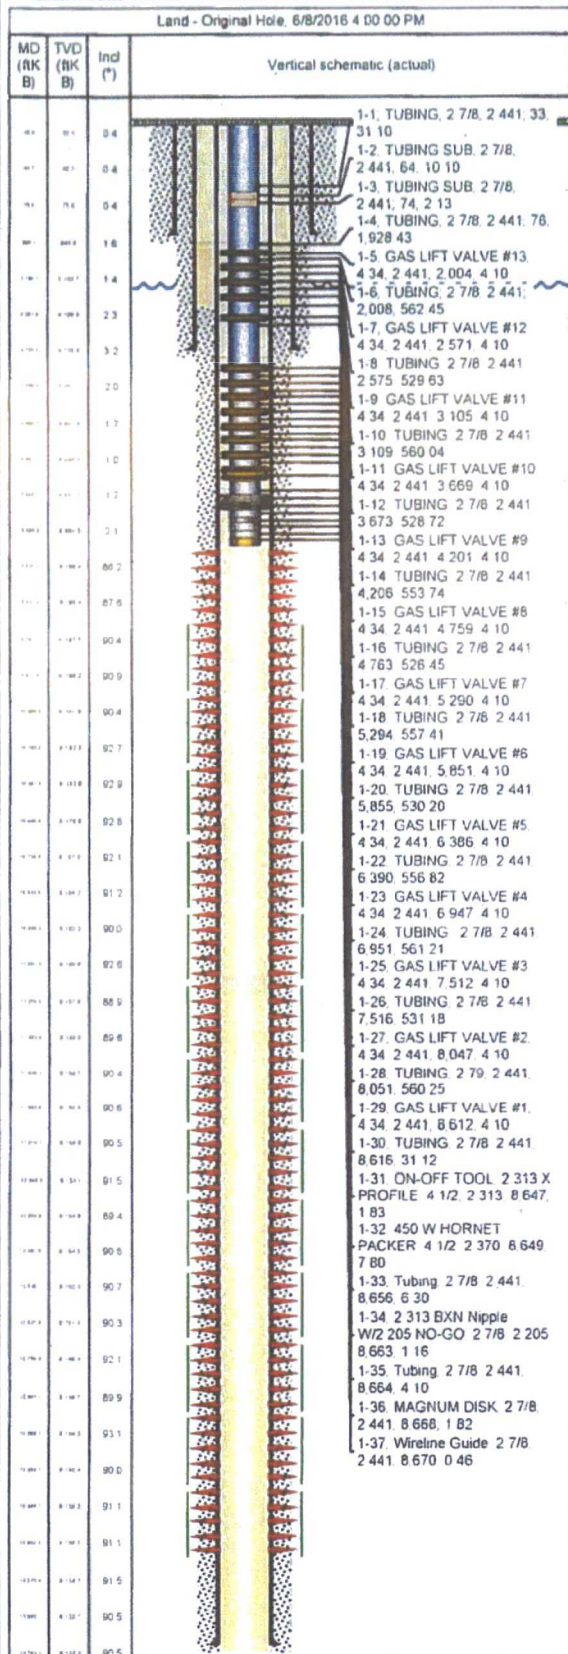


Tubing Strings									
Tubing Description		Planned Run		Set Depth (MD) (ft)		Set Depth (TVD) (ft)		Run Date	
Tubing - Production		N		8,670.3		8,666.8		6/8/2016	
Run Date		Run Job		Pull Date		Pull Job			
6/8/2016		Complete, 4/20/2016 00:00							
Jts	Item Des	OD (in)	ID (in)	WT (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Blm (ftKB)
1	TUBING	2 7/8	2 441	6.50	L-80	8RD	31 10	32.5	63.6
1	TUBING SUB	2 7/8	2 441	6.50	L-80	8RD	10 10	63.6	73.7
1	TUBING SUB	2 7/8	2 441	6.50	L-80	8RD	2 13	73.7	75.8
62	TUBING	2 7/8	2 441	6.50	L-80	8RD	1,928.4 3	75.8	2,004.3
1	GAS LIFT VALVE #13	4 335	2 441			8RD	4 10	2,004.3	2,008.4
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	562.45	2,008.4	2,570.8
1	GAS LIFT VALVE #12	4 335	2 441			8RD	4 10	2,570.8	2,574.9
17	TUBING	2 7/8	2 441	6.50	L-80	8RD	529.63	2,574.9	3,104.5
1	GAS LIFT VALVE #11	4 335	2 441			8RD	4 10	3,104.5	3,108.6
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	560.04	3,108.6	3,668.7
1	GAS LIFT VALVE #10	4 335	2 441			8RD	4 10	3,668.7	3,672.8
17	TUBING	2 7/8	2 441	6.50	L-80	8RD	528.72	3,672.8	4,201.5
1	GAS LIFT VALVE #9	4 335	2 441			8RD	4 10	4,201.5	4,205.6
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	553.74	4,205.6	4,759.3
1	GAS LIFT VALVE #8	4 335	2 441			8RD	4 10	4,759.3	4,763.4
17	TUBING	2 7/8	2 441	6.50	L-80	8RD	526.45	4,763.4	5,289.9
1	GAS LIFT VALVE #7	4 335	2 441			8RD	4 10	5,289.9	5,294.0
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	557.41	5,294.0	5,851.4
1	GAS LIFT VALVE #6	4 335	2 441			8RD	4 10	5,851.4	5,855.5
17	TUBING	2 7/8	2 441	6.50	L-80	8RD	530.20	5,855.5	6,385.7
1	GAS LIFT VALVE #5	4 335	2 441			8RD	4 10	6,385.7	6,389.8
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	556.82	6,389.8	6,946.6
1	GAS LIFT VALVE #4	4 335	2 441			8RD	4 10	6,946.6	6,950.7
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	561.21	6,950.7	7,511.9
1	GAS LIFT VALVE #3	4 335	2 441			8RD	4 10	7,511.9	7,516.0
17	TUBING	2 7/8	2 441	6.50	L-80	8RD	531.18	7,516.0	8,047.2
1	GAS LIFT VALVE #2	4 335	2 441			8TRD	4 10	8,047.2	8,051.3
18	TUBING	2 7/8	2 441	6.50	L-80	8RD	560.25	8,051.3	8,611.6
1	GAS LIFT VALVE #1	4 335	2 441			8RD	4 10	8,611.6	8,615.7
1	TUBING	2 7/8	2 441	6.50	L-80	8RD	31.12	8,615.7	8,646.8
1	ON-OFF TOOL, 2 313 X PROFILE	4 1/2	2 313			8RD	1.83	8,646.8	8,648.6
1	450 W HORNET PACKER	4 1/2	2 370			8RD	7.80	8,648.6	8,656.4
1	Tubing	2 7/8	2 441	6.40	L-80	8RD	6.30	8,656.4	8,662.7



Tubing Summary

Well Name SALADO DRAW EA 19 FED P6 006H	Lease Salado Draw EA 19 Fed P6	Field Name WILDCAT (HOBBS)	Business Unit Mid-Continent	
Ground Elevation (ft) 3,205.00	Original RKB Elevation (ft) 3,237.60	Current RKB Elevation 3,237.60, 12/15/2015	Mud Line Elevation (ft)	Water Depth (ft)
Current KB to Ground (ft) 32.60	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)	

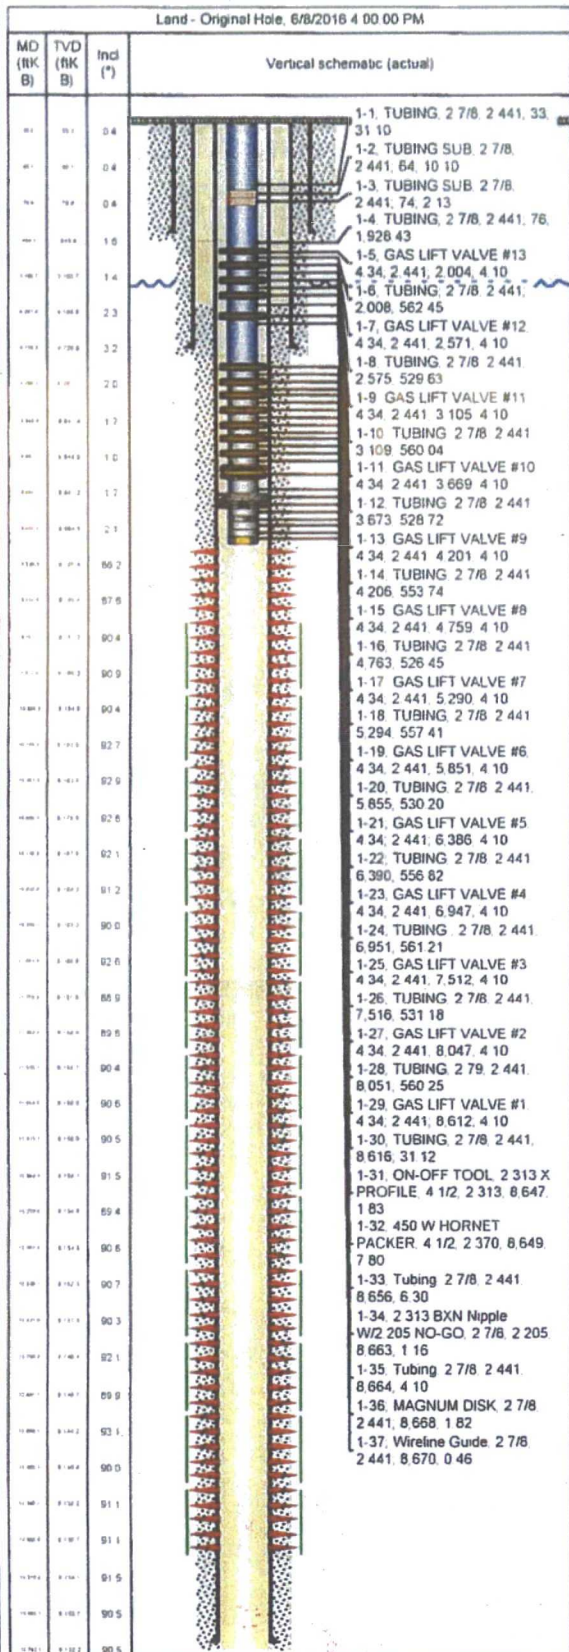

Jts	Item Des	OD (in)	ID (in)	WI (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Btm (ftKB)
1	2 313 BXN Nipple W/2 205 NO-GO	2 7/8	2 205			8RD	1.16	8,662.7	8,663.9
1	Tubing	2 7/8	2 441	6.40	L-80	8RD	4.10	8,663.9	8,668.0
1	MAGNUM DISK	2 7/8	2 441			8RD	1.82	8,668.0	8,669.8
1	Wireline Guide	2 7/8	2 441			8RD	0.46	8,669.8	8,670.3

Rod Strings

Red Description	Planned Run?	Set Depth (ftKB)	Set Depth (TVD) (ftKB)
Run Date	Run Job	Pull Date	Pull Job

Rod Components

Jts	Item Des	OD (in)	Grade	Model	Len (ft)	Top (ftKB)	Btm (ftKB)
-----	----------	---------	-------	-------	----------	------------	------------
