

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENTFORM APPROVED  
OMB NO. 1004-0137  
Expires: January 31, 2018**SUNDRY NOTICES AND REPORTS**  
*Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.*Lease Serial No.  
MCC068037

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.

8. Well Name and No.  
MESCALERO 29 FEDERAL 29. API Well No.  
30-025-3597210. Field and Pool or Exploratory Area  
GEM; STRAWN, EAST11. County or Parish, State  
LEA COUNTY, NM

SUBMIT IN TRIPLICATE - Other instructions on page 2

## 1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

## 2. Name of Operator

CIMAREX ENERGY CO. OF COLORADO

Contact: AMITHY CRAWFORD

Email: acrawford@cimarex.com

## 3a. Address

202 S. CHEYENNE AVE, STE 1000  
TULSA, OK 74103

## 3b. Phone No. (include area code)

Ph: 432-620-1909

## 4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 26 T19S R34E 1200FNL 1700FEL

## 12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Hydraulic Fracturing	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input checked="" type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

Cimarex respectfully requests to plugback the Morrow formation and recompleat into the Strawn zone. see procedure below.

Notify BLM 24 hours prior to starting operations  
Max Treating Pressure = 8,500 psi

1. Hold operational safety meeting on location; discuss all risk and potential dangers.
2. MIRU Pulling unit.
3. Kill well if necessary w/ 2% KCL.
4. Unset Versa set packer @ 13,150'.
5. TOOH w/ 2-3/8" tbg.
6. PU 4-3/4" bit and 5-1/2" casing scraper. RIH to 13,300'.

SEE ATTACHED FOR  
CONDITIONS OF APPROVAL

14. I hereby certify that the foregoing is true and correct.

Electronic Submission #377286 verified by the BLM Well Information System  
For CIMAREX ENERGY CO. OF COLORADO, sent to the Hobbs  
Committed to AFMSS for processing by DEBORAH MCKINNEY on 05/30/2017 ( )

Name (Printed/Typed) AMITHY CRAWFORD

Title REGULATORY ANALYST

Signature (Electronic Submission)

Date 05/25/2017

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By Mustafa Hague

Title PETROLEUM ENGINEER

Date 8-1-2017

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office CPO

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

\*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\*

**Additional data for EC transaction #377286 that would not fit on the form**

**32. Additional remarks, continued**

7. TOOH, LD bit and scraper. PU 5-1/2" CIBP.
8. TIH to 13,300' and set CIBP. *Pump 25 sacks of C/S H cement on top of CIBP.*
9. Release from the CIBP and PU 1 joint, Circulate well w/ 375 bbls of 2% KCL.
10. TOOH w/ 2-3/8" tbg and LD.
11. Pressure test casing to Max Treating Pressure: 8,500 psi. Hold for 30 minutes.
  - a. Bleed off pressure after 30 minutes.
12. RU WL. RIH w/ 4" Select fire perforating guns and a gamma ray gun.
  - a. Correlate gamma ray back to Halliburton "Cement Bond/Gamma Ray/Collar Log" dated 01-21-04 @ 18:00
13. Perforate the Strawn, 12,234' - 12,337' w/ 0.41" EH, 120-degree phasing, and 29 total shots.
14. RD WL. RU Frac Crew and pressure test lines to MTP: 8,500 psi.
15. Frac the perforated interval w/ 300,000 lbs of proppant and 234,260 gals of slickwater with 17# linear gel and 17# XL borate.
16. RU flowback equipment in such a way that production can be turned to the battery once hydrocarbons are detected.
17. Flowback well until it dies (if at all).
18. Set pumping unit. RIH w/ tbg and rods.
19. Return to production.




20" csg @ 40'  
Cmt w/4 yds cement

13 3/8" 54.5# J55 csg @ 429'  
Cmt w/490 sx, circ to surface

9 5/8" 40# P110 csg @ 3440'  
Cmt w/1200 sx, circ to surface

5 1/2" 17# P110 csg @ 13,768'  
Cmt w/3700 sx circ to surface

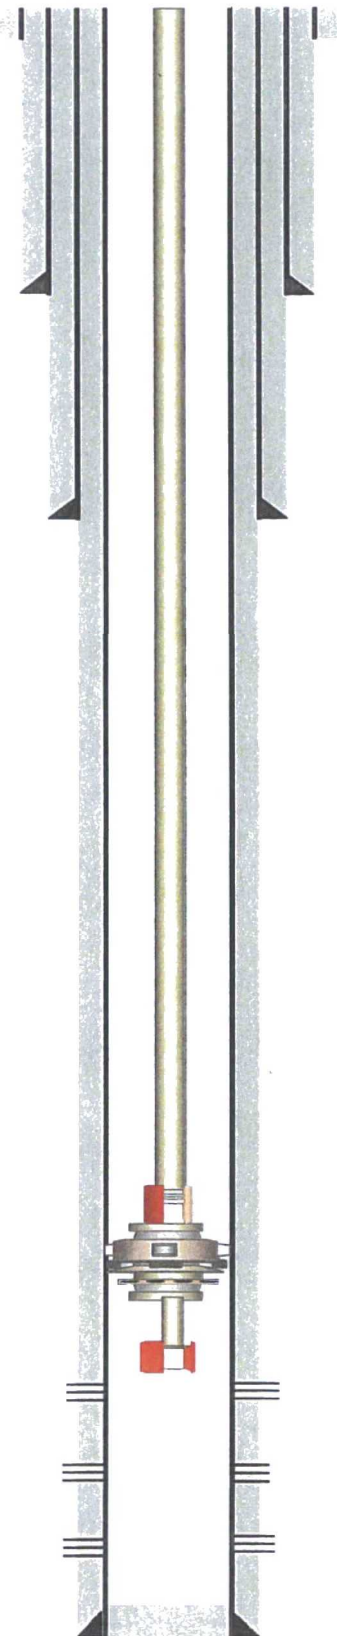

PBTD: 13,698'  
TD: 13,770'

**Cimarex Energy Co. of Colorado**  
**MESCALERO "29" FED COM #2**

API 30-025-35972  
1200' FNL & 1700' FEL, Sec 29, T19S R34E  
Lea County, NM  
GL 3697' KB 3720'

## CURRENT

17 1/2" hole to 429'

12 1/4" hole to 3440'

DV tool @ 4649'

Packer Set @13,150'

Morrow Perfs  
13,320'-25', 13,222'-32, 13,329'-38', 13,343'-45'  
13,509'-16', 13,521'-29' (5/04)

8 3/4" hole to TD 13,770'






20" csg @ 40'  
Cmt w/4 yds cement

13 3/8" 54.5# J55 csg @ 429'  
Cmt w/490 sx, circ to surface

9 5/8" 40# P110 csg @ 3440'  
Cmt w/1200 sx, circ to surface

5 1/2" 17# P110 csg @ 13,768'  
Cmt w/3700 sx circ to surface

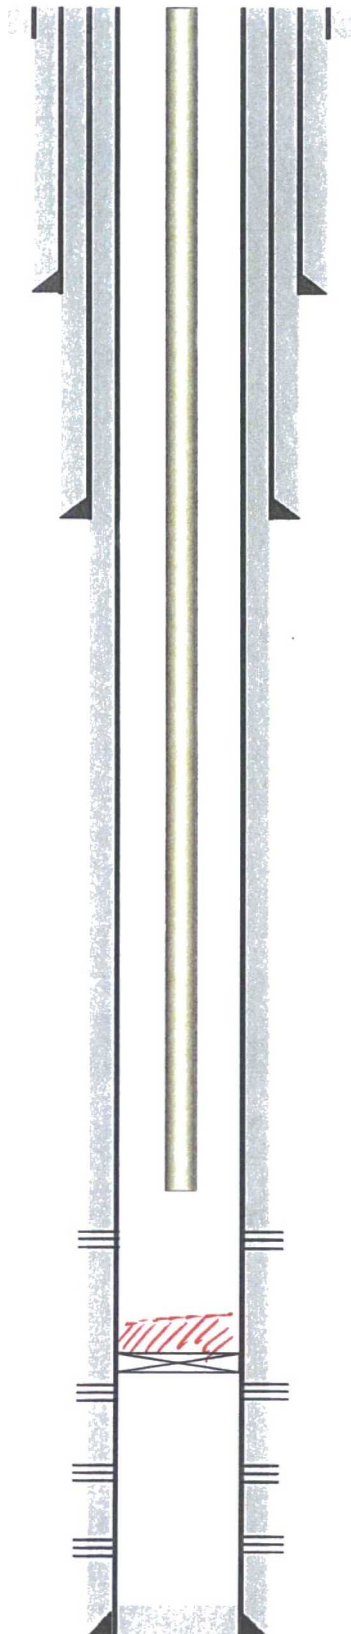

PBTD: 13,698'  
TD: 13,770'

**Cimarex Energy Co. of Colorado**  
**MESCALERO "29" FED COM #2**

API 30-025-35972  
1200' FNL & 1700' FEL, Sec 29, T19S R34E  
Lea County, NM  
GL 3697' KB 3720'

## PROPOSED

17 1/2" hole to 429'

12 1/4" hole to 3440'

DV tool @ 4649'

Strawn Perfs  
12,234' - 12,337'

*CIBP Set @ 13,300'. 25 sacks of C15 H cement  
on top of CIBP - WOC & Tag*

Morrow Perfs  
13,320'-25', 13,222'-32, 13,329'-38', 13,343'-45'  
13,509'-16', 13,521'-29' (5/04)

8 3/4" hole to TD 13,770'



AFE No:

**Procedure Sheet – Hobbs District**  
PLEASE COMMENCE WITH WORK PER PROCEDURE

**Mecalero 29 Federal Com 2**  
Recomplete Well in Strawn Sand

Current Well Data:

KB 23' above GL  
TVD/PBTD 13,770'/13,698'  
KOP N/A Vertical Well  
Perfs Morrow (13,320' - 13,529')

Casing Size	Weight	Grade	Thread	Set at	Cmt	Remarks
13 3/8"	54.5#	J-55	ST&C	429'	490	TOC - SURF
9 5/8"	40#	P110	LT&C	3440'	1200	TOC - SURF
5 1/2"	17#	P110	LT&C	13768'	2440	TOC - SURF

Tubing 415 jts of 2-3/8" 4.7# L80 8rd  
Packer 5-1/2" Versa Set Packer @ 13,150'

Procedure:

**Notify BLM 24 hours prior to starting operations**  
**Max Treating Pressure = 8,500 psi**

1. Hold operational safety meeting on location; discuss all risk and potential dangers.
2. MIRU Pulling unit.
3. Kill well if necessary w/ 2% KCL.
4. Unset Versa set packer @ 13,150'.
5. TOOH w/ 2-3/8" tbg.
6. PU 4-3/4" bit and 5-1/2" casing scraper. RIH to 13,300'.
7. TOOH, LD bit and scraper. PU 5-1/2" CIBP.
8. TIH to 13,300' and set CIBP. *ump 25 sacks of C1S H cement on top of CIBP*
9. Release from the CIBP and PU 1 joint, Circulate well w/ 375 bbls of 2% KCL.
10. TOOH w/ 2-3/8" tbg and LD.
11. Pressure test casing to **Max Treating Pressure: 8,500 psi**. Hold for 30 minutes.
  - a. Bleed off pressure after 30 minutes.
12. RU WL. RIH w/ 4" Select fire perforating guns and a gamma ray gun.



AFE No:

- a. Correlate gamma ray back to Halliburton "Cement Bond/Gamma Ray/Collar Log"  
dated 01-21-04 @ 18:00
13. Perforate the Strawn, 12,234' – 12,337' w/ 0.41" EH, 120-degree phasing, and 29 total shots.
14. RD WL. RU Frac Crew and pressure test lines to **MTP: 8,500 psi**.
15. Frac the perforated interval w/ 300,000 lbs of proppant and 234,260 gals of slickwater with 17# linear gel and 17# XL borate.
16. RU flowback equipment in such a way that production can be turned to the battery once hydrocarbons are detected.
17. Flowback well until it dies (if at all).
18. Set pumping unit. RIH w/ tbg and rods.
19. Return to production.

**Mescalero 29 Federal 2**  
**30-025-35972**  
**Cimarex Energy**  
**Conditions of Approval**

Timing Limitation Stipulation / Condition of Approval for lesser prairie-chicken:

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually.

During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 feet from the source of the noise. Exceptions to these restrictions may be granted by BLM's Cassandra Brooks <crbrooks@blm.gov> 575.234.2232

**Notify BLM at 575-393-3612 (Lea County) a minimum of 24 hours prior to commencing work.**

**Work to be completed by November 01, 2017.**

1. Must conduct a casing integrity test before perforating and fracturing. Submit results to BLM. The CIT is to be performed on the production casing to max treating pressure. Notify BLM if test fails.
2. Before casing or a liner is added or replaced, prior BLM approval of the design is required. Use notice of intent Form 3160-5.
3. Surface disturbance beyond the originally approved pad must have prior approval.
4. Closed loop system required.
5. All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of work over operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



6. Operator to have H2S monitoring equipment on location.
7. A minimum of a 2000 (2M) BOP to be used. All blowout preventer (BOP) and related equipment (BOPE) shall comply with reasonable well control requirements. A two ram system with a blind ram and a pipe ram designed for the size of the work string shall be adequate. Tapered work strings will require an additional pipe ram. The manifold shall comply with Onshore Oil and Gas Order #2 Attachment I (2M Diagrams of Choke Manifold Equipment). The accumulator system shall have an immediately available power source to close the rams and retain 200 psi above pre-charge. The pre-charge test shall follow requirements in Onshore Order #2.
8. **Subsequent sundry required detailing work done, a C-102 form, and completion report for the new formations. Operator to include well bore schematic of current well condition when work is complete.**
9. **See attached for General Plugback Guidelines**

**MHH 08012017**



**BUREAU OF LAND MANAGEMENT**  
**Carlsbad Field Office**  
**620 East Greene Street**  
**Carlsbad, New Mexico 88220**  
**575-234-5972**

**Permanent Abandonment of Production Zone Conditions of Approval**

Failure to comply with the following Conditions of Approval may result in a Notice of Incidents of Noncompliance (INC) in accordance with 43 CFR 3163.1.

1. Plug back operations shall commence within **ninety (90)** days from this approval. **If you are unable to plug back the well by the 90<sup>th</sup> day provide this office, prior to the 90<sup>th</sup> day, with the reason for not meeting the deadline and a date when we can expect the well to be plugged back. Failure to do so will result in enforcement action.**
  2. **Notification:** Contact the appropriate BLM office at least 24 hours prior to the commencing of any plug back operations. For wells in Eddy County, call 575-361-2822. For wells in Lea County, call 575-393-3612
  3. **Blowout Preventers:** A blowout preventer (BOP), as appropriate, shall be installed before commencing any plugging operation. The BOP must be installed and maintained as per API and manufacturer recommendations. The minimum BOP requirement is a 2M system for a well not deeper than 9,090 feet; a 3M system for a well not deeper than 13,636 feet; and a 5M system for a well not deeper than 22,727 feet.
  4. **Mud Requirement:** Mud shall be placed between all plugs. Minimum consistency of plugging mud shall be obtained by mixing at the rate of 25 sacks (50 pounds each) of gel per 100 barrels of **brine** water. Minimum nine (9) pounds per gallon.
  5. **Cement Requirement:** Sufficient cement shall be used to bring any required plug to the specified depth and length. Any given cement volumes on the proposed plugging procedure are merely estimates and are not final. Unless specific approval is received, no plug except the surface plug shall be less than 25 sacks of cement. Any plug that requires a tag will have a minimum WOC time of 4 hours.  
In lieu of a cement plug across perforations in a cased hole (not for any other plugs), a bridge plug set within 50 feet to 100 feet above the perforations shall be capped with 25 sacks of cement.  
**Before pumping cement on top of CIBP, tag will be required to verify depth. Based on depth, a tag of the cement may be deemed necessary.**
- Unless otherwise specified in the approved procedure, the cement plug shall consist of either **Neat Class "C"**, for up to 7,500 feet of depth or **Neat Class "H"**, for deeper than 7,500 feet plugs.
6. **Subsequent Plug back Reporting:** Within 30 days after plug back work is completed, file one original and three copies of the Subsequent Report, Form 3160-5 to BLM. The report should give in detail the manner in which the plug back work was carried out, the extent (by depths) of cement plugs placed, and the size and location (by depths) of casing left in the well. **Show date work was completed.** If plugging back to a new zone submit a Completion Report, form 3160-4 with the Subsequent Report.
  7. **Trash:** All trash, junk and other waste material shall be contained in trash cages or bins to prevent scattering and will be removed and deposited in an approved sanitary landfill. Burial on site is not permitted.
