


TEST DEPTH: 4,246 FEET
TEST DATE: FEB. 5, 1971

TIME	P.S.I. @ 4246 FEET	REMARKS
9:45 A.M.	1277	
10:00	1277	GAUGE REACHED 4246 FEET
10:15	1277	
10:30	1271	WELL OPENED
10:45	1268	
11:00	1259	
11:15	1232	
11:30	1206	
11:45 A.M.	1131	
12:00 NOON	1136	


TIME	P.S.I. @ 4246 FEET	REMARKS
12:10 P.M.	1062	
12:15	1061	
12:25	1061	1ST RATE
12:35	1101	
12:45	1141	
1:00	1141	2ND RATE
1:15	1176	
1:30	1176	3RD RATE
1:45	1216	
2:00 P.M.	1216	4TH RATE, GAUGE OUT, END TEST

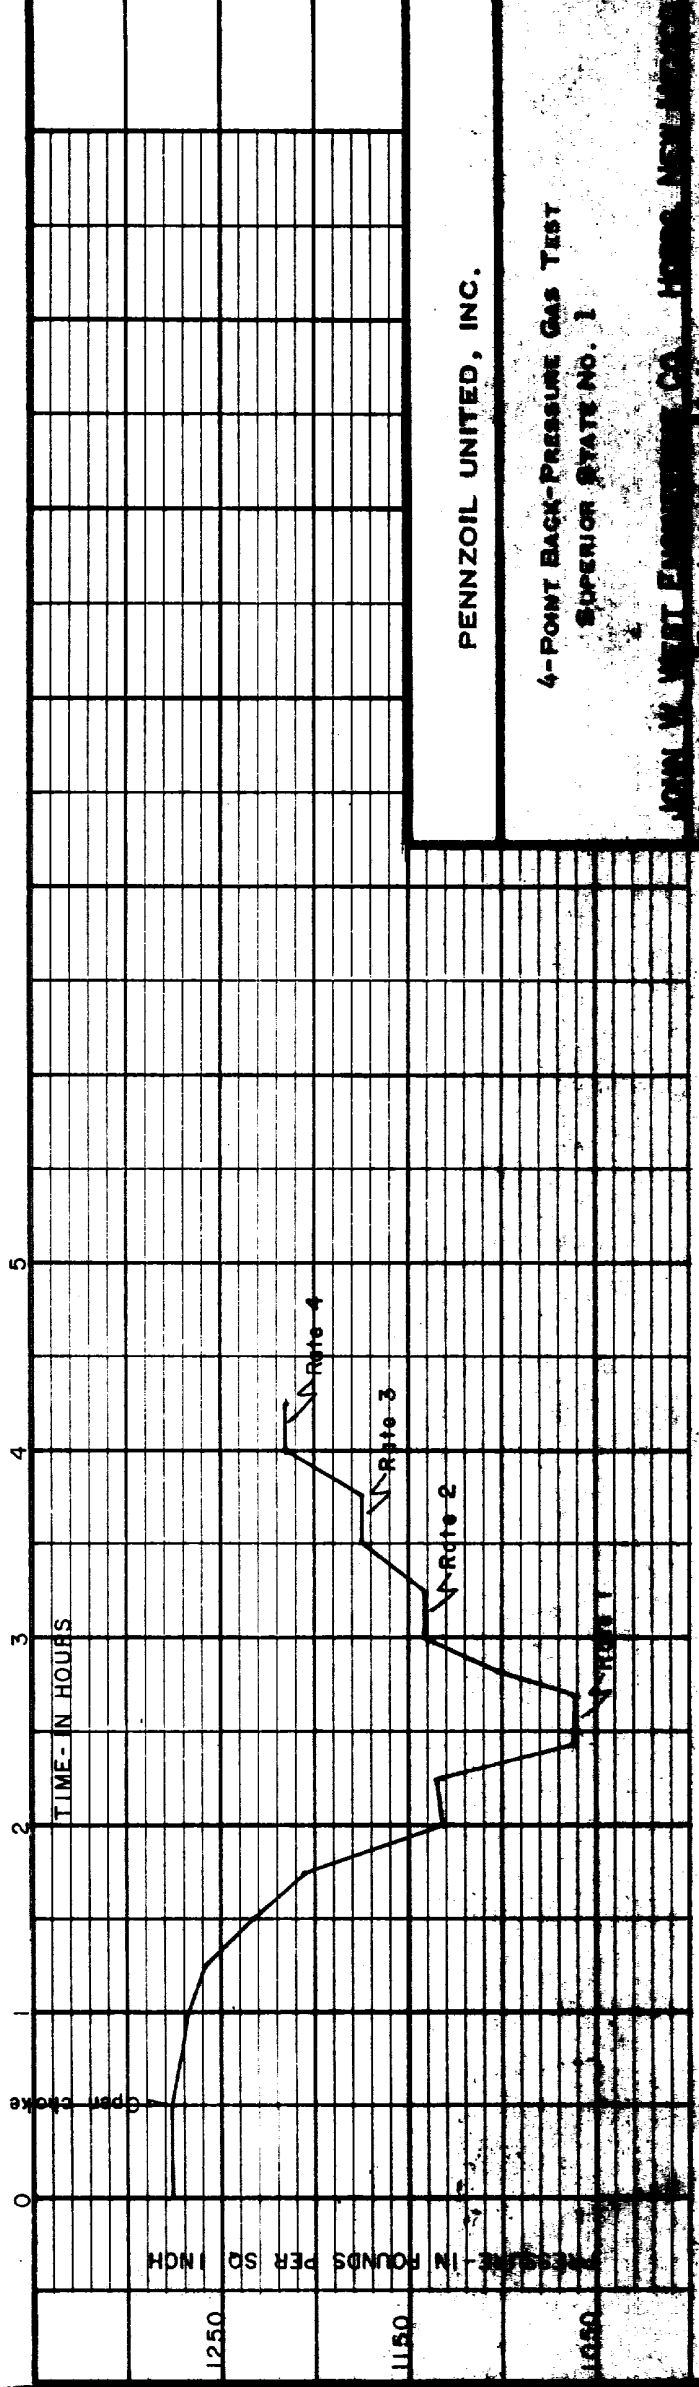

PENNZOIL UNITED, INC.

4-POINT BACK-PRESSURE GAS TEST
SUPERIOR STATE NO. 1

JOHN W. WEST ENGINEERING CO. HOUSTON, NEW HAMPSHIRE
Form 2-5-71 (Revised 1-1-71)



LTR



Job separation sheet

BOTTOM HOLE PRESSURE SURVEY REPORT

OPERATOR PENNZOIL UNITED, INC.
LEASE SUPERIOR STATE
WELL NO. 1
FIELD WILDCAT
DATE 2-4-71 TIME 10:00 A.M.
STATUS SHUT-IN TEST DEPTH 4,246'
TIME S.I. LAST TEST DATE
CAS. PRES. BHP LAST TEST
TUB. PRES. 1116# BHP CHANGE
ELEV. FLUID TOP
DATUM WATER TOP
TEMP 108°F. RUN BY A. ALLMAN
CLOCK NO. 4052 GAUGE NO. 12434
ELEMENT NO. 16531-N

DEPTH	PRESSURE	GRADIENT
000	1116	
2000	1192	.038
3000	1230	.038
4000	1269	.039
4246	1277	.039

