


ASHLAND PIPE LINE COMPANY ENGINEERING DEPARTMENT			SHEET
			AFE
SUBJECT SALINE NO. 1 BRINE WELL SECTION 36, 18S, 37E., LCA Co. NMPM			DISTRICT
			DRAWING
BY S. ROGERS.	CHECKED BY	APPROVED BY	DATE 7/29/94

0427-6 (02/91)

API #30-02S-12803
SALINE NO. 1 BRINE WELL
AS COMPLETED 7/22/94

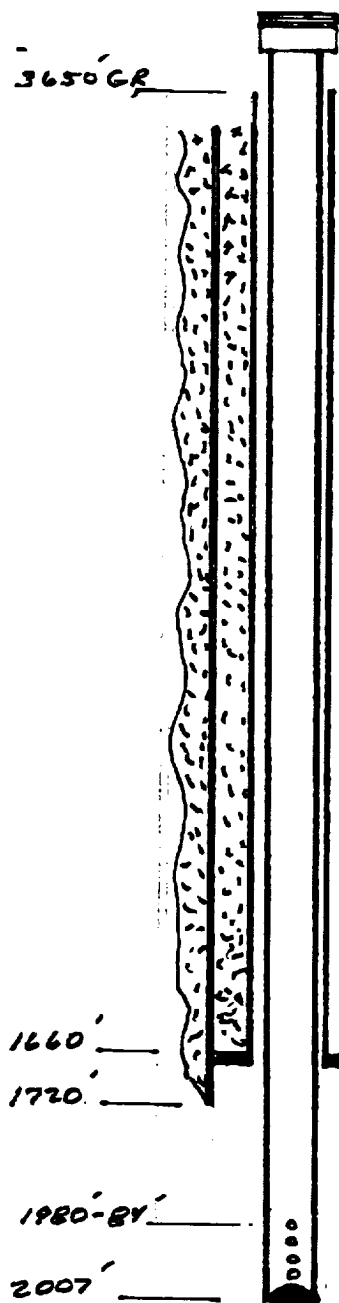

1660' - FORMATION PACKER SHOES, FLOAT COLLAR, 5 1/2" 15.5# J-55 CASING CEMENT W/200 SX HEAT AND 65 SX W/2% CACL2 - TOC 5 FT FROM SURFACE BY CBL.

1720' - 8 5/8 24# CASING. CEMENTED WITH 334 SX 50-50 POZ W/18% GEL AND 3% SALT, AND 100 SX 50-50 POZ W/2% CACL2 - CIRC. 26 615 CEMENT. (FROM C-103 SUBMITTED 5-26-63).

64 JTS 2 7/8 J-55 TUBING - 2007 FT.
OPEN ENDED W/4 PERFORATIONS AT 1980-1984
