


TEST DATE: MAY 15 to 17, 1982
TEST DEPTH: 13,492 FEET

ELEMENT NO: 20203
RANGE: 0-10,000 PSI
CLOCK NO: 22496
RANGE: 0-72 Hour

NOTE: See tabulation of Times and Pressures on attached sheet.

TIME IN HOURS

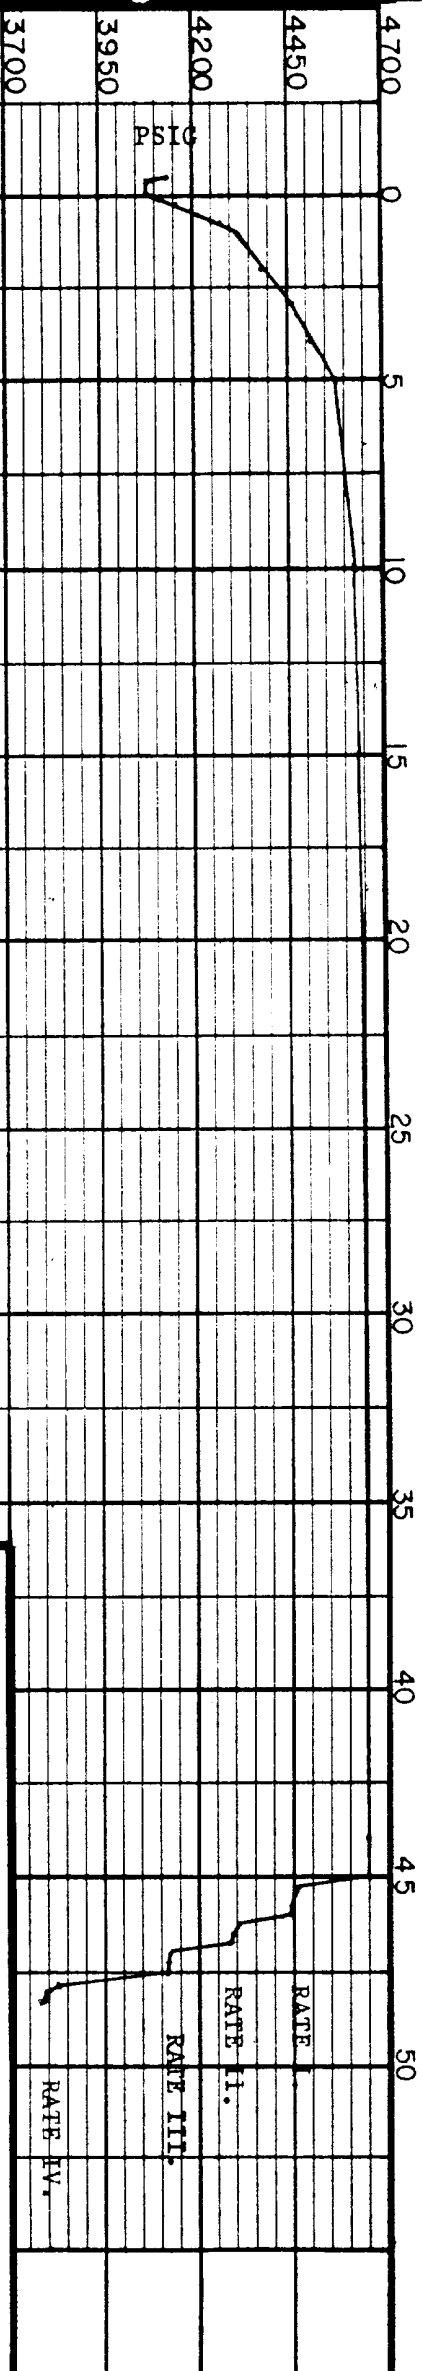

AMOCO PRODUCTION COMPANY

DUNN FEDERAL COM NO. 2

BOTTOM HOLE PRESSURE BUILD-UP TEST, AND PRESSURES
FOR CALCULATING 4-POINT BACK PRESSURE TEST.

JOHN W. WEST ENGINEERING CO. HOBBES, NEW MEXICO

Date: 5-18-82 Drawn by: bsm Scale: as shown

AMOCO PRODUCTION COMPANY
DUNN FEDERAL NO. 2
BOTTOM HOLE PRESSURE BUILD-UP TEST, AND
PRESSURES FOR CALCULATING 4-POINT BACK PRESSURE TEST.
TABULATION OF TIMES AND PRESSURES.

TEST CONDUCTED BY:
JOHN WEST ENGINEERING COMPANY

TEST DATE: MAY 15 to 17, 1982
TEST DEPTH: 13,492
ELEMENT NO: 20203 (0-10,000 psi)
OPERATOR: Bobby Thomason

<u>DATE</u>	<u>TIME</u>	<u>CUM HRS./MIN.</u>	<u>PSIG @ 13,492'</u>	<u>CENTER OF PERFORATIONS PSIG CORRECTED TO 13,603'</u>
5-15-82	12:00 Noon		4133 gauge reached 13,492'	4144
	12:30 P.M.		4066	4077
	1:00 P.M.	00 Hrs. 00 Min.	4066	4077
	1:15 P.M.	00 15	4143	4154
	1:30 P.M.	00 30	4204	4215
	1:45 P.M.	00 45	4260	4271
	2:00 P.M.	01 00	4316	4327
	3:00 P.M.	02 00	4378	4389
	4:00 P.M.	03 00	4449	4460
	5:00 P.M.	04 00	4500	4511
	6:00 P.M.	05 00	4556	4567
5-15-82	11:00 P.M.	10 00	4628	4639
5-16-82	4:00 A.M.	15 00	4633	4644
5-16-82	9:00 A.M.	20 00	4638	4649
5-17-82	9:00 A.M.	44 00	4638	4649 gauge out to make grad stops.
	9:50 A.M.		4638	4649 gauge back to 13,492
	10:00 A.M.	00 Hrs. 00 Min.	4638	4649 after grad. stops.
	10:15 A.M.	00 15	4444	4455
	10:30 A.M.	00 30	4439	4450
	10:45 A.M.	00 45	4434	4445
	11:00 A.M.	01 00	4434	4445 End Rate I
	11:15 A.M.	01 15	4291	4302
	11:30 A.M.	01 30	4281	4292
	11:45 A.M.	01 45	4276	4287 End Rate II
	12:00 Noon	02 00	4112	4123
	12:15 P.M.	02 15	4107	4118
	12:30 P.M.	02 30	4102	4113 End Rate III
	12:45 P.M.	02 45	3808	3819
	1:00 P.M.	03 00	3783	3794
5-17-82	1:15 P.M.	03 15	3778	3789 End Rate IV
