


K.B. - 17' AGL

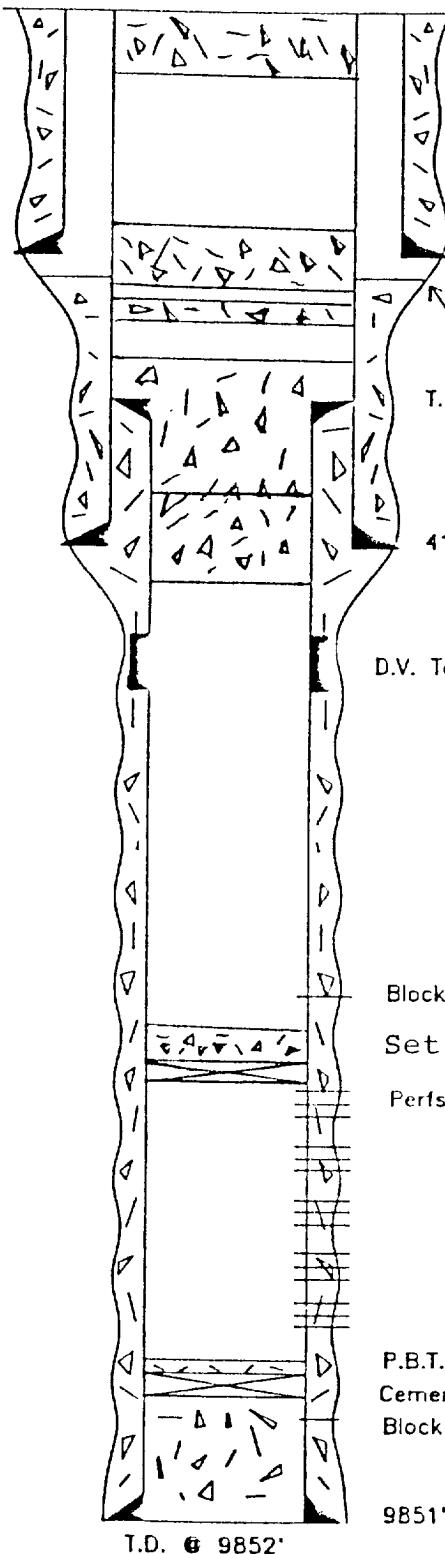

Set 50' (17 sxs) cement plug at surface

430' - 13 3/8" csg. cmt. w/450 sxs circ. 150 sxs to surface
Set 100' (34 sxs) cement plug @ 13 3/8" shoe
T.O.C. @ 440'
360-460'Set 50' (17 sxs) cement plug across top salt
T.O.L. @ 3705'; 1575-1625'. Set 600' cement plug (112 sxs)
across 7" line top (3705') &
9 5/8" shoe (4135') from
3600-4200'

4135' - 9 5/8", 47# csg. cmt. w/2310 sxs

D.V. Tool @ 4534'

Block sqz. @ 9250'

Set CIBP @ ± 9400' plus 35' (6 sxs) cement cap

Perfs 9442'-52' (20 holes)

9460'-63' (3 holes)

9550'-56' (22 holes)

9586'-95' (36 holes)

9604'-08' (6 holes)

P.B.T.D. @ 9616'

Cement Retainer @ 9630'

Block sqz. @ 9655'

9851' - 7, 29#, P-110, csg.

Cmt. w/343 sxs in 2 stages

GOVERNMENT "9" NO. 2

1980' FSL & 660'

SEC. 9, T-19S, R-35E
