


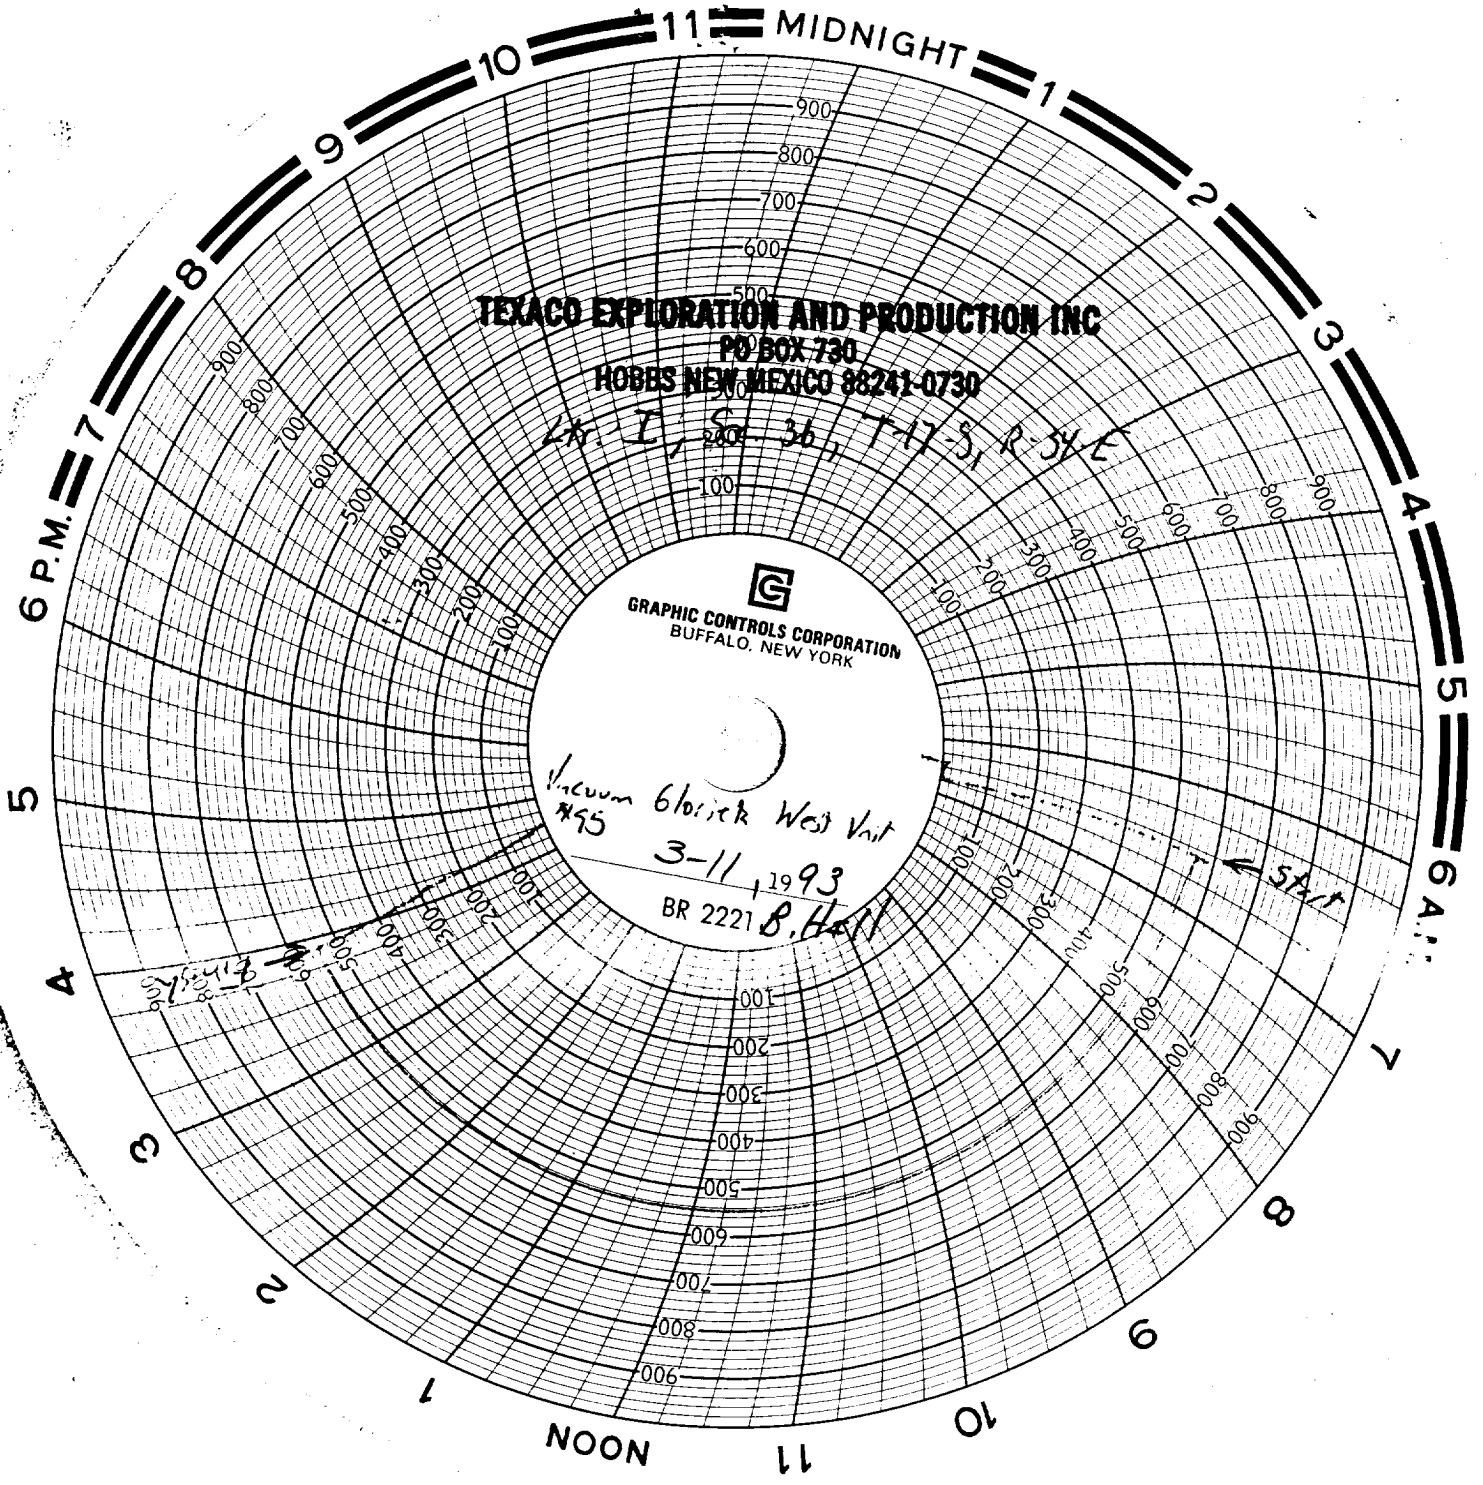

TEXACO EXPLORATION AND PRODUCTION INC

PO BOX 730

HOBBS NEW MEXICO 88241-0730

4x L, S, 3b, T-17-S, R-34-E



GRAPHIC CONTROLS CORPORATION
BUFFALO, NEW YORK

Vacuum 6/brick West Unit
#95

3-11, 1993

BR 2221 B. Hall

5A/T

4-17-93



PACKER INSTALLATION PLAN

PREPARED FOR <i>Randy Trammell</i>		COMPANY <i>Texaco E&P Inc.</i>		DATE <i>March 10, 1993</i>	
LEASE <i>V.G.W.U.</i>	WELL No. <i>#95</i>	FIELD	CO./PARISH <i>Lea</i>	STATE <i>New Mexico</i>	☒ NEW COMPLETION ☐ WORKOVER

INSTALLATION	ITEM	LENGTH	FROM	TO	DESCRIPTION	OD	ID
		<i>14.00'</i>	<i>KB</i>	<i>GL</i>	<i>Elevation</i>		
	<i>1</i>	<i>5858.67'</i>	<i>14.00'</i>	<i>5872.67'</i>	<i>(180 joints) 2 3/8" EUE 8rd Cement Lined J-55 Tubing</i>	<i>2.375"</i>	<i>1.69"</i>
	<i>2</i>	<i>.76'</i>	<i>5872.67'</i>	<i>5873.43'</i>	<i>2 3/8" EUE 8rd Stainless Steel Cross-over</i>	<i>2.375"</i>	<i>1.69"</i>
	<i>3</i>	<i>1.97'</i>	<i>5873.43'</i>	<i>5875.40'</i>	<i>5 1/2" x 2 3/8" Plastic Coated XL On-Off Tool w/ 1.43" "F" Profile cut in 316 Stainless Steel Gudgeon</i>	<i>4.375"</i>	<i>1.43"</i>
	<i>4</i>	<i>3.73'</i>	<i>5875.40'</i>	<i>5879.13'</i>	<i>5 1/2" x 17-20" x 2 3/8" Plastic Coated G-VI Injection Packer w/ AVA Rubber System</i>	<i>4.625"</i>	<i>1.938"</i>
	<i>5</i>	<i>.52'</i>	<i>5879.13'</i>	<i>5879.65'</i>	<i>2 3/8" EUE 8rd Nickel Plated Pump Out Plug-Wireline Re-entry Guide</i>	<i>3.063"</i>	<i>2.000"</i>
	<i>*Note: The G-VI is set at 5875.40' w/ 10,000* Tension pulled into the tubing string.</i>						
	<i>The backside tested to 500 psi.</i>						

GENERAL REMARKS			PACKER TYPE	RETRIEVING METHOD Include shear release or collet snap value
			top	
COMP. FLUID TYPE AND WEIGHT <i>Fresh Water w/ Corrosion Inhibitor</i>			middle	
ESTIMATED BHP			lower	
ESTIMATED BHP				
MAX. ANGLE AND KICKOFF DEPTH (ft)				
GAND CONTROL				

DATE	OPERATOR'S NAME	ARFA	DEVELOPMENT
------	-----------------	------	-------------
