


Name

Address

Ph.

Remarks:

*Amoco production well -
bad cement job. No cement
above or below Glorita*

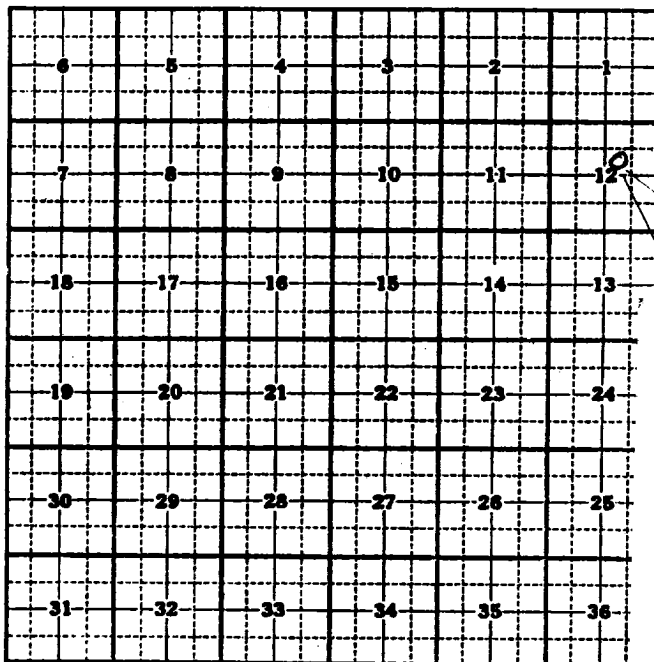

T 20 N R 33 E State Harding
or County


Name

Address

Ph.


Remarks:

*Amoco disposal well -
in Glorita.*

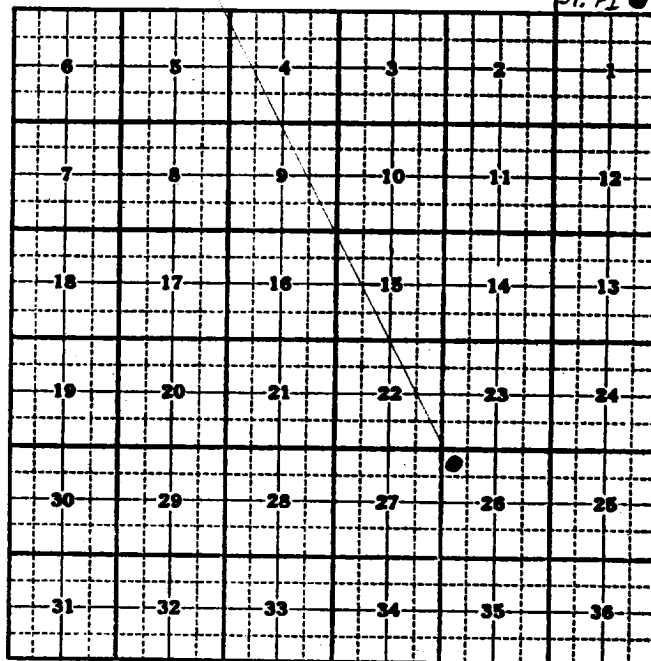

T 19 N R 34 E State Union
or County

Amoco 20N-33E-See 12

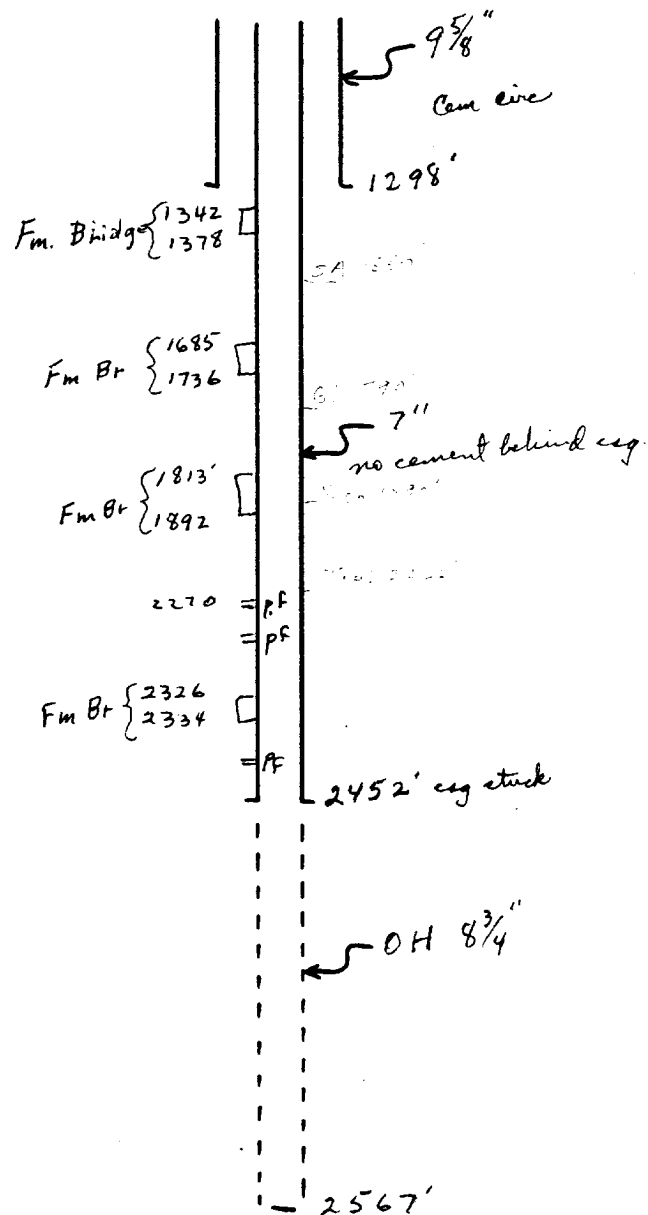

(Carl)

10/17/83

Think this is too far away to
be any problem.

JWR

Joe:

I have been puzzling over this deal -
have looked at all logs. It is a very strange
situation of unusual casing, poor cement on prod. cas.
etc. The squeeze cementing is obviously for
isolation of Tubb.

My concern is, what might happen when
massive injection into the Glorieta begins (with
full scale production). Could pressures at Sec 12,
20N-33E increase the normal 200-300 psi Glorieta
to a point that fluids from that zone might move
up (and maybe down) outside of casing?

Carl
