

TEST DATE: MARCH 27, 1982
TEST DEPTH: 11,113 FEET
ELEMENT NO: 34912
RANGE: 0-8000 PSI
CLOCK NO: 22507
RANGE: 0-72 HOURS

DATE
3-27-82

TIME
9:00 A.M.
9:15 A.M.
9:30 A.M.
9:45 A.M.
10:00 A.M.

CUM HRS./MIN.
00 Hrs. 00 Min.
00 15
00 30
00 45
01 00

PSIG @ 11,113 FEET
3796 Open Choke, Begin Test.
3776 12/64 Choke
3763
3767
3767 End Rate I

10:15 A.M.
10:30 A.M.
10:45 A.M.

01 15
01 30
01 45

3743 14/64 Choke
3722
3706 End Rate II

3600 18/64 Choke
3522
3473
3449 End Rate III

11:00 A.M.
11:15 A.M.
11:30 A.M.
11:45 A.M.


02 00
02 15
02 30
02 45

3310 23/64 Choke
3229 End Rate IV

12:00 Noon
12:15 P.M.

03 00
03 15

TIME IN HOURS

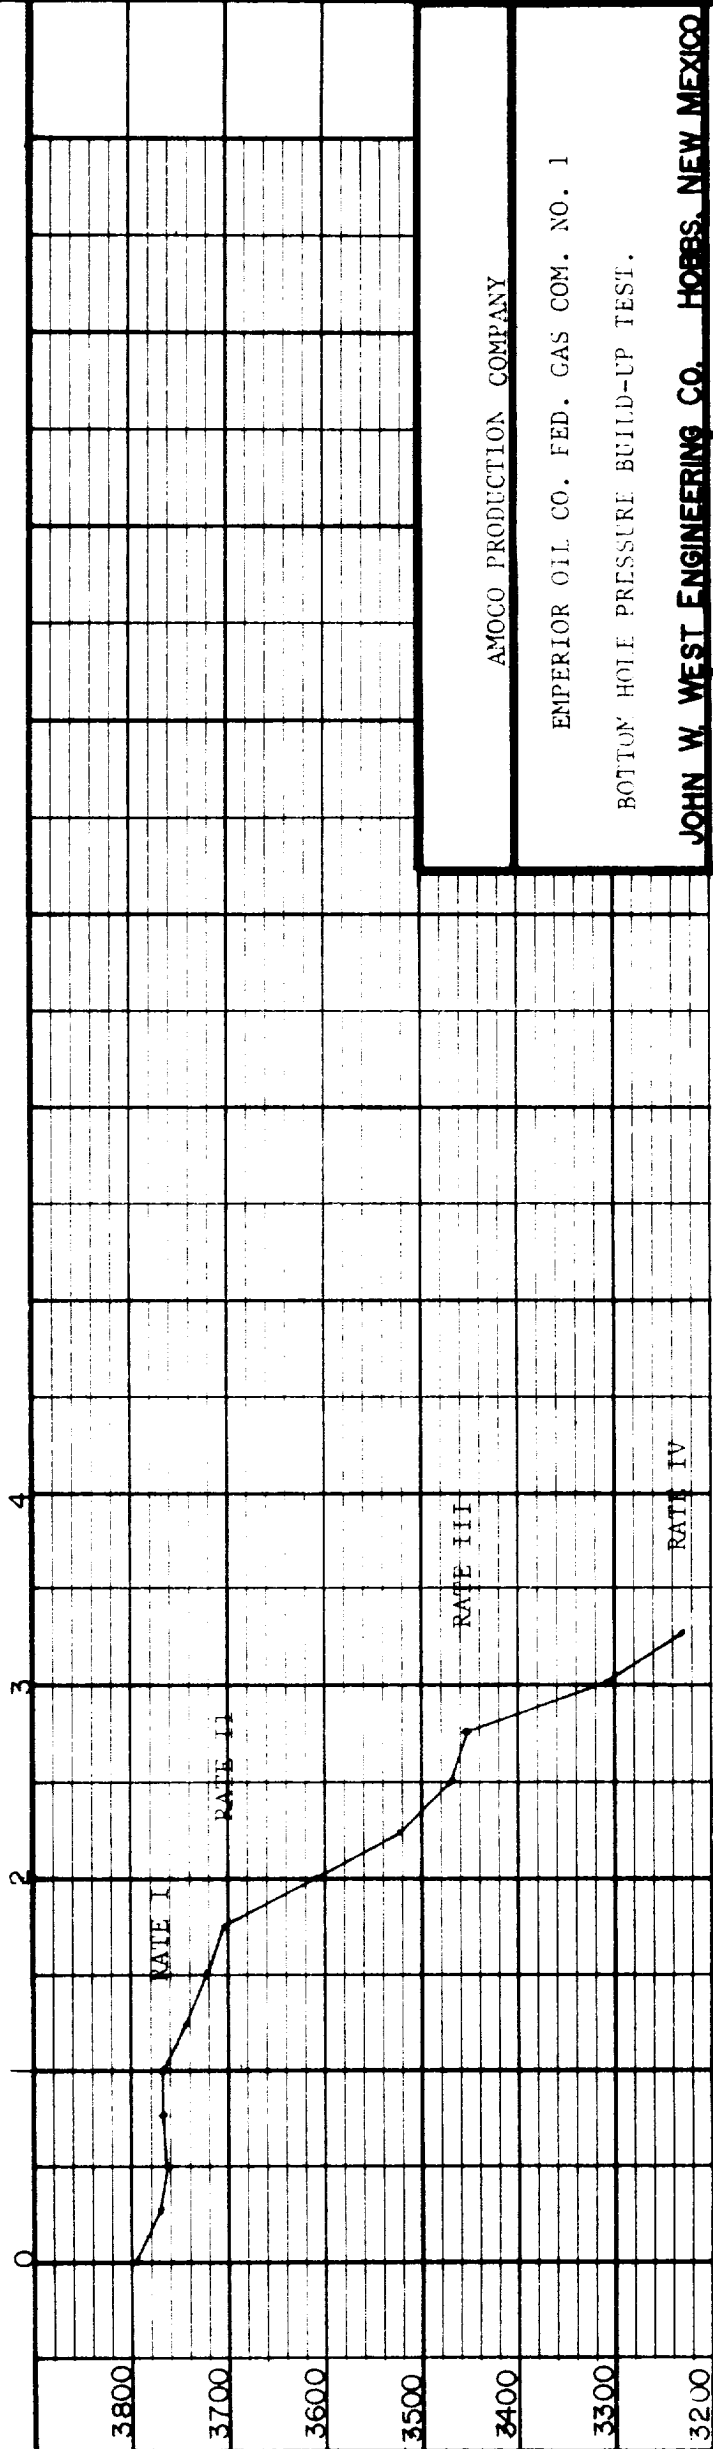

AMOCO PRODUCTION COMPANY

EMPERIOR OIL CO. FED. GAS COM. NO. 1

BOTTOM HOLE PRESSURE BUILD-UP TEST.

JOHN W. WEST ENGINEERING CO. HOBBS, NEW MEXICO

Date: 3-29-82 Drawn by: bsm Scale: as shown
