

District I
1625 N. French Dr., Hobbs, NM 88240
District II
1301 W. Grand Avenue, Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised October 12, 2005
Submit to Appropriate District Office
State Lease- 4 Copies
Fee Lease- 3 Copies

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number 30-015-34643	Pool Code 75260	Pool Name Cottonwood Creek; WC, West (Gas)
Property Code	Property Name ANIMAS C 3 FEE	Well Number 1H
OCRID No. 7377	Operator Name EOG RESOURCES, INC.	Elevation 3593'

Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
1	3	16 SOUTH	24 EAST, N.M.P.M.		1880	SOUTH	660'	EAST	EDDY

Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
L	3	16 SOUTH	24 EAST, N.M.P.M.		1880	SOUTH	660	WEST	EDDY

Dedicated Acres 320	Joint or Infill	Consolidation Code	Order No.
-------------------------------	-----------------	--------------------	-----------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

BOTTOM HOLE LOCATION
NEW MEXICO EAST
NAD 1927
Y=709241.2
X=423536.6
LAT.: N 32.9495289
LONG.: W 104.5825963

SURFACE LOCATION
NEW MEXICO EAST
NAD 1927
Y=709242.0
X=427521.3
LAT.: N 32.9495564
LONG.: W 104.5896087


SCALE: 1" = 2000'

RECEIVED
FEB 21 2006
OCC-ARTESIA

OPERATOR CERTIFICATION
I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.
Donny G. Glanton 2/10/06
Signature Date
Donny G. Glanton
Printed Name

SURVEYOR CERTIFICATION
I hereby certify that the well location shown on this plat has plotted from field notes of actual surveys made by me or under my supervision and that the same is true and correct to the best of my belief.
15079
JANUARY 23, 2006
Date of Survey
Signature and Seal of Professional Surveyor
Terry J. Paul
Certificate Number 15079
WD# 060119WL-h (cde)

New Mexico Double Horseshoe Reserve Pit Design

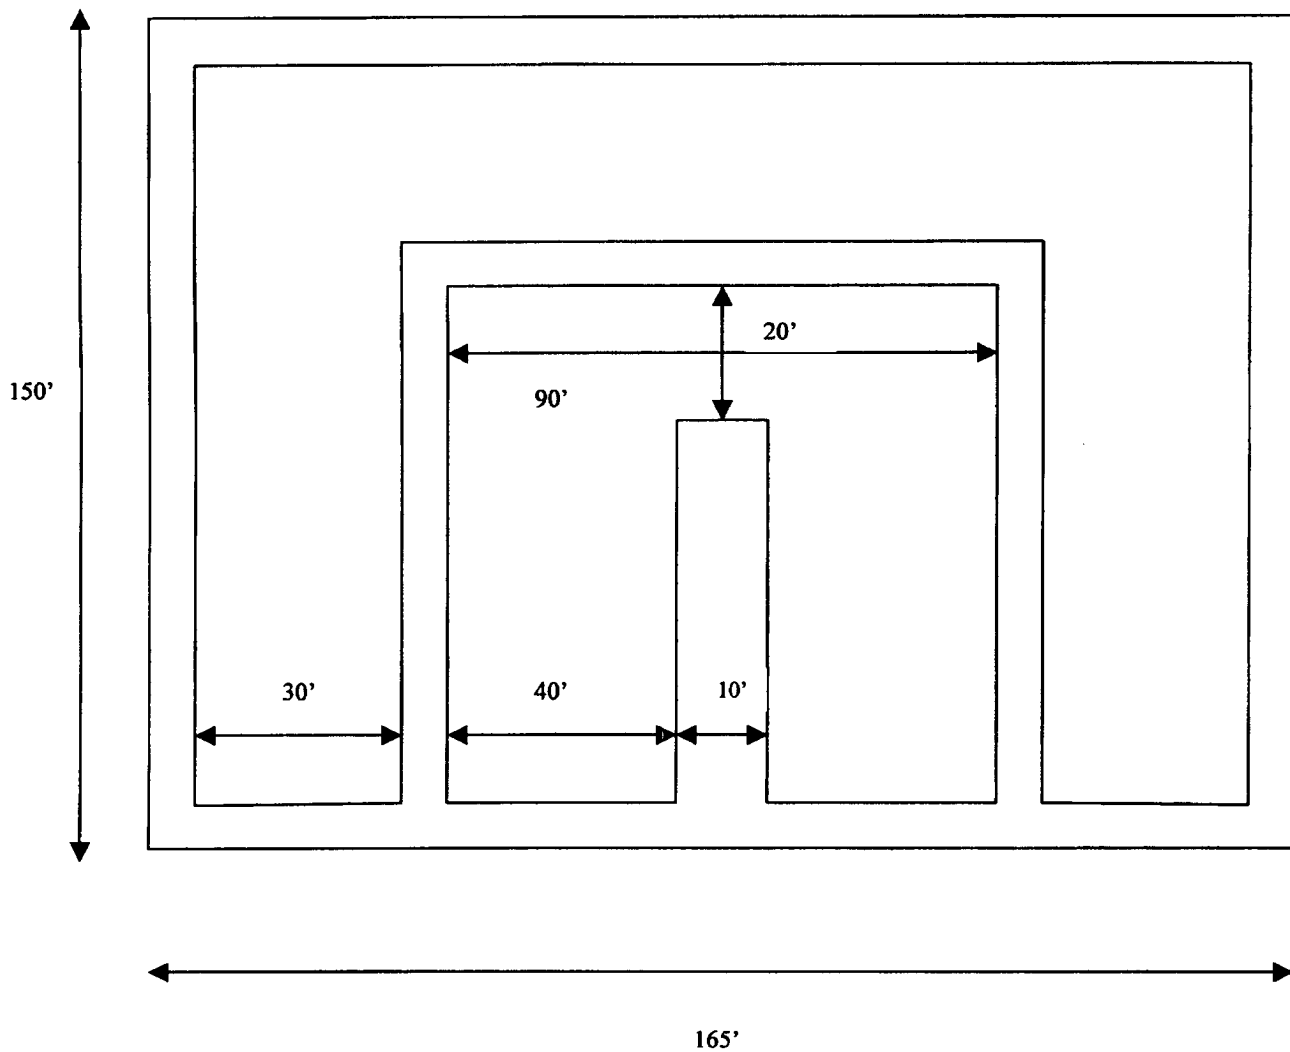

Approximate Inside Reserve Volume: 4500 bbls
Approximate Outside Reserve Volume: 5800 bbls

Permit Information:

Well Name: Animas C 3 Fee #1H

Location:

SL 1880' FSL & 660' FEL, Section 3, T-16-S, R-24-E, Eddy Co., N.M.

BHL 1880' FSL & 660' FWL, Section 3, T-16-S, R-24-E, Eddy Co., N.M.

Casing Program:

Casing	Setting Depth	Hole Size	Casing Size	Casing Weight	Casing Grade	Desired TOC
Surface	900'	9-7/8"	7"	23#	J-55	Surface
Production	8,462'	6-1/8"	4 1/2"	11.6#	P-110	Surface

Cement Program:

Depth	No. Sacks	Slurries:
900'	150	Lead: Premium Plus + 2% CaCl ₂ + 3% Econolite + 1/4 pps Flocele
	175	Tail: Premium Plus + 2% CaCl ₂ + 1/4 pps Flocele
8,462'	400	Lead: Interfill C + 1/4 pps Flocele
	350	Tail: Premium Cement + 100% Acid Soluble Additive + 0.6% Halad®-344 + 0.8% Econolite + 0.2% HR-55

Mud Program:

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 – 900'	Fresh - Gel	8.6-8.8	28-34	N/c
900' – 4,400'	Cut Brine	8.8-9.2	28-34	N/c
4,400' – 5,200'	Cut Brine	8.8-9.2	28-34	10-15
4,200' – 8,462'	Polymer (Lateral)	9.0-9.4	40-45	10-20

February 13, 2006

State of New Mexico Energy, Minerals and Natural Resources
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

To Whom It May Concern:

I am writing to request a waiver for the inclusion of an H₂S Contingency Plan for the Animas C 3 Fee Com #1H. The current plan is to complete this well in the Wolfcamp, which is sweet, and I do not anticipate encountering any H₂S bearing formations during drilling operations.

Sincerely,


Ron McIntyre
Drilling Engineer

RECEIVED
FEB 21 2006
OCU-ANIMAS

EOG - Midland (3)

Thames

Animas C 3 Fee #1H

Animas C 3 Fee #1H

Animas C 3 Fee #1H

Plan: Plan #1 021306

Standard Planning Report

13 February, 2006

EOG RESOURCES INC.

Planning Report

Database:	EDM	Local Co-ordinate Reference:	Well Animas C 3 Fee #1H
Company:	EOG - Midland (3)	TVD Reference:	WELL @ 3610.0ft (Original Well Elev)
Project:	Thames	MD Reference:	WELL @ 3610.0ft (Original Well Elev)
Site:	Animas C 3 Fee #1H	North Reference:	Grid
Well:	Animas C 3 Fee #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Animas C 3 Fee #1H		
Design:	Plan #1 021306		

Project	Thames		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	Animas C 3 Fee #1H		
Site Position:		Northing:	709,242.00 ft
From:	Map	Easting:	427,521.30 ft
Position Uncertainty:	0.0 ft	Slot Radius:	"
		Latitude:	32° 56' 58.403 N
		Longitude:	104° 34' 10.584 W
		Grid Convergence:	-0.13 °

Well	Animas C 3 Fee #1H, Eddy County, NM		
Well Position	+N/-S	0.0 ft	Northing: 709,242.00 ft
	+E/-W	0.0 ft	Easting: 427,521.30 ft
Position Uncertainty	0.0 ft	Wellhead Elevation:	ft
		Latitude:	32° 56' 58.403 N
		Longitude:	104° 34' 10.584 W
		Ground Level:	3,593.0 ft

Wellbore	Animas C 3 Fee #1H		
Magnetics	Model Name	Sample Date	Declination
	IGRF2005	2/13/2006	(°)
			8.71
			Dip Angle
			(°)
			60.79
			Field Strength
			(nT)
			49,457

Design	Plan #1 021306		
Audit Notes:			
Version:	Phase:	PROTOTYPE	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W
	(ft)	(ft)	(ft)
	0.0	0.0	0.0
			Direction
			(°)
			269.99

Plan Sections										
Measured Depth	Inclination	Azimuth	Vertical Depth	+N/-S	+E/-W	Dogleg Rate	Build Rate	Turn Rate	TFO	Target
(ft)	(°)	(°)	(ft)	(ft)	(ft)	(°/100ft)	(°/100ft)	(°/100ft)	(°)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
4,268.0	0.00	0.00	4,268.0	0.0	0.0	0.00	0.00	0.00	0.00	
4,868.0	90.00	269.99	4,650.0	-0.1	-382.0	15.00	15.00	0.00	269.99	
4,885.0	90.51	269.99	4,649.9	-0.1	-399.0	3.00	3.00	-0.01	-0.19	
8,470.9	90.51	269.99	4,618.0	-0.8	-3,984.7	0.00	0.00	0.00	0.00	PBHL Animas C 3 Fe

EOG RESOURCES INC.

Planning Report

Database:	EDM	Local Co-ordinate Reference:	Well Animas C 3 Fee #1H
Company:	EOG - Midland (3)	TVD Reference:	WELL @ 3610.0ft (Original Well Elev)
Project:	Thames	MD Reference:	WELL @ 3610.0ft (Original Well Elev)
Site:	Animas C 3 Fee #1H	North Reference:	Grid
Well:	Animas C 3 Fee #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Animas C 3 Fee #1H		
Design:	Plan #1 021306		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,268.0	0.00	0.00	4,268.0	0.0	0.0	0.0	0.00	0.00	0.00
KOP @ 4268' MD/TVD									
4,275.0	1.05	269.99	4,275.0	0.0	-0.1	0.1	15.00	15.00	0.00
4,300.0	4.80	269.99	4,300.0	0.0	-1.3	1.3	15.00	15.00	0.00
4,325.0	8.55	269.99	4,324.8	0.0	-4.2	4.2	15.00	15.00	0.00
4,350.0	12.30	269.99	4,349.4	0.0	-8.8	8.8	15.00	15.00	0.00
4,375.0	16.05	269.99	4,373.6	0.0	-14.9	14.9	15.00	15.00	0.00
4,400.0	19.80	269.99	4,397.4	0.0	-22.6	22.6	15.00	15.00	0.00
4,425.0	23.55	269.99	4,420.6	0.0	-31.8	31.8	15.00	15.00	0.00
4,450.0	27.30	269.99	4,443.2	0.0	-42.5	42.5	15.00	15.00	0.00

EOG RESOURCES INC.

Planning Report

Database:	EDM	Local Co-ordinate Reference:	Well Animas C 3 Fee #1H
Company:	EOG - Midland (3)	TVD Reference:	WELL @ 3610.0ft (Original Well Elev)
Project:	Thames	MD Reference:	WELL @ 3610.0ft (Original Well Elev)
Site:	Animas C 3 Fee #1H	North Reference:	Grid
Well:	Animas C 3 Fee #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Animas C 3 Fee #1H		
Design:	Plan #1 021306		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
4,475.0	31.05	269.99	4,465.0	0.0	-54.7	54.7	15.00	15.00	0.00	
4,500.0	34.80	269.99	4,486.0	0.0	-68.3	68.3	15.00	15.00	0.00	
4,525.0	38.55	269.99	4,506.0	0.0	-83.2	83.2	15.00	15.00	0.00	
4,550.0	42.30	269.99	4,525.1	0.0	-99.4	99.4	15.00	15.00	0.00	
4,575.0	46.05	269.99	4,543.0	0.0	-116.9	116.9	15.00	15.00	0.00	
4,600.0	49.80	269.99	4,559.8	0.0	-135.4	135.4	15.00	15.00	0.00	
4,625.0	53.55	269.99	4,575.3	0.0	-155.0	155.0	15.00	15.00	0.00	
4,650.0	57.30	269.99	4,589.4	0.0	-175.6	175.6	15.00	15.00	0.00	
4,675.0	61.05	269.99	4,602.3	0.0	-197.1	197.1	15.00	15.00	0.00	
4,700.0	64.80	269.99	4,613.6	0.0	-219.3	219.3	15.00	15.00	0.00	
4,725.0	68.54	269.99	4,623.5	0.0	-242.3	242.3	15.00	15.00	0.00	
4,750.0	72.29	269.99	4,631.9	0.0	-265.8	265.8	15.00	15.00	0.00	
4,775.0	76.04	269.99	4,638.7	-0.1	-289.9	289.9	15.00	15.00	0.00	
4,800.0	79.79	269.99	4,644.0	-0.1	-314.3	314.3	15.00	15.00	0.00	
4,825.0	83.54	269.99	4,647.6	-0.1	-339.0	339.0	15.00	15.00	0.00	
4,850.0	87.29	269.99	4,649.6	-0.1	-364.0	364.0	15.00	15.00	0.00	
4,868.0	90.00	269.99	4,650.0	-0.1	-382.0	382.0	15.00	15.00	0.00	
End of Curve @ 4868' MD / 4650' TVD										
4,885.0	90.51	269.99	4,649.9	-0.1	-399.0	399.0	3.00	3.00	-0.01	
4,900.0	90.51	269.99	4,649.8	-0.1	-414.0	414.0	0.00	0.00	0.00	
5,000.0	90.51	269.99	4,648.9	-0.1	-514.0	514.0	0.00	0.00	0.00	
5,100.0	90.51	269.99	4,648.0	-0.1	-613.9	613.9	0.00	0.00	0.00	
5,200.0	90.51	269.99	4,647.1	-0.1	-713.9	713.9	0.00	0.00	0.00	
5,300.0	90.51	269.99	4,646.2	-0.2	-813.9	813.9	0.00	0.00	0.00	
5,400.0	90.51	269.99	4,645.3	-0.2	-913.9	913.9	0.00	0.00	0.00	
5,500.0	90.51	269.99	4,644.4	-0.2	-1,013.9	1,013.9	0.00	0.00	0.00	
5,600.0	90.51	269.99	4,643.6	-0.2	-1,113.9	1,113.9	0.00	0.00	0.00	
5,700.0	90.51	269.99	4,642.7	-0.2	-1,213.9	1,213.9	0.00	0.00	0.00	
5,800.0	90.51	269.99	4,641.8	-0.3	-1,313.9	1,313.9	0.00	0.00	0.00	
5,900.0	90.51	269.99	4,640.9	-0.3	-1,413.9	1,413.9	0.00	0.00	0.00	
6,000.0	90.51	269.99	4,640.0	-0.3	-1,513.9	1,513.9	0.00	0.00	0.00	
6,100.0	90.51	269.99	4,639.1	-0.3	-1,613.9	1,613.9	0.00	0.00	0.00	
6,200.0	90.51	269.99	4,638.2	-0.3	-1,713.9	1,713.9	0.00	0.00	0.00	
6,300.0	90.51	269.99	4,637.3	-0.4	-1,813.9	1,813.9	0.00	0.00	0.00	
6,400.0	90.51	269.99	4,636.4	-0.4	-1,913.9	1,913.9	0.00	0.00	0.00	
6,500.0	90.51	269.99	4,635.5	-0.4	-2,013.9	2,013.9	0.00	0.00	0.00	
6,600.0	90.51	269.99	4,634.7	-0.4	-2,113.9	2,113.9	0.00	0.00	0.00	
6,700.0	90.51	269.99	4,633.8	-0.4	-2,213.9	2,213.9	0.00	0.00	0.00	
6,800.0	90.51	269.99	4,632.9	-0.5	-2,313.9	2,313.9	0.00	0.00	0.00	
6,900.0	90.51	269.99	4,632.0	-0.5	-2,413.9	2,413.9	0.00	0.00	0.00	
7,000.0	90.51	269.99	4,631.1	-0.5	-2,513.9	2,513.9	0.00	0.00	0.00	
7,100.0	90.51	269.99	4,630.2	-0.5	-2,613.9	2,613.9	0.00	0.00	0.00	
7,200.0	90.51	269.99	4,629.3	-0.5	-2,713.9	2,713.9	0.00	0.00	0.00	
7,300.0	90.51	269.99	4,628.4	-0.6	-2,813.9	2,813.9	0.00	0.00	0.00	
7,400.0	90.51	269.99	4,627.5	-0.6	-2,913.9	2,913.9	0.00	0.00	0.00	
7,500.0	90.51	269.99	4,626.6	-0.6	-3,013.9	3,013.9	0.00	0.00	0.00	
7,600.0	90.51	269.99	4,625.8	-0.6	-3,113.8	3,113.8	0.00	0.00	0.00	
7,700.0	90.51	269.99	4,624.9	-0.6	-3,213.8	3,213.8	0.00	0.00	0.00	
7,800.0	90.51	269.99	4,624.0	-0.7	-3,313.8	3,313.8	0.00	0.00	0.00	
7,900.0	90.51	269.99	4,623.1	-0.7	-3,413.8	3,413.8	0.00	0.00	0.00	
8,000.0	90.51	269.99	4,622.2	-0.7	-3,513.8	3,513.8	0.00	0.00	0.00	
8,100.0	90.51	269.99	4,621.3	-0.7	-3,613.8	3,613.8	0.00	0.00	0.00	
8,200.0	90.51	269.99	4,620.4	-0.7	-3,713.8	3,713.8	0.00	0.00	0.00	

EOG RESOURCES INC.

Planning Report

Database:	EDM	Local Co-ordinate Reference:	Well Animas C 3 Fee #1H
Company:	EOG - Midland (3)	TVD Reference:	WELL @ 3610.0ft (Original Well Elev)
Project:	Thames	MD Reference:	WELL @ 3610.0ft (Original Well Elev)
Site:	Animas C 3 Fee #1H	North Reference:	Grid
Well:	Animas C 3 Fee #1H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Animas C 3 Fee #1H		
Design:	Plan #1 021306		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
8,300.0	90.51	269.99	4,619.5	-0.8	-3,813.8	3,813.8	0.00	0.00	0.00	
8,400.0	90.51	269.99	4,618.6	-0.8	-3,913.8	3,913.8	0.00	0.00	0.00	
8,470.9	90.51	269.99	4,618.0	-0.8	-3,984.7	3,984.7	0.00	0.00	0.00	
PBHL Animas C 3 Fee #1H										

Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude
- hit/miss target									
- Shape									
PBHL Animas C 3 Fee #	0.00	0.00	4,618.0	-0.8	-3,984.7	709,241.20	423,536.60	32° 56' 58.304 N	104° 34' 57.346 W
- plan hits target									
- Point									

Plan Annotations					
Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates			
		+N/-S (ft)	+E/-W (ft)	Comment	
4,268.0	4,268.0	0.0	0.0	KOP @ 4268' MD/TVD	
4,868.0	4,650.0	-0.1	-382.0	End of Curve @ 4868' MD / 4650' TVD	

SITE DETAILS: Animas C 3 Fee #1H

Site Centre Northing: 709242.00
Easting: 427521.30

Positional Uncertainty: 0.0
Convergence: -0.13
Local North: Grid

PROJECT DETAILS: Thames

Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001

System Datum: Mean Sea Level

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
4268.0	0.00	0.00	4268.0	0.0	0.0	0.00	0.00	0.0	
4868.0	90.00	269.99	4650.0	-0.1	-382.0	15.00	269.99	382.0	
4885.0	90.51	269.99	4649.9	-0.1	-399.0	3.00	-0.19	399.0	
8470.9	90.51	269.99	4618.0	-0.8	-3984.7	0.00	0.00	3984.7	PBHL Animas C 3 Fee #1H

