Co leted as producing
oil well 7-10-58

P & A 3-8-77

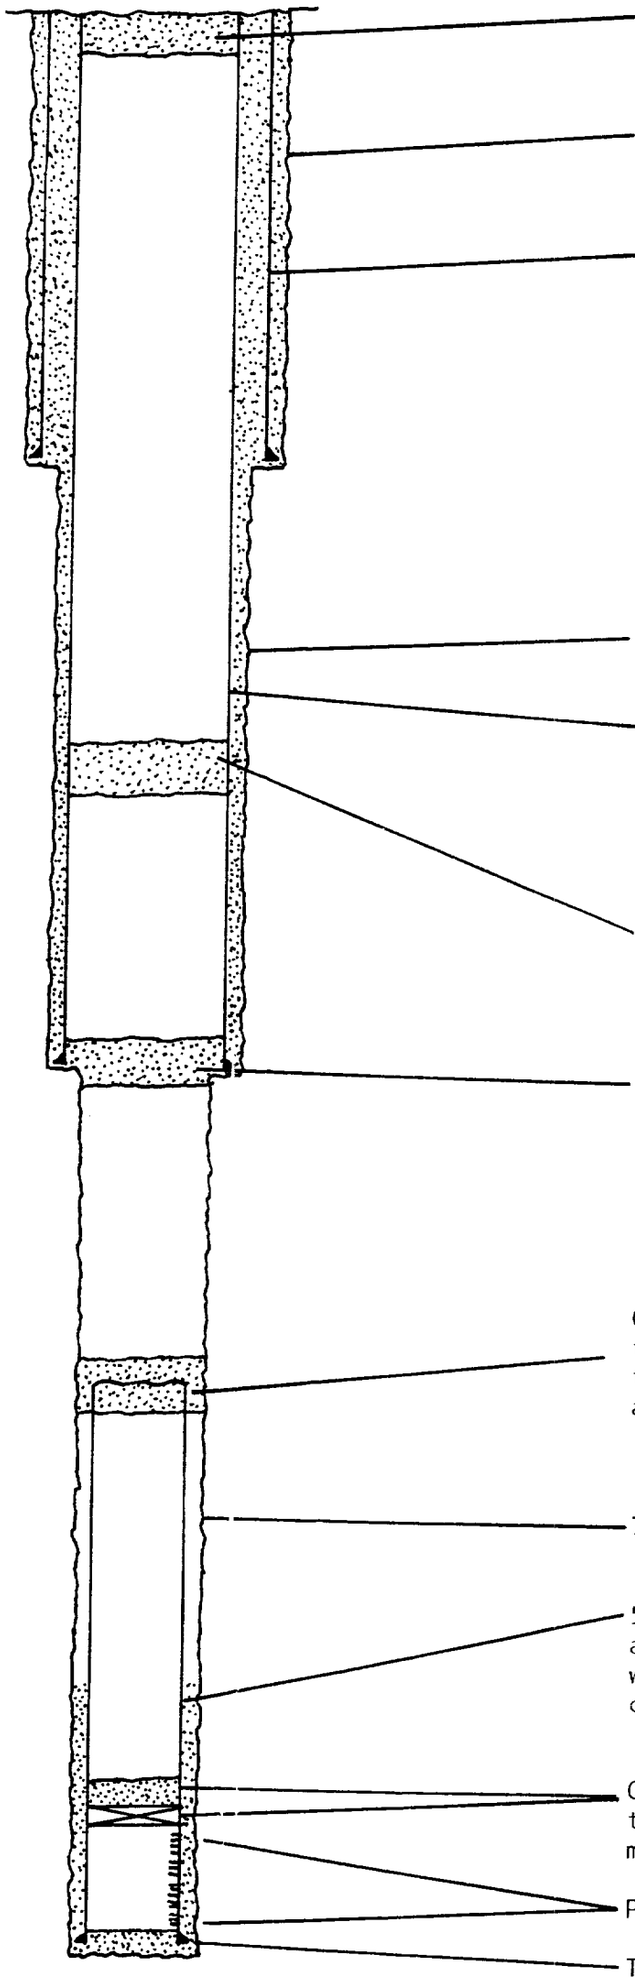

18 sx. cement plug 0-50'

17 1/2" hole

13 3/8" 48 lb. surface casing @ 416'. Cemented with 500 sx. cement. Cement circulated.

11 3/4" hole

8 5/8" intermediate casing, 28 and 32 lb., @ 4280'. Cemented with 3300 sx. cement. Cement circulated

40 sx. cement plug 1550'-1650'

50 sx. cement plug 4230'-4330'

Cut and pulled 5 1/2" production casing from 4597'. Spotted 100' cement plug 4547'-4647' across 5 1/2" stub.

7 7/8" hole

5 1/2" production casing, 15.5 and 17 lb., @ 10010'. Cemented with 450 sx. cement. Cement top calculated @ 7916'.

Cast iron bridge plug @ 9700', topped with 20 sx., 150', of cement.

Perforations 9790'-9960'

TD 10010', PBTD 9980'

Gulf Oil Corporation Maud Saunders #4
Location: 1815' FSL & 660' FWL Sec. 34-T14S-R33E

PRESENT CONDITION

Proposed Disposal Well

Attachment C-108 VI (b) 6
