ENSOLUM

April 29, 2026

New Mexico Oil Conservation Division
1220 South St. Francis Drive
Santa Fe, New Mexico 87505

Re: Closure Request
Jones Federal B 3 Battery
Incident Numbers: nMLB1129240104 & nAPP2520569781
BLM Lease #: NMNM0107697
Eddy County, New Mexico

To Whom it May Concern:

Ensolum, LLC (Ensolum), on behalf of Devon Energy Production Company, LP (Devon), has prepared this *Closure Request* to document excavation and soil sampling activities performed to address fluid releases at the Jones Federal B 3 Battery (Site). Based on the excavation activities and analytical results from the soil sampling events, Devon is submitting this *Closure Request*, describing remediation and reclamation that has occurred and requesting closure for Incident Numbers nMLB1129240104 and nAPP2520569781.

SITE DESCRIPTION AND RELEASE SUMMARY

The Site is located in Unit K, Section 24, Township 19 South, Range 31 East, in Eddy County, New Mexico (32.64265223°, -103.824532°) and is associated with oil and gas exploration and production operations on Federal Land managed by the Bureau of Land Management (BLM).

On July 24, 2025, a pump discharge line developed a leak. This resulted in the release of approximately 2 barrels (bbls) of crude oil onto the caliche pad, road, and pasture land managed by the BLM. No fluids were able to be recovered. Devon reported the release to the New Mexico Oil Conservation Division (NMOCD) via email on August 07, 2023, and submitted an Initial C-141 Report (C-141) on August 22, 2023. The release was assigned Incident Number nMLB1129240104.

On July 24, 2025, A lightning strike caused a fire at the Site. This resulted in the release of approximately 5 bbls of crude oil and 2 bbls of produced water onto the caliche pad, road, and pasture land managed by the BLM. No fluids were able to be recovered. Devon reported the release to the NMOCD via web portal on August 08, 2025, and submitted a C-141 on August 13, 2025. The release was assigned Incident Number nAPP2520569781.

SITE CHARACTERIZATION AND CLOSURE CRITERIA

The Site was characterized to assess the applicability of Table I, Closure Criteria for Soils Impacted by a Release, of Title 19, Chapter 15, Part 29, Section 12 (19.15.29.12) of the New Mexico Administrative Code (NMAC) Site Assessment/Characterization. Potential Site receptors are identified on Figure 1.

The closest permitted groundwater well with depth to groundwater data is New Mexico Office of the State Engineer (NMOSE) well CP-2091 POD1, with a depth to water measurement of greater than

105 feet below ground surface (bgs). The well was located within the Site for assessing depth to water, and the most recent documented water level measurement was collected on October 28, 2025, indicating groundwater was not present in the boring and that groundwater is present at depths greater than 105 feet bgs. All wells used for depth to groundwater determination are depicted on Figure 1 and the referenced well records are included in Appendix A.

The closest continuously flowing or significant watercourse to the Site is an intermittent dry wash, located approximately 2.38 miles northwest of the Site. The Site is greater than 200 feet from a lakebed, sinkhole, or playa lake and greater than 300 feet from an occupied residence, school, hospital, institution, church, or wetland. The Site is greater than 1,000 feet to a freshwater well or spring and is not within a 100-year floodplain or overlying a subsurface mine. The Site is not underlain by unstable geology (low potential karst designation area). Site receptors are identified on Figure 1.

Based on the results of the Site Characterization, the following NMOCD Table I Closure Criteria (Closure Criteria) apply:

- Benzene: 10 milligrams per kilogram (mg/kg)
- Benzene, toluene, ethylbenzene, and total xylenes (BTEX): 50 mg/kg
- Total petroleum hydrocarbons (TPH)-gasoline range organics (GRO) and TPH-diesel range organics (DRO): 1,000 mg/kg
- TPH: 2,500 mg/kg
- Chloride: 20,000 mg/kg

A reclamation requirement of 600 mg/kg chloride and 100 mg/kg TPH was applied to the top 4 feet of the area that was impacted by the release and will be reclaimed following remediation, per 19.15.29.13.D(1) NMAC.

ENVIRONMENTAL DESKTOP REVIEW

An Information for Planning and Consultation (IPaC) report was generated on August 08, 2025, and the report identified five species, Piping Plover (*Charadrius melodus*), Northern Aplomado Falcon (*Falco femoralis septentrionalis*), Texas Hornshell (*Popenaias popeii),* Dunes Sagebrush Lizard (*sceloporus arenicolus*), and Monarch Butterfly (*Danaus plexippus*), as having the potential to occur within areas near the Site; however, no critical habitats for those species were flagged in the area. In regard to one of the identified species having the potential to be at the Site, the Texas Hornshell, Ensolum conducted a review of the Candidate Conservation Agreement with Assurances (CCAA) map tool of observed habitat locations and concluded there was no documented habitat anywhere near the Site.

One of the species identified as having potential to occur is the Dunes Sagebrush Lizard; a review of the United States Fish and Wildlife Service (USFWS) map revealed the Site is located within a documented range of this species. The species was not identified during remediation activities.

A New Mexico Environmental Review Tool (NMERT) report was generated on August 08, 2025, and no sensitive species with critical habitats were flagged within the project area. There were no rare plants flagged in any of the federal and state databases for the area. There is a chance for birds to be nesting in the area, so during project activities if a nest was found, then work would have stopped until proper mitigation efforts are in place and/or the juvenile birds have fledged.

Copies of the IPaC and NMERT documents are included in Appendix B.

SITE ASSESSMENT AND DELINEATION SOIL SAMPLING ACTIVITIES

Between July 29 and November 12, 2025, Ensolum personnel were onsite to delineate the extent of the release as indicated by field screening and laboratory analytical results. Eighteen delineation soil samples (SS01 through SS18) were collected from areas surrounding the release extent to verify the lateral extent at ground surface and 1-foot bgs. A total of 21 boreholes (BH01 through BH21) were advanced via hand auger and air rotary drill within the release extent, around the caliche pad to assess the vertical extent of the release. Delineation soil samples were collected from each borehole at depths ranging from ground surface to 50 feet bgs. Soil sample locations are depicted on Figure 2.

All delineation soil samples were field screened for chloride using Hach® chloride QuanTab® test strips and for TPH using a PetroFLAG® Soil Analyzer. Field screening results and observations for the boreholes were logged on lithologic/soil sampling logs, which are included in Appendix C. Photographic documentation of delineation are included in Appendix D.

All soil samples were placed directly into pre-cleaned glass jars, labeled with the location, date, time, sampler name, method of analysis, and immediately placed on ice. The soil samples were transported under strict chain-of-custody procedures to Envirotech Analytical Laboratory (Envirotech) in Farmington, New Mexico, for analysis of the following chemicals of concern (COCs): BTEX following United States Environmental Protection Agency (EPA) Method 8021B; TPH-GRO, TPH-DRO, and TPH-oil range organics (ORO) following EPA Method 8015M/D; and chloride following EPA Method 300.0.

Through the assessment and delineation process, the following nomenclature changes were applied on laboratory chain of custodies:

- On page 378 incorrect sample names were originally used and corrected.

LABORATORY ANALYTICAL RESULTS

Lateral delineation soil samples SS01, SS03, SS05, SS06, SS08, SS10, SS11, and SS13 through SS18 surrounding the release extent and caliche pad were in compliance with the strictest Closure Criteria at ground surface and 1-foot bgs. Laboratory analytical results for delineation soil samples collected from boreholes BH03, BH04, BH06, BH10 through BH13, BH16, BH18, and BH21 were all in compliance with the strictest Closure Criteria at depths ranging from 1-foot to 50 feet bgs. Laboratory analytical results for delineation soil samples collected from boreholes BH01 through BH21 contained TPH and/or chloride concentrations exceeding the reclamation requirement and Site closure criteria around the Site.

As a result of delineation activities, impacted and waste-containing soil was identified in the release extent and across the caliche pad and excavation was necessary to support reclamation requirements. Laboratory results for the delineation soil samples are summarized in Table 1 and laboratory analytical reports are included in Appendix E.

EXCAVATION AND CONFIRMATION SOIL SAMPLING ACTIVITIES

The excavation of impacted and waste-containing soil was completed utilizing a tracked excavator, loader, and dump trucks. To direct excavation activities, soil was field screened for TPH utilizing a PetroFLAG® soil analyzer system and chloride utilizing Hach® chloride QuanTab® test strips. Photographic documentation of excavation activities is included in Appendix D.

Prior to beginning excavation activities at the Site, Devon requested an alternative sampling plan to collect confirmation soil samples at a frequency of no more than 400 square feet from the floor of the excavation and sidewall soil samples at a frequency of no more than 200 square feet from the sidewalls of the excavation to the NMOCD on January 20, 2026; the variance request was approved by the NMOCD on January 21, 2026. On January 23 through March 11, 2026, 5-point composite confirmation samples were collected by placing five equivalent aliquots of soil into a resealable plastic bag and homogenizing the samples by thoroughly mixing. Composite soil samples FS01 through FS113 were collected from the floor of the excavation at depths ranging from 2 feet to 17 feet bgs. Composite soil samples SW01 through SW27, SW31, and SW32 were collected from the sidewalls of the excavation in the top 4 feet of the subsurface. Composite soil samples SW28 through SW30 and SW33 through SW55 were collected from the sidewalls of the excavation at depths ranging from 4 feet to 16 feet bgs. The soil samples were collected, handled, and analyzed following the same procedures as described above.

The final excavation extent measured approximately 44,032 square feet. A total of approximately 11,176 cubic yards of waste-containing soil was removed during the excavation activities. The waste-containing soil was transported and properly disposed of at the Lea Land Disposal. The excavation extent and excavation soil sample locations are presented in Figure 3.

Through the assessment and delineation process, the following nomenclature changes were applied on laboratory chain of custodies:

- On page 447 incorrect sample dates were copied onto the form that was used and corrected.
- On page 528 the incorrect sample number FS08 was corrected to FS108
- On page 641 sample SW36 was updated to include the full range of the sample depth to 4’-10’
- On page 777 the incorrect sample number SW47 was used and corrected to SW50

LABORATORY ANALYTICAL RESULTS

Laboratory analytical results for all final excavation sidewall samples (SW01 through SW55) and excavation floor samples (FS01 through FS113) indicated all COC concentrations were compliant with the reclamation requirement and Site Closure Criteria. Laboratory analytical results are summarized in Tables 2 and 3 and laboratory analytical reports are included as Appendix E.

RECLAMATION ACTIVITIES

Reclamation of the pad was conducted, and as such, a reclamation requirement of 600 mg/kg chloride and 100 mg/kg TPH were applied to the top 4 feet of the subsurface that was impacted by the releases per 19.15.29.13.D (1) NMAC for the top 4 feet of areas that was reclaimed following remediation.

- The excavation was backfilled with caliche (BF01) below 2 feet bgs and locally sourced topsoil (BF02) from ground surface to 2 feet bgs to match surrounding grade. Laboratory analytical results are summarized in Table 4 and laboratory analytical reports are included as Appendix E;
- Soil in the vicinity of the release includes: Berino complex, Fine sand, 0 to 17 inches, Sandy clay loam, 17 to 58 inches and Loamy sand, 58 to 60 inches according to the United States Department of Agriculture (USDA) Natural Resources Conservation Service (NRCS) Web Soil Survey completed on November 14, 2025;

- The backfilled areas will be seeded utilizing a weed-free seed mix designed by the BLM to meet reclamation standards for this region, which will be: BLM Seed Mixture #1, for Loamy Sites;
- The seed mixture will be distributed with either a push broadcaster seed spreader, tractor operated broadcast seed spreader, drill seeding, or other means;
- Application of the seed mixture will be at a coverage of 10 pounds of seeds per acre of reclaimed pasture with distribution by a drilling method or 20 pounds of seeds per acre of reclaimed pasture with distribution by a broadcast method;
- Erosion control management is not anticipated, but if needed, will potentially include:
    - The placement of waddles in areas with a propensity for high run off rates;
    - Straw cover if high winds are anticipated to support moisture retention and limit wind from blowing seeds away before they have had time to germinate; and/or
    - Other erosional control best management practices (BMP) as necessary to support timely and healthy regrowth of vegetation in disturbed areas;
- Seeding is anticipated to be completed in the Spring or Fall when temperatures and precipitation is most conducive for vegetation growth. In general, seeding should occur approximately one month after the last frost in the Spring up until approximately one month prior to the first fall frost. Ensolum understands the optimal time to seed is between July and early September, which will be adhered to for this Site;
- Bi-annual inspections (at a minimum) will take place on the location until revegetation is consistent with local natural vegetation density. The Site will be inspected the following Fall to assess the success of regrowth. If necessary, an additional application of the BLM-approved pure live seed mixture will be applied as well as any needed BMPs installed to support growth and limit erosion;
- Upon completion of revegetation, a copy of the C-103 submitted to NMOCD will also be submitted to BLM for final inspection and release.

RECLAMATION CLOSURE REQUEST

Site assessment and excavation activities were conducted at the Site to address the July 2025 releases. Following remediation efforts, 113 composite confirmation floor soil samples (FS01 through FS113) and 55 composite confirmation sidewall samples (SW01 though SW55) were collected. Laboratory analytical results for the excavation soil samples collected from the final excavation extent indicated all COC concentrations were in compliance with Site Closure Criteria and with the reclamation requirement in the top 4 feet of soil for all areas. Based on the soil sample analytical results, no further remediation was required. Reclamation was completed as described above.

Based on horizontal and vertical delineation sampling, depth to groundwater greater than 105 feet bgs, and confirmation soil sample laboratory analytical results in compliance with their respective Closure Criteria and reclamation requirement, Devon believes these remedial actions have been protective of human health, the environment, and groundwater. As such, Devon respectfully requests reclamation closure for Incident Numbers nMLB1129240104 and nAPP2520569781.

If you have any questions or comments, please contact Mrs. Ashley Urzedo at (575) 988-0055 or aurzedo@ensolum.com.

Sincerely,
Ensolum, LLC

Cole Burton
Project Manager

Daniel R. Moir, PG (licensed in WY & TX)
Associate Principal, Geologist

cc: Jim Raley, Devon
BLM

Appendices:

Figure 1	Site Receptor Map
Figure 2	Delineation Soil Sample Locations
Figure 3	Confirmation Soil Sample Locations

Table 1	Soil Sample Analytical Results (Delineation Soil Samples)
Table 2	Soil Sample Analytical Results (Confirmation Soil Samples)
Table 3	Soil Sample Analytical Results (Sidewall Soil Samples)
Table 4	Soil Sample Analytical Results (Backfill Soil Sample)

Appendix A	Well Record and Log
Appendix B	Environmental Desktop Review
Appendix C	Lithologic Soil Sampling Logs
Appendix D	Photographic Log
Appendix E	Laboratory Analytical Reports & Chain-of-Custody Documentation
Appendix F	NMOCD Correspondence

ENSOLUM

FIGURES

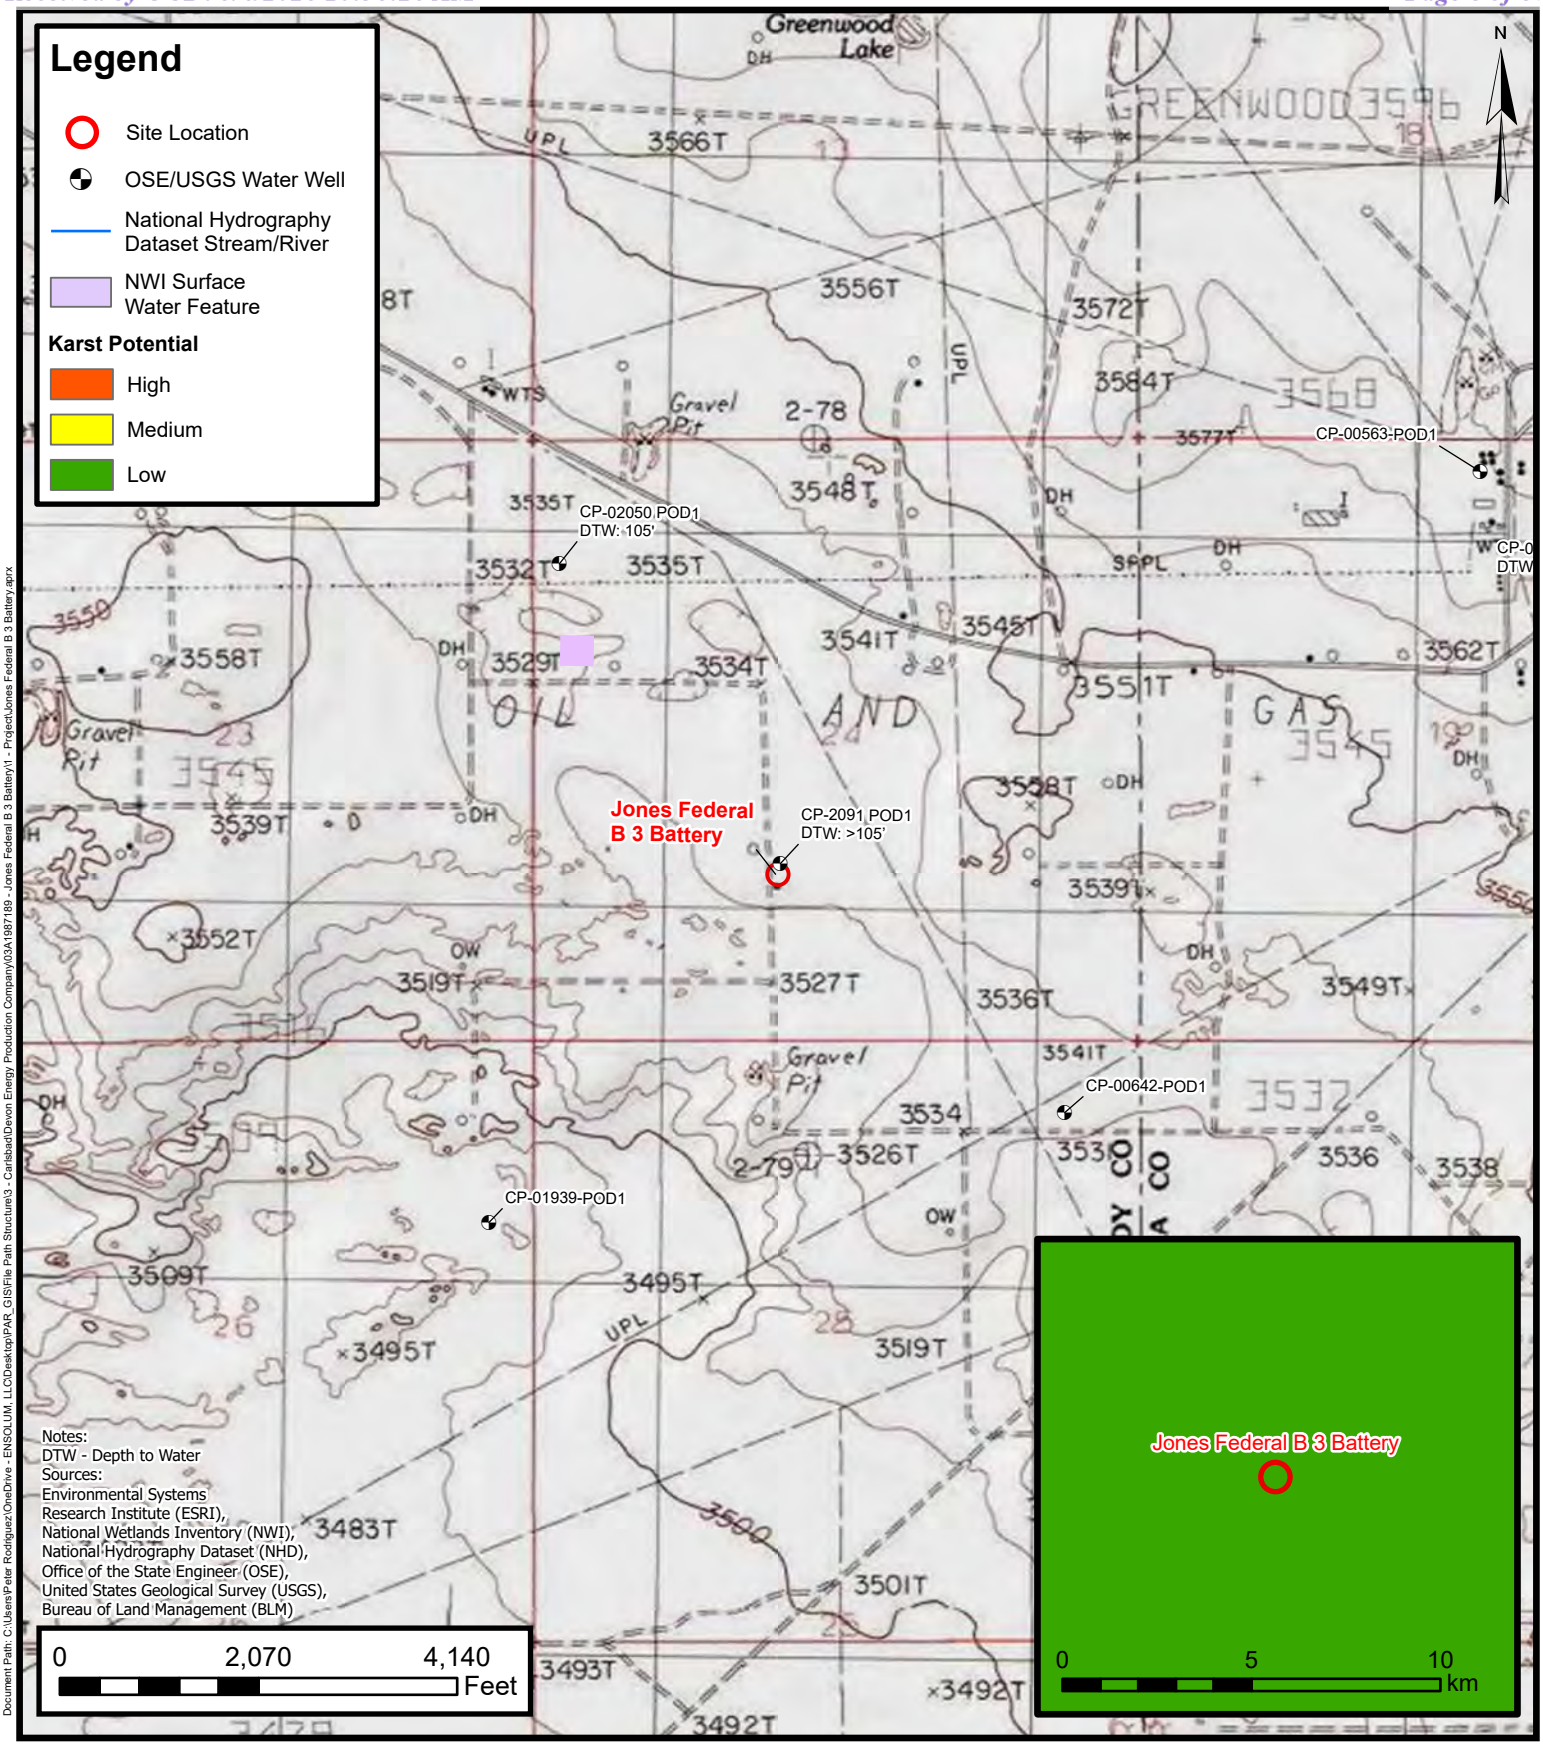

Document Path: C:\Users\Peter Rodriguez\OneDrive - ENSOLUM, LLC\Desktop\PAR_GIS\File Path Structure\3 - Carlsbad\Devon Energy Production Company\03A1987189 - Jones Federal B 3 Battery\1 - Project\Jones Federal B 3 Battery.aprx

ENSOLUM
Environmental, Engineering and Hydrogeologic Consultants

Site Receptor Map

Devon Energy Production Company, LP
Jones Federal B 3 Battery
Incident Numbers: nMLB1129240104 & nAPP2520569781
Unit K, Section 24, T 19S, R 31E
Eddy County, New Mexico

FIGURE

1

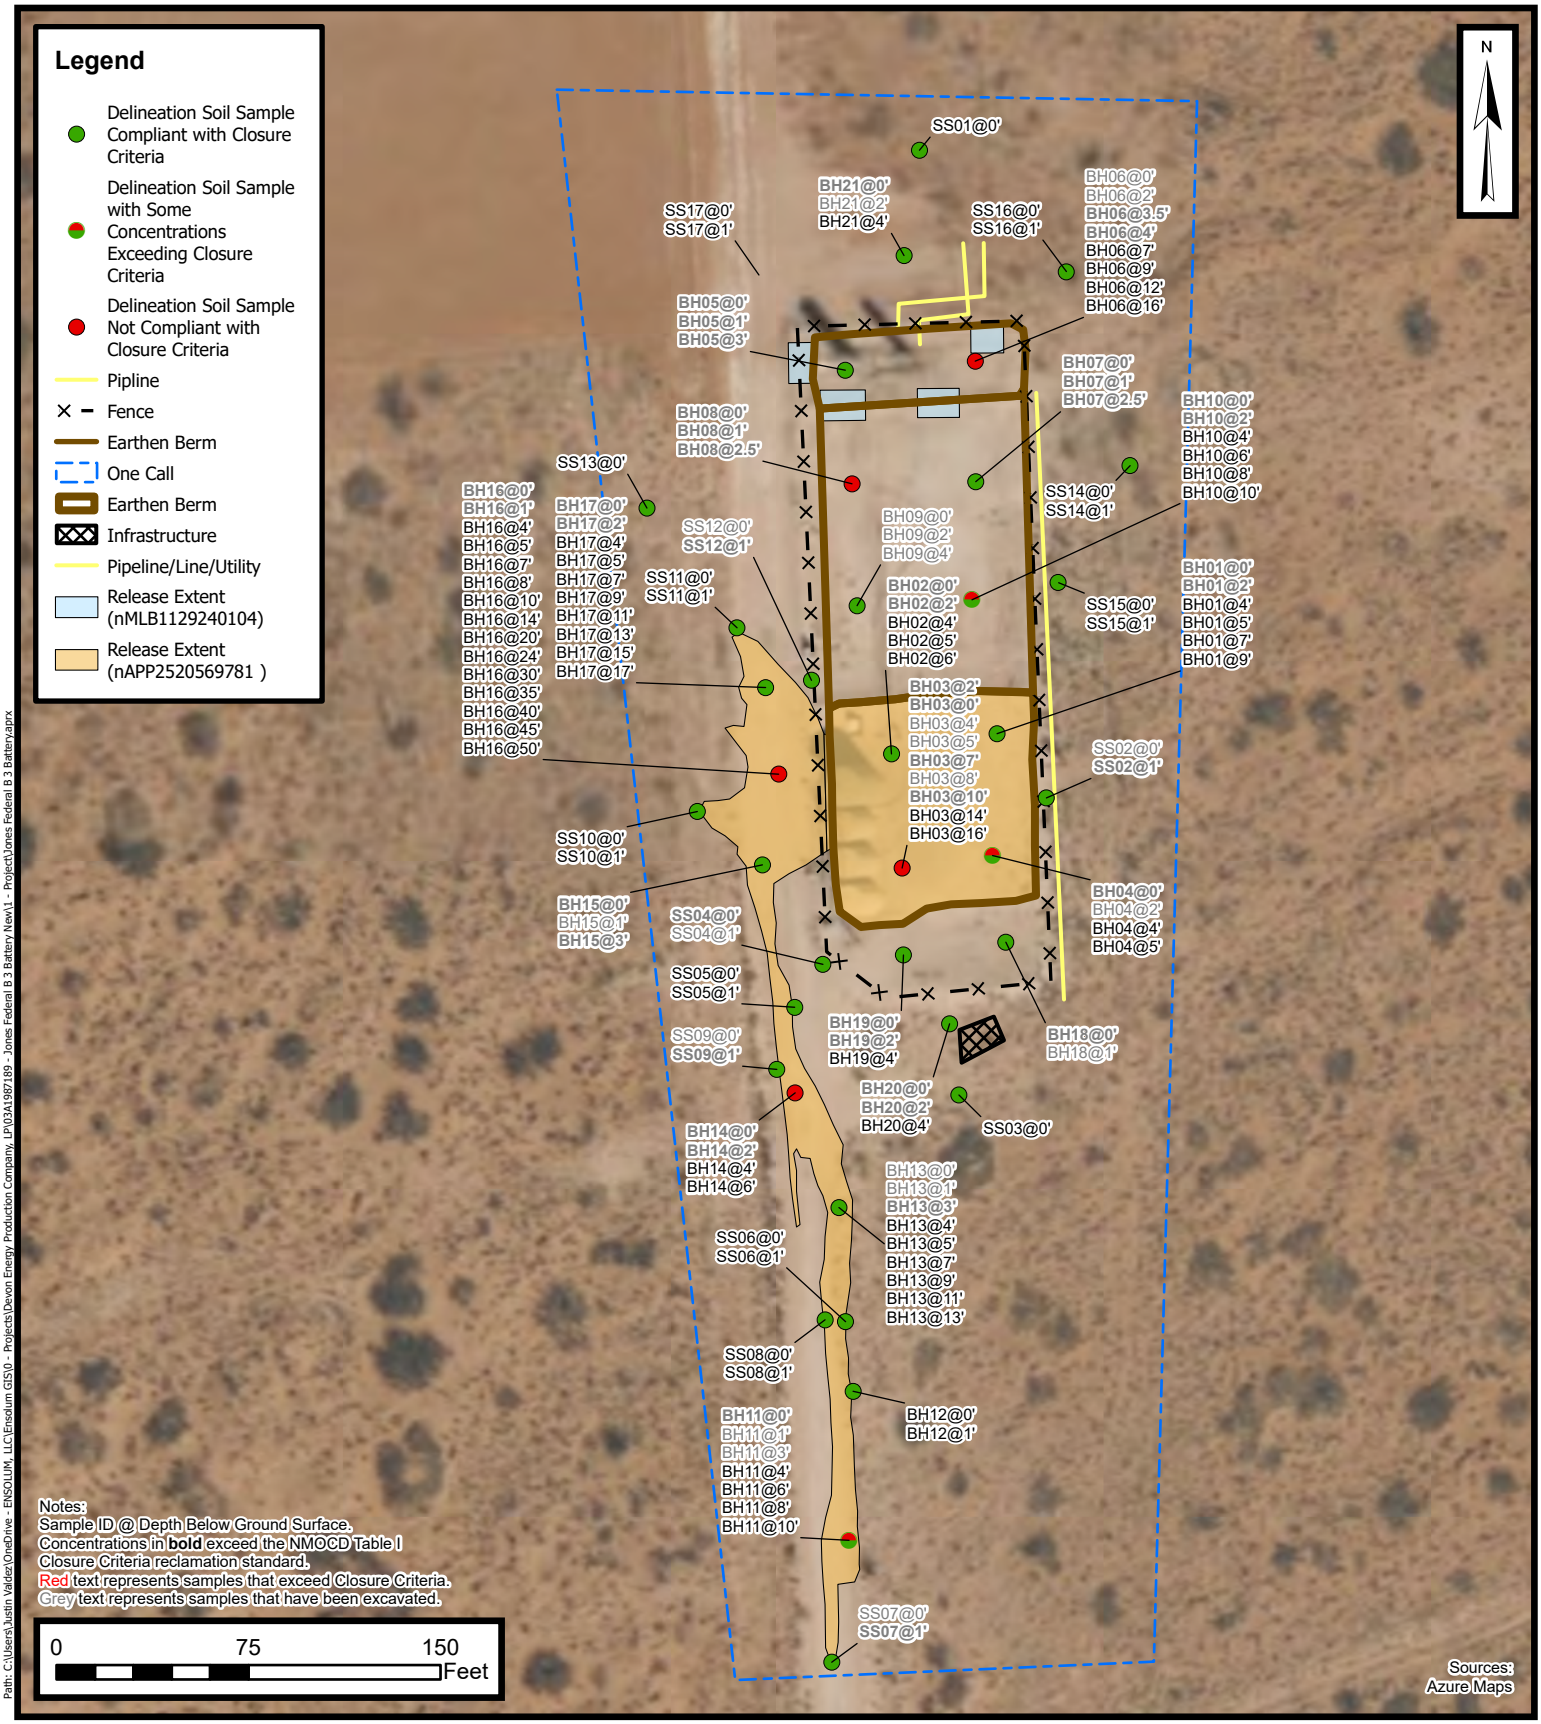

ENSOLUM
Environmental, Engineering and Hydrogeologic Consultants

Delineation Soil Sample Locations

Devon Energy Production Company, LP
Jones Federal B 3 Battery
Incident Number: nAPP2520569781 and nMLB1129240104
Unit K, Section 24, Township 19 South, Range 31 East
Eddy County, New Mexico

FIGURE
2

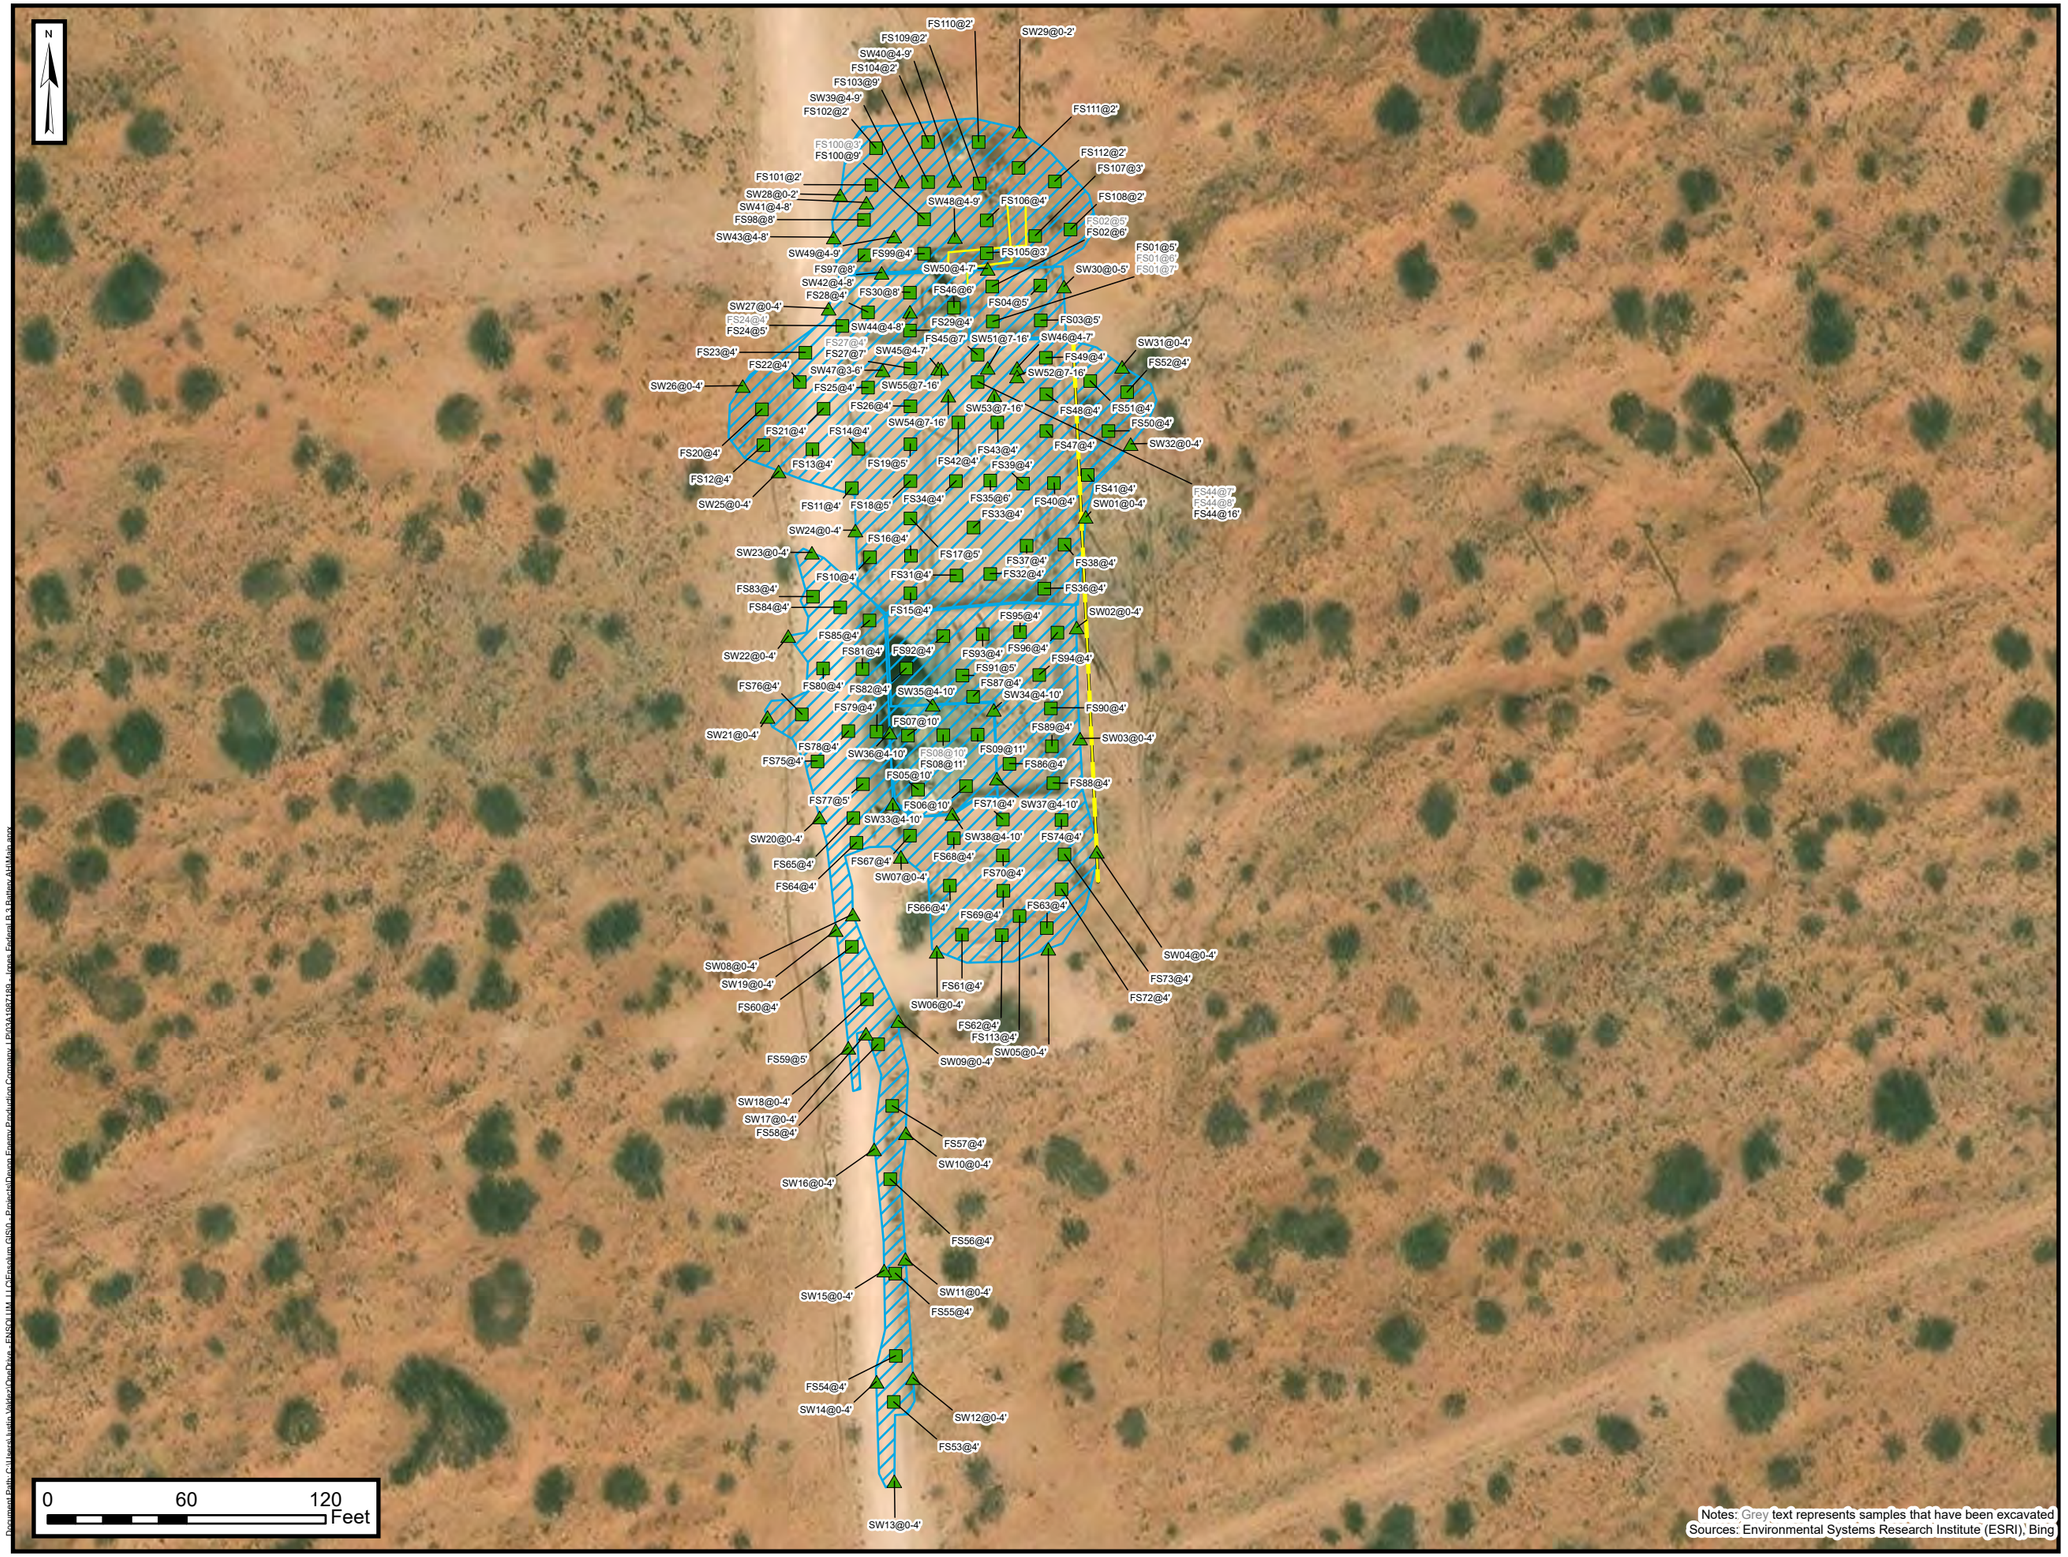

Legend

- Confirmation Floor Sample in Compliance with Closure Criteria
- Confirmation Sidewall Sample in Compliance with Closure Criteria
- Oil and Gas Utility Line
- Pipeline
- Excavation Extent

Confirmation Soil Sample Location

Devon Energy Production Company, LP
Jones Federal B 3 Battery
Incident Numbers: nMLB1129240104 & nAPP2520569781
Unit K, Section 24, T 19S, R 31E
Eddy County, New Mexico

FIGURE 3

ENSOLUM
Environmental, Engineering and Hydrogeologic Consultants

Document Path: C:\Users\kalina.vidal\Desktop\Projects\Devon Energy Production Company\20240129269 - Jones Federal B 3 Battery\MXD\Jones Federal B 3 Battery AtkMap.aprx

ENSOLUM

TABLES

ENSOLUM

TABLE 1
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Delineation Soil Samples										
SS01*	8/19/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS02*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	379
SS02*	7/29/2025	1	<0.0250	<0.0500	<20.0	55.7	108	55.7	**164**	**935**
SS03*	8/19/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	77.1
SS04*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**616**
SS04*	7/29/2025	1	<0.0250	<0.0500	<20.0	32.5	<50.0	32.5	32.5	404
SS05*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	345
SS05*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	406
SS06*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS06*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS07*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS07*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**613**
SS08*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS08*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS09*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS09*	7/29/2025	1	<0.0250	<0.0500	<20.0	38.7	66.0	38.7	**105**	91.0
SS10*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS10*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS11*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS11*	7/29/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS12*	7/29/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	530
SS12*	7/29/2025	1	<0.0250	<0.0500	<20.0	496	504	496	**1,000**	206
SS13*	8/19/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS14*	11/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	66.1
SS14*	11/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS15*	11/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS15*	11/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	42.0
SS16*	11/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS16*	11/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS17*	11/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	27.2
SS17*	11/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	39.5

ENSOLUM

TABLE 1
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Delineation Soil Samples										
SS18*	11/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SS18*	11/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
BH01*	8/7/2025	0	<0.0250	0.2305	<20.0	424	919.0	424	**1,343**	**9,480**
BH01*	8/11/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**1,840**
BH01	8/11/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,550
BH01	8/11/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,420
BH01	8/12/2025	7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,300
BH01	8/12/2025	9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	3,380
BH02*	8/7/2025	0	<0.0250	<0.0500	<20.0	192	264	192	**456**	**6,910**
BH02*	8/11/2025	2	<0.0250	<0.0500	<20.0	827	760	827	**1,587**	520
BH02	8/11/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	262
BH02	8/11/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	760
BH02	8/12/2025	6	<0.0250	<0.0500	<20.0	42.7	<50.0	42.7	<50.0	698
BH03*	8/7/2025	0	<0.0250	0.3673	<20.0	873	1,290	873	**2,163**	**6,070**
BH03*	8/11/2025	2	<0.0250	<0.0500	<20.0	205	271	205	**476**	**1,600**
BH03	8/11/2025	4	<0.0250	<0.0500	<20.0	132	196	132	328	1,430
BH03	8/11/2025	5	<0.0250	<0.0500	<20.0	162	225	162	387	322
BH03	8/12/2025	7	<0.0250	0.646	25.5	6,350	1,520	6,376	7,896	198
BH03	10/29/2025	8	<0.0250	<0.0500	<20.0	229	164	229	393	22.0
BH03	10/29/2025	10	<0.0250	0.3696	<20.0	7,500	3,330	7,500	10,830	<20.0
BH03	10/29/2025	14	<0.0250	<0.0500	<20.0	206	169	206	375	58.0
BH03	10/29/2025	16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	96
BH04*	8/7/2025	0	<0.0250	0.618	<20.0	12,500	8,950	**12,500**	**21,450**	**3,610**
BH04*	8/13/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	31.2
BH04	8/13/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,990
BH04	8/13/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	212
BH05*	8/7/2025	0	<0.0250	<0.0500	<20.0	838	1,380	838	**2,218**	76.3
BH05*	8/21/2025	1	<0.0250	<0.0500	<20.0	666	909	666	**1,575**	<20.0
BH05*	8/21/2025	3	<0.0250	<0.0500	<20.0	257	351	257	**608**	55.7

ENSOLUM

TABLE 1
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
BH06, BH09, BH10			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Delineation Soil Samples										
BH06*	8/7/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	59.7
BH06*	8/21/2025	2	<0.0250	<0.0500	<20.0	116	163	116	279	538
BH06*	8/21/2025	3.5	<0.0250	<0.0500	<20.0	1,470	1,740	**1,470**	**3,210**	**818**
BH06	8/7/2025	4	<0.0250	<0.0500	<20.0	2,790	2,040	**2,790**	**4,830**	551
BH06	8/7/2025	7	<0.0250	<0.0500	<20.0	271	280	271	**551**	**692**
BH06	8/7/2025	9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	483
BH06	8/7/2025	12	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**874**
BH06	8/7/2025	16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	474
BH07*	8/21/2025	0	<0.0250	1.6049	28.8	524	285	**553**	**838**	68.6
BH07*	8/21/2025	1	<0.0250	<0.0500	<20.0	49.8	78.2	48.9	**128**	178
BH07*	8/21/2025	2.5	<0.0250	<0.0500	<20.0	199	171	199	**370**	901
BH08*	8/21/2025	0	<0.0250	<0.0500	<20.0	60.5	71.7	60.5	**132**	47.9
BH08*	8/21/2025	1	<0.0250	<0.0500	<20.0	1,600	1,540	**1,600**	**3,140**	594
BH08*	8/21/2025	2.5	<0.0250	<0.0500	<20.0	230	309	230	539	**2,920**
BH09*	8/21/2025	0	<0.0250	<0.0500	<20.0	94.6	216	94.6	311	<20.0
BH09*	8/21/2025	2	<0.0250	<0.0500	<20.0	41.3	107	41.3	148	<20.0
BH09	8/21/2025	4	<0.0250	<0.0500	<20.0	107	156	107	263	72.4
BH10*	8/7/2025	0	<0.0250	<0.0500	<20.0	9,870	10,200	**9,870**	**20,070**	179
BH10*	8/12/2025	2	<0.0250	1.319	54.8	6,990	2,460	**7,044**	**9,505**	197
BH10	8/12/2025	4	<0.0250	0.1843	<20.0	855	674.0	855	1,529	396
BH10	8/12/2025	6	<0.0250	0.0501	<20.0	<25.0	<50.0	<25.0	<50.0	435
BH10	8/12/2025	8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**757**
BH10	8/12/2025	10	<0.0250	<0.0500	<20.0	41.8	<50.0	41.8	41.8	46.3
BH11*	8/12/2025	0	<0.0250	<0.0500	<20.0	1,110	649	**1,110**	**1,759**	367
BH11*	8/12/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
BH11*	8/12/2025	3	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	410
BH11	8/12/2025	4	<0.0250	<0.0500	<20.0	33.5	<50.0	33.5	33.5	588
BH11	8/12/2025	6	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,530
BH11	8/12/2025	8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	747
BH11	8/12/2025	10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	30.2
BH12*	8/12/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	285
BH12*	8/14/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0

ENSOLUM

TABLE 1
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Delineation Soil Samples										
BH13*	8/14/2025	0	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
BH13*	8/14/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	26.1
BH13*	8/14/2025	3	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**2,550**
BH13	8/14/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,180
BH13	8/14/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,810
BH13	8/14/2025	7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,040
BH13	8/14/2025	9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,530
BH13	8/14/2025	11	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,140
BH13	8/14/2025	13	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	80.9
BH14*	8/14/2025	0	<0.0250	<0.0500	<20.0	2,790	1,750	**2,790**	**4,540**	**1,690**
BH14*	8/14/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**1,370**
BH14	8/14/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,920
BH14	8/14/2025	6	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,740
BH15*	8/14/2025	0	<0.0250	<0.0500	<20.0	166	92.3	166	258	**2,300**
BH15*	8/19/2025	1	<0.0250	<0.0500	<20.0	93.0	168	93.0	261	552
BH15*	8/19/2025	3	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**955**
BH16*	8/14/2025	0	<0.0250	<0.0500	<20.0	1,040	421	**1,040**	**1,461**	**7,950**
BH16*	8/14/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**755**
BH16	8/14/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	6,610
BH16	8/14/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	6,380
BH16	8/14/2025	7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	6,760
BH16	10/29/2025	8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	4,520
BH16	10/29/2025	10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,140
BH16	10/29/2025	14	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	4,400
BH16	10/29/2025	20	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,380
BH16	10/29/2025	24	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	756
BH16	10/29/2025	30	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,470
BH16	10/29/2025	35	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,560
BH16	10/29/2025	40	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,260
BH16	10/29/2025	45	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	693
BH16	10/29/2025	50	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	447

ENSOLUM

TABLE 1
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Delineation Soil Samples										
BH17*	8/14/2025	0	<0.0250	<0.0500	<20.0	179	143	179	**322**	124
BH17*	8/14/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**626**
BH17	8/14/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	5,030
BH17	8/14/2025	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	3,080
BH17	8/14/2025	7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,980
BH17	8/14/2025	9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,550
BH17	8/19/2025	11	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	389
BH17	8/19/2025	13	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,280
BH17	8/19/2025	15	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,720
BH17	8/19/2025	17	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,690
BH18*	8/21/2025	0	<0.0250	<0.0500	<20.0	55.8	71.4	55.8	**127**	<20.0
BH18*	8/21/2025	1	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
BH19*	8/21/2025	0	<0.0250	<0.0500	<20.0	956	1,380	956	**2,336**	50.0
BH19*	8/21/2025	2	<0.0250	<0.0500	<20.0	166	213	166	**379**	<20.0
BH19	8/21/2025	4	<0.0250	<0.0500	<20.0	105	184	105	**289**	<20.0
BH20*	8/21/2025	0	<0.0250	<0.0500	<20.0	31.9	94.4	31.9	**126**	<20.0
BH20*	8/21/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	**731**
BH20	8/21/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,220
BH21*	8/21/2025	0	<0.0250	<0.0500	<20.0	54.7	64.6	54.7	**119**	328
BH21*	8/21/2025	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	126
BH21	8/21/2025	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	551

Notes:

bgs: below ground surface

mg/kg: milligrams per kilogram

NMOCD: New Mexico Oil Conservation Division

NMAC: New Mexico Administrative Code

Grey text represents samples that have been excavated

Red *text represents samples that exceed Closure Criteria*

"<": Laboratory Analytical result is less than reporting limit

Concentrations in ***bold*** *exceed the reclamation standard where applicable.*

GRO: Gasoline Range Organics

DRO: Diesel Range Organics

ORO: Oil Range Organics

TPH: Total Petroleum Hydrocarbon

BTEX: Benzene, Toluene, Ethylbenzene, and Xylenes

** Indicates sample was collected in area to be reclaimed after remediation is complete; reclamation for chloride in the top 4 feet is 600 mg/kg and total TPH is 100 mg/kg.*

ENSOLUM

TABLE 2
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Excavation Floor Soil Samples										
FS01	2/3/2026	5	<0.0250	<0.0500	<20.0	1,030	698	1,030	1,728	784
FS01	2/12/2026	6	<0.0250	<0.0500	<20.0	1,870	752	1,870	2,622	1,170
FS01	2/25/2026	7	<0.0250	<0.0500	<20.0	286	163	286	449	1,330
FS02	2/3/2026	5	<0.0250	<0.0500	<20.0	1,160	825	1,160	1,985	924
FS02	2/12/2026	6	<0.0250	<0.500	<20.0	<25.0	<50.0	<25.0	<50.0	1680
FS03	2/3/2026	5	<0.0250	<0.0500	<20.0	68.6	113	68.6	181.6	669
FS04	2/3/2026	5	<0.0250	<0.0500	<20.0	47.9	65.0	47.9	113	631
FS05	1/30/2026	10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,160
FS06	1/29/2026	10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,240
FS07	2/9/2026	10	<0.0250	<0.0500	<20.0	924	400	924	1,324	<20.0
FS08	1/30/2026	10	<0.0250	<0.0500	<20.0	1,150	627	1,150	1,777	33.6
FS08	2/9/2026	11	<0.0250	<0.0500	<20.0	562	313	562	875	22.2
FS09	2/3/2026	11	<0.0250	<0.0500	<20.0	565	394	565	959	<20.0
FS10	2/10/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	686
FS11	2/10/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	355
FS12	2/5/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	83.6
FS13	2/12/2026	4	<0.0250	<0.0500	<20.0	124	80.8	124	204.8	436
FS14	2/10/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	103
FS15	2/2/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	449
FS16	2/2/2026	4	<0.0250	<0.0500	<20.0	404	494	404	898	66.9
FS17	2/3/2026	5	<0.0250	<0.0500	<20.0	124	141	124	265	88.7
FS18	2/4/2026	5	<0.0250	<0.0500	<20.0	27.5	<50.0	27.5	27.5	526
FS19	2/4/2026	5	<0.0250	0.102	<20.0	863	313	863	1,176	2,370
FS20	2/5/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	391
FS21	2/12/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	737
FS22	2/12/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	259
FS23	2/12/2026	4	<0.0250	<0.0500	<20.0	218	141	218	359	420
FS24	2/11/2026	4	<0.0250	<0.0500	<20.0	1,330	673	1,330	2,003	1,530
FS24	2/25/2026	5	<0.0250	<0.0500	<20.0	41.9	<50.0	41.9	41.9	154
FS25	2/10/2026	4	<0.0250	<0.0500	<20.0	54.5	<50.0	54.5	54.5	135
FS26	2/4/2026	4	<0.0250	<0.0500	<20.0	670	335	670	1,005	1,930

ENSOLUM

TABLE 2
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Excavation Floor Soil Samples										
FS27	2/4/2026	4	<0.0250	<0.0500	<20.0	1,660	904	1,660	2,564	824
FS27	2/25/2026	7	<0.0250	<0.0500	<20.0	194	112	194	306	953
FS28	2/11/2026	4	<0.0250	<0.0500	<20.0	483	373	483	856	993
FS29	2/4/2026	4	<0.0250	<0.0500	<20.0	970	807	970	1,777	444
FS30	2/10/2026	8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	674
FS31	2/2/2026	4	<0.0250	<0.0500	<20.0	52.7	93.3	52.7	146	543
FS32	2/2/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	270
FS33	2/2/2026	4	<0.0250	<0.0500	<20.0	640	487	640	1,127	404
FS34	2/2/2026	4	<0.0250	0.166	<20.0	810	371	810	1,181	285
FS35	2/5/2026	6	<0.0250	<0.0500	<20.0	481	319	481	800	552
FS36	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	920
FS37	1/30/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
FS38	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	62.3
FS39	2/4/2026	4	<0.0250	<0.0500	<20.0	170	172	170	342	574
FS40	1/30/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	198
FS41	1/30/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,310
FS42	2/3/2026	4	<0.0250	<0.0500	<20.0	328	307	328	635	987
FS43	2/3/2026	4	<0.0250	0.0536	<20.0	1,130	971	1,130	2,101	2,370
FS43	2/12/2026	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,080
FS44	2/6/2026	7	<0.0250	<0.0500	<20.0	1,750	791	1,750	2,541	2,030
FS44	2/25/2026	8	<0.0250	<0.0500	<20.0	1,590	727	1,590	2,317	1,510
FS44	3/11/2026	16	<0.0250	<0.0500	<20.0	80.7	<50.0	80.7	80.7	293
FS45	2/12/2026	7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,670
FS46	2/6/2026	6	<0.0250	<0.0500	<20.0	391	299	391	690	1,620
FS47	2/2/2026	4	<0.0250	<0.0500	<20.0	182	195	182	377	1,670
FS48	2/2/2026	4	<0.0250	<0.0500	<20.0	353	373	353	726	2,040
FS49	2/2/2026	4	<0.0250	<0.0500	<20.0	611	486	611	1,097	1,350
FS50	1/30/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,070
FS51	2/2/2026	4	<0.0250	<0.0500	<20.0	298	261	298	559	2,250
FS52	1/30/2026	4	<0.0250	<0.0500	<20.0	28.5	<50.0	28.5	28.5	189
FS53	2/5/2026	4	<0.0250	<0.0500	<20.0	34.4	<50.0	34.4	34.4	645

ENSOLUM

TABLE 2
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Excavation Floor Soil Samples										
FS54	2/5/2026	4	<0.0250	0.0472	<20.0	40.3	<50.0	40.3	40.3	485
FS55	2/5/2026	4	<0.0250	0.0270	<20.0	241	172.0	241	413	153
FS56	2/5/2026	4	<0.0250	<0.0500	<20.0	45.2	<50.0	45.2	45.2	77.2
FS57	2/6/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	966
FS58	2/6/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,480
FS59	2/9/2026	5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,080
FS60	2/11/2026	4	<0.0250	<0.0500	<20.0	136	90.8	136	226.8	1,180
FS61	1/23/2026	4	<0.0250	<0.0500	<20.0	452	490	452	942	453
FS62	1/23/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	221
FS63	1/23/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	30.2
FS64	2/11/2026	4	<0.0250	<0.0500	<20.0	30.6	<50.0	30.6	30.6	587
FS65	2/9/2026	4	<0.0250	<0.0500	<20.0	84.8	<50.0	84.8	<50.0	1,660
FS66	1/23/2026	4	<0.0250	<0.0500	<20.0	494	441	494	935	1,010
FS67	1/29/2026	4	<0.0250	<0.0500	<20.0	56.2	56.3	56.2	112.5	51.3
FS68	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	219
FS69	1/23/2026	4	<0.0250	<0.0500	<20.0	651	709	651	1,360	1,890
FS70	1/28/2026	4	<0.0250	<0.0500	<20.0	131	206	131	337	61.6
FS71	1/28/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	111
FS72	1/23/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	39.6
FS73	1/23/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
FS74	1/23/2026	4	<0.0250	<0.0500	<20.0	32.0	55.8	32.0	87.8	1,140
FS75	2/12/2026	4	<0.0250	<0.0500	<20.0	307	271	307	578	935
FS76	2/12/2026	4	<0.0250	<0.0500	<20.0	420	278	420	698	764
FS77	2/9/2026	5	<0.0250	<0.0500	<20.0	455	262	455	717	1,310
FS78	2/12/2026	4	<0.0250	<0.0500	<20.0	313	295	313	608	921

ENSOLUM

TABLE 2
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Excavation Floor Soil Samples										
FS79	2/9/2026	4	<0.0250	<0.0500	<20.0	80.2	58.1	80.2	138.3	865
FS80	2/12/2026	4	<0.0250	<0.0500	<20.0	214	213	214	427	1,500
FS81	2/10/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	5,560
FS82	1/30/2026	4	<0.0250	<0.0500	<20.0	95.9	117	95.9	212.9	530
FS83	2/12/2026	4	<0.0250	<0.0500	<20.0	295	214	295	509	2,430
FS84	2/10/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	5,130
FS85	2/10/2026	4	<0.0250	<0.0500	<20.0	39.9	<50.0	39.9	39.9	815
FS86	1/28/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	998
FS87	1/28/2026	4	<0.0250	<0.0500	<20.0	44.9	67.0	44.9	111.9	86.9
FS88	1/23/2026	4	<0.0250	<0.0500	<20.0	38.1	69.0	38.1	107.1	1,850
FS89	1/28/2026	4	<0.0250	<0.0500	<20.0	30.9	<50.0	30.9	31	1,580
FS90	1/28/2026	4	<0.0250	<0.0500	<20.0	102	99.4	102	201.4	2,460
FS91	2/3/2026	5	<0.0250	<0.0500	<20.0	101	123	101	224	1,130
FS92	1/30/2026	4	<0.0250	<0.0500	<20.0	187	222	187	409	807
FS93	1/30/2026	4	<0.0250	<0.0500	<20.0	139	158	139	297	1,330
FS94	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	3,850
FS95	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,300
FS96	1/29/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	4,020
FS97	2/11/2026	8	<0.0250	<0.0500	<20.0	59.5	<50.0	59.5	59.5	623
FS98	2/11/2026	8	<0.0250	<0.0500	<20.0	54.3	<50.0	54.3	54.3	815
FS99	2/9/2026	4	<0.0250	<0.0500	<20.0	457	445	457	902	534
FS100	2/6/2026	3	<0.0250	<0.0500	<20.0	49.6	68.2	49.6	117.8	230
FS100	2/26/2026	9	<0.0250	<0.0500	<20.0	93.8	<50.0	93.8	93.8	537
FS101*	2/6/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	223
FS102*	2/6/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	290
FS103	2/10/2026	9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	264
FS104*	2/4/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	73.3
FS105	2/4/2026	3	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	304

ENSOLUM

TABLE 2
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			**10**	**50**	**NE**	**NE**	**NE**	**NE**	**100**	**600**
NMOCD Table I Closure Criteria (NMAC 19.15.29)			**10**	**50**	**NE**	**NE**	**NE**	**1,000**	**2,500**	**20,000**
Excavation Floor Soil Samples										
FS106	2/25/2026	4	<0.0250	<0.0500	<20.0	671	378	671	1,049	602
FS107*	2/4/2026	3	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	236
FS108*	2/3/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	308
FS109*	2/3/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
FS110*	2/3/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	49.3
FS111*	2/4/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	50.3
FS112*	2/4/2026	2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
FS113	2/26/2026	4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,230

Notes:

bgs: below ground surface

mg/kg: milligrams per kilogram

NMOCD: New Mexico Oil Conservation Division

NMAC: New Mexico Administrative Code

Grey text represents samples that have been excavated

Red *text represents samples that exceed Closure Criteria*

"<": Laboratory Analytical result is less than reporting limit

GRO: Gasoline Range Organics

DRO: Diesel Range Organics

ORO: Oil Range Organics

TPH: Total Petroleum Hydrocarbon

BTEX: Benzene, Toluene, Ethylbenzene, and Xylenes

Concentrations in ***bold*** *exceed the reclamation standard where applicable.*

** Indicates sample was collected in area to be reclaimed after remediation is complete; reclamation for chloride in the top 4 feet is 600 mg/kg and total TPH is 100 mg/kg.*

ENSOLUM

TABLE 3
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			10	50	NE	NE	NE	NE	100	600
NMOCD Table I Closure Criteria (NMAC 19.15.29)			10	50	NE	NE	NE	1,000	2,500	20,000
Sidewall Soil Samples										
SW01*	1/30/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	105
SW02*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	116
SW03*	2/4/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW04*	1/30/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	31.8
SW05*	2/4/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	49.8
SW06*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW07*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW08*	2/11/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW09*	2/6/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	66.6
SW10*	2/6/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	21.8
SW11*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW12*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW13*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW14*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW15*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW16*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	29.2
SW17*	2/6/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW18*	2/11/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	56.5
SW19*	2/11/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW20*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	43.9
SW21*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	41.7
SW22*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW23*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW24*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	246
SW25*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW26*	2/5/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW27*	2/12/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW28*	2/11/2026	0-2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	55.9
SW29*	2/10/2026	0-2	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW30*	2/10/2026	0-5	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	82.6
SW31*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0

ENSOLUM

TABLE 3
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			**10**	**50**	**NE**	**NE**	**NE**	**NE**	**100**	**600**
NMOCD Table I Closure Criteria (NMAC 19.15.29)			**10**	**50**	**NE**	**NE**	**NE**	**1,000**	**2,500**	**20,000**
Sidewall Soil Samples										
SW32*	2/10/2026	0-4	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	81.8
SW33	2/4/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,290
SW34	2/4/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	44.5
SW35	2/4/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,880
SW36	2/9/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,070
SW37	2/4/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	3,220
SW38	2/4/2026	4-10	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	423
SW39	2/13/2026	4-9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	2,190
SW40	2/13/2026	4-9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	1,200
SW41	2/13/2026	4-8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	172
SW42	2/13/2026	4-8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	329
SW43	2/13/2026	4-8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	162
SW44	2/13/2026	4-8	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	179
SW45	2/13/2026	4-7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	224
SW46	2/13/2026	4-7	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	588
SW47	2/13/2026	3-6	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	183
SW48	2/27/2026	4-9	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	677
SW49	2/27/2026	4-9	<0.0250	<0.0500	<20.0	50.8	<50.0	50.8	50.8	765
SW50	2/26/2026	4-7	<0.0250	<0.0500	<20.0	116	92.3	116	208.3	1,370
SW51	3/11/2026	7-16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	130
SW52	3/11/2026	7-16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	457
SW53	3/11/2026	7-16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
SW54	3/11/2026	7-16	<0.0250	<0.0500	<20.0	67.1	<50.0	67.1	67.1	368
SW55	3/11/2026	7-16	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	159

Notes:

bgs: below ground surface
mg/kg: milligrams per kilogram
NMOCD: New Mexico Oil Conservation Division
NMAC: New Mexico Administrative Code
Grey text represents samples that have been excavated
Red *text represents samples that exceed Closure Criteria*
Concentrations in ***bold*** *exceed the reclamation standard where applicable.*
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
ORO: Oil Range Organics
TPH: Total Petroleum Hydrocarbon
BTEX: Benzene, Toluene, Ethylbenzene, and Xylenes
"<": Laboratory Analytical result is less than reporting limit

** Indicates sample was collected in area to be reclaimed after remediation is complete; reclamation for chloride in the top 4 feet is 600 mg/kg and total TPH is 100 mg/kg.*

ENSOLUM

TABLE 4
SOIL SAMPLE ANALYTICAL RESULTS
Jones Federal B 3 Battery
Devon Energy Production Company, LP
Eddy County, New Mexico

Sample Designation	Date	Depth (feet bgs)	Benzene (mg/kg)	Total BTEX (mg/kg)	TPH GRO (mg/kg)	TPH DRO (mg/kg)	TPH ORO (mg/kg)	GRO+DRO (mg/kg)	Total TPH (mg/kg)	Chloride (mg/kg)
NMOCD Reclamation Requirement (NMAC 19.15.29.13.D)			**10**	**50**	**NE**	**NE**	**NE**	**NE**	**100**	**600**
NMOCD Table I Closure Criteria (NMAC 19.15.29)			**10**	**50**	**NE**	**NE**	**NE**	**1,000**	**2,500**	**20,000**
Sidewall Soil Samples										
BF01	1/19/2026	NA	<0.0250	<0.0500	<20.0	<25.0	<50.0	<25.0	<50.0	<20.0
BF02	2/5/2026	NA	<0.0250	<0.0500	<20.1	<25.1	<50.1	<25.1	<50.1	71.1

Notes:

bgs: below ground surface

mg/kg: milligrams per kilogram

NMOCD: New Mexico Oil Conservation Division

NMAC: New Mexico Administrative Code

Grey text represents samples that have been excavated

Red *text represents samples that exceed Closure Criteria*

"<": Laboratory Analytical result is less than reporting limit

Concentrations in ***bold*** *exceed the reclamation standard where applicable.*

GRO: Gasoline Range Organics

DRO: Diesel Range Organics

ORO: Oil Range Organics

TPH: Total Petroleum Hydrocarbon

BTEX: Benzene, Toluene, Ethylbenzene, and Xylenes

** Indicates sample was collected in area to be reclaimed after remediation is complete; reclamation for chloride in the top 4 feet is 600 mg/kg and total TPH is 100 mg/kg.*

ENSOLUM

APPENDIX A

Well Record and Log

WELL RECORD & LOG

OFFICE OF THE STATE ENGINEER

www.ose.state.nm.us

1. GENERAL AND WELL LOCATION

OSE POD NO. (WELL NO.): Pod 1	WELL TAG ID NO.	OSE FILE NO(S): CP-2091
WELL OWNER NAME(S): Devon Energy Production Company, LP		PHONE (OPTIONAL)
WELL OWNER MAILING ADDRESS: 5313 Buena Vista Dr.		CITY: Carlsbad STATE: NM ZIP: 88220

WELL LOCATION (FROM GPS)		DEGREES	MINUTES	SECONDS	
	LATITUDE	32	38	34.49	N
	LONGITUDE	103	49	28.11	W

* ACCURACY REQUIRED: ONE TENTH OF A SECOND
* DATUM REQUIRED: WGS 84

DESCRIPTION RELATING WELL LOCATION TO STREET ADDRESS AND COMMON LANDMARKS – PLSS (SECTION, TOWNSHIP, RANGE) WHERE AVAILABLE: Section 24 Township 19s Range 31e

2. DRILLING & CASING INFORMATION

LICENSE NO.	NAME OF LICENSED DRILLER	NAME OF WELL DRILLING COMPANY
WD-1862	James Hawley	H&R Enterprises, LLC

DRILLING STARTED	DRILLING ENDED	DEPTH OF COMPLETED WELL (FT)	BORE HOLE DEPTH (FT)	DEPTH WATER FIRST ENCOUNTERED (FT)
10-28-25	10-28-25	105'	105'	N/A

COMPLETED WELL IS: ☐ ARTESIAN ☑ DRY HOLE ☐ SHALLOW (UNCONFINED) — STATIC WATER LEVEL IN COMPLETED WELL (FT): N/A

DRILLING FLUID: ☑ AIR ☐ MUD ADDITIVES – SPECIFY:

DRILLING METHOD: ☑ ROTARY ☐ HAMMER ☐ CABLE TOOL ☐ OTHER – SPECIFY:

DEPTH (feet bgl) FROM	DEPTH (feet bgl) TO	BORE HOLE DIAM (inches)	CASING MATERIAL AND/OR GRADE (include each casing string, and note sections of screen)	CASING CONNECTION TYPE (add coupling diameter)	CASING INSIDE DIAM. (inches)	CASING WALL THICKNESS (inches)	SLOT SIZE (inches)
0	105'	6"	No casing left in hole				

3. ANNULAR MATERIAL

DEPTH (feet bgl) FROM	DEPTH (feet bgl) TO	BORE HOLE DIAM. (inches)	LIST ANNULAR SEAL MATERIAL AND GRAVEL PACK SIZE-RANGE BY INTERVAL	AMOUNT (cubic feet)	METHOD OF PLACEMENT
			N/A		

WR-20 WELL RECORD & LOG (Version 04/30/19)

FOR OSE INTERNAL USE

FILE NO.	POD NO.	TRN NO.
LOCATION	WELL TAG ID NO.	PAGE 1 OF 2

4. HYDROGEOLOGIC LOG OF WELL

DEPTH (feet bgl) FROM	DEPTH (feet bgl) TO	THICKNESS (feet)	COLOR AND TYPE OF MATERIAL ENCOUNTERED - INCLUDE WATER-BEARING CAVITIES OR FRACTURE ZONES **(attach supplemental sheets to fully describe all units)**	WATER BEARING? (YES / NO)	ESTIMATED YIELD FOR WATER-BEARING ZONES (gpm)
0'	20'	20'	Red Sandy Clay	Y ✓ N	
20'	25'	5'	Sand	Y ✓ N	
25'	30'	5'	Caliche	Y ✓ N	
30'	40'	10'	Sandy Caliche	Y ✓ N	
40'	55'	15'	Red Sandy Clay	Y ✓ N	
55'	70'	15'	Sand	Y ✓ N	
70'	80'	10'	Red Clay	Y ✓ N	
80'	105'	25'	Gray Sandy Clay	Y ✓ N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	
				Y N	

METHOD USED TO ESTIMATE YIELD OF WATER-BEARING STRATA:

☐ PUMP ☐ AIR LIFT ☐ BAILER ☑ OTHER – SPECIFY: dry hole

TOTAL ESTIMATED WELL YIELD (gpm): 0.00

5. TEST; RIG SUPERVISION

WELL TEST: TEST RESULTS - ATTACH A COPY OF DATA COLLECTED DURING WELL TESTING, INCLUDING DISCHARGE METHOD, START TIME, END TIME, AND A TABLE SHOWING DISCHARGE AND DRAWDOWN OVER THE TESTING PERIOD.

MISCELLANEOUS INFORMATION: Depth to groundwater bore was gauged for water on 10-31-25 at the Devon Jones Federal B 3 Battery Remediation site. DTGW bore was dry. Temporary well casing was removed, bore hole was backfilled with drill cuttings to 10' BGS. Hydrated bentonite hole plug was poured from 10' BGS to surface.

PRINT NAME(S) OF DRILL RIG SUPERVISOR(S) THAT PROVIDED ONSITE SUPERVISION OF WELL CONSTRUCTION OTHER THAN LICENSEE:

Nathan Smelcer

6. SIGNATURE

BY SIGNING BELOW, I CERTIFY THAT TO THE BEST OF MY KNOWLEDGE AND BELIEF, THE FOREGOING IS A TRUE AND CORRECT RECORD OF THE ABOVE DESCRIBED WELL. I ALSO CERTIFY THAT THE WELL TAG, IF REQUIRED, HAS BEEN INSTALLED AND THAT THIS WELL RECORD WILL ALSO BE FILED WITH THE PERMIT HOLDER WITHIN 30 DAYS AFTER THE COMPLETION OF WELL DRILLING.

JAMES Hawley — SIGNATURE OF DRILLER / PRINT SIGNEE NAME

10/31/25 — DATE

FOR OSE INTERNAL USE — WR-20 WELL RECORD & LOG (Version 04/30/2019)

FILE NO.	POD NO.	TRN NO.	
LOCATION		WELL TAG ID NO.	PAGE 2 OF 2

PLUGGING RECORD

NOTE: A Well Plugging Plan of Operations shall be approved by the State Engineer prior to plugging - 19.27.4 NMAC

I. GENERAL / WELL OWNERSHIP:

State Engineer Well Number: CP-2091 Pod 1

Well owner: Devon Energy Production Company, LP Phone No.: 575-689-7597

Mailing address: 5315 Buena Vista Dr.

City: Carlsbad State: NM Zip code: 88220

II. WELL PLUGGING INFORMATION:

1) Name of well drilling company that plugged well: H&R Enterprises, LLC

2) New Mexico Well Driller License No.: WD-1862 Expiration Date: 6/16/27

3) Well plugging activities were supervised by the following well driller(s)/rig supervisor(s): Nathan Smelcer

4) Date well plugging began: 10-31-25 Date well plugging concluded: 10-31-25

5) GPS Well Location: Latitude: 32 deg, 38 min, 34.49 sec
Longitude: 103 deg, 49 min, 28.11 sec, WGS 84

6) Depth of well confirmed at initiation of plugging as: 105 ft below ground level (bgl), by the following manner: well sounder

7) Static water level measured at initiation of plugging: N/A ft bgl

8) Date well plugging plan of operations was approved by the State Engineer: 9/11/25

9) Were all plugging activities consistent with an approved plugging plan? yes If not, please describe differences between the approved plugging plan and the well as it was plugged (attach additional pages as needed):

10) Log of Plugging Activities - Label vertical scale with depths, and indicate separate plugging intervals with horizontal lines as necessary to illustrate material or methodology changes. Attach additional pages if necessary.

For each interval plugged, describe within the following columns:

Depth (ft bgl)	Plugging Material Used (include any additives used)	Volume of Material Placed (gallons)	Theoretical Volume of Borehole/ Casing (gallons)	Placement Method (tremie pipe, other)	Comments ("casing perforated first", "open annular space also plugged", etc.)
	0' - 10' Hydrated Bentonite	Approx. 15 gallons	15 gallons	pour	
	10' - 105' Drill Cuttings	Approx. 140 gallons	140 Gallons	pour	

MULTIPLY		BY		AND OBTAIN
cubic feet	x	7.4805	=	gallons
cubic yards	x	201.97	=	gallons

III. SIGNATURE:

I, James Hawley, say that I am familiar with the rules of the Office of the State Engineer pertaining to the plugging of wells and that each and all of the statements in this Plugging Record and attachments are true to the best of my knowledge and belief.

Signature of Well Driller

10/31/25
Date

Version: September 8, 2009
Page 2 of 2

ENSOLUM

APPENDIX B

Environmental Desktop Review

Received by OCD: 5/4/2026 10:36:24 AM

New Mexico Department of Game and Fish
Project ID: NMERT-4934
Project Number: 03A1987189

PROJECT INFORMATION

Project Title:	Jones Federal B 3 Battery
Project Type:	ENERGY DEVELOPMENT, OIL AND GAS TRANSMISSION (PIPELINE), OIL AND GAS PIPELINES, MAINTENANCE OR EXISTING AREAS
Latitude/Longitude (DMS):	32.642140 / -103.824587
County(s):	EDDY
Project Description:	Ensolum, LLC (Ensolum), on behalf of Devon Energy Production Company, LP (Devon), has prepared the following Remediation Summary to document assessment activities associated with a crude oil release at the Jones Federal B 3 Battery (Site) located in Unit K, Section 24, Township 19 South, Range 31 East, in Eddy County, New Mexico. The Site (32.64265223, -103.824532) is associated with oil and gas exploration and production operations on Federal Land managed by the Bureau of Land Management (BLM). The spill area is depicted in Figure 1. On July 24, 2025, A lightning strike caused a fire at the Site. This resulted in the release of approx. 10 bbls of crude oil onto the caliche pad, road and pasture land managed by the BLM. Release coordinates are as follows: 32.64265223, -103.824532. No fluids were able to be recovered. Devon notified the BLM of the approx.. 10 bbl release via email on April 10, 2025 (Appendix A) . The release impacted a total surface area of 6,741 ft2. The fire department responded immediately to the fire and was able to extinguish it to prevent further spread of contaminated materials. Ensolum, is conducting an environmental desktop review for consultation.

REQUESTOR INFORMATION

Project Organization:	
Contact Name:	Azad Vojdani
Email Address:	avojdani@ensolum.com
Organization:	Ensolum, LLC
Address:	3122 National Parks Hwy, Carlsbad NM 88220
Phone:	5752666183

OVERALL STATUS

The information contained within this report comprises the recommendations of the New Mexico Department of Game and Fish (Department) for management and mitigation of proposed project impacts to wildlife and habitat resources; see the Project Recommendations section below for further details. No further consultation with the Department is required based on the project's location and, with implementation of mitigation measures described in the Project Recommendations section below, no adverse effects to wildlife or important habitats are anticipated. However, a Department biologist may be in touch within 30 days if they determine that further review is required.

Released to Imaging: 6/17/2026 3:16:23 PM

Received by OCD: 5/4/2026 10:36:24 AM

About this report:

- This environmental review is based on the project description and location that was entered. The report must be updated if the project type, area, or operational components are modified.
- This is a preliminary environmental screening assessment and report. It is not a substitute for the potential wildlife knowledge gained by having a biologist conduct a field survey of the project area. Federal status and plant data are provided as a courtesy to users. The review is also not intended to replace consultation required under the federal Endangered Species Act (ESA), including impact analyses for federal resources from the U.S. Fish and Wildlife Service (USFWS) using their Information for Planning and Consultation tool.
- This report contains information on wildlife species protected under the ESA and the Wildlife Conservation Act (WCA), Species of Greatest Conservation Need (SGCN), and Species of Economic and Recreational Importance (SERI). Species listed under the ESA are protected from take at the federal level and under the WCA are protected from take at the state level. SGCN are identified in the State Wildlife Action Plan (SWAP) for New Mexico; all of these species are considered to be of conservation concern but not all of them are protected from take at the state or federal level. The harvest of all SERI is regulated at the state level. The Department has no authority to designate critical habitat for species listed under the WCA; only the USFWS can designate critical habitat for species listed under the ESA.
- The New Mexico Environmental Review Tool (ERT) utilizes species observation locations and species habitat suitability models, both of which are subject to ongoing change and refinement. Inclusion or omission of a species within a report cannot guarantee species presence or absence within your project area. To determine occurrence of any species listed in this report, or other wildlife that may be present within your project area, onsite surveys conducted by a qualified biologist during appropriate, species-specific survey timelines may be necessary.
- The Department encourages use of the ERT to modify proposed projects for avoidance, minimization, or mitigation of wildlife impacts. However, the ERT is not intended to be used in a repeatedly iterative fashion to adjust project attributes until a previously determined recommendation is generated. The ERT serves to assess impacts once project details are developed. The New Mexico Crucial Habitat Assessment Tool, the data layers from which are included in the ERT, is the appropriate system for advising early-stage project planning and design to avoid areas of anticipated wildlife concerns and associated regulatory requirements.

Released to Imaging: 6/17/2026 3:16:23 PM

New Mexico Department of Game and Fish
Project ID: NMERT-4934
Project Number: 03A1987189

Jones Federal B 3 Battery

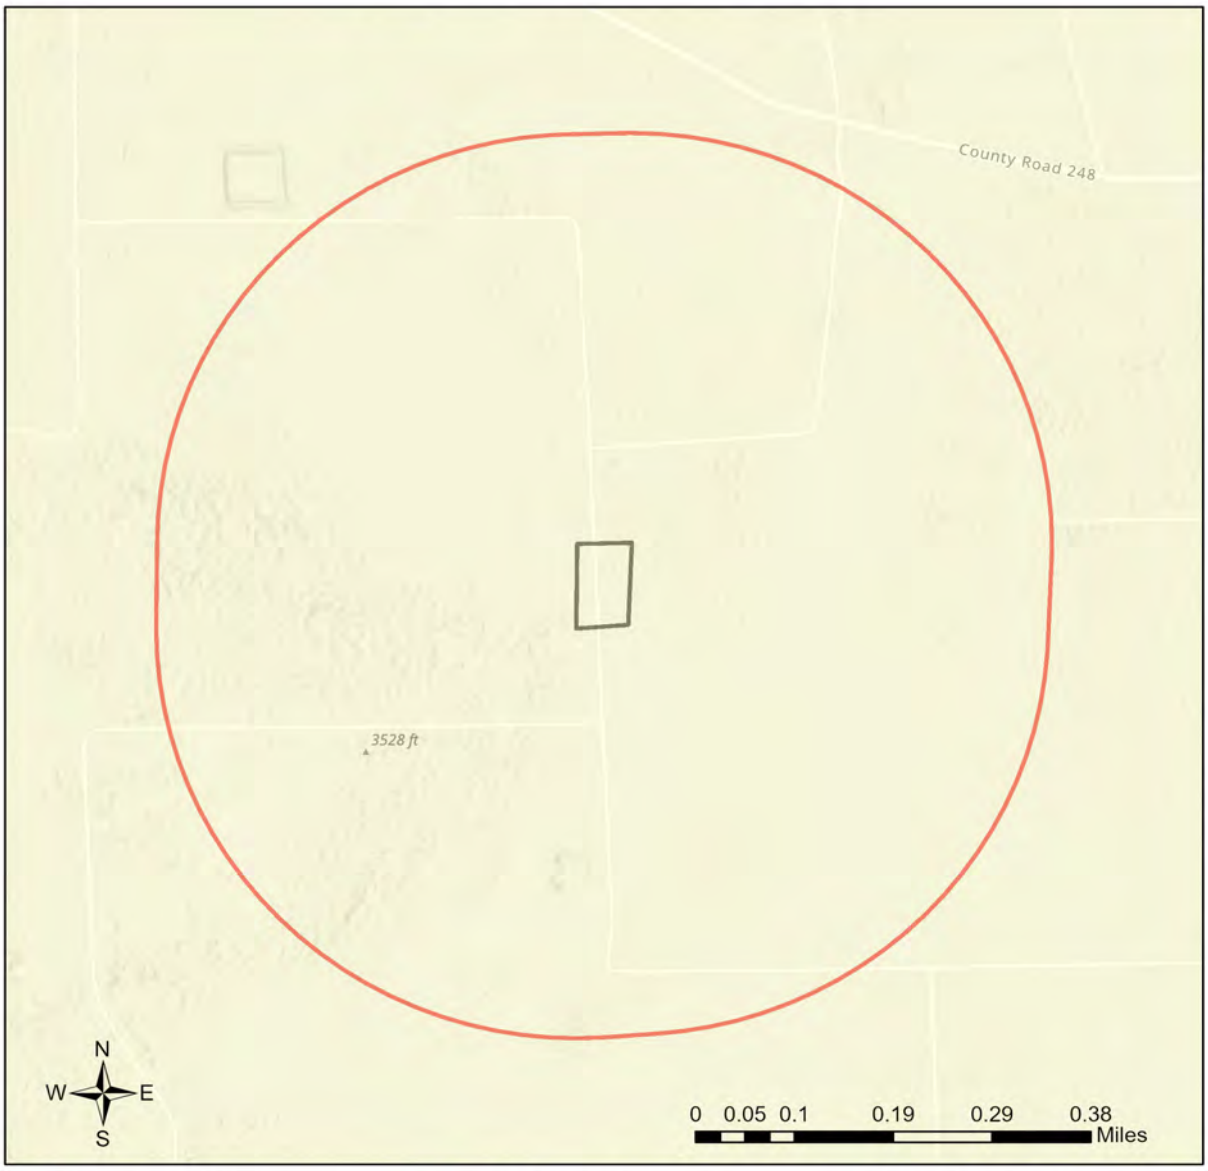

- Buffered Project Boundary
- Project_Boundary
- Bureau of Land Management
- City Land
- County Land
- Department of Defense
- Department of Energy
- NM Department of Game & Fish
- NM State Forestry Division
- NM State Parks
- National Park Service
- Other Federal Agency
- Other Federal Agency
- State Land Office
- State of New Mexico
- Tribal Land
- U.S. Army Corps of Engineers
- U.S. Bureau of Reclamation
- U.S. Department of Agriculture
- U.S. Fish and Wildlife Service
- U.S. Forest Service
- U.S. Natural Resources Conservation Service

NHNM, USGS, USFS, US Census Bureau, NMDGF
Esri, NASA, NGA, USGS, FEMA
Esri Community Maps Contributors, New Mexico State University, Texas Parks & Wildlife, CONANP, Esri, TomTom, Garmin, SafeGraph, GeoTechnologies, Inc, METI/NASA, USGS, EPA, NPS, US Census

Released to Imaging: 6/17/2026 3:16:23 PM

Received by OCD: 5/4/2026 10:36:24 AM

New Mexico Department of Game and Fish
Project ID: NMERT-4934
Project Number: 03A1987189

Special Status Animal Species Potentially within 650 Meters of Project Area

Common Name	Scientific Name	USFWS (ESA)	NMDGF (WCA)	NMDGF SGCN/SERI	USFS	USFS SCC	BLM
Barking Frog	Craugastor augusti			SGCN			
Lesser Prairie-Chicken	Tympanuchus pallidicinctus	LE		SGCN	Sensitive Species		BLM SENSITIVE
Elf Owl	Micrathene whitneyi			SGCN			BLM WATCH
Western Burrowing Owl	Athene cunicularia hypugaea			SGCN	Sensitive Species	USFS R3 SCC	BLM SENSITIVE
Common Nighthawk	Chordeiles minor			SGCN			
Loggerhead Shrike	Lanius ludovicianus			SGCN		USFS R3 SCC	BLM WATCH
Bell's Vireo	Vireo bellii		T	SGCN			BLM SENSITIVE
Varied Bunting	Passerina versicolor		T	SGCN	Sensitive Species		
Vesper Sparrow	Pooecetes gramineus			SGCN			
Spotted Bat	Euderma maculatum		T	SGCN	Sensitive Species	USFS R3 SCC	BLM SENSITIVE
Black-Tailed Prairie Dog	Cynomys ludovicianus			SGCN	Sensitive Species		BLM SENSITIVE
Mule Deer	Odocoileus hemionus			SERI			
Pronghorn	Antilocapra americana			SERI			
Dunes Sagebrush Lizard	Sceloporus arenicolus		E	SGCN			BLM SENSITIVE
Desert Massasauga	Sistrurus catenatus edwardsii			SGCN			

Common Name hyperlink takes you to species account in bison-m.org; Scientific Name hyperlink takes you to information in NatureServe Explorer; ESA = Endangered Species Act, C = Candidate, LE = Listed Endangered, LT = Listed Threatened, XN = Non-essential Experimental Population, for other ESA codes see this website; WCA = Wildlife Conservation Act, E = Endangered, T = Threatened; SERI = Species of Economic and Recreational Importance; SGCN = Species of Greatest Conservation Need; USFS = U.S. Forest Service, Sensitive Species = A species likely to occur on USFS lands that is of concern for a potential reduction in population viability; SCC = Species of Conservation Concern; BLM = Bureau of Land Management, BLM SENSITIVE = A species that occurs on BLM lands and whose viability is at risk, BLM WATCH = Species that may be added to the sensitive species list in future pending new information regarding species status.

Released to Imaging: 6/17/2026 3:16:23 PM

Received by OCD: 5/4/2026 10:36:24 AM

Project Recommendations

Open trenches excavated for underground water or oil and gas pipelines, powerlines, or fiber optic communication lines can unintentionally entrap and cause the unnecessary mortality of amphibians, reptiles, and small mammals, and can cause injury to large mammals. Trapped animals can die from exposure, starvation, crushing from pipe-laying, entombment from trenching backfilling, drowning, and predation. This unnecessary wildlife mortality can be avoided by implementing conservation measures including: concurrent trenching, pipe-laying, and backfilling operations to minimize the amount of trench left open overnight or longer; construction escape ramps; and employing biological monitors to remove trapped animals. Periods of highest activity for amphibians and reptiles vulnerable to entrapment include summer months and wet weather, and they can be active both day and night. Small mammals subject to entrapment are active year-round and generally most active at night.
Implementing the general trenching conservation measures outlined in the Department's Trenching Project Guidelines will help minimize unnecessary mortality of wildlife. Best management practices should include, at minimum, the following mitigation measures.

- Whenever possible, locate trenching activities within previously disturbed areas, such as existing road or pipeline right-of-ways. To the extent possible, avoid trenching in undisturbed habitat.
- Trench during the cooler months (October – March).
- Utilize concurrent trenching, pipe- or cable-laying, and backfilling. Keep trenching, pipe- or cable-laying, and backfilling crews as close together as possible to minimize the amount of open trench at any given time. When trenching activities are temporarily halted (e.g., overnight, weekends, holidays, weather shutdowns), protect wildlife from accessing any open trench between digging and backfilling operations by using one or more of the methods described below.
- Avoid leaving trenches open overnight. When trenches cannot be backfilled immediately, escape ramps should be constructed at least every 90 meters and preferably 30 meters. Escape ramps can be constructed parallel or perpendicular to the existing trench. The escape ramp slope should be less than 45 degrees (1:1). If pipe or cable has been installed but backfilling has not occurred, escape ramps may need to be constructed on both sides of the trench, since, unless the pipe is elevated enough to allow animals to move underneath it, the pipe or cable may block access of amphibians, reptiles, and small mammals to the ramps if only constructed on one side.
- Trenches that have been left open overnight should be inspected the following day by a qualified biological monitor and trapped animals removed as soon as possible, especially where state- or federally-listed threatened or endangered amphibians, reptiles, or small mammals occur. Untrained personnel should not attempt to remove trapped wildlife because of the potential to injure animals and the possibility of injury from venomous snakes. Required tools for removal will include snake tongs for removing snakes and a dip net for capturing and removing amphibians and small mammals. Many animals trapped in a trench will burrow under loose soil. To the extent possible, the biological monitor should disturb loose soil in the trench to uncover and remove trapped animals. Animals should be relocated at least 50 meters away from the open trench in undisturbed habitat.
- When pipe has been laid in the trench, end caps should be placed on the open end(s) of the pipe to preclude animals from entering. Pipe staged outside the trench should be capped until placed in the trench or checked for wildlife before being placed into the trench.
- Most wildlife can be protected by constructing silt fence completely around the open trench. Silt fence should be supported from sagging by t-posts, rebar, or stakes and buried at the base to preclude animals from moving below the fence. If construction of a silt fence is a required best management practice for erosion control, then, to preclude the need for a biological monitor, escape ramps, and concurrent backfilling, the guidelines for silt fence installation and maintenance in the Trenching Project Guidelines should be followed.

Released to Imaging: 6/17/2026 3:16:23 PM

Our preliminary assessment indicates your project occurs in Lesser Prairie-chicken Crucial Habitat Category 3 (Modeled Habitat Zone).

The Lesser Prairie-chicken (*Tympanuchus pallidicintus*) (LPC) was designated as a SGCN in New Mexico and the southern Distinct Population Segment, including populations in New Mexico and Texas, is federally listed as Endangered. The LPC Interstate Working Group has developed the Southern Great Plains Crucial Habitat Assessment Tool (SGP-CHAT) to designate and prioritize areas for LPC conservation activities and development. Our preliminary assessment indicates your project occurs in LPC habitat. For more information on the SGP-CHAT, contact Chanda Pettie, Industry LPC Program Contact with the Western Association of Fish and Wildlife Agencies, at (719) 207-5053 or chanda.pettie@wafwa.org.
If your project has potential to lead to take (including harassment, harm, pursuit, hunting, shooting, wounding, killing, trapping, capturing, collecting, or attempting to engage in these activities) of a LPC and you entered into the Candidate Conservation Agreement (CCA) or CCA with Assurances (CCAA) for the LPC with CEHMM, the Department recommends you contact CEHMM (575-885-3700). If your project may lead to take of a LPC and you did not enter the CCA/A with CEHMM, the Department recommends you contact Lauren Rangel, at 505-761-4745 or lauren_rangel@fws.gov, who is the species lead for the LPC in the Ecological Services Office with USFWS. She is also the contact for the rangewide renewable energy Habitat Conservation Plan (HCP) if relevant for your project. The Department recommends a qualified, permitted biologist conduct surveys for the LPC according to these Lesser Prairie-chicken Survey Protocols (or others recommended by USFWS) and following any training as required by USFWS.

Burrowing owl (*Athene cunicularia*) may occur within your project area. Burrowing owls are protected from take by the Migratory Bird Treaty Act and under New Mexico state statute. Before any ground disturbing activities occur, the Department recommends that a preliminary burrowing owl survey be conducted by a qualified biologist using the Department's Burrowing Owl Survey Protocol. Should burrowing owls be documented in the project area, please contact the Department or USFWS for further recommendations regarding relocation or avoidance of impacts.

Your proposed project intersects dunes sagebrush lizard (*Sceloporus arenicolus*) (DSL) habitat. The DSL is listed as Endangered under the ESA by the USFWS and as Endangered by the State of New Mexico under the New Mexico WCA. The Center of Excellence for Hazardous Materials Management (CEHMM) entered into an agreement with USFWS to work in cooperation with private landowners and industry to support conservation for the DSL while continuing to work on the land. If your project has potential to lead to take (including harassment, harm, pursuit, hunting, shooting, wounding, killing, trapping, capturing, collecting, or attempting to engage in these activities) of a DSL and you entered into the Candidate Conservation Agreement (CCA) or CCA with Assurances (CCAA) for the DSL with CEHMM, the Department recommends you contact CEHMM (575-885-3700). If your project may lead to take of a DSL and you did not enter the CCA/A with CEHMM, the Department recommends you contact Marilyn Wright, at 505-761-4715 or marilyn_wright@fws.gov, who is the species lead for the DSL in the Ecological Services Office with USFWS. The Department recommends a qualified, permitted biologist conduct surveys for the DSL according to any survey protocol recommended by, and following any training required by, USFWS.

Prairie dog colonies may occur within the vicinity of your project area. Both black-tailed prairie dogs (*Cynomys ludovicianus*) and Gunnison's prairie dogs (*Cynomys gunnisoni*) are designated as New Mexico SGCN, and their colonies provide important habitat for other grassland wildlife. Wherever possible, occupied prairie dog colonies should be left undisturbed, and all project activities should be directed off the colony. Any burrows that are located on the project site should be surveyed by a qualified biologist to determine whether burrows are active or inactive and whether burrowing owls may be utilizing the site. Colonies within the range of the black-tailed prairie dog can be surveyed by a qualified biologist diurnally, year-round using binoculars. Colonies within the range of the Gunnison's prairie dog can be surveyed by a qualified biologist diurnally, using binoculars during the warmer months from April through October and by searching for fairly fresh scat and lack of cobwebs or debris at the mouths of burrows during the cold months (November through March). If ground-disturbing activities cannot be relocated off the prairie dog colony, or if project activities involve control of prairie dogs, the Department recommends live-trapping and relocation of prairie dogs. The Department can provide recommendations regarding suitability of potential translocation areas and procedures.

Disclaimers regarding recommendations:

- The Department provides technical guidance to support the persistence of all protected species of native fish and wildlife, including game and nongame wildlife species. Species listed within this report include those that have been documented to occur within the project area, and others that may not have been documented but are projected to occur within the project vicinity.
- Recommendations are provided by the Department under the authority of § 17-1-5.1 New Mexico Statutes Annotated 1978, to provide "communication and consultation with federal and other state agencies, local governments and communities, private organizations and affected interests responsible for habitat, wilderness, recreation, water quality and environmental protection to ensure comprehensive conservation services for hunters, anglers and nonconsumptive wildlife users".
- The Department has no authority for management of plants or Important Plant Areas. The New Mexico Endangered Plant Program, under the Energy, Minerals, and Natural Resources Department's Forestry Division, identifies and develops conservation measures necessary to ensure the survival of plant species within New Mexico. Plant status information is provided within this report as a courtesy to users. Recommendations provided within the ERT may not be sufficient to preclude impacts to rare or sensitive plants, unless conservation measures are identified in coordination with the Endangered Plant Program.
- Additional coordination and/or consultation may also be necessary under the federal ESA or National Environmental Policy Act (NEPA). Further site-specific mitigation recommendations may be proposed during ESA consultation and/or NEPA analyses or through coordination with affected federal agencies.

United States Department of the Interior

FISH AND WILDLIFE SERVICE
New Mexico Ecological Services Field Office
2105 Osuna Road Ne
Albuquerque, NM 87113-1001
Phone: (505) 346-2525 Fax: (505) 346-2542

In Reply Refer To: 08/08/2025 20:48:20 UTC
Project Code: 2025-0133576
Project Name: Jones Federal B 3 Battery

Subject: List of threatened and endangered species that may occur in your proposed project location or may be affected by your proposed project

To Whom It May Concern:

Thank you for your recent request for information on federally listed species and important wildlife habitats that may occur in your project area. The U.S. Fish and Wildlife Service (Service) has responsibility for certain species of New Mexico wildlife under the Endangered Species Act (ESA) of 1973 as amended (16 USC 1531 et seq.), the Migratory Bird Treaty Act as amended (16 USC 701-715), and the Bald and Golden Eagle Protection Act as amended (16 USC 668-668(c)). We are providing the following guidance to assist you in determining which federally imperiled species may or may not occur within your project area, and to recommend some conservation measures that can be included in your project design.

The enclosed species list identifies threatened, endangered, proposed and candidate species, as well as proposed and final designated critical habitat, that may occur within the boundary of your proposed project and/or may be affected by your proposed project. The species list fulfills the requirements of the U.S. Fish and Wildlife Service (Service) under section 7(c) of the ESA of 1973, as amended (16 U.S.C. 1531 *et seq.*).

New information based on updated surveys, changes in the abundance and distribution of species, changed habitat conditions, or other factors could change this list. Please feel free to contact us if you need more current information or assistance regarding the potential impacts to federally proposed, listed, and candidate species and federally designated and proposed critical habitat. Please note that under 50 CFR 402.12(e) of the regulations implementing section 7 of the ESA, the accuracy of this species list should be verified after 90 days. The Service recommends that verification be completed by visiting the IPaC website at regular intervals during project planning and implementation for updates to species lists and information. An updated list may be requested through the IPaC system by completing the same process used to receive the enclosed list.

The purpose of the ESA is to provide a means whereby threatened and endangered species and

the ecosystems upon which they depend may be conserved. Under sections 7(a)(1) and 7(a)(2) of the ESA and its implementing regulations (50 CFR 402 *et seq.*), Federal agencies are required to utilize their authorities to carry out programs for the conservation of threatened and endangered species and to determine whether projects may affect threatened and endangered species and/or designated critical habitat.

A Biological Assessment is required for construction projects (or other undertakings having similar physical impacts) that are major Federal actions significantly affecting the quality of the human environment as defined in the National Environmental Policy Act (NEPA; 42 USC 4332(2) (c)). For projects other than major construction activities, the Service suggests that a biological evaluation similar to a Biological Assessment be prepared to determine whether the project may affect listed or proposed species and/or designated or proposed critical habitat. Recommended contents of a Biological Assessment are described at 50 CFR 402.12.

If a Federal agency determines, based on the Biological Assessment or biological evaluation, that listed species and/or designated critical habitat may be affected by the proposed project, the agency is required to consult with the Service pursuant to 50 CFR 402. In addition, the Service recommends that candidate species, proposed species and proposed critical habitat be addressed within the consultation. More information on the regulations and procedures for section 7 consultation, including the role of permit or license applicants, can be found in the "Endangered Species Consultation Handbook" at https://www.fws.gov/sites/default/files/documents/endangered-species-consultation-handbook.pdf.

Candidate Species and Other Sensitive Species

A list of candidate and other sensitive species in your area is also attached. Candidate species and other sensitive species are species that have no legal protection under the ESA, although we recommend that candidate and other sensitive species be included in your surveys and considered for planning purposes. The Service monitors the status of these species. If significant declines occur, these species could potentially be listed. Therefore, actions that may contribute to their decline should be avoided.

Lists of sensitive species including State-listed endangered and threatened species are compiled by New Mexico State agencies. These lists, along with species information, can be found at the following websites.

Biota Information System of New Mexico (BISON-M): www.bison-m.org

New Mexico State Forestry. The New Mexico Endangered Plant Program: https://www.emnrd.nm.gov/sfd/rare-plants/

New Mexico Rare Plant Technical Council, New Mexico Rare Plants: nmrareplants.unm.edu

Natural Heritage New Mexico, online species database: nhnm.unm.edu

WETLANDS AND FLOODPLAINS

Under Executive Orders 11988 and 11990, Federal agencies are required to minimize the destruction, loss, or degradation of wetlands and floodplains, and preserve and enhance their natural and beneficial values. These habitats should be conserved through avoidance, or mitigated to ensure that there would be no net loss of wetlands function and value.

We encourage you to use the National Wetland Inventory (NWI) maps in conjunction with ground-truthing to identify wetlands occurring in your project area. The Service's NWI program website, www.fws.gov/wetlands/Data/Mapper.html, integrates digital map data with other resource information. We also recommend you contact the U.S. Army Corps of Engineers for permitting requirements under section 404 of the Clean Water Act if your proposed action could impact floodplains or wetlands.

MIGRATORY BIRDS

In addition to responsibilities to protect threatened and endangered species under the ESA, there are additional responsibilities under the Migratory Bird Treaty Act (MBTA) and the Bald and Golden Eagle Protection Act (BGEPA) to protect native birds from project-related impacts. Any activity resulting in take of migratory birds, including eagles, is prohibited unless otherwise permitted by the Service (50 CFR 10.12 and 16 USC 668(a)). For more information regarding these Acts, see https://www.fws.gov/program/migratory-bird-permit/what-we-do.

It is the responsibility of the project proponent to comply with these Acts by identifying potential impacts to migratory birds and eagles within applicable NEPA documents (when there is a Federal nexus) or a Bird/Eagle Conservation Plan (when there is no Federal nexus). Proponents should implement conservation measures to avoid or minimize the production of project-related stressors or minimize the exposure of birds and their resources to the project-related stressors. For more information on avian stressors and recommended conservation measures, see https://www.fws.gov/library/collections/threats-birds. We also recommend review of the Birds of Conservation Concern list (https://www.fws.gov/media/birds-conservation-concern-2021) to fully evaluate the effects to the birds at your site. This list identifies migratory and non-migratory bird species (beyond those already designated as federally threatened or endangered) that represent top conservation priorities for the Service, and are potentially threatened by disturbance, habitat impacts, or other project development activities.

In addition to MBTA and BGEPA, Executive Order 13186: *Responsibilities of Federal Agencies to Protect Migratory Birds*, obligates all Federal agencies that engage in or authorize activities that might affect migratory birds, to minimize those effects and encourage conservation measures that will improve bird populations. Executive Order 13186 thereby provides additional protection for both migratory birds and migratory bird habitat. Please visit https://www.fws.gov/partner/council-conservation-migratory-birds for information regarding the implementation of Executive Order 13186.

We suggest you contact the New Mexico Department of Game and Fish, and the New Mexico

Energy, Minerals, and Natural Resources Department, Forestry Division for information regarding State protected and at-risk species fish, wildlife, and plants.

For further consultation with the Service we recommend submitting inquiries or assessments electronically to our incoming email box at nmesfo@fws.gov, where it will be more promptly routed to the appropriate biologist for review.

We appreciate your concern for threatened and endangered species. The Service encourages Federal agencies to include conservation of threatened and endangered species into their project planning to further the purposes of the Act. Please include the Consultation Code in the header of this letter with any request for consultation or correspondence about your project that you submit to our office.

Attachment(s):

- Official Species List
- Bald & Golden Eagles
- Migratory Birds

OFFICIAL SPECIES LIST

This list is provided pursuant to Section 7 of the Endangered Species Act, and fulfills the requirement for Federal agencies to "request of the Secretary of the Interior information whether any species which is listed or proposed to be listed may be present in the area of a proposed action".

This species list is provided by:

New Mexico Ecological Services Field Office
2105 Osuna Road Ne
Albuquerque, NM 87113-1001
(505) 346-2525

PROJECT SUMMARY

Project Code: 2025-0133576
Project Name: Jones Federal B 3 Battery
Project Type: NPL Site Remediation
Project Description: The site is located at 32.64265223, -103.824532. The size of the area to be disturbed is 6,741 ft sq. Within the defined polygon.

Project Location:

The approximate location of the project can be viewed in Google Maps: https://www.google.com/maps/@32.6422117,-103.82462375658604,14z

Counties: Eddy County, New Mexico

ENDANGERED SPECIES ACT SPECIES

There is a total of 5 threatened, endangered, or candidate species on this species list.

Species on this list should be considered in an effects analysis for your project and could include species that exist in another geographic area. For example, certain fish may appear on the species list because a project could affect downstream species.

IPaC does not display listed species or critical habitats under the sole jurisdiction of NOAA Fisheries[1], as USFWS does not have the authority to speak on behalf of NOAA and the Department of Commerce.

See the "Critical habitats" section below for those critical habitats that lie wholly or partially within your project area under this office's jurisdiction. Please contact the designated FWS office if you have questions.

---

1. NOAA Fisheries, also known as the National Marine Fisheries Service (NMFS), is an office of the National Oceanic and Atmospheric Administration within the Department of Commerce.

BIRDS

NAME	STATUS
Northern Aplomado Falcon *Falco femoralis septentrionalis* Population: U.S.A (AZ, NM) No critical habitat has been designated for this species. Species profile: https://ecos.fws.gov/ecp/species/1923 General project design guidelines: https://ipac.ecosphere.fws.gov/project/FMDCPCO5OFEUPOMMRSNEEPH3VE/documents/generated/8928.pdf	Experimental Population, Non-Essential
Piping Plover *Charadrius melodus* Population: [Atlantic Coast and Northern Great Plains populations] - Wherever found, except those areas where listed as endangered. There is **final** critical habitat for this species. Your location does not overlap the critical habitat. Species profile: https://ecos.fws.gov/ecp/species/6039	Threatened

REPTILES

NAME	STATUS
Dunes Sagebrush Lizard *Sceloporus arenicolus* No critical habitat has been designated for this species. Species profile: https://ecos.fws.gov/ecp/species/6631 General project design guidelines: https://ipac.ecosphere.fws.gov/project/FMDCPCO5OFEUPOMMRSNEEPH3VE/documents/generated/9027.pdf	Endangered

CLAMS

NAME	STATUS
Texas Hornshell *Popenaias popeii* There is **proposed** critical habitat for this species. Your location does not overlap the critical habitat. Species profile: https://ecos.fws.gov/ecp/species/919 General project design guidelines: https://ipac.ecosphere.fws.gov/project/FMDCPCO5OFEUPOMMRSNEEPH3VE/documents/generated/9180.pdf	Endangered

INSECTS

NAME	STATUS
Monarch Butterfly *Danaus plexippus* There is **proposed** critical habitat for this species. Your location does not overlap the critical habitat. Species profile: https://ecos.fws.gov/ecp/species/9743	Proposed Threatened

CRITICAL HABITATS

THERE ARE NO CRITICAL HABITATS WITHIN YOUR PROJECT AREA UNDER THIS OFFICE'S JURISDICTION.

YOU ARE STILL REQUIRED TO DETERMINE IF YOUR PROJECT(S) MAY HAVE EFFECTS ON ALL ABOVE LISTED SPECIES.

BALD & GOLDEN EAGLES

Bald and Golden Eagles are protected under the Bald and Golden Eagle Protection Act [2] and the Migratory Bird Treaty Act (MBTA) [1]. Any person or organization who plans or conducts activities that may result in impacts to Bald or Golden Eagles, or their habitats, should follow appropriate regulations and consider implementing appropriate avoidance and minimization measures, as described in the various links on this page.

---

1. The Bald and Golden Eagle Protection Act of 1940.
2. The Migratory Birds Treaty Act of 1918.
3. 50 C.F.R. Sec. 10.12 and 16 U.S.C. Sec. 668(a)

Bald and Golden Eagles are protected under the Bald and Golden Eagle Protection Act and the Migratory Bird Treaty Act (MBTA). Any person or organization who plans or conducts activities that may result in impacts to Bald or Golden Eagles, or their nests, should follow appropriate regulations and implement required avoidance and minimization measures, as described in the various links on this page.

The data in this location indicates that no eagles have been observed in this area. This does not mean eagles are not present in your project area, especially if the area is difficult to survey. Please review the 'Steps to Take When No Results Are Returned' section of the Supplemental Information on Migratory Birds and Eagles document to determine if your project is in a poorly surveyed area. If it is, you may need to rely on other resources to determine if eagles may be present (e.g. your local FWS field office, state surveys, your own surveys).

Any person or organization who plans or conducts activities that may result in impacts to bald or golden eagles, or their habitats, should follow appropriate regulations and consider implementing appropriate conservation measures, as described in the links below. Specifically, please review the "Supplemental Information on Migratory Birds and Eagles".

MIGRATORY BIRDS

The Migratory Bird Treaty Act (MBTA) [1] prohibits the take (including killing, capturing, selling, trading, and transport) of protected migratory bird species without prior authorization by the Department of Interior U.S. Fish and Wildlife Service (Service).

---

1. The Migratory Birds Treaty Act of 1918.

2. The Bald and Golden Eagle Protection Act of 1940.
3. 50 C.F.R. Sec. 10.12 and 16 U.S.C. Sec. 668(a)

For guidance on when to schedule activities or implement avoidance and minimization measures to reduce impacts to migratory birds on your list, see the "Probability of Presence Summary" below to see when these birds are most likely to be present and breeding in your project area.

NAME	BREEDING SEASON
Cactus Wren *Campylorhynchus brunneicapillus guttatus* This is a Bird of Conservation Concern (BCC) only in particular Bird Conservation Regions (BCRs) in the continental USA https://ecos.fws.gov/ecp/species/8834	Breeds Mar 5 to Sep 30
Cassin's Sparrow *Peucaea cassinii* This is a Bird of Conservation Concern (BCC) only in particular Bird Conservation Regions (BCRs) in the continental USA https://ecos.fws.gov/ecp/species/9512	Breeds Aug 1 to Oct 10
Eastern Meadowlark *Sturnella magna* This is a Bird of Conservation Concern (BCC) only in particular Bird Conservation Regions (BCRs) in the continental USA https://ecos.fws.gov/ecp/species/9455	Breeds Apr 25 to Aug 31
Henry's Common Nighthawk *Chordeiles minor henryi* This is a Bird of Conservation Concern (BCC) only in particular Bird Conservation Regions (BCRs) in the continental USA https://ecos.fws.gov/ecp/species/11979	Breeds May 21 to Aug 25

PROBABILITY OF PRESENCE SUMMARY

The graphs below provide our best understanding of when birds of concern are most likely to be present in your project area. This information can be used to tailor and schedule your project activities to avoid or minimize impacts to birds. Please make sure you read "Supplemental Information on Migratory Birds and Eagles", specifically the FAQ section titled "Proper Interpretation and Use of Your Migratory Bird Report" before using or attempting to interpret this report.

Probability of Presence (■)

Green bars; the bird's relative probability of presence in the 10km grid cell(s) your project overlaps during that week of the year.

Breeding Season (■)
Yellow bars; liberal estimate of the timeframe inside which the bird breeds across its entire range.

Survey Effort (|)
Vertical black lines; the number of surveys performed for that species in the 10km grid cell(s) your project area overlaps.

No Data (–)
A week is marked as having no data if there were no survey events for that week.

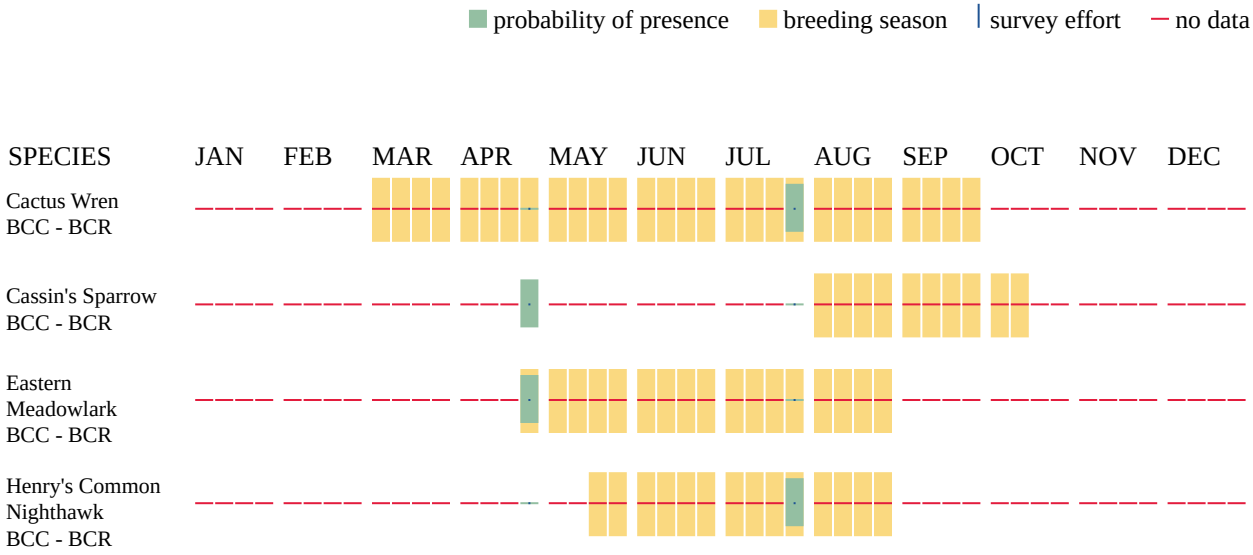

Additional information can be found using the following links:

- Eagle Management https://www.fws.gov/program/eagle-management
- Measures for avoiding and minimizing impacts to birds https://www.fws.gov/library/collections/avoiding-and-minimizing-incidental-take-migratory-birds
- Nationwide avoidance and minimization measures for birds
- Supplemental Information for Migratory Birds and Eagles in IPaC https://www.fws.gov/media/supplemental-information-migratory-birds-and-bald-and-golden-eagles-may-occur-project-action

IPAC USER CONTACT INFORMATION

Agency: Ensolum, LLC
Name: Azad Vojdani
Address: 3122 National Parks Hwy
City: Carlsbad
State: NM
Zip: 88220
Email avojdani@ensolum.com
Phone: 5752666183

ENSOLUM

APPENDIX C

Lithologic Soil Sampling Logs

ENSOLUM

Sample Name: BH01	Date: 8/12/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642590, -103.824473	Hole Diameter: 3"	Total Depth: 9'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	5,236		N			1	SP	(1-3') SAND with trace silt, brown, fine grain, non-cohesive, poorly graded, has odor.
D	4,827.2		N	BH01	2	2		
D	453.6		N			3		(3') Has trace clay, non-plastic, and no odor.
D	1,601.6		N	BH01	4	4	CCHE	(4') CALICHE with little silt, tan, fine to medium grain, well graded, has some fine brown sand, non-cohesive and no odor.
D	1,719.2		N	BH01	5	5	SP-SM	(5-7') SAND with silt and little caliche, light brown, fine to medium grain, poorly graded, non-cohesive, and no odor.
D	1,836.8		N			6		
D	2,240		N	BH01	7	7		(7') Reddish brown.
D	1,836.8		N			8	SP	(8-9') SAND with few silt, light brown, fine grain, non-cohesive.
D	5,236		N	BH01	9	9		(9') Fine to medium grain, reddish brown.

Refusal @ 9 feet bgs

ENSOLUM

	Sample Name: BH02	Date: 8/12/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642570, -103.824608	Hole Diameter: 3"	Total Depth: 6'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	711.2		N			1	CCHE	(1-2') CALICHE with few silt, tan, fine to coarse, grain, poorly graded, and non-cohesive.
D	576.8		N	BH02	2	2		(2') Fine to medium grain, well graded, has sheen, no odor.
M	<168	2,272	N			3	SP	(3-5') SAND with trace silt, fine grain, dark brown, has sheen, poorly graded, non-cohesive and no odor.
M	453.6	151	N	BH02	4	4		
M	784		N	BH02	5	5		
D	644		N	BH02	6	6	CCHE	(6') CALICHE with sand, tan, fine to medium grain, poorly graded, non-cohesive.

Total Depth @ 6 feet bgs

ENSOLUM

	Sample Name: BH03	Date: 8/12/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642447, -103.824595	Hole Diameter: 3"	Total Depth: 22'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. On 10/29/25, Air rotary drill was utilized to delineate 8-22' bgs.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	8,422.4		N			1	CCHE	(1-2') CALICHE with silt and sand, brown, fine to coarse grain, well graded, non-cohesive.
D	2,240		N	BH03	2	2		
M	2,240		N			3	SP	(3-5') SAND with trace silt, dark brown, fine grain, non-cohesive.
M	2,100		N	BH03	4	4		
M	397.6	1,884	N	BH03	5	5		
M	4,827.2		Y			6	SP-SC	SAND with clay, brown, fine grain, medium plasticity, poorly graded, strong odor.
D	246.4	>1,250	N	BH03	7	7	CCHE	CALICHE with sand and some silt, tan, fine to coarse grain, well graded, non-cohesive.
M	162.4	364	N	BH03	8	8	SP	Sand with trace clay, brown, fine grain, poorly graded, non-plastic and no odor.
M	162.4		Y			9	SW	(9-10') Sand with trace silt, brown, fine to coarse grain, well graded, has odor and sheen.
M	162.4	>1,250	N	BH03	10	10		
D	162.4		N			12		(12')Sand with some silt, brown, fine to coarse grain, well graded, non-cohesive, has odor and sheen.
D	162.4	408	N	BH03	14	14	SP	(14-16') Sand with some silt, brown, fine grain, poorly graded, no odor and non-cohesive.
M	<162.4	32	N	BH03	16	16		

ENSOLUM

	Sample Name: BH03	Date: 8/12/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642447, -103.824595	Hole Diameter: 3"	Total Depth: 22'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. On 10/29/25, Air rotary drill was utilized to delineate 8-22' bgs.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	229.6		N			18		(18')Sand, brown, fine to coarse grain, well graded, non-cohesive and no odor.
D	414.4	8	N			20	SW	(20-22') Sand with little clay, brown, fine to coarse grain, well graded, low plasticity and no odor.
D	162.4	45	N			22		

Total depth @ 22 feet bgs

ENSOLUM

	Sample Name: BH04	Date: 8/11/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642459, -103.824480	Hole Diameter: 3"	Total Depth: 5'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	168	2,342	N			1	CCHE	(1') CALICHE with sand, trace silt, tan, fine to medium grain, poorly sorted, non-cohesive.
D	<168		N	BH04	2	2	SP	(2-5') SAND with trace silt, dark brown, fine grain, poorly sorted, non-cohesive.
D	<168	705	N			3		
M	2,553.6		N	BH04	4	4		(4') Few clay, non-plastic.
M	168	84	N	BH04	5	5		(5') Some clay, low plasticity.

Total Depth @ 5 feet bgs

ENSOLUM

	Sample Name: BH05	Date: 8/21/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642982, -103.824661	Hole Diameter: 3"	Total Depth: 3'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	Vapor (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D				BH05	0	0	CCHE	CALICHE
D	ND	>1000	N	BH05	1	1	SP-SM	Sand, Non Plastic, Fine Grain.
D	ND	856	N			2		
D	ND		N	BH05	3	3		

Refusal @ 3 feet bgs

ENSOLUM

Sample Name: BH06	Date: 8/21/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642990, -103.824495	Hole Diameter: 3"	Total Depth: 22'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. On 10/28/2025 Air rotary drill was utilized to delineate 4-22' bgs.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D				BH06	0	0	CCHE	CALICHE
D	207		N			1	SP-SM	(1-3.5') SAND, Non Plastic, Fine Grain.
D	644		N	BH06	2	2		
D	856		N			3		
D	935		N	BH06	3.5			
D	526.4	Error		BH06	4	4	CCHE	CALICHE, tan, fine to coarse grain, well graded, non-cohesive and no odor.
D	722.4		N			5	SW	(5-7') SAND with silt, fine to coarse grain, light brown, well graded, non-cohesive, and no odor.
D	795.2		N			6		
D	655.2		N	BH06	7	7		
D	722.4		N			8	SP	(8-10') SAND with few silt, brown, fine to medium grain, poorly graded, non-cohesive, and no odor.
D	588		N	BH06	9	9		
D	795.2		N			10		
D	1,041.6		N	BH06	12	12		(12-14') SAND with trace silt, brown, fine to medium grain, poorly graded, non-cohesive, and no odor.
D	1,226.4		N			14		

ENSOLUM

Sample Name: BH06	Date: 8/21/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella, U. Santillana	Method: Hand Auger
Coordinates: 32.642990, -103.824495	Hole Diameter: 3"	Total Depth: 22'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. On 10/28/2025 Air rotary drill was utilized to delineate 4-22' bgs.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	526.4	28	N	BH06	16	16	SP	(16-18') SAND with trace silt, brown, fine to medium grain, poorly graded, non-cohesive and no odor.
D	1,131.2		N			18		
D	1,327.2		N			20	SC	(20-22') CLAYEY, coarse sand, brown, well graded and non-plastic.
D	1,226.4		N			22		

Total Depth @ 22 feet bgs

ENSOLUM

Sample Name: BH07	Date: 8/21/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642861, -103.824497	Hole Diameter: 3"	Total Depth: 2.5'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH07	0	0	CCHE	Sandy Caliche, Non Plastic, Coarse to Fine Grain.
D	207		N	BH07	1	1	SP-SM	Sand, Non Plastic, Fine Grain.
D	1,293		N			2		
D	644		N	BH07	2.5	2.5		

Refusal @ 2.5 feet bgs

ENSOLUM

Sample Name: BH08	Date: 8/21/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642860, -103.824654	Hole Diameter: 3"	Total Depth: 2.5'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH08	0	0		
D	784		N	BH08	1	1	CCHE	Sandy Caliche, Non Plastic, Coarse to Fine Grain.
D	784		N			2	SP-SM	Sand, Non Plastic, Fine Grain.
D	1,836		N	BH08	2.5	2.5		Sand with Caliche, Non Plastic, Coarse to Fine Grain.

Refusal @ 2.5 feet bgs

ENSOLUM

Sample Name: BH09	Date: 8/21/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642729, -103.824649	Hole Diameter: 3"	Total Depth: 4'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH09	0	0		
D	ND	439	N			1		
D	ND	244	N	BH09	2	2	SP-SM	Sand, Non Plastic, Fine Grain.
D	ND	257	N			3		
D	ND		N	BH09	4	4		

Total Depth @ 4 feet bgs

ENSOLUM

Sample Name: BH10	Date: 8/12/2025
Site Name: Jones Federal B 3 Battery	
Incident Number: nMLB1129240104 & nAPP2520569781	
Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US / Method: Hand Auger
Coordinates: 32.642735, -103.824503	Hole Diameter: 3" / Total Depth: 12'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M			Y			1		
M			Y	BH10	2	2	SP	(1-2') SAND with trace silt, dark brown, fine grain, non-cohesive, strong odor.
M			Y			3	SP-SC	(3-4') SAND with clay, dark brown, fine grain, non-plastic, strong odor.
M	2,968		N	BH10	4	4		(4') Low plasticity, has odor.
D			N			5	CCHE	(5') CALICHE with strong odor.
D	576.8		N	BH10	6	6	SP-SM	(6-9') SAND with silt, tan, fine to medium grain, non-cohesive, has odor.
D			N			7		(7') Strong odor.
D	711.2		N	BH10	8	8		
D	784		N			9		(8-9') With some clay, reddish brown, non-plastic, poorly graded, has odor.
D	168	49	N	BH10	10	10	SP	(10-12') SAND with trace silt, brown, fine grain, non-cohesive.
D	168	18	N			11		
D	168		N			12		

Total Depth @ 12 feet bgs

ENSOLUM

Sample Name: BH11	Date: 8/13/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.641725,-103.824672	Hole Diameter: 3"	Total Depth: 10'

Comments: Field screening conducted with HACH Chloride Test Strips and Petroflag® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	<168	174	N	BH11	1	1	SP	(1-3') SAND with trace clay, fine grain, brown, non-plastic, slight odor.
D	<168	159	N			2		
D	296.8	58	N	BH11	3	3		(2-3') Few clay.
D	576.8	272	N	BH11	4	4	SP-SM	(4-5') SAND with silt, tan, fine grain, non-cohesive.
D	856.8		N			5		
D	1109		N	BH11	6	6	SP	(6-10') SAND with little silt, brown, fine to medium grain, non-cohesive, poorly graded.
D	935.2		N			7	SW	(7') Some silt, fine to coarse grain.
D	644		N	BH11	8	8	SP-SM	(8') With silt.
D	644		N			9	SW-SM	(9') With silt, fine to coarse grain.
D	296.8	79	N	BH11	10	10	SP	(10') Little silt, fine grain.

Total Depth @ 10 feet bgs

ENSOLUM

Sample Name: BH12	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.641886,-103.824665	Hole Diameter: 3"	Total Depth: 5'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M	<168	34	N	BH12	1	1	SP	(1-3') SAND with trace silt, brown, fine grain, non-cohesive.
M	<168	28	N			2		
M	<168		N			3		(3') Sand with little silt.
D	<168		N			4	CCHE	(4-5) CALICHE, with sand and silt, tan, fine to medium grain, non-cohesive, poorly graded.
D	168		N			5		(5') Fine to coarse grain, reddish tan, well graded.

Total Depth @ 5 feet bgs

ENSOLUM

Sample Name: BH13	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642083, -103.824680	Hole Diameter: 3"	Total Depth: 13'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M	<168		N	BH13	1	1	SP	(1-3') SAND, brown, fine grain, non-cohesive, poorly graded, no odor.
M	1,601.6		N			2		(2') Few silt.
M	2,912		N	BH13	3	3		(3') Some silt.
D	2,240		N	BH13	4	4	CCHE	(4-5') CALICHE with some sand and silt, tan, fine to coarse grain, non-cohesive, poorly graded.
D	2,553.6		N	BH13	5	5		(5') Well graded.
D	1,388.8		N			6	SW-SM	(6-7') SAND with silt, brown, fine to coarse grain, well graded, non-cohesive.
D	1,719.2		N	BH13	7	7		(7') Some caliche
D	1,293.6		N			8	SW	SAND with some silt, dark brown, fine to coarse grain, non-cohesive.
D	1,108.8		N	BH13	9	9	SC	CLAYEY sand with some silt, dark brown, fine to coarse grain, non-cohesive.
D	1,108.8		N			10	SW-SM	(10-11') SAND with silt, brown, fine to coarse grain, well graded.
D	1,019.2		N	BH13	11	11		
D	296.8	103	N			12	SP	(12-13') SAND with trace silt, brown, fine grain, non-cohesive.
D	<168	36	N	BH13	13	13		

ENSOLUM

Sample Name: BH14	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642207, -103.824735	Hole Diameter: 3"	Total Depth: 6.5'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG ® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M	<168		N			1		(1-3') SAND, dark brown, fine grain, non-cohesive.
M	1,834		N	BH14	2	2	SP	(2') With trace silt.
D	1,719		N			3		(3') With some silt, tan, fine to medium grain.
D	1,834		N	BH14	4	4	CCHE	(4-5') CALICHE with sand and little silt, tan, fine to medium grain, non-cohesive, poorly graded.
D	1,719		N			5		(5') Well graded.
D	1,719		N	BH14	6	6	SC	(6-6.5') CLAYEY sand, reddish brown, fine to coarse grain, well graded, non-plastic.
D	1,294		N			6.5		

Refusal @ 6.5 feet bgs

ENSOLUM

Sample Name: BH16	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642549, -103.824751	Hole Diameter: 3"	Total Depth: 50'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	856.8		N	BH16	1	1	SP	(1-3') SAND, brown, fine grain, non-cohesive.
D	2,912		N			2		(2') Few silt.
D	5,667.2		N			3		(3') Little silt, fine to coarse grain, some caliche.
D	7,778.4		N	BH16	4	4	CCHE	(4-5') CALICHE with silt, tan, fine grain, non-cohesive.
D	8,422.4		N	BH16	5	5		
D	7,190.4		N			6	SP	(6-7') SAND with some silt, tan fine grain, non-cohesive.
D	7,778.4		N	BH16	7	7	SW	(7') Fine to coarse grain, reddish brown.
D	5,079		N	BH16	8	8	SW-SM	SAND with silt, tan, fine to coarse grain, non-cohesive, no odor.
D	4,318		N			9	SP-SM	(9-12') SAND with silt, brown, fine grain, non-cohesive, no odor.
D	4,687		N	BH16	10	10		
D	1,355		N			12		
D	1,943		N	BH16	14	14	SP	SAND with little clay and silt, brown, fine grain non-cohesive and non-plastic.

ENSOLUM

	Sample Name: BH16	Date: 10/29/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642549, -103.824751	Hole Diameter: 3"	Total Depth: 50'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D	3,651		N			16		
D	3,651		N			18	SW	(16-18') SAND with little silt, brown, fine to coarse grain, non-cohesive.
D	1,691		N	BH16	20	20		
D	1,462		N			22		(20-26') SAND with trace silt, brown, fine grain, non-cohesive.
D	974		N	BH16	24	24	SP	(22-24') Fine to medium grain.
D	1,254		N			26		
D	2,744		N			28		(26') Grayish brown, fine grain.
D	2,391		N	BH16	30	30	CCHE	(28-30') CALICHE, tan, fine to coarse grain, well graded, non-cohesive.
D	2,234		N			32		
D	1,355		N	BH16	35	35	SW	(32-35') SAND with some silt, brown, fine to coarse grain, non-cohesive and no odor.
D	1,064		N	BH16	40	40	SP-SM	SAND with silt, brown, fine grain, non-cohesive.
D	739		N	BH16	45	45	SP-SC	SAND with clay, brown, fine to medium grain, non-cohesive.
D	375		N	BH16	50	50		

ENSOLUM

Sample Name: BH17	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642642, -103.824766	Hole Diameter: 3"	Total Depth: 17'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. 10-17' screened 8/19/2025.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M	168		N			1		
M	711		N	BH17	2	2	SP	(1-3') SAND with trace silt, brown, fine grain, non-cohesive.
D	2,391		N			3		
D	3,590		N	BH17	4	4		
D	3,590		N	BH17	5	5	CCHE	(4-5') CALICHE with sand and silt, light brown, fine to medium grain, poorly graded, non-cohesive.
D	5,667		N			6		(6') CALICHE, with sand and silt, brown, fine to coarse grain, poorly graded, non-cohesive.
D	3,343		N	BH17	7	7		
D	3,343		N			8	SP	(7-9') SAND with some silt, brown, fine grain, non-cohesive.
D	3,589		N	BH17	9	9		
M	1,495		N			10		
M	347		N	BH17	11	11		
M	644		N			12	SP	(10-12') SAND with trace silt, brown, fine grain, non-cohesive.

ENSOLUM

Sample Name: BH17	Date: 8/14/2025	
Site Name: Jones Federal B 3 Battery		
Incident Number: nMLB1129240104 & nAPP2520569781		
Job Number: 03A1987189		
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: US	Method: Hand Auger
Coordinates: 32.642642, -103.824766	Hole Diameter: 3"	Total Depth: 17'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included. 10-17' screened 8/19/2025.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
M	1,601		N	BH17	13	13	SP-SM	SAND with silt, brown, fine grain, non-cohesive.
M	1,601		N			14		Fine to coarse grain, little small gravel, well graded.
M	1,495		N	BH17	15	15	SP-SC	(15-16') SAND with clay, brown, fine to medium grain, non-plastic.
M	1,388		N			16		
M	1,294		N	BH17	17	17	SW	SAND with silt, brown, fine to coarse grain.

Refusal @ 17 feet bgs

ENSOLUM

	Sample Name: BH18	Date: 8/21/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642367, -103.824465	Hole Diameter: 3"	Total Depth: 4'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH18	0	0		
D	ND	32	N	BH18	1	1		
D	ND		N			2	SP-SM	SAND, Non Plastic, Fine Grain.
D	ND		N			3		
D	ND		N			4		

Total Depth @ 4 feet bgs

ENSOLUM

	Sample Name: BH19	Date: 8/21/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642354, -103.824596	Hole Diameter: 3"	Total Depth: 4'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH19	0	0		
D	ND	426	N			1		
D	ND		N	BH19	2	2	SP-SM	Sand, Non Plastic, Fine Grain.
D	ND		N			3		
D	ND	472	N	BH19	4	4		

Total Depth @ 4 feet bgs

ENSOLUM

	Sample Name: BH20	Date: 8/21/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.642279, -103.824537	Hole Diameter: 3"	Total Depth: 4'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH20	0	0		
D	ND	622	N			1		
D	784		N	BH20	2	2	SP-SM	Sand, Non Plastic, Fine Grain.
D	2,100		N			3		
D	2,240		N	BH20	4	4	CCHE	Caliche, Non Plastic, Coarse to Fine Grain.

Total Depth @ 4 feet bgs

ENSOLUM

	Sample Name: BH21	Date: 8/21/2025
	Site Name: Jones Federal B 3 Battery	
	Incident Number: nMLB1129240104 & nAPP2520569781	
	Job Number: 03A1987189	
LITHOLOGIC / SOIL SAMPLING LOG	Logged By: Israel Estrella	Method: Hand Auger
Coordinates: 32.643105, -103.824585	Hole Diameter: 3"	Total Depth: 4'

Comments: Field screening conducted with HACH Chloride Test Strips and PetroFLAG® for chloride and TPH, respectively. Chloride test performed with 1:4 dilution factor of soil to distilled water. 40% correction factors included.

Moisture Content	Chloride (ppm)	TPH (ppm)	Staining	Sample ID	Sample Depth (ft bgs)	Depth (ft bgs)	USCS/Rock Symbol	Lithologic Descriptions
D			N	BH21	0	0		
D	ND	41	N			1		
D	ND		N	BH21	2	2	SP-SM	Sand, Non Plastic, Fine Grain.
D	784		N			3		
D	453		N	BH21	4	4		

Total Depth @ 4 feet bgs

ENSOLUM

APPENDIX D

Photographic Log

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 1	Date 7/24/2025	
Description Site Investigation		
View South		
Photograph 2	Date 7/28/2025	
Description Site Investigation		
View North		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 3	Date 7/28/2025	
Description Site Investigation		
View North		
Photograph 4	Date 7/28/2025	
Description Site Investigation		
View South		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 5	Date 7/29/2025	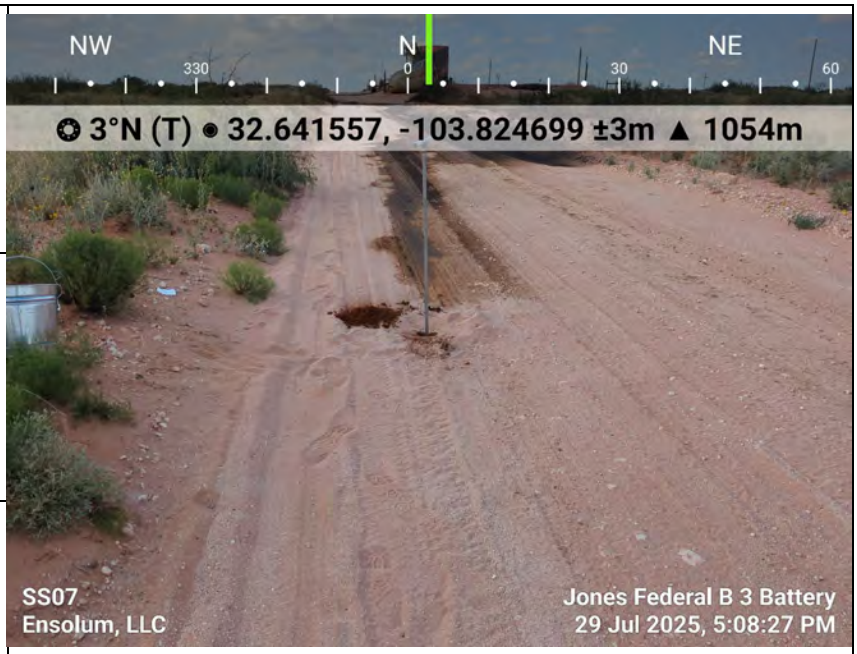
Description Delineation		
View North		
Photograph 6	Date 7/29/2025	
Description Delineation		
View North		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 7	Date 8/11/2025	
Description Delineation		
View Southeast		
Photograph 8	Date 8/12/2025	
Description Delineation		
View Northwest		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 9	Date 8/13/2025	
Description Delineation		
View Northwest		
Photograph 10	Date 8/14/2025	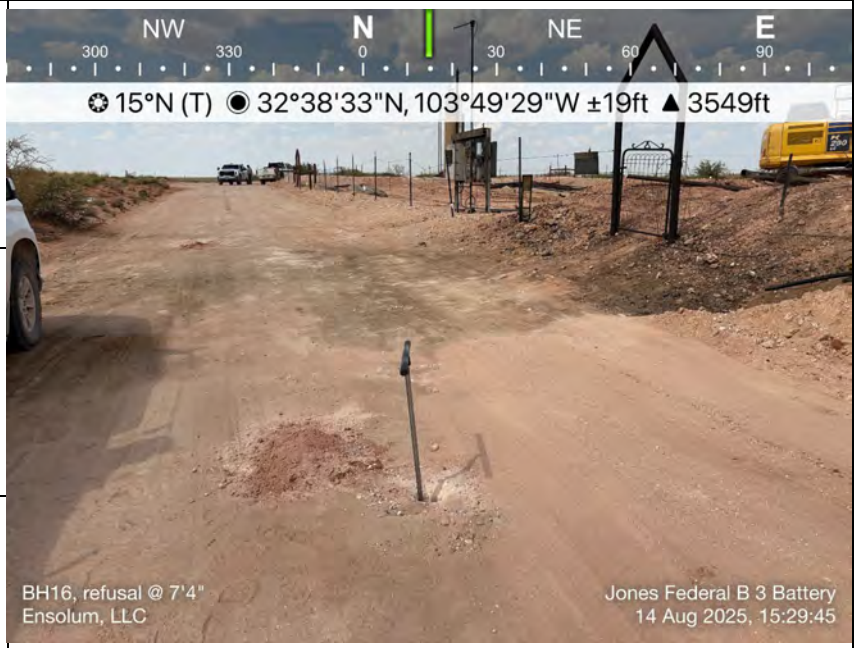
Description Delineation		
View North		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 11	Date 8/19/2025	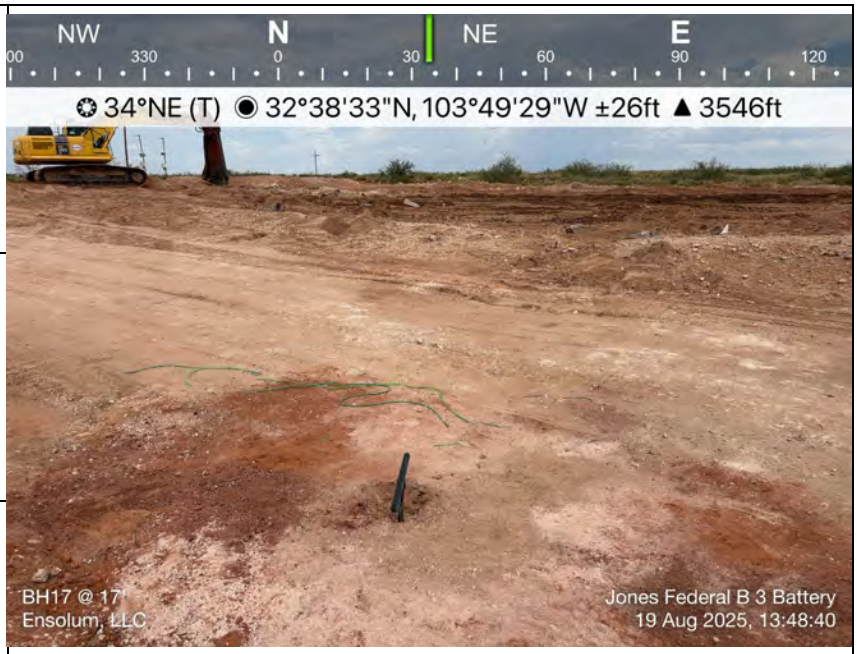
Description Delineation		
View Northeast		
Photograph 12	Date 8/21/2025	
Description Delineation		
View South		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 13	Date 10/28/2025	
Description Delineation		
View Southwest		
Photograph 14	Date 10/29/2025	
Description Delineation		
View North		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 15	Date 1/20/2026	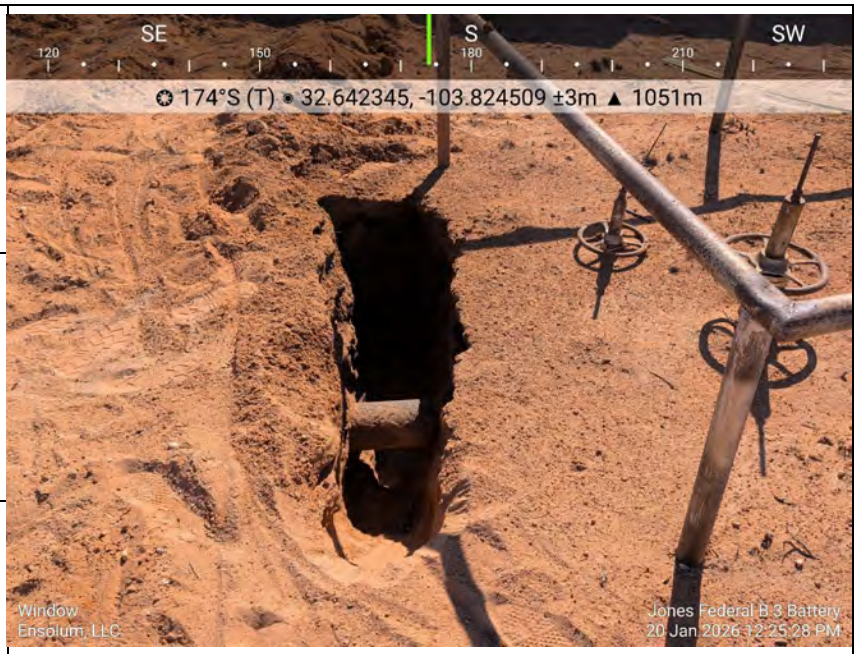
Description Hydro-vac pipelines		
View South		
Photograph 16	Date 1/22/2026	
Description Excavation		
View Northeast		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 17	Date 1/23/2026	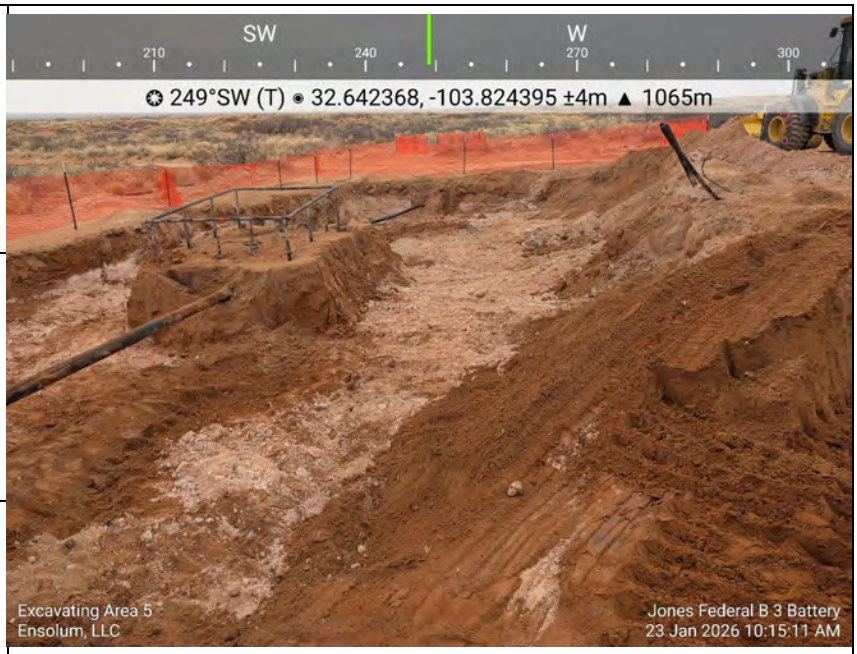
Description Excavation		
View West		
Photograph 18	Date 1/28/2026	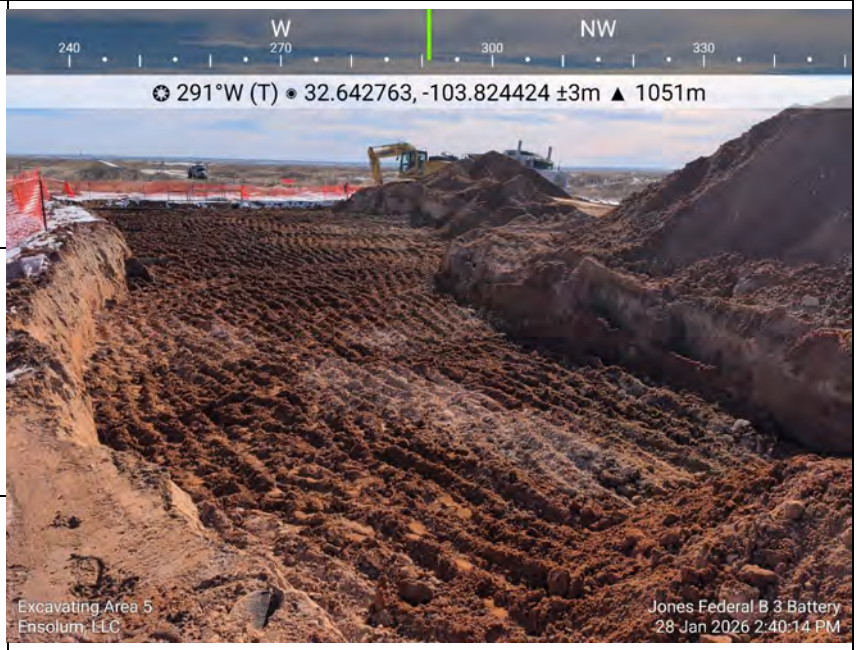
Description Excavation		
View West		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 19	Date 1/29/2026	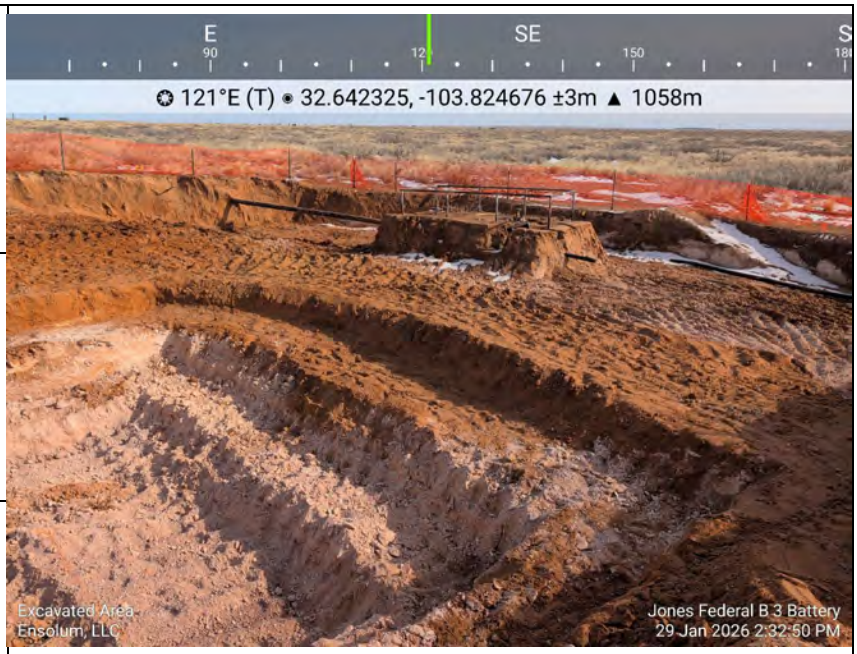
Description Excavation		
View Southeast		
Photograph 20	Date 1/29/2026	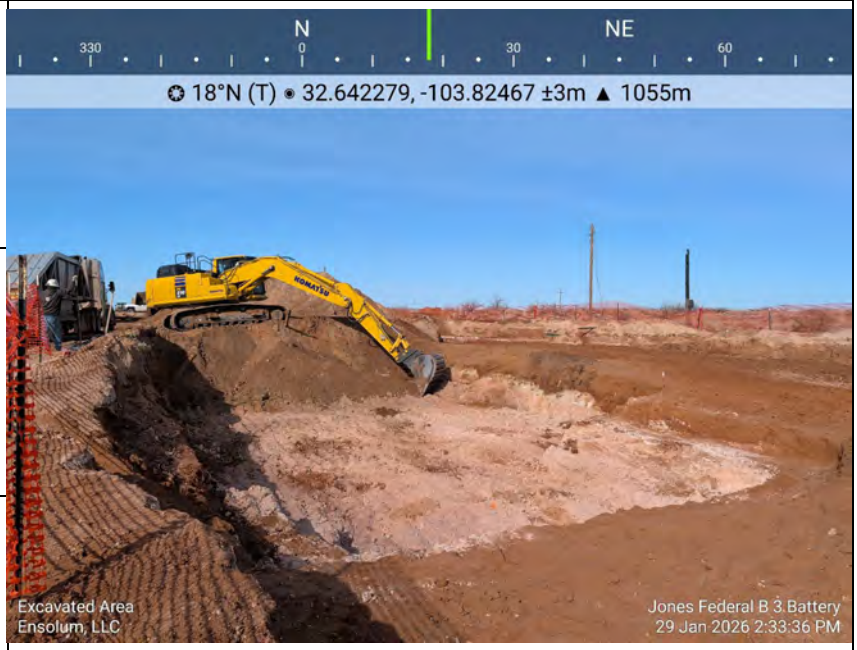
Description Excavation		
View North		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 21	Date 1/30/2026	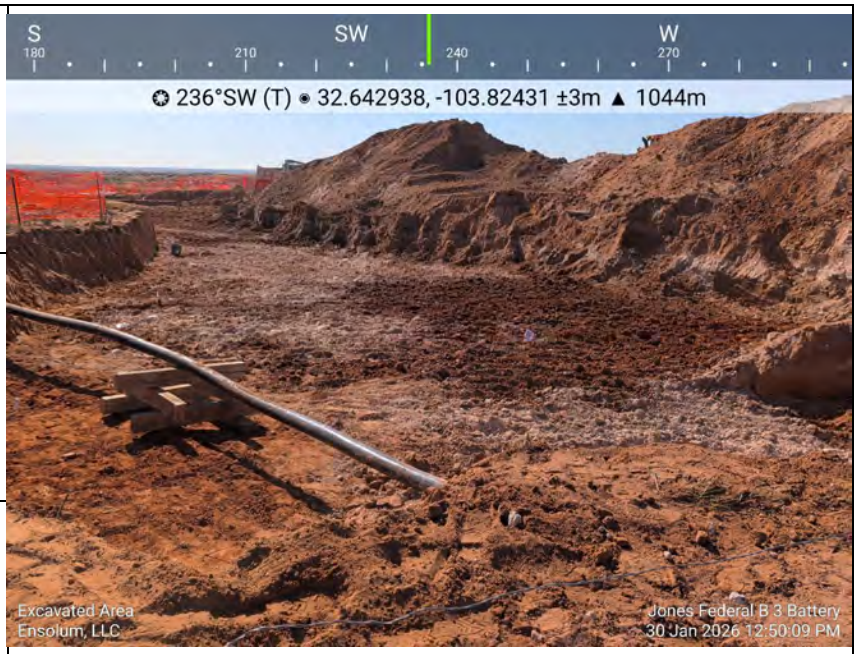
Description Excavation		
View Southwest		
Photograph 22	Date 1/30/2026	
Description Excavation		
View Southwest		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 23	Date 2/2/2026	
Description Excavation		
View East		
Photograph 24	Date 2/2/2026	
Description Excavation		
View Northwest		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 25	Date 2/3/2026	
Description Excavation		
View Southwest		
Photograph 26	Date 2/4/2026	
Description Excavation		
View Northwest		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 27	Date 2/5/2026	
Description Excavation		
View South		
Photograph 28	Date 2/6/2026	
Description Excavation		
View East		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 29	Date 2/6/2026	
Description Backfill road		
View Southwest		
Photograph 30	Date 2/9/2026	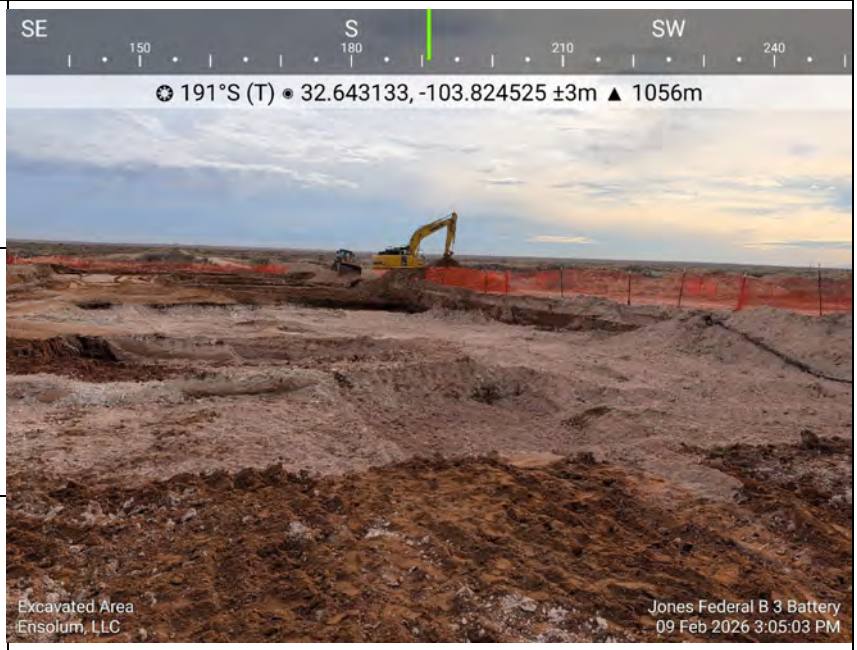
Description Excavation		
View Southwest		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 31	Date 2/10/2026	
Description Excavation		
View Northwest		
Photograph 32	Date 2/10/2026	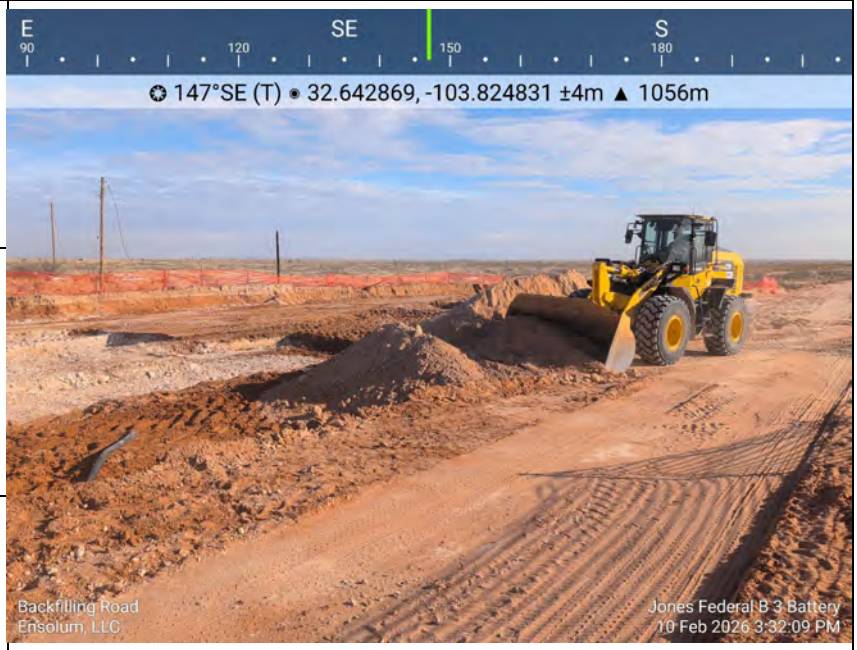
Description Backfill road		
View Southeast		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 33	Date 2/11/2026	
Description Excavation		
View North		
Photograph 34	Date 2/12/2026	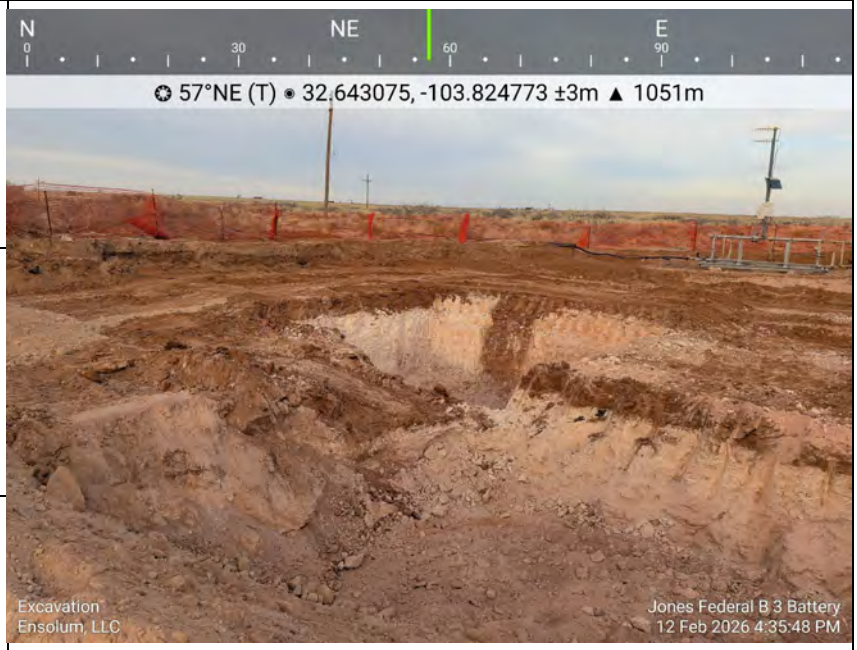
Description Excavation		
View Northeast		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 35	Date 2/13/2026	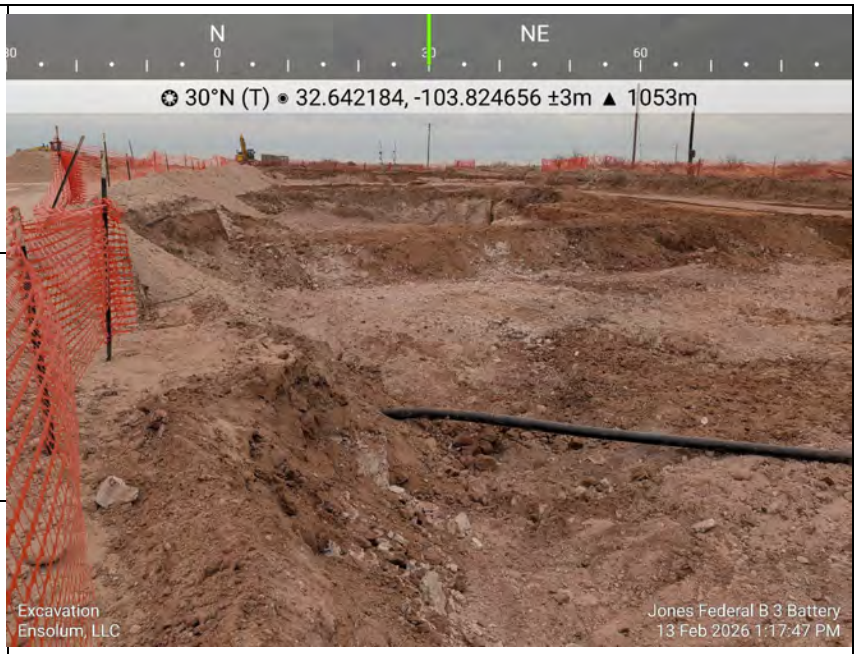
Description Excavation		
View Northeast		
Photograph 36	Date 2/13/2026	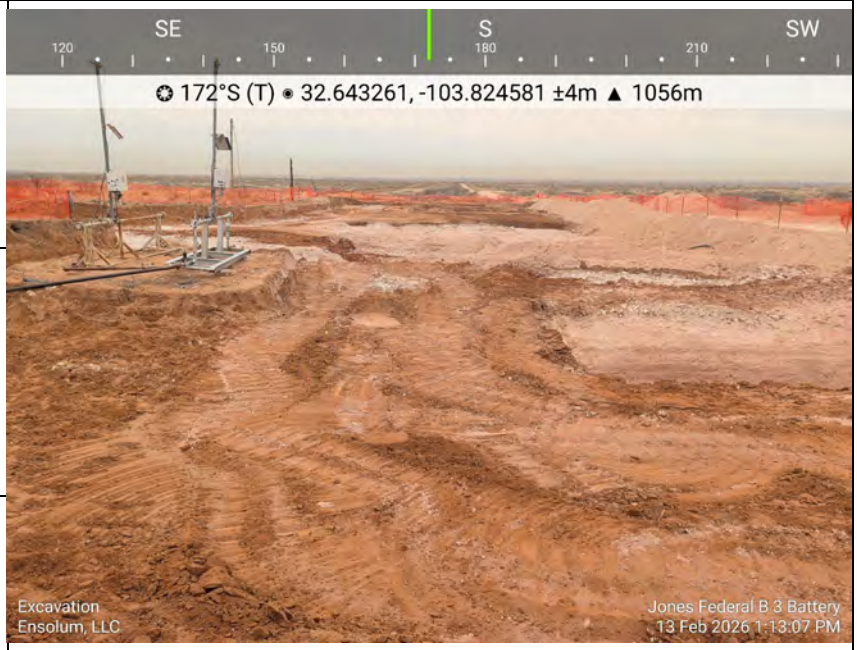
Description Excavation		
View South		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 37	Date 2/24/2026	
Description Excavation (Around south pipeline header)		
View East		
Photograph 38	Date 2/24/2026	
Description Excavation		
View Northeast		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 39	Date 2/26/2026	
Description Excavation (Around south pipeline header)		
View Southwest		
Photograph 40	Date 2/26/2026	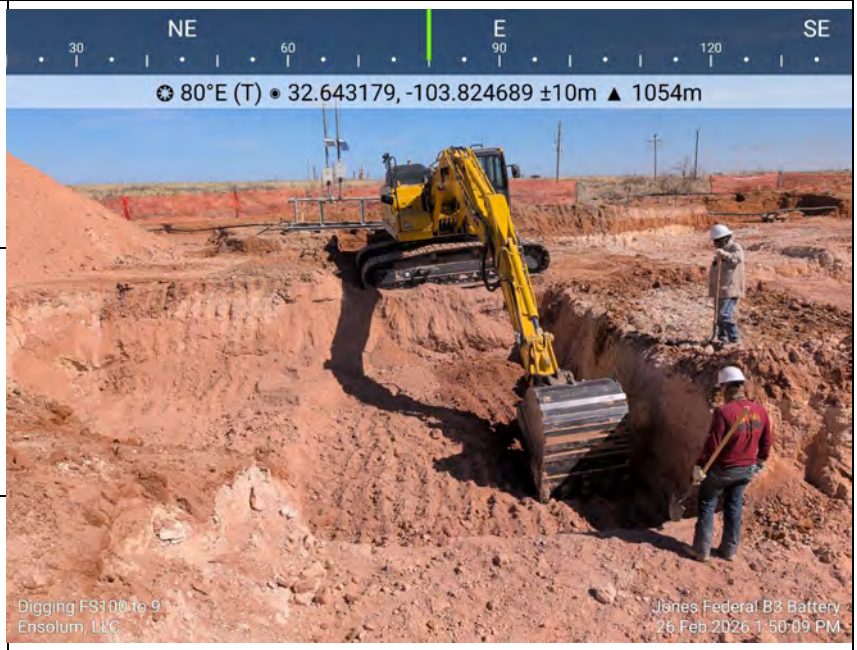
Description Excavation		
View East		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 41	Date 2/27/2026	
Description Excavation		
View East		
Photograph 42	Date 2/27/2026	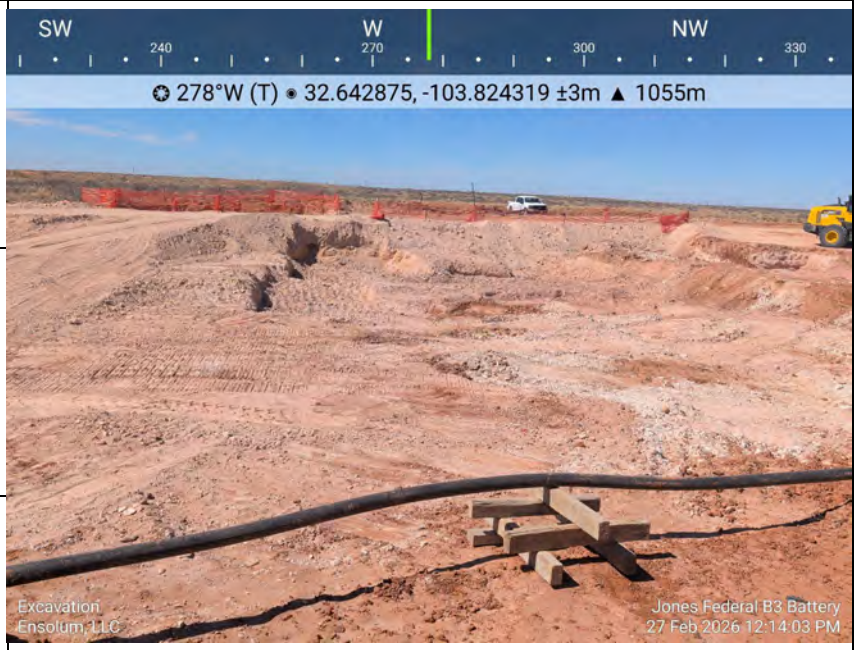
Description Excavation		
View West		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 43	Date 3/10/2026	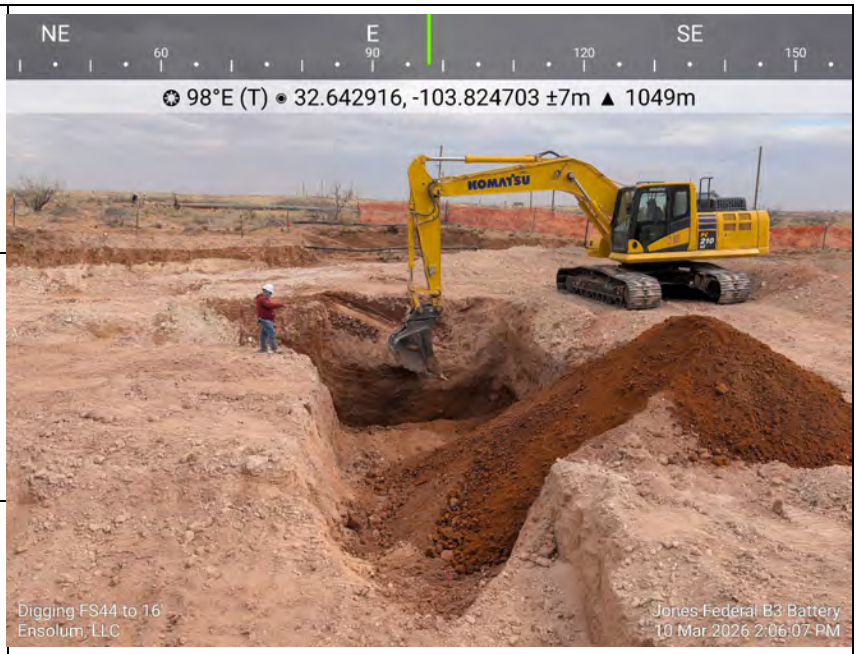
Description Excavation (FS44)		
View East		
Photograph 44	Date 3/11/2026	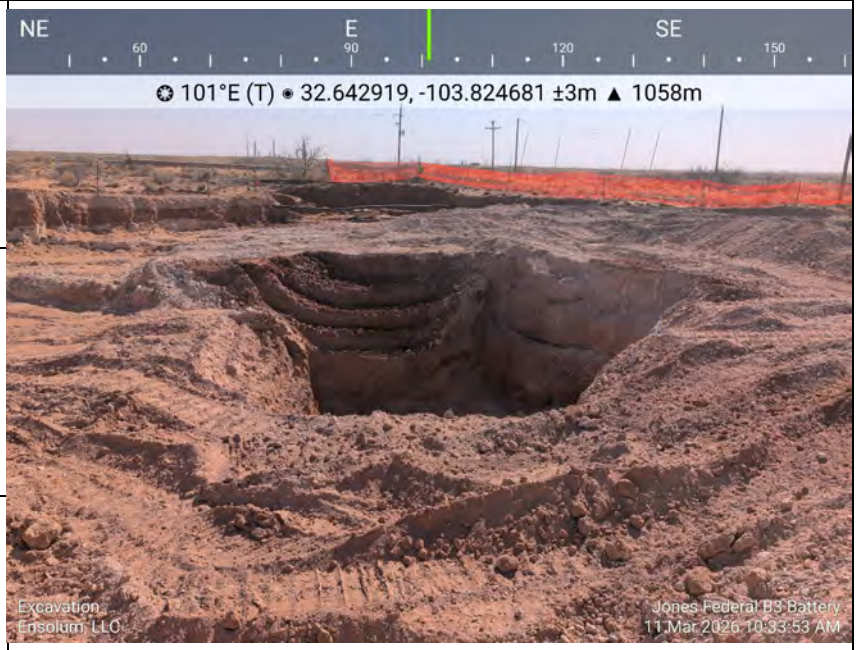
Description Sample collection		
View East		

ENSOLUM

Photographic Log

Devon Energy Production Company, LP
Jones Federal B 3 Battery
nMLB1129240104 & nAPP2520569781

Photograph 45	Date 3/20/2026	
Description Backfill		
View Southeast		
Photograph 46	Date 3/20/2026	
Description Backfill		
View North		

ENSOLUM

APPENDIX E

Laboratory Analytical Reports & Chain-of-Custody Documentation

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E507349
Job Number:	01058-0007
Received:	7/31/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/6/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/6/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E507349
Date Received: 7/31/2025 8:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 7/31/2025 8:00:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

SS02-0’ 6

SS02-1’ 7

SS04-0’ 8

SS04-1’ 9

SS05-0’ 10

SS05-1’ 11

SS06-0’ 12

SS06-1’ 13

SS07-0’ 14

SS07-1’ 15

SS08-0’ 16

SS08-1’ 17

SS09-0’ 18

SS09-1’ 19

SS10-0’ 20

SS10-1’ 21

SS11-0’ 22

SS11-1’ 23

SS12-0’ 24

SS12-1’ 25

Table of Contents (continued)

QC Summary Data 26

QC - Volatile Organics by EPA 8021B 26

QC - Nonhalogenated Organics by EPA 8015D - GRO 27

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 28

QC - Anions by EPA 300.0/9056A 29

Definitions and Notes 30

Chain of Custody etc. 31

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/06/25 15:15

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
SS02-0'	E507349-01A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS02-1'	E507349-02A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS04-0'	E507349-03A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS04-1'	E507349-04A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS05-0'	E507349-05A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS05-1'	E507349-06A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS06-0'	E507349-07A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS06-1'	E507349-08A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS07-0'	E507349-09A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS07-1'	E507349-10A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS08-0'	E507349-11A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS08-1'	E507349-12A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS09-0'	E507349-13A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS09-1'	E507349-14A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS10-0'	E507349-15A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS10-1'	E507349-16A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS11-0'	E507349-17A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS11-1'	E507349-18A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS12-0'	E507349-19A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.
SS12-1'	E507349-20A	Soil	07/29/25	07/31/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS02-0'

E507349-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.7 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.4 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*88.0 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**379**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS02-1'

E507349-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.9 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.0 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	**55.7**	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	**108**	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*87.3 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**935**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS04-0'

E507349-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.8 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.8 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*87.9 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**616**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS04-1'

E507349-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.8 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.3 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	**32.5**	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*86.0 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**404**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS05-0'

E507349-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.9 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*82.8 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**345**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS05-1'

E507349-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.6 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.6 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*87.5 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**406**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS06-0'

E507349-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/04/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/04/25	
Toluene	ND	0.0250	1	08/01/25	08/04/25	
o-Xylene	ND	0.0250	1	08/01/25	08/04/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/04/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*89.7 %*	*70-130*	*08/01/25*	*08/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.6 %*	*70-130*	*08/01/25*	*08/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*87.5 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS06-1'

E507349-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.4 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.7 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*86.8 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS07-0'

E507349-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.2 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.4 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*84.0 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS07-1'

E507349-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.3 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*87.3 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**613**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS08-0'

E507349-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.2 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.9 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*84.3 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS08-1'

E507349-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.8 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*84.2 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS09-0'

E507349-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.0 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.3 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*85.7 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS09-1'

E507349-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	**38.7**	25.0	1	08/01/25	08/04/25	
Oil Range Organics (C28-C36)	**66.0**	50.0	1	08/01/25	08/04/25	
Surrogate: n-Nonane		*84.7 %*	*61-141*	*08/01/25*	*08/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**91.0**	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS10-0'

E507349-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.6 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*85.7 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS10-1'

E507349-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.4 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.1 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*85.5 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS11-0'

E507349-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.0 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.4 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*83.7 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS11-1'

E507349-18

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.2 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.5 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*90.4 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	ND	20.0	1	08/01/25	08/01/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS12-0'

E507349-19

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.7 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.0 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	ND	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*85.8 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**530**	20.0	1	08/01/25	08/02/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

SS12-1'

E507349-20

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Benzene	ND	0.0250	1	08/01/25	08/05/25	
Ethylbenzene	ND	0.0250	1	08/01/25	08/05/25	
Toluene	ND	0.0250	1	08/01/25	08/05/25	
o-Xylene	ND	0.0250	1	08/01/25	08/05/25	
p,m-Xylene	ND	0.0500	1	08/01/25	08/05/25	
Total Xylenes	ND	0.0250	1	08/01/25	08/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.2 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2531156
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/01/25	08/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.8 %*	*70-130*	*08/01/25*	*08/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2531173
Diesel Range Organics (C10-C28)	**496**	25.0	1	08/01/25	08/05/25	
Oil Range Organics (C28-C36)	**504**	50.0	1	08/01/25	08/05/25	
Surrogate: n-Nonane		*98.2 %*	*61-141*	*08/01/25*	*08/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2531161
Chloride	**206**	20.0	1	08/01/25	08/02/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2531156-BLK1)									Prepared: 08/01/25 Analyzed: 08/04/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.25*		*8.00*		*90.6*	*70-130*			
LCS (2531156-BS1)									Prepared: 08/01/25 Analyzed: 08/05/25
Benzene	4.32	0.0250	5.00		86.4	70-130			
Ethylbenzene	4.38	0.0250	5.00		87.6	70-130			
Toluene	4.41	0.0250	5.00		88.3	70-130			
o-Xylene	4.46	0.0250	5.00		89.2	70-130			
p,m-Xylene	8.90	0.0500	10.0		89.0	70-130			
Total Xylenes	13.4	0.0250	15.0		89.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.77*		*8.00*		*84.6*	*70-130*			
Matrix Spike (2531156-MS1)				**Source: E507349-07**					Prepared: 08/01/25 Analyzed: 08/06/25
Benzene	4.65	0.0250	5.00	ND	93.1	70-130			
Ethylbenzene	4.76	0.0250	5.00	ND	95.1	70-130			
Toluene	4.77	0.0250	5.00	ND	95.4	70-130			
o-Xylene	4.76	0.0250	5.00	ND	95.2	70-130			
p,m-Xylene	9.63	0.0500	10.0	ND	96.3	70-130			
Total Xylenes	14.4	0.0250	15.0	ND	95.9	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.75*		*8.00*		*84.4*	*70-130*			
Matrix Spike Dup (2531156-MSD1)				**Source: E507349-07**					Prepared: 08/01/25 Analyzed: 08/06/25
Benzene	5.19	0.0250	5.00	ND	104	70-130	10.9	27	
Ethylbenzene	5.30	0.0250	5.00	ND	106	70-130	10.9	26	
Toluene	5.31	0.0250	5.00	ND	106	70-130	10.8	20	
o-Xylene	5.28	0.0250	5.00	ND	106	70-130	10.3	25	
p,m-Xylene	10.7	0.0500	10.0	ND	107	70-130	10.7	23	
Total Xylenes	16.0	0.0250	15.0	ND	107	70-130	10.6	26	
Surrogate: 4-Bromochlorobenzene-PID	*6.70*		*8.00*		*83.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2531156-BLK1)									Prepared: 08/01/25 Analyzed: 08/04/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.25*		*8.00*		*90.6*	*70-130*			
LCS (2531156-BS2)									Prepared: 08/01/25 Analyzed: 08/05/25
Gasoline Range Organics (C6-C10)	39.8	20.0	50.0		79.7	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.45*		*8.00*		*93.1*	*70-130*			
Matrix Spike (2531156-MS2)				**Source: E507349-07**					Prepared: 08/01/25 Analyzed: 08/06/25
Gasoline Range Organics (C6-C10)	49.2	20.0	50.0	ND	98.5	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.49*		*8.00*		*93.6*	*70-130*			
Matrix Spike Dup (2531156-MSD2)				**Source: E507349-07**					Prepared: 08/01/25 Analyzed: 08/05/25
Gasoline Range Organics (C6-C10)	48.3	20.0	50.0	ND	96.6	70-130	1.95	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.36*		*8.00*		*92.1*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2531173-BLK1)									Prepared: 08/01/25 Analyzed: 08/04/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*43.0*		*50.0*		*86.0*	*61-141*			
LCS (2531173-BS1)									Prepared: 08/01/25 Analyzed: 08/04/25
Diesel Range Organics (C10-C28)	260	25.0	250		104	66-144			
Surrogate: n-Nonane	*44.5*		*50.0*		*89.1*	*61-141*			
Matrix Spike (2531173-MS1)				**Source: E507349-18**					Prepared: 08/01/25 Analyzed: 08/04/25
Diesel Range Organics (C10-C28)	276	25.0	250	ND	110	56-156			
Surrogate: n-Nonane	*45.6*		*50.0*		*91.2*	*61-141*			
Matrix Spike Dup (2531173-MSD1)				**Source: E507349-18**					Prepared: 08/01/25 Analyzed: 08/04/25
Diesel Range Organics (C10-C28)	268	25.0	250	ND	107	56-156	2.86	20	
Surrogate: n-Nonane	*45.1*		*50.0*		*90.1*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/6/2025 3:15:04PM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2531161-BLK1)									Prepared: 08/01/25 Analyzed: 08/01/25
Chloride	ND	20.0							
LCS (2531161-BS1)									Prepared: 08/01/25 Analyzed: 08/01/25
Chloride	256	20.0	250		102	90-110			
Matrix Spike (2531161-MS1)				**Source: E507349-09**					Prepared: 08/01/25 Analyzed: 08/01/25
Chloride	257	20.0	250	ND	103	80-120			
Matrix Spike Dup (2531161-MSD1)				**Source: E507349-09**					Prepared: 08/01/25 Analyzed: 08/01/25
Chloride	256	20.0	250	ND	102	80-120	0.404	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/06/25 15:15

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E501349	Job Number 01058.0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information | **Analysis and Method** | **EPA Program**

EPA Program: SDWA | CWA | RCRA; Compliance Y or N; PWSID #

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
1021	7/29/2025	S	1	SS02 - 0'		1									X			2.2	
1643	7/29/2025	S	1	SS02 - 1'		2									X			3.1	
1223	7/29/2025	S	1	SS04 - 0'		3									X			3.0	
1655	7/29/2025	S	1	SS04 - 1'		4									X			2.8	
1035	7/29/2025	S	1	SS05 - 0'		5									X			2.6	
1659	7/29/2025	S	1	SS05 - 1'		6									X			3.4	
1038	7/29/2025	S	1	SS06 - 0'		7									X			3.6	
1704	7/29/2025	S	1	SS06 - 1'		8									X			3.1	
1136	7/29/2025	S	1	SS07 - 0'		9									X			3.0	
1709	7/29/2025	S	1	SS07 - 1'		10									X			2.6	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, jmccauley@ensolum.com, akone@ensolum.com, jgonzalezz@ensolum.com, jhinkle@ensolum.com, eplugge@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Jarad McCauley

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	7-30-25	0800	Michelle Gonzales	7.30.25	0800
Michelle Gonzales	7.30.25	1430	Marissa Gonzales	7.30.25	1430
Marissa Gonzales	7.30.25	1903		7.30.25	1903
	7.30.25	2300	Caleb Mao	7.31.25	800
	Date	Time		Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E507349	Job Number 01058-0007	1D 2D 3D Std: X	NM: X CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
1140	7/29/2025	S	1	SS08 - 0'		11									X			2.0	
1714	7/29/2025	S	1	SS08 - 1'		12									X			2.4	
1142	7/29/2025	S	1	SS09 - 0'		13									X			3.4	
1720	7/29/2025	S	1	SS09 - 1'		14									X			3.2	
1144	7/29/2025	S	1	SS10 - 0'		15									X			3.0	
1725	7/29/2025	S	1	SS10 - 1'		16									X			2.8	
1146	7/29/2025	S	1	SS11 - 0'		17									X			2.6	
1731	7/29/2025	S	1	SS11 - 1'		18									X			3.8	
1306	7/29/2025	S	1	SS12 - 0'		19									X			3.4	
1745	7/29/2025	S	1	SS12 - 1'		20									X			2.6	

Analysis and Method | **EPA Program**: SDWA / CWA / RCRA; Compliance Y or N; PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, jmccauley@ensolum.com, akone@ensolum.com, jgonzalezz@ensolum.com, jhinkle@ensolum.com, eplugge@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Jarad McCauley

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	7-30-25	0800	Michelle Gonzales	7-30-25	0800
Michelle Gonzales	7-30-25	1430	Marissa Gonzales	7.30.25	1430
Marissa Gonzales	7.30.25	1903		7.30.25	1903
	7.30.25	2300	Cattle Mac	7.31.25	800
	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 7/31/2025 11:07:21AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	07/31/25 08:00	Work Order ID:	E507349
Phone:	(505) 382-1211	Date Logged In:	07/30/25 14:59	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/06/25 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508114
Job Number:	01058-0007
Received:	8/12/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/18/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/18/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508114
Date Received: 8/12/2025 7:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/12/2025 7:30:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH01-0’ 5
- BH02-0’ 6
- BH03-0’ 7
- BH04-0’ 8
- BH05-0’ 9
- BH06-0’ 10
- BH07-0’ 11
- BH08-0’ 12
- BH09-0’ 13
- BH10-0’ 14

QC Summary Data 15

- QC - Volatile Organics by EPA 8021B 15
- QC - Nonhalogenated Organics by EPA 8015D - GRO 16
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 17
- QC - Anions by EPA 300.0/9056A 18

Definitions and Notes 19

Chain of Custody etc. 20

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/18/25 11:20

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH01-0'	E508114-01A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH02-0'	E508114-02A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH03-0'	E508114-03A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH04-0'	E508114-04A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH05-0'	E508114-05A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH06-0'	E508114-06A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH07-0'	E508114-07A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH08-0'	E508114-08A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH09-0'	E508114-09A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.
BH10-0'	E508114-10A	Soil	08/07/25	08/12/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH01-0'

E508114-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	**0.0605**	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	**0.0676**	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	**0.103**	0.0500	1	08/12/25	08/12/25	
Total Xylenes	**0.170**	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*104 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**424**	25.0	1	08/12/25	08/12/25	
Oil Range Organics (C28-C36)	**919**	50.0	1	08/12/25	08/12/25	
Surrogate: n-Nonane		*125 %*	*61-141*	*08/12/25*	*08/12/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**9480**	200	10	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH02-0'

E508114-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**192**	25.0	1	08/12/25	08/12/25	
Oil Range Organics (C28-C36)	**264**	50.0	1	08/12/25	08/12/25	
Surrogate: n-Nonane		*122 %*	*61-141*	*08/12/25*	*08/12/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**6910**	200	10	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH03-0'

E508114-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	**0.0949**	0.0250	1	08/12/25	08/12/25	
Toluene	**0.0774**	0.0250	1	08/12/25	08/12/25	
o-Xylene	**0.0700**	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	**0.125**	0.0500	1	08/12/25	08/12/25	
Total Xylenes	**0.195**	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**873**	25.0	1	08/12/25	08/12/25	
Oil Range Organics (C28-C36)	**1290**	50.0	1	08/12/25	08/12/25	
Surrogate: n-Nonane		*120 %*	*61-141*	*08/12/25*	*08/12/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**6070**	100	5	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH04-0'

E508114-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	**0.166**	0.0250	1	08/12/25	08/12/25	
Toluene	**0.126**	0.0250	1	08/12/25	08/12/25	
o-Xylene	**0.108**	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	**0.218**	0.0500	1	08/12/25	08/12/25	
Total Xylenes	**0.326**	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.3 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**12500**	500	20	08/12/25	08/14/25	
Oil Range Organics (C28-C36)	**8950**	1000	20	08/12/25	08/14/25	
Surrogate: n-Nonane		*79.9 %*	*61-141*	*08/12/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**3610**	40.0	2	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH05-0'

E508114-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*106 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**838**	250	10	08/12/25	08/14/25	
Oil Range Organics (C28-C36)	**1380**	500	10	08/12/25	08/14/25	
Surrogate: n-Nonane		*99.1 %*	*61-141*	*08/12/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**76.3**	20.0	1	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH06-0'

E508114-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.9 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	ND	25.0	1	08/12/25	08/12/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/12/25	08/12/25	
Surrogate: n-Nonane		*103 %*	*61-141*	*08/12/25*	*08/12/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**59.7**	20.0	1	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH07-0'

E508114-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.5 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**64.1**	25.0	1	08/12/25	08/13/25	
Oil Range Organics (C28-C36)	**114**	50.0	1	08/12/25	08/13/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/12/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**402**	20.0	1	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH08-0'

E508114-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.3 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	ND	25.0	1	08/12/25	08/13/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/12/25	08/13/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*08/12/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**1180**	20.0	1	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH09-0'

E508114-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.3 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**529**	25.0	1	08/12/25	08/13/25	
Oil Range Organics (C28-C36)	**931**	50.0	1	08/12/25	08/13/25	
Surrogate: n-Nonane		*125 %*	*61-141*	*08/12/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**284**	20.0	1	08/12/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

BH10-0'

E508114-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Benzene	ND	0.0250	1	08/12/25	08/12/25	
Ethylbenzene	ND	0.0250	1	08/12/25	08/12/25	
Toluene	ND	0.0250	1	08/12/25	08/12/25	
o-Xylene	ND	0.0250	1	08/12/25	08/12/25	
p,m-Xylene	ND	0.0500	1	08/12/25	08/12/25	
Total Xylenes	ND	0.0250	1	08/12/25	08/12/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.5 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533042
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/12/25	08/12/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/12/25*	*08/12/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2533037
Diesel Range Organics (C10-C28)	**9870**	500	20	08/12/25	08/13/25	
Oil Range Organics (C28-C36)	**10200**	1000	20	08/12/25	08/13/25	
Surrogate: n-Nonane		*102 %*	*61-141*	*08/12/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2533054
Chloride	**179**	20.0	1	08/12/25	08/13/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533042-BLK1)									Prepared: 08/12/25 Analyzed: 08/12/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.87*		*8.00*		*98.3*	*70-130*			
LCS (2533042-BS1)									Prepared: 08/12/25 Analyzed: 08/12/25
Benzene	3.98	0.0250	5.00		79.6	70-130			
Ethylbenzene	3.94	0.0250	5.00		78.8	70-130			
Toluene	3.97	0.0250	5.00		79.4	70-130			
o-Xylene	4.01	0.0250	5.00		80.1	70-130			
p,m-Xylene	8.04	0.0500	10.0		80.4	70-130			
Total Xylenes	12.0	0.0250	15.0		80.3	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.84*		*8.00*		*98.1*	*70-130*			
Matrix Spike (2533042-MS1)				**Source: E508113-06**					Prepared: 08/12/25 Analyzed: 08/12/25
Benzene	4.57	0.0250	5.00	ND	91.3	70-130			
Ethylbenzene	4.52	0.0250	5.00	ND	90.3	70-130			
Toluene	4.55	0.0250	5.00	ND	90.9	70-130			
o-Xylene	4.54	0.0250	5.00	ND	90.9	70-130			
p,m-Xylene	9.19	0.0500	10.0	ND	91.9	70-130			
Total Xylenes	13.7	0.0250	15.0	ND	91.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.95*		*8.00*		*99.3*	*70-130*			
Matrix Spike Dup (2533042-MSD1)				**Source: E508113-06**					Prepared: 08/12/25 Analyzed: 08/12/25
Benzene	4.18	0.0250	5.00	ND	83.6	70-130	8.79	27	
Ethylbenzene	4.12	0.0250	5.00	ND	82.5	70-130	9.04	26	
Toluene	4.16	0.0250	5.00	ND	83.2	70-130	8.89	20	
o-Xylene	4.22	0.0250	5.00	ND	84.4	70-130	7.35	25	
p,m-Xylene	8.43	0.0500	10.0	ND	84.3	70-130	8.64	23	
Total Xylenes	12.7	0.0250	15.0	ND	84.3	70-130	8.21	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.00*		*8.00*		*99.9*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533042-BLK1)									Prepared: 08/12/25 Analyzed: 08/12/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.11*		*8.00*		*114*	*70-130*			
LCS (2533042-BS2)									Prepared: 08/12/25 Analyzed: 08/12/25
Gasoline Range Organics (C6-C10)	53.3	20.0	50.0		107	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.04*		*8.00*		*113*	*70-130*			
Matrix Spike (2533042-MS2)				**Source: E508113-06**					Prepared: 08/12/25 Analyzed: 08/12/25
Gasoline Range Organics (C6-C10)	49.0	20.0	50.0	ND	98.0	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.68*		*8.00*		*109*	*70-130*			
Matrix Spike Dup (2533042-MSD2)				**Source: E508113-06**					Prepared: 08/12/25 Analyzed: 08/12/25
Gasoline Range Organics (C6-C10)	47.5	20.0	50.0	ND	95.0	70-130	3.06	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.88*		*8.00*		*111*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: HM

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533037-BLK1)									Prepared: 08/12/25 Analyzed: 08/12/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*59.3*		*50.0*		*119*	*61-141*			
LCS (2533037-BS1)									Prepared: 08/12/25 Analyzed: 08/12/25
Diesel Range Organics (C10-C28)	259	25.0	250		104	66-144			
Surrogate: n-Nonane	*51.0*		*50.0*		*102*	*61-141*			
Matrix Spike (2533037-MS1)				**Source: E508114-07**					Prepared: 08/12/25 Analyzed: 08/12/25
Diesel Range Organics (C10-C28)	336	25.0	250	64.1	109	56-156			
Surrogate: n-Nonane	*54.9*		*50.0*		*110*	*61-141*			
Matrix Spike Dup (2533037-MSD1)				**Source: E508114-07**					Prepared: 08/12/25 Analyzed: 08/12/25
Diesel Range Organics (C10-C28)	319	25.0	250	64.1	102	56-156	5.27	20	
Surrogate: n-Nonane	*55.8*		*50.0*		*112*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/18/2025 11:20:41AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533054-BLK1)									Prepared: 08/12/25 Analyzed: 08/12/25
Chloride	ND	20.0							
LCS (2533054-BS1)									Prepared: 08/12/25 Analyzed: 08/12/25
Chloride	257	20.0	250		103	90-110			
Matrix Spike (2533054-MS1)				**Source: E508114-03**					Prepared: 08/12/25 Analyzed: 08/13/25
Chloride	6150	100	250	6070	34.1	80-120			M4
Matrix Spike Dup (2533054-MSD1)				**Source: E508114-03**					Prepared: 08/12/25 Analyzed: 08/13/25
Chloride	5990	100	250	6070	NR	80-120	2.73	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/18/25 11:20

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508114	1D 2D 3D Std: x	NM: x; CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr	Job Number 01058(0007		
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method: DRO/ORO by 8015; GRO/DRO by 8015; BTEX by 8021; VOC by 8260; Chloride 300.0; TCEQ 1005 - TX; RCRA 8 Metals; BGDOC - NM; BGDOC - TX

EPA Program: SDWA; CWA; RCRA

Compliance: Y or N

PWSID #:

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	BGDOC - NM	Sample Temp	Remarks
1002	8/7/25	S	1	BH01-0'		1	X	1.2	
1004				BH02-0'		2		1.4	
1007				BH03-0'		3		1.6	
1008				BH04-0'		4		1.2	
1222				BH05-0'		5		1.8	
1224				BH06-0'		6		1.6	
1404				BH07-0'		7		2.0	
1402				BH08-0'		8		2.0	
1400				BH09-0'		9		2.2	
1359				BH10-0'		10		2.4	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/8/25	900	Michelle Gonzales	8-11-25	0711
Michelle Gonzales	8-11-25	1400	Marissa Gonzales	8-11-25	1400
Marissa Gonzales	8-11-25	1730	Andrew Musso	8.11.25	1730
Andrew Musso	8.11.25	2145	[signature]	8.12.25	730
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/12/2025 10:33:50AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/12/25 07:30	Work Order ID:	E508114
Phone:	(505) 382-1211	Date Logged In:	08/11/25 14:52	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/18/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508136
Job Number:	01058-0007
Received:	8/13/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/19/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/19/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508136
Date Received: 8/13/2025 7:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/13/2025 7:00:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH01-2’ 5
- BH01-4’ 6
- BH01-5’ 7
- BH02-2’ 8
- BH02-4’ 9
- BH02-5’ 10
- BH03-2’ 11
- BH03-4’ 12
- BH03-5’ 13
- BH04-2’ 14
- BH04-4’ 15
- BH04-5’ 16

QC Summary Data 17

- QC - Volatile Organic Compounds by EPA8260B 17
- QC - Nonhalogenated Organics by EPA 8015D - GRO 18
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 19
- QC - Anions by EPA 300.0/9056A 20

Definitions and Notes 21

Chain of Custody etc. 22

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/19/25 09:25

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH01-2'	E508136-01A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH01-4'	E508136-02A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH01-5'	E508136-03A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH02-2'	E508136-04A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH02-4'	E508136-05A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH02-5'	E508136-06A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH03-2'	E508136-07A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH03-4'	E508136-08A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH03-5'	E508136-09A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH04-2'	E508136-10A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH04-4'	E508136-11A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.
BH04-5'	E508136-12A	Soil	08/11/25	08/13/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH01-2'

E508136-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*109 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*95.8 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*109 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*95.8 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/13/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/13/25	
Surrogate: n-Nonane		*90.7 %*	*61-141*	*08/13/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1840**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH01-4'

E508136-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*98.4 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*98.4 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	**54.7**	25.0	1	08/13/25	08/13/25	
Oil Range Organics (C28-C36)	**62.4**	50.0	1	08/13/25	08/13/25	
Surrogate: n-Nonane		*94.6 %*	*61-141*	*08/13/25*	*08/13/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1550**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH01-5'

E508136-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*91.2 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1420**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH02-2'

E508136-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*98.6 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*98.6 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	**827**	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	**760**	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*92.7 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**520**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH02-4'

E508136-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*90.5 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**262**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH02-5'

E508136-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*101 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*101 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*89.8 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**760**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH03-2'

E508136-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	**205**	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	**271**	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*92.4 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1600**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH03-4'

E508136-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*99.9 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*99.9 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	**132**	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	**196**	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*87.0 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1430**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH03-5'

E508136-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	**162**	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	**225**	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*89.5 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**322**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH04-2'

E508136-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*101 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*111 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*101 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*88.5 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**31.2**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH04-4'

E508136-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*89.6 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**1990**	20.0	1	08/13/25	08/13/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

BH04-5'

E508136-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Benzene	ND	0.0250	1	08/13/25	08/13/25	
Ethylbenzene	ND	0.0250	1	08/13/25	08/13/25	
Toluene	ND	0.0250	1	08/13/25	08/13/25	
o-Xylene	ND	0.0250	1	08/13/25	08/13/25	
p,m-Xylene	ND	0.0500	1	08/13/25	08/13/25	
Total Xylenes	ND	0.0250	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533072
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/13/25	08/13/25	
Surrogate: Bromofluorobenzene		*110 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: 1,2-Dichloroethane-d4		*102 %*	*70-130*	*08/13/25*	*08/13/25*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*08/13/25*	*08/13/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533075
Diesel Range Organics (C10-C28)	ND	25.0	1	08/13/25	08/14/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/13/25	08/14/25	
Surrogate: n-Nonane		*91.1 %*	*61-141*	*08/13/25*	*08/14/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533077
Chloride	**212**	20.0	1	08/13/25	08/13/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

Volatile Organic Compounds by EPA 8260B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533072-BLK1)									Prepared: 08/13/25 Analyzed: 08/13/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: Bromofluorobenzene	*0.554*		*0.500*		*111*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.492*		*0.500*		*98.3*	*70-130*			
Surrogate: Toluene-d8	*0.523*		*0.500*		*105*	*70-130*			
LCS (2533072-BS1)									Prepared: 08/13/25 Analyzed: 08/13/25
Benzene	2.71	0.0250	2.50		108	70-130			
Ethylbenzene	2.69	0.0250	2.50		108	70-130			
Toluene	2.65	0.0250	2.50		106	70-130			
o-Xylene	2.58	0.0250	2.50		103	70-130			
p,m-Xylene	5.35	0.0500	5.00		107	70-130			
Total Xylenes	7.93	0.0250	7.50		106	70-130			
Surrogate: Bromofluorobenzene	*0.525*		*0.500*		*105*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.521*		*0.500*		*104*	*70-130*			
Surrogate: Toluene-d8	*0.517*		*0.500*		*103*	*70-130*			
Matrix Spike (2533072-MS1)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Benzene	2.48	0.0250	2.50	ND	99.0	48-131			
Ethylbenzene	2.46	0.0250	2.50	ND	98.3	45-135			
Toluene	2.41	0.0250	2.50	ND	96.4	48-130			
o-Xylene	2.44	0.0250	2.50	ND	97.6	43-135			
p,m-Xylene	5.01	0.0500	5.00	ND	100	43-135			
Total Xylenes	7.45	0.0250	7.50	ND	99.4	43-135			
Surrogate: Bromofluorobenzene	*0.549*		*0.500*		*110*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.515*		*0.500*		*103*	*70-130*			
Surrogate: Toluene-d8	*0.513*		*0.500*		*103*	*70-130*			
Matrix Spike Dup (2533072-MSD1)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Benzene	2.51	0.0250	2.50	ND	100	48-131	1.40	23	
Ethylbenzene	2.54	0.0250	2.50	ND	102	45-135	3.26	27	
Toluene	2.44	0.0250	2.50	ND	97.5	48-130	1.20	24	
o-Xylene	2.50	0.0250	2.50	ND	99.9	43-135	2.33	27	
p,m-Xylene	5.11	0.0500	5.00	ND	102	43-135	1.90	27	
Total Xylenes	7.61	0.0250	7.50	ND	101	43-135	2.04	27	
Surrogate: Bromofluorobenzene	*0.546*		*0.500*		*109*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.491*		*0.500*		*98.2*	*70-130*			
Surrogate: Toluene-d8	*0.513*		*0.500*		*103*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533072-BLK1)									Prepared: 08/13/25 Analyzed: 08/13/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: Bromofluorobenzene	*0.554*		*0.500*		*111*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.492*		*0.500*		*98.3*	*70-130*			
Surrogate: Toluene-d8	*0.523*		*0.500*		*105*	*70-130*			
LCS (2533072-BS2)									Prepared: 08/13/25 Analyzed: 08/13/25
Gasoline Range Organics (C6-C10)	59.3	20.0	50.0		119	70-130			
Surrogate: Bromofluorobenzene	*0.567*		*0.500*		*113*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.498*		*0.500*		*99.5*	*70-130*			
Surrogate: Toluene-d8	*0.534*		*0.500*		*107*	*70-130*			
Matrix Spike (2533072-MS2)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Gasoline Range Organics (C6-C10)	49.5	20.0	50.0	ND	99.1	70-130			
Surrogate: Bromofluorobenzene	*0.561*		*0.500*		*112*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.489*		*0.500*		*97.8*	*70-130*			
Surrogate: Toluene-d8	*0.517*		*0.500*		*103*	*70-130*			
Matrix Spike Dup (2533072-MSD2)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Gasoline Range Organics (C6-C10)	58.3	20.0	50.0	ND	117	70-130	16.2	20	
Surrogate: Bromofluorobenzene	*0.563*		*0.500*		*113*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.485*		*0.500*		*96.9*	*70-130*			
Surrogate: Toluene-d8	*0.527*		*0.500*		*105*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533075-BLK1)									Prepared: 08/13/25 Analyzed: 08/13/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*45.1*		*50.0*		*90.2*	*61-141*			
LCS (2533075-BS1)									Prepared: 08/13/25 Analyzed: 08/13/25
Diesel Range Organics (C10-C28)	245	25.0	250		98.2	66-144			
Surrogate: n-Nonane	*45.6*		*50.0*		*91.3*	*61-141*			
Matrix Spike (2533075-MS1)				**Source: E508135-05**					Prepared: 08/13/25 Analyzed: 08/13/25
Diesel Range Organics (C10-C28)	248	25.0	250	ND	99.3	56-156			
Surrogate: n-Nonane	*46.2*		*50.0*		*92.4*	*61-141*			
Matrix Spike Dup (2533075-MSD1)				**Source: E508135-05**					Prepared: 08/13/25 Analyzed: 08/13/25
Diesel Range Organics (C10-C28)	236	25.0	250	ND	94.6	56-156	4.90	20	
Surrogate: n-Nonane	*44.9*		*50.0*		*89.8*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/19/2025 9:25:38AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533077-BLK1)									Prepared: 08/13/25 Analyzed: 08/13/25
Chloride	ND	20.0							
LCS (2533077-BS1)									Prepared: 08/13/25 Analyzed: 08/13/25
Chloride	253	20.0	250		101	90-110			
Matrix Spike (2533077-MS1)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Chloride	1700	20.0	250	1550	61.4	80-120			M4
Matrix Spike Dup (2533077-MSD1)				**Source: E508136-02**					Prepared: 08/13/25 Analyzed: 08/13/25
Chloride	1750	20.0	250	1550	80.2	80-120	2.72	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/19/25 09:25

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508136O	Job Number 0058.0007	1D 2D 3D Std: x	NM: x CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method: DRO/ORO by 8015; GRO/DRO by 8015; BTEX by 8021; VOC by 8260; Chloride 300.0; TCEQ 1005 - TX; RCRA 8 Metals; BGDOC - NM; BGDOC - TX

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	BGDOC - NM	Sample Temp	Remarks
946	8/11/25	S	1	BH01-2'		1	X	3.0	
953				BH01-4'		2		2.6	
1036				BH01-5'		3		2.4	
1114				BH02-2'		4		3.0	
1121				BH02-4'		5		3.1	
1124				BH02-5'		6		2.2	
1249				BH03-2'		7		2.0	
1339				BH03-4'		8		1.8	
1342				BH03-5'		9		2.0	
1434				BH04-2'		10		1.6	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	8/12/25	900	Michelle Gonzales	8.12.25	0900
Michelle Gonzales	8.12.25	1445	Marissa Gonzales	8.12.25	1445
Marissa Gonzales	8.12.25	1830	Andrew Musso	8.12.25	1830
Andrew Musso	8.12.25	2245	Cailtyn Mar	8.13.25	700
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) / N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508136	Job Number 01058.0007	1D 2D 3D Std: x	NM: x CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
1437	8/11/25	S	1	BH04-4'		11									X			2.0	
1440	↓	↓	↓	BH04-5'		12									X			1.2	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/12/25	900	Michelle Gonzales	8.12.25	0900
Michelle Gonzales	8.12.25	1445	Marissa Gonzales	8-12-25	1445
Marissa Gonzales	8.12.25	1830	Andrew Musso	8.12.25	1830
Andrew Musso	8.12.25	2245	Caitlin Mason	8.13.25	700
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/13/2025 9:45:59AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/13/25 07:00	Work Order ID:	E508136
Phone:	(505) 382-1211	Date Logged In:	08/12/25 15:33	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/19/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508158
Job Number:	01058-0007
Received:	8/14/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/20/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/20/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508158
Date Received: 8/14/2025 7:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/14/2025 7:15:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH01-7’ 5
- BH01-9’ 6
- BH02-6’ 7
- BH03-7’ 8
- BH10-2’ 9
- BH10-4’ 10
- BH10-6’ 11
- BH10-8’ 12
- BH10-10’ 13

QC Summary Data 14

- QC - Volatile Organics by EPA 8021B 14
- QC - Nonhalogenated Organics by EPA 8015D - GRO 15
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 16
- QC - Anions by EPA 300.0/9056A 17

Definitions and Notes 18

Chain of Custody etc. 19

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/20/25 08:56

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH01-7'	E508158-01A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH01-9'	E508158-02A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH02-6'	E508158-03A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH03-7'	E508158-04A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH10-2'	E508158-05A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH10-4'	E508158-06A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH10-6'	E508158-07A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH10-8'	E508158-08A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.
BH10-10'	E508158-09A	Soil	08/12/25	08/14/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH01-7'

E508158-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/14/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/14/25	
Toluene	ND	0.0250	1	08/14/25	08/14/25	
o-Xylene	ND	0.0250	1	08/14/25	08/14/25	
p,m-Xylene	ND	0.0500	1	08/14/25	08/14/25	
Total Xylenes	ND	0.0250	1	08/14/25	08/14/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.1 %*	*70-130*	*08/14/25*	*08/14/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/14/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.6 %*	*70-130*	*08/14/25*	*08/14/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*97.7 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**2300**	40.0	2	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH01-9'

E508158-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	ND	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/14/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*86.0 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.8 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*94.7 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**3380**	40.0	2	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH02-6'

E508158-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	ND	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/14/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.6 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.7 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	**42.7**	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*95.8 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**698**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH03-7'

E508158-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	**0.129**	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	**0.0727**	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	**0.444**	0.0500	1	08/14/25	08/15/25	
Total Xylenes	**0.517**	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.6 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	**25.5**	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*94.2 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	**6350**	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	**1520**	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*103 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**198**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH10-2'

E508158-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	**0.325**	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	**0.194**	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	**0.801**	0.0500	1	08/14/25	08/15/25	
Total Xylenes	**0.994**	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*92.6 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	**54.8**	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.7 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	**6990**	125	5	08/15/25	08/19/25	
Oil Range Organics (C28-C36)	**2460**	250	5	08/15/25	08/19/25	
Surrogate: n-Nonane		*99.9 %*	*61-141*	*08/15/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**197**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH10-4'

E508158-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	**0.0813**	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	**0.0264**	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	**0.0763**	0.0500	1	08/14/25	08/15/25	
Total Xylenes	**0.103**	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*82.4 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.5 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	**855**	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	**674**	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*99.8 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**396**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH10-6'

E508158-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	ND	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	**0.0501**	0.0500	1	08/14/25	08/15/25	
Total Xylenes	**0.0501**	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*82.7 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.7 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/18/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/18/25	
Surrogate: n-Nonane		*96.7 %*	*61-141*	*08/15/25*	*08/18/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**435**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH10-8'

E508158-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	ND	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/14/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.0 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.5 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*99.2 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**757**	20.0	1	08/14/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

BH10-10'

E508158-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Benzene	ND	0.0250	1	08/14/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/14/25	08/15/25	
Toluene	ND	0.0250	1	08/14/25	08/15/25	
o-Xylene	ND	0.0250	1	08/14/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/14/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/14/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.2 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2533097
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/14/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.2 %*	*70-130*	*08/14/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533137
Diesel Range Organics (C10-C28)	**41.8**	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*94.0 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2533117
Chloride	**46.3**	20.0	1	08/14/25	08/15/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533097-BLK1)									Prepared: 08/14/25 Analyzed: 08/14/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*6.99*		*8.00*		*87.4*	*70-130*			
LCS (2533097-BS1)									Prepared: 08/14/25 Analyzed: 08/14/25
Benzene	5.18	0.0250	5.00		104	70-130			
Ethylbenzene	5.31	0.0250	5.00		106	70-130			
Toluene	5.31	0.0250	5.00		106	70-130			
o-Xylene	5.24	0.0250	5.00		105	70-130			
p,m-Xylene	10.7	0.0500	10.0		107	70-130			
Total Xylenes	16.0	0.0250	15.0		106	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.07*		*8.00*		*88.4*	*70-130*			
Matrix Spike (2533097-MS1)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/14/25
Benzene	5.13	0.0250	5.00	ND	103	70-130			
Ethylbenzene	5.24	0.0250	5.00	ND	105	70-130			
Toluene	5.25	0.0250	5.00	ND	105	70-130			
o-Xylene	5.17	0.0250	5.00	ND	103	70-130			
p,m-Xylene	10.6	0.0500	10.0	ND	106	70-130			
Total Xylenes	15.8	0.0250	15.0	ND	105	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.98*		*8.00*		*87.3*	*70-130*			
Matrix Spike Dup (2533097-MSD1)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/14/25
Benzene	5.22	0.0250	5.00	ND	104	70-130	1.79	27	
Ethylbenzene	5.34	0.0250	5.00	ND	107	70-130	1.93	26	
Toluene	5.36	0.0250	5.00	ND	107	70-130	2.07	20	
o-Xylene	5.27	0.0250	5.00	ND	105	70-130	1.80	25	
p,m-Xylene	10.8	0.0500	10.0	ND	108	70-130	1.65	23	
Total Xylenes	16.0	0.0250	15.0	ND	107	70-130	1.70	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.06*		*8.00*		*88.2*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533097-BLK1)									Prepared: 08/14/25 Analyzed: 08/14/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.39*		*8.00*		*92.3*	*70-130*			
LCS (2533097-BS2)									Prepared: 08/14/25 Analyzed: 08/14/25
Gasoline Range Organics (C6-C10)	52.6	20.0	50.0		105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.50*		*8.00*		*93.7*	*70-130*			
Matrix Spike (2533097-MS2)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/14/25
Gasoline Range Organics (C6-C10)	51.6	20.0	50.0	ND	103	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.44*		*8.00*		*93.1*	*70-130*			
Matrix Spike Dup (2533097-MSD2)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/14/25
Gasoline Range Organics (C6-C10)	50.6	20.0	50.0	ND	101	70-130	1.91	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.65*		*8.00*		*95.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533137-BLK1)									Prepared: 08/15/25 Analyzed: 08/15/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*45.0*		*50.0*		*89.9*	*61-141*			
LCS (2533137-BS1)									Prepared: 08/15/25 Analyzed: 08/15/25
Diesel Range Organics (C10-C28)	247	25.0	250		99.0	66-144			
Surrogate: n-Nonane	*46.7*		*50.0*		*93.4*	*61-141*			
Matrix Spike (2533137-MS1)				**Source: E508158-07**					Prepared: 08/15/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	276	25.0	250	ND	110	56-156			
Surrogate: n-Nonane	*47.1*		*50.0*		*94.1*	*61-141*			
Matrix Spike Dup (2533137-MSD1)				**Source: E508158-07**					Prepared: 08/15/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	266	25.0	250	ND	107	56-156	3.40	20	
Surrogate: n-Nonane	*47.6*		*50.0*		*95.2*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/20/2025 8:56:51AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533117-BLK1)									Prepared: 08/14/25 Analyzed: 08/15/25
Chloride	ND	20.0							
LCS (2533117-BS1)									Prepared: 08/14/25 Analyzed: 08/15/25
Chloride	252	20.0	250		101	90-110			
Matrix Spike (2533117-MS1)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/15/25
Chloride	264	20.0	250	ND	106	80-120			
Matrix Spike Dup (2533117-MSD1)				**Source: E508157-06**					Prepared: 08/14/25 Analyzed: 08/15/25
Chloride	264	20.0	250	ND	106	80-120	0.0690	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/20/25 08:56

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508158	Job Number 01058-0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information							Analysis and Method										EPA Program	
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX	SDWA / CWA / RCRA	
																	Compliance Y or N	
																	PWSID #	
935	8/12/25	S	1	BH01-7'		1									x		Samle Temp: 2.9	Remarks
1018	8/12/25	↓	↓	BH01-9'		2									↓		2.6	
945	↓			BH02-6'		3											2.5	
1113				BH03-7'		4											2.3	
1247				BH10-2'		5											2.7	
1253				BH10-4'		6											2.9	
1326				BH10-6'		7											3.0	
1356				BH10-8'		8											3.4	
1434	↓	↓	↓	BH10-10'		9									↓		3.3	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/13/25	900	Michelle Gonzales	8-13-25	0900
[signature]	8-13-25	1500	Marissa Gonzales	8-13-25	1500
Marissa Gonzales	8-13-25	1650	Andrew Musso	8.13.25	1900
Andrew Musso	8.14.25	0345	Noe Sdo	8-14-25	0715
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____ Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/14/2025 11:39:48AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/14/25 07:15	Work Order ID:	E508158
Phone:	(505) 382-1211	Date Logged In:	08/13/25 15:44	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/20/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508177
Job Number:	01058-0007
Received:	8/15/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/21/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/21/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508177
Date Received: 8/15/2025 7:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/15/2025 7:30:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH12-0’ 5
- BH11-0’ 6
- BH11-1’ 7
- BH11-3’ 8
- BH11-4’ 9
- BH11-6’ 10
- BH11-8’ 11
- BH11-10’ 12

QC Summary Data 13

- QC - Volatile Organics by EPA 8021B 13
- QC - Nonhalogenated Organics by EPA 8015D - GRO 14
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 15
- QC - Anions by EPA 300.0/9056A 16

Definitions and Notes 17

Chain of Custody etc. 18

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/21/25 09:02

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH12-0'	E508177-01A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-0'	E508177-02A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-1'	E508177-03A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-3'	E508177-04A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-4'	E508177-05A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-6'	E508177-06A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-8'	E508177-07A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.
BH11-10'	E508177-08A	Soil	08/13/25	08/15/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH12-0'

E508177-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*92.0 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.3 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*93.1 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**285**	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-0'

E508177-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*93.8 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.5 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533139
Diesel Range Organics (C10-C28)	**1110**	25.0	1	08/15/25	08/19/25	
Oil Range Organics (C28-C36)	**649**	50.0	1	08/15/25	08/19/25	
Surrogate: n-Nonane		*98.2 %*	*61-141*	*08/15/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**367**	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-1'

E508177-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.4 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*86.6 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	ND	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-3'

E508177-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.1 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*85.8 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*97.7 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**410**	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-4'

E508177-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.9 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.0 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	**33.5**	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*97.9 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**588**	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-6'

E508177-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.2 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.2 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*101 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**1530**	20.0	1	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-8'

E508177-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.7 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*86.7 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/15/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/15/25	
Surrogate: n-Nonane		*99.9 %*	*61-141*	*08/15/25*	*08/15/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**747**	40.0	2	08/15/25	08/15/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

BH11-10'

E508177-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Benzene	ND	0.0250	1	08/15/25	08/15/25	
Ethylbenzene	ND	0.0250	1	08/15/25	08/15/25	
Toluene	ND	0.0250	1	08/15/25	08/15/25	
o-Xylene	ND	0.0250	1	08/15/25	08/15/25	
p,m-Xylene	ND	0.0500	1	08/15/25	08/15/25	
Total Xylenes	ND	0.0250	1	08/15/25	08/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.8 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2533127
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/15/25	08/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*84.8 %*	*70-130*	*08/15/25*	*08/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2533139
Diesel Range Organics (C10-C28)	ND	25.0	1	08/15/25	08/16/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/15/25	08/16/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/15/25*	*08/16/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2533130
Chloride	**30.2**	20.0	1	08/15/25	08/15/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533127-BLK1)									Prepared: 08/15/25 Analyzed: 08/15/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.45*		*8.00*		*93.1*	*70-130*			
LCS (2533127-BS1)									Prepared: 08/15/25 Analyzed: 08/15/25
Benzene	5.60	0.0250	5.00		112	70-130			
Ethylbenzene	5.39	0.0250	5.00		108	70-130			
Toluene	5.51	0.0250	5.00		110	70-130			
o-Xylene	5.48	0.0250	5.00		110	70-130			
p,m-Xylene	10.9	0.0500	10.0		109	70-130			
Total Xylenes	16.4	0.0250	15.0		109	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.74*		*8.00*		*96.7*	*70-130*			
Matrix Spike (2533127-MS1)				**Source: E508177-07**					Prepared: 08/15/25 Analyzed: 08/15/25
Benzene	5.72	0.0250	5.00	ND	114	70-130			
Ethylbenzene	5.50	0.0250	5.00	ND	110	70-130			
Toluene	5.64	0.0250	5.00	ND	113	70-130			
o-Xylene	5.57	0.0250	5.00	ND	111	70-130			
p,m-Xylene	11.1	0.0500	10.0	ND	111	70-130			
Total Xylenes	16.7	0.0250	15.0	ND	111	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.58*		*8.00*		*94.7*	*70-130*			
Matrix Spike Dup (2533127-MSD1)				**Source: E508177-07**					Prepared: 08/15/25 Analyzed: 08/15/25
Benzene	5.26	0.0250	5.00	ND	105	70-130	8.42	27	
Ethylbenzene	5.10	0.0250	5.00	ND	102	70-130	7.42	26	
Toluene	5.19	0.0250	5.00	ND	104	70-130	8.36	20	
o-Xylene	5.15	0.0250	5.00	ND	103	70-130	7.82	25	
p,m-Xylene	10.3	0.0500	10.0	ND	103	70-130	7.80	23	
Total Xylenes	15.4	0.0250	15.0	ND	103	70-130	7.80	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.56*		*8.00*		*94.5*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533127-BLK1)									Prepared: 08/15/25 Analyzed: 08/15/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.02*		*8.00*		*87.8*	*70-130*			
LCS (2533127-BS2)									Prepared: 08/15/25 Analyzed: 08/15/25
Gasoline Range Organics (C6-C10)	51.0	20.0	50.0		102	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.15*		*8.00*		*89.4*	*70-130*			
Matrix Spike (2533127-MS2)				**Source: E508177-07**					Prepared: 08/15/25 Analyzed: 08/15/25
Gasoline Range Organics (C6-C10)	52.3	20.0	50.0	ND	105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.10*		*8.00*		*88.7*	*70-130*			
Matrix Spike Dup (2533127-MSD2)				**Source: E508177-07**					Prepared: 08/15/25 Analyzed: 08/15/25
Gasoline Range Organics (C6-C10)	53.6	20.0	50.0	ND	107	70-130	2.49	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.93*		*8.00*		*86.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533139-BLK1)									Prepared: 08/15/25 Analyzed: 08/15/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*46.9*		*50.0*		*93.8*	*61-141*			
LCS (2533139-BS1)									Prepared: 08/15/25 Analyzed: 08/15/25
Diesel Range Organics (C10-C28)	241	25.0	250		96.5	66-144			
Surrogate: n-Nonane	*47.6*		*50.0*		*95.1*	*61-141*			
Matrix Spike (2533139-MS1)				**Source: E508177-02**					Prepared: 08/15/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	1500	25.0	250	1110	156	56-156			
Surrogate: n-Nonane	*51.2*		*50.0*		*102*	*61-141*			
Matrix Spike Dup (2533139-MSD1)				**Source: E508177-02**					Prepared: 08/15/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	1550	25.0	250	1110	176	56-156	3.36	20	M4
Surrogate: n-Nonane	*49.4*		*50.0*		*98.7*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/21/2025 9:02:11AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2533130-BLK1)									Prepared: 08/15/25 Analyzed: 08/15/25
Chloride	ND	20.0							
LCS (2533130-BS1)									Prepared: 08/15/25 Analyzed: 08/15/25
Chloride	256	20.0	250		102	90-110			
Matrix Spike (2533130-MS1)				**Source: E508176-02**					Prepared: 08/15/25 Analyzed: 08/15/25
Chloride	254	20.0	250	ND	101	80-120			
Matrix Spike Dup (2533130-MSD1)				**Source: E508176-02**					Prepared: 08/15/25 Analyzed: 08/15/25
Chloride	255	20.0	250	ND	102	80-120	0.614	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/21/25 09:02

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO # 216585 26

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508177	Job Number 01058.0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method: DRO/ORO by 8015; GRO/DRO by 8015; BTEX by 8021; VOC by 8260; Chloride 300.0; TCEQ 1005 - TX; RCRA 8 Metals; BGDOC - NM; BGDOC - TX

EPA Program: SDWA | CWA | RCRA; Compliance Y or N; PWSID #

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	BGDOC - NM	Sample Temp	Remarks
1224	8/13/25	S	1	BH12 - 0'		1	x	3.6	
1222	↓	↓	↓	BH11 - 0'		2	↓	4.2	
1233				BH11 - 1'		3		4.3	
1240				BH11 - 3'		4		4.5	
1305				BH11 - 4'		5		3.8	
1415				BH11 - 6'		6		4.0	
1424				BH11 - 8'		7		4.2	
1458	↓	↓	↓	BH11 - 10'		8	↓	4.4	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/14/25	900	Michelle Gonzales	8.14.25	0900
Michelle Gonzales	8-14-25	1445	Mariana Gonzales	8-14-25	1445
Mariana Gonzales	8-14-25	1846	Andrew Musso	8.14.25	1840
Andrew Musso	8.14.25	2330	Caitlin Mars	8.15.25	730
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/15/2025 10:33:42AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/15/25 07:30	Work Order ID:	E508177
Phone:	(505) 382-1211	Date Logged In:	08/15/25 08:05	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/21/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508195
Job Number:	01058-0007
Received:	8/16/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/22/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/22/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508195
Date Received: 8/16/2025 8:15:29AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/16/2025 8:15:29AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

BH13-0’ 6

BH14-0’ 7

BH15-0’ 8

BH16-0’ 9

BH17-0’ 10

BH12-1’ 11

BH13-1’ 12

BH13-3’ 13

BH13-4’ 14

BH13-5’ 15

BH13-7’ 16

BH13-9’ 17

BH13-11’ 18

BH13-13’ 19

BH14-2’ 20

BH14-4’ 21

BH14-6’ 22

BH17-2’ 23

BH17-4’ 24

BH17-5’ 25

Table of Contents (continued)

BH17-7’ 26

BH17-9’ 27

BH16-1’ 28

BH16-4’ 29

BH16-5’ 30

BH16-7’ 31

QC Summary Data 32

QC - Volatile Organics by EPA 8021B 32

QC - Nonhalogenated Organics by EPA 8015D - GRO 34

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 36

QC - Anions by EPA 300.0/9056A 38

Definitions and Notes 40

Chain of Custody etc. 41

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/22/25 11:53

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH13-0'	E508195-01A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH14-0'	E508195-02A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH15-0'	E508195-03A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH16-0'	E508195-04A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-0'	E508195-05A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH12-1'	E508195-06A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-1'	E508195-07A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-3'	E508195-08A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-4'	E508195-09A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-5'	E508195-10A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-7'	E508195-11A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-9'	E508195-12A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-11'	E508195-13A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH13-13'	E508195-14A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH14-2'	E508195-15A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH14-4'	E508195-16A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH14-6'	E508195-17A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-2'	E508195-18A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-4'	E508195-19A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-5'	E508195-20A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-7'	E508195-21A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH17-9'	E508195-22A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH16-1'	E508195-23A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH16-4'	E508195-24A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH16-5'	E508195-25A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.
BH16-7'	E508195-26A	Soil	08/14/25	08/16/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-0'

E508195-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.8 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	ND	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH14-0'

E508195-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.2 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	**2790**	250	10	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	**1750**	500	10	08/19/25	08/19/25	
Surrogate: n-Nonane		*92.3 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1690**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH15-0'

E508195-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*99.1 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	**166**	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	**92.3**	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*103 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**2300**	40.0	2	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH16-0'

E508195-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.1 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	**1040**	50.0	2	08/19/25	08/21/25	
Oil Range Organics (C28-C36)	**421**	100	2	08/19/25	08/21/25	
Surrogate: n-Nonane		*102 %*	*61-141*	*08/19/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**7950**	100	5	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-0'

E508195-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	**179**	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	**143**	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*101 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**124**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH12-1'

E508195-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.5 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*115 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*101 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	ND	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-1'

E508195-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.7 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*102 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**26.1**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-3'

E508195-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.6 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/19/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/19/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**2550**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-4'

E508195-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.6 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**2180**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-5'

E508195-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.0 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*111 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**2810**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-7'

E508195-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.7 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**2040**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-9'

E508195-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.6 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*114 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*110 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1530**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-11'

E508195-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.6 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1140**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH13-13'

E508195-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.0 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**80.9**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH14-2'

E508195-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.0 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1370**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH14-4'

E508195-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*106 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1920**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH14-6'

E508195-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.2 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**1740**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-2'

E508195-18

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.7 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**626**	20.0	1	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-4'

E508195-19

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.1 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*112 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**5030**	40.0	2	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-5'

E508195-20

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Benzene	ND	0.0250	1	08/18/25	08/20/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/20/25	
Toluene	ND	0.0250	1	08/18/25	08/20/25	
o-Xylene	ND	0.0250	1	08/18/25	08/20/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/20/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/20/25	
Surrogate: 4-Bromochlorobenzene-PID		*95.9 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534017
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/20/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/20/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2534060
Diesel Range Organics (C10-C28)	ND	25.0	1	08/19/25	08/20/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/19/25	08/20/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/19/25*	*08/20/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534050
Chloride	**3080**	40.0	2	08/19/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-7'

E508195-21

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.0 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*111 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**2980**	40.0	2	08/18/25	08/18/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH17-9'

E508195-22

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**2550**	20.0	1	08/18/25	08/18/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH16-1'

E508195-23

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.5 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**755**	20.0	1	08/18/25	08/18/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH16-4'

E508195-24

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.8 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**6610**	100	5	08/18/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH16-5'

E508195-25

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.1 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**6380**	100	5	08/18/25	08/19/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

BH16-7'

E508195-26

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Benzene	ND	0.0250	1	08/18/25	08/19/25	
Ethylbenzene	ND	0.0250	1	08/18/25	08/19/25	
Toluene	ND	0.0250	1	08/18/25	08/19/25	
o-Xylene	ND	0.0250	1	08/18/25	08/19/25	
p,m-Xylene	ND	0.0500	1	08/18/25	08/19/25	
Total Xylenes	ND	0.0250	1	08/18/25	08/19/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.9 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2534016
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/18/25	08/19/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/18/25*	*08/19/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534033
Diesel Range Organics (C10-C28)	ND	25.0	1	08/18/25	08/19/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/18/25	08/19/25	
Surrogate: n-Nonane		*110 %*	*61-141*	*08/18/25*	*08/19/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2534031
Chloride	**6760**	100	5	08/18/25	08/19/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534016-BLK1)									Prepared: 08/18/25 Analyzed: 08/18/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.79*		*8.00*		*97.4*	*70-130*			
LCS (2534016-BS1)									Prepared: 08/18/25 Analyzed: 08/18/25
Benzene	5.39	0.0250	5.00		108	70-130			
Ethylbenzene	5.32	0.0250	5.00		106	70-130			
Toluene	5.38	0.0250	5.00		108	70-130			
o-Xylene	5.33	0.0250	5.00		107	70-130			
p,m-Xylene	10.8	0.0500	10.0		108	70-130			
Total Xylenes	16.1	0.0250	15.0		108	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.75*		*8.00*		*96.9*	*70-130*			
Matrix Spike (2534016-MS1)				**Source: E508195-22**					Prepared: 08/18/25 Analyzed: 08/19/25
Benzene	5.04	0.0250	5.00	ND	101	70-130			
Ethylbenzene	4.96	0.0250	5.00	ND	99.3	70-130			
Toluene	5.02	0.0250	5.00	ND	100	70-130			
o-Xylene	4.99	0.0250	5.00	ND	99.8	70-130			
p,m-Xylene	10.1	0.0500	10.0	ND	101	70-130			
Total Xylenes	15.1	0.0250	15.0	ND	100	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.80*		*8.00*		*97.6*	*70-130*			
Matrix Spike Dup (2534016-MSD1)				**Source: E508195-22**					Prepared: 08/18/25 Analyzed: 08/19/25
Benzene	4.95	0.0250	5.00	ND	98.9	70-130	1.95	27	
Ethylbenzene	4.89	0.0250	5.00	ND	97.8	70-130	1.53	26	
Toluene	4.92	0.0250	5.00	ND	98.5	70-130	1.86	20	
o-Xylene	4.88	0.0250	5.00	ND	97.6	70-130	2.25	25	
p,m-Xylene	9.91	0.0500	10.0	ND	99.1	70-130	1.55	23	
Total Xylenes	14.8	0.0250	15.0	ND	98.6	70-130	1.78	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.62*		*8.00*		*95.3*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534017-BLK1)									Prepared: 08/18/25 Analyzed: 08/20/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.95*		*8.00*		*99.3*	*70-130*			
LCS (2534017-BS1)									Prepared: 08/18/25 Analyzed: 08/20/25
Benzene	4.87	0.0250	5.00		97.3	70-130			
Ethylbenzene	4.88	0.0250	5.00		97.7	70-130			
Toluene	4.89	0.0250	5.00		97.9	70-130			
o-Xylene	4.91	0.0250	5.00		98.3	70-130			
p,m-Xylene	9.91	0.0500	10.0		99.1	70-130			
Total Xylenes	14.8	0.0250	15.0		98.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.68*		*8.00*		*96.0*	*70-130*			
Matrix Spike (2534017-MS1)				**Source: E508195-08**					Prepared: 08/18/25 Analyzed: 08/20/25
Benzene	4.90	0.0250	5.00	ND	98.1	70-130			
Ethylbenzene	4.93	0.0250	5.00	ND	98.7	70-130			
Toluene	4.94	0.0250	5.00	ND	98.9	70-130			
o-Xylene	4.95	0.0250	5.00	ND	98.9	70-130			
p,m-Xylene	10.0	0.0500	10.0	ND	100	70-130			
Total Xylenes	14.9	0.0250	15.0	ND	99.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.82*		*8.00*		*97.8*	*70-130*			
Matrix Spike Dup (2534017-MSD1)				**Source: E508195-08**					Prepared: 08/18/25 Analyzed: 08/20/25
Benzene	4.50	0.0250	5.00	ND	90.0	70-130	8.59	27	
Ethylbenzene	4.53	0.0250	5.00	ND	90.7	70-130	8.43	26	
Toluene	4.53	0.0250	5.00	ND	90.7	70-130	8.64	20	
o-Xylene	4.58	0.0250	5.00	ND	91.5	70-130	7.76	25	
p,m-Xylene	9.21	0.0500	10.0	ND	92.1	70-130	8.26	23	
Total Xylenes	13.8	0.0250	15.0	ND	91.9	70-130	8.09	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.67*		*8.00*		*95.9*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534016-BLK1)									Prepared: 08/18/25 Analyzed: 08/18/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.78*		*8.00*		*110*	*70-130*			
LCS (2534016-BS2)									Prepared: 08/18/25 Analyzed: 08/18/25
Gasoline Range Organics (C6-C10)	44.9	20.0	50.0		89.9	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.17*		*8.00*		*115*	*70-130*			
Matrix Spike (2534016-MS2)				**Source: E508195-22**					Prepared: 08/18/25 Analyzed: 08/19/25
Gasoline Range Organics (C6-C10)	47.8	20.0	50.0	ND	95.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.03*		*8.00*		*113*	*70-130*			
Matrix Spike Dup (2534016-MSD2)				**Source: E508195-22**					Prepared: 08/18/25 Analyzed: 08/19/25
Gasoline Range Organics (C6-C10)	53.8	20.0	50.0	ND	108	70-130	11.8	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.02*		*8.00*		*113*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534017-BLK1)									Prepared: 08/18/25 Analyzed: 08/20/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.39*		*8.00*		*105*	*70-130*			
LCS (2534017-BS2)									Prepared: 08/18/25 Analyzed: 08/20/25
Gasoline Range Organics (C6-C10)	45.5	20.0	50.0		91.0	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.79*		*8.00*		*110*	*70-130*			
Matrix Spike (2534017-MS2)				**Source: E508195-08**					Prepared: 08/18/25 Analyzed: 08/20/25
Gasoline Range Organics (C6-C10)	49.4	20.0	50.0	ND	98.8	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.06*		*8.00*		*113*	*70-130*			
Matrix Spike Dup (2534017-MSD2)				**Source: E508195-08**					Prepared: 08/18/25 Analyzed: 08/20/25
Gasoline Range Organics (C6-C10)	54.0	20.0	50.0	ND	108	70-130	8.90	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.16*		*8.00*		*114*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534033-BLK1)									Prepared: 08/18/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*58.9*		*50.0*		*118*	*61-141*			
LCS (2534033-BS1)									Prepared: 08/18/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	281	25.0	250		112	66-144			
Surrogate: n-Nonane	*53.3*		*50.0*		*107*	*61-141*			
Matrix Spike (2534033-MS1)				**Source: E508206-01**					Prepared: 08/18/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	296	25.0	250	ND	119	56-156			
Surrogate: n-Nonane	*56.7*		*50.0*		*113*	*61-141*			
Matrix Spike Dup (2534033-MSD1)				**Source: E508206-01**					Prepared: 08/18/25 Analyzed: 08/18/25
Diesel Range Organics (C10-C28)	290	25.0	250	ND	116	56-156	2.08	20	
Surrogate: n-Nonane	*55.4*		*50.0*		*111*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: RAS

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534060-BLK1)									Prepared: 08/19/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*51.4*		*50.0*		*103*	*61-141*			
LCS (2534060-BS1)									Prepared: 08/19/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	278	25.0	250		111	66-144			
Surrogate: n-Nonane	*51.0*		*50.0*		*102*	*61-141*			
Matrix Spike (2534060-MS1)				**Source: E508195-11**					Prepared: 08/19/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	308	25.0	250	ND	123	56-156			
Surrogate: n-Nonane	*56.1*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2534060-MSD1)				**Source: E508195-11**					Prepared: 08/19/25 Analyzed: 08/19/25
Diesel Range Organics (C10-C28)	300	25.0	250	ND	120	56-156	2.52	20	
Surrogate: n-Nonane	*54.6*		*50.0*		*109*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534031-BLK1)									Prepared: 08/18/25 Analyzed: 08/18/25
Chloride	ND	20.0							
LCS (2534031-BS1)									Prepared: 08/18/25 Analyzed: 08/18/25
Chloride	250	20.0	250		100	90-110			
Matrix Spike (2534031-MS1)				**Source: E508187-04**					Prepared: 08/18/25 Analyzed: 08/18/25
Chloride	376	20.0	250	134	96.9	80-120			
Matrix Spike Dup (2534031-MSD1)				**Source: E508187-04**					Prepared: 08/18/25 Analyzed: 08/18/25
Chloride	377	20.0	250	134	97.4	80-120	0.284	20	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/22/2025 11:53:45AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534050-BLK1)									Prepared: 08/19/25 Analyzed: 08/19/25
Chloride	ND	20.0							
LCS (2534050-BS1)									Prepared: 08/19/25 Analyzed: 08/19/25
Chloride	264	20.0	250		106	90-110			
Matrix Spike (2534050-MS1)				**Source: E508195-09**					Prepared: 08/19/25 Analyzed: 08/19/25
Chloride	2420	20.0	250	2180	94.9	80-120			
Matrix Spike Dup (2534050-MSD1)				**Source: E508195-09**					Prepared: 08/19/25 Analyzed: 08/19/25
Chloride	2480	20.0	250	2180	119	80-120	2.47	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/22/25 11:53

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# ESO 8195	Job Number 01058-0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals	BGDOC - NM	BGDOC - TX	Sample Temp	Remarks
925	8/14/25	S	1	BH13-0'		1								X		4.1	
1031				BH14-0'		2										4.3	
1635				BH15-0'		3										4.0	
1310				BH16-0'		4										4.5	
1210				BH17-0'		5										4.7	
919				BH12-1'		6										4.9	
929				BH13-1'		7										4.5	
933				BH13-3'		8										4.7	
935				BH13-4'		9										4.9	
938				BH13-5'		10										4.3	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/15/25	900	Michelle Gonzales	8-15-25	0900
Michelle Gonzales	8-15-25	1500	Marissa Gonzales	8-15-25	1500
Marissa Gonzales	8-15-25	2300	[signature]	8-16-25	0815
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____ Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Page 256 of 874

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 216585 26

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508195	Job Number 01058-0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method: DRO/ORO by 8015; GRO/DRO by 8015; BTEX by 8021; VOC by 8260; Chloride 300.0; TCEQ 1005 - TX; RCRA 8 Metals; BGDOC - NM; BGDOC - TX

EPA Program: SDWA | CWA | RCRA; Compliance Y or N; PWSID #

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	BGDOC - NM	Sample Temp	Remarks
1021	8/14/25	S	1	BH13-7'		11	X	5.3	
1036	"	"	"	BH13-9'		12	"	5.1	
1122	"	"	"	BH13-11'		13	"	5.3	
1143	"	"	"	BH13-13'		14	"	4.9	
1034	"	"	"	BH14-2'		15	"	4.7	
1057	"	"	"	BH14-4'		16	"	5.0	
1135	"	"	"	BH14-6'		17	"	4.8	
1236	"	"	"	BH17-2'		18	"	4.6	
1306	"	"	"	BH17-4'		19	"	4.9	
1310	"	"	"	BH17-5'		20	"	4.7	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/15/25	900	Michelle Gonzales	8.15.25	0900
Michelle Gonzales	8-15-25	1500	Marissa Gonzales	8 1525	1500
Marissa Gonzales	8-15-25	2300	[signature]	8-16-25	0815
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____ Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Page 257 of 874

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508195	Job Number 01058-0007	1D 2D 3D Std: x	NM: x CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information							Analysis and Method										EPA Program	
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		SDWA / CWA / RCRA
1543	8/14/25	S	1	BH17-7'		21									X		5.0	Compliance Y or N
1550				BH17-9'		22											5.3	PWSID #
1315				BH16-1'		23											4.5	Remarks
1345				BH16-4'		24											4.8	
1351				BH16-5'		25											4.8	
1514				BH16-7'		26											4.9	

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, lestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	8/15/25	900	Michelle Gonzales	8-15-25	0900
Michelle Gonzales	8-15-25	1500	Marissa Gonzales	8-15-25	1500
Marissa Gonzales	8-15-25	2300		8-16-25	0815

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____ Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Page 258 of 874

Envirotech Analytical Laboratory

Printed: 8/18/2025 10:33:45AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/16/25 08:15	Work Order ID:	E508195
Phone:	(505) 382-1211	Date Logged In:	08/15/25 16:08	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/22/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508229
Job Number:	01058-0007
Received:	8/21/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/27/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/27/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508229
Date Received: 8/21/2025 7:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/21/2025 7:30:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH17-11’ 5
- BH17-13’ 6
- BH17-15’ 7
- BH17-17’ 8
- SS01-0’ 9
- SS03-0’ 10
- SS13-0’ 11
- BH15-1’ 12
- BH15-3’ 13

QC Summary Data 14

- QC - Volatile Organics by EPA 8021B 14
- QC - Nonhalogenated Organics by EPA 8015D - GRO 15
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 16
- QC - Anions by EPA 300.0/9056A 17

Definitions and Notes 18

Chain of Custody etc. 19

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/27/25 08:52

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH17-11'	E508229-01A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
BH17-13'	E508229-02A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
BH17-15'	E508229-03A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
BH17-17'	E508229-04A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
SS01-0'	E508229-05A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
SS03-0'	E508229-06A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
SS13-0'	E508229-07A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
BH15-1'	E508229-08A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.
BH15-3'	E508229-09A	Soil	08/19/25	08/21/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH17-11'

E508229-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.8 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*113 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*112 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**389**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH17-13'

E508229-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*99.3 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*111 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**1280**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH17-15'

E508229-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.2 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*108 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**1720**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH17-17'

E508229-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.5 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*110 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**1690**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

SS01-0'

E508229-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.0 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	ND	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

SS03-0'

E508229-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*97.6 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**77.1**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

SS13-0'

E508229-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.1 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	ND	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH15-1'

E508229-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.0 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	**93.0**	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	**168**	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**552**	20.0	1	08/21/25	08/21/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

BH15-3'

E508229-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Benzene	ND	0.0250	1	08/21/25	08/21/25	
Ethylbenzene	ND	0.0250	1	08/21/25	08/21/25	
Toluene	ND	0.0250	1	08/21/25	08/21/25	
o-Xylene	ND	0.0250	1	08/21/25	08/21/25	
p,m-Xylene	ND	0.0500	1	08/21/25	08/21/25	
Total Xylenes	ND	0.0250	1	08/21/25	08/21/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.6 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2534091
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/21/25	08/21/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*08/21/25*	*08/21/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2534088
Diesel Range Organics (C10-C28)	ND	25.0	1	08/21/25	08/21/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/21/25	08/21/25	
Surrogate: n-Nonane		*112 %*	*61-141*	*08/21/25*	*08/21/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2534101
Chloride	**955**	20.0	1	08/21/25	08/22/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534091-BLK1)									Prepared: 08/21/25 Analyzed: 08/22/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.96*		*8.00*		*99.6*	*70-130*			
LCS (2534091-BS1)									Prepared: 08/21/25 Analyzed: 08/21/25
Benzene	5.14	0.0250	5.00		103	70-130			
Ethylbenzene	5.07	0.0250	5.00		101	70-130			
Toluene	5.12	0.0250	5.00		102	70-130			
o-Xylene	5.10	0.0250	5.00		102	70-130			
p,m-Xylene	10.3	0.0500	10.0		103	70-130			
Total Xylenes	15.4	0.0250	15.0		103	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.98*		*8.00*		*99.7*	*70-130*			
Matrix Spike (2534091-MS1)				**Source: E508229-02**					Prepared: 08/21/25 Analyzed: 08/21/25
Benzene	4.74	0.0250	5.00	ND	94.8	70-130			
Ethylbenzene	4.66	0.0250	5.00	ND	93.2	70-130			
Toluene	4.72	0.0250	5.00	ND	94.3	70-130			
o-Xylene	4.72	0.0250	5.00	ND	94.5	70-130			
p,m-Xylene	9.49	0.0500	10.0	ND	94.9	70-130			
Total Xylenes	14.2	0.0250	15.0	ND	94.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.89*		*8.00*		*98.6*	*70-130*			
Matrix Spike Dup (2534091-MSD1)				**Source: E508229-02**					Prepared: 08/21/25 Analyzed: 08/21/25
Benzene	5.04	0.0250	5.00	ND	101	70-130	6.16	27	
Ethylbenzene	4.95	0.0250	5.00	ND	99.0	70-130	5.99	26	
Toluene	5.01	0.0250	5.00	ND	100	70-130	6.07	20	
o-Xylene	4.99	0.0250	5.00	ND	99.9	70-130	5.58	25	
p,m-Xylene	10.1	0.0500	10.0	ND	101	70-130	5.90	23	
Total Xylenes	15.1	0.0250	15.0	ND	100	70-130	5.79	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.03*		*8.00*		*100*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534091-BLK1)									Prepared: 08/21/25 Analyzed: 08/22/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.53*		*8.00*		*107*	*70-130*			
LCS (2534091-BS2)									Prepared: 08/21/25 Analyzed: 08/21/25
Gasoline Range Organics (C6-C10)	49.2	20.0	50.0		98.5	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.75*		*8.00*		*109*	*70-130*			
Matrix Spike (2534091-MS2)				**Source: E508229-02**					Prepared: 08/21/25 Analyzed: 08/21/25
Gasoline Range Organics (C6-C10)	50.7	20.0	50.0	ND	101	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.75*		*8.00*		*109*	*70-130*			
Matrix Spike Dup (2534091-MSD2)				**Source: E508229-02**					Prepared: 08/21/25 Analyzed: 08/21/25
Gasoline Range Organics (C6-C10)	50.5	20.0	50.0	ND	101	70-130	0.333	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.68*		*8.00*		*108*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534088-BLK1)									Prepared: 08/21/25 Analyzed: 08/21/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*54.0*		*50.0*		*108*	*61-141*			
LCS (2534088-BS1)									Prepared: 08/21/25 Analyzed: 08/21/25
Diesel Range Organics (C10-C28)	309	25.0	250		124	66-144			
Surrogate: n-Nonane	*51.8*		*50.0*		*104*	*61-141*			
Matrix Spike (2534088-MS1)				**Source: E508227-01**					Prepared: 08/21/25 Analyzed: 08/21/25
Diesel Range Organics (C10-C28)	327	25.0	250	ND	131	56-156			
Surrogate: n-Nonane	*52.3*		*50.0*		*105*	*61-141*			
Matrix Spike Dup (2534088-MSD1)				**Source: E508227-01**					Prepared: 08/21/25 Analyzed: 08/21/25
Diesel Range Organics (C10-C28)	349	25.0	250	ND	140	56-156	6.35	20	
Surrogate: n-Nonane	*59.0*		*50.0*		*118*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/27/2025 8:52:39AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2534101-BLK1)									Prepared: 08/21/25 Analyzed: 08/21/25
Chloride	ND	20.0							
LCS (2534101-BS1)									Prepared: 08/21/25 Analyzed: 08/21/25
Chloride	257	20.0	250		103	90-110			
Matrix Spike (2534101-MS1)				**Source: E508222-03**					Prepared: 08/21/25 Analyzed: 08/21/25
Chloride	443	20.0	250	202	96.1	80-120			
Matrix Spike Dup (2534101-MSD1)				**Source: E508222-03**					Prepared: 08/21/25 Analyzed: 08/21/25
Chloride	453	20.0	250	202	100	80-120	2.31	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/27/25 08:52

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 216585226

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508229	Job Number 01058-0007	1D 2D 3D Std: x	NM x, CO, UT, TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information							Analysis and Method										EPA Program		
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		SDWA	CWA	RCRA
																		Compliance	Y or N	
																		PWSID #		
1017	8-19-25	S	1	BH17-11'		1									X			2.4	Sample Temp	Remarks
1058				BH17-13'		2												2.0		
1141				BH17-15'		3												3.2		
1339				BH17-17'		4												3.4		
1339				SS01-0'		5												2.6		
1344				SS03-0'		6												2.6		
1455				SS13-0'		7												3.0		
1408				BH15-1'		8												3.2		
1416				BH15-3'		9												3.1		

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/20/25	900	Michelle Gonzalez	8.20.25	0900
[signature]	8.20.25	1245	Marissa Gonzales	8.20.25	1245
Marissa Gonzales	8-20-25	1615	Andrew Musso	8.20.25	1615
Andrew Musso	8.20.25	2045	Caitlin Mars	8.21.25	730
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/21/2025 9:30:54AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/21/25 07:30	Work Order ID:	E508229
Phone:	(505) 382-1211	Date Logged In:	08/20/25 14:46	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	08/27/25 07:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E508261
Job Number:	01058-0007
Received:	8/22/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
8/29/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 8/29/25

Ashley Giovengo
6488 7 Rivers Hwy
Artesia, NM 88210

Project Name: Jones Federal B 3 Battery
Workorder: E508261
Date Received: 8/22/2025 3:50:00PM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 8/22/2025 3:50:00PM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

BH05-1’ 6

BH05-3’ 7

BH06-2’ 8

BH06-3.5’ 9

BH07-0’ 10

BH07-1’ 11

BH07-2.5’ 12

BH08-0’ 13

BH08-1’ 14

BH08-2.5’ 15

BH09-0’ 16

BH09-2’ 17

BH09-4’ 18

BH18-0’ 19

BH18-1’ 20

BH19-0’ 21

BH19-2’ 22

BH19-4’ 23

BH20-0’ 24

BH20-2’ 25

Table of Contents (continued)

BH20-4’ 26

BH21-0’ 27

BH21-2’ 28

BH21-4’ 29

QC Summary Data 30

QC - Volatile Organics by EPA 8021B 30

QC - Nonhalogenated Organics by EPA 8015D - GRO 32

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 34

QC - Anions by EPA 300.0/9056A 36

Definitions and Notes 38

Chain of Custody etc. 39

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/29/25 11:58

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH05-1'	E508261-01A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH05-3'	E508261-02A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH06-2'	E508261-03A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH06-3.5'	E508261-04A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH07-0'	E508261-05A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH07-1'	E508261-06A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH07-2.5'	E508261-07A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH08-0'	E508261-08A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH08-1'	E508261-09A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH08-2.5'	E508261-10A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH09-0'	E508261-11A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH09-2'	E508261-12A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH09-4'	E508261-13A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH18-0'	E508261-14A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH18-1'	E508261-15A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH19-0'	E508261-16A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH19-2'	E508261-17A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH19-4'	E508261-18A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH20-0'	E508261-19A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH20-2'	E508261-20A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH20-4'	E508261-21A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH21-0'	E508261-22A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH21-2'	E508261-23A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.
BH21-4'	E508261-24A	Soil	08/21/25	08/22/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH05-1'

E508261-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.5 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**666**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**909**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH05-3'

E508261-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.4 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**257**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**351**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*111 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**55.7**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH06-2'

E508261-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.3 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**116**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**163**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**538**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH06-3.5'

E508261-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.5 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**1470**	250	10	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**1740**	500	10	08/25/25	08/26/25	
Surrogate: n-Nonane		*104 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**818**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH07-0'

E508261-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	**0.0944**	0.0250	1	08/25/25	08/26/25	
Toluene	**0.0565**	0.0250	1	08/25/25	08/26/25	
o-Xylene	**0.334**	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	**0.393**	0.0500	1	08/25/25	08/26/25	
Total Xylenes	**0.727**	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.6 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	**28.8**	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.0 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**524**	50.0	2	08/25/25	08/29/25	
Oil Range Organics (C28-C36)	**285**	100	2	08/25/25	08/29/25	
Surrogate: n-Nonane		*97.0 %*	*61-141*	*08/25/25*	*08/29/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**68.6**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH07-1'

E508261-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.8 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**49.8**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**78.2**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*90.5 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**178**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH07-2.5'

E508261-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.3 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.3 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**199**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**171**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**901**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH08-0'

E508261-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**60.5**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**71.7**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*94.1 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**47.9**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH08-1'

E508261-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*82.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**1660**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**1540**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**594**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH08-2.5'

E508261-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.6 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.9 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**230**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**309**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*114 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**2920**	40.0	2	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH09-0'

E508261-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*84.1 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**94.6**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**216**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH09-2'

E508261-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*83.8 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**41.3**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**107**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*93.7 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH09-4'

E508261-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*85.6 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**107**	25.0	1	08/25/25	08/27/25	
Oil Range Organics (C28-C36)	**156**	50.0	1	08/25/25	08/27/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*08/25/25*	*08/27/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**72.4**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH18-0'

E508261-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*85.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**55.8**	25.0	1	08/25/25	08/27/25	
Oil Range Organics (C28-C36)	**71.4**	50.0	1	08/25/25	08/27/25	
Surrogate: n-Nonane		*92.8 %*	*61-141*	*08/25/25*	*08/27/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH18-1'

E508261-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.8 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.7 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	ND	25.0	1	08/25/25	08/27/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/25/25	08/27/25	
Surrogate: n-Nonane		*88.6 %*	*61-141*	*08/25/25*	*08/27/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH19-0'

E508261-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*87.1 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.4 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**956**	25.0	1	08/25/25	08/27/25	
Oil Range Organics (C28-C36)	**1380**	50.0	1	08/25/25	08/27/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/25/25*	*08/27/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**50.0**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH19-2'

E508261-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.1 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.2 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**166**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**213**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*109 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH19-4'

E508261-18

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*89.4 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.1 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**105**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**184**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*91.1 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH20-0'

E508261-19

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*89.1 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.3 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	**31.9**	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	**94.4**	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*90.5 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	ND	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH20-2'

E508261-20

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Benzene	ND	0.0250	1	08/25/25	08/26/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/26/25	
Toluene	ND	0.0250	1	08/25/25	08/26/25	
o-Xylene	ND	0.0250	1	08/25/25	08/26/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/26/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/26/25	
Surrogate: 4-Bromochlorobenzene-PID		*89.0 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535012
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/26/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.5 %*	*70-130*	*08/25/25*	*08/26/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2535014
Diesel Range Organics (C10-C28)	ND	25.0	1	08/25/25	08/28/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/25/25	08/28/25	
Surrogate: n-Nonane		*91.4 %*	*61-141*	*08/25/25*	*08/28/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535016
Chloride	**731**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH20-4'

E508261-21

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Benzene	ND	0.0250	1	08/25/25	08/25/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/25/25	
Toluene	ND	0.0250	1	08/25/25	08/25/25	
o-Xylene	ND	0.0250	1	08/25/25	08/25/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/25/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/25/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.4 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/25/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.0 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2535010
Diesel Range Organics (C10-C28)	ND	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*101 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535015
Chloride	**2220**	40.0	2	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH21-0'

E508261-22

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Benzene	ND	0.0250	1	08/25/25	08/25/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/25/25	
Toluene	ND	0.0250	1	08/25/25	08/25/25	
o-Xylene	ND	0.0250	1	08/25/25	08/25/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/25/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/25/25	
Surrogate: 4-Bromochlorobenzene-PID		*90.1 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/25/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.7 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2535010
Diesel Range Organics (C10-C28)	**54.7**	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	**64.6**	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*99.9 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535015
Chloride	**328**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH21-2'

E508261-23

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Benzene	ND	0.0250	1	08/25/25	08/25/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/25/25	
Toluene	ND	0.0250	1	08/25/25	08/25/25	
o-Xylene	ND	0.0250	1	08/25/25	08/25/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/25/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/25/25	
Surrogate: 4-Bromochlorobenzene-PID		*90.3 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/25/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.3 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2535010
Diesel Range Organics (C10-C28)	ND	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535015
Chloride	**126**	20.0	1	08/25/25	08/25/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

BH21-4'

E508261-24

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Benzene	ND	0.0250	1	08/25/25	08/25/25	
Ethylbenzene	ND	0.0250	1	08/25/25	08/25/25	
Toluene	ND	0.0250	1	08/25/25	08/25/25	
o-Xylene	ND	0.0250	1	08/25/25	08/25/25	
p,m-Xylene	ND	0.0500	1	08/25/25	08/25/25	
Total Xylenes	ND	0.0250	1	08/25/25	08/25/25	
Surrogate: 4-Bromochlorobenzene-PID		*88.8 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2535007
Gasoline Range Organics (C6-C10)	ND	20.0	1	08/25/25	08/25/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.3 %*	*70-130*	*08/25/25*	*08/25/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2535010
Diesel Range Organics (C10-C28)	ND	25.0	1	08/25/25	08/26/25	
Oil Range Organics (C28-C36)	ND	50.0	1	08/25/25	08/26/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*08/25/25*	*08/26/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2535015
Chloride	**551**	20.0	1	08/25/25	08/25/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535007-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*6.48*		*8.00*		*81.0*	*70-130*			
LCS (2535007-BS1)									Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	4.95	0.0250	5.00		99.0	70-130			
Ethylbenzene	4.88	0.0250	5.00		97.5	70-130			
Toluene	4.93	0.0250	5.00		98.7	70-130			
o-Xylene	4.84	0.0250	5.00		96.7	70-130			
p,m-Xylene	9.88	0.0500	10.0		98.8	70-130			
Total Xylenes	14.7	0.0250	15.0		98.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.91*		*8.00*		*86.4*	*70-130*			
Matrix Spike (2535007-MS1)				**Source: E508259-06**					Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	4.81	0.0250	5.00	ND	96.2	70-130			
Ethylbenzene	4.67	0.0250	5.00	ND	93.3	70-130			
Toluene	4.77	0.0250	5.00	ND	95.4	70-130			
o-Xylene	4.67	0.0250	5.00	ND	93.5	70-130			
p,m-Xylene	9.48	0.0500	10.0	ND	94.8	70-130			
Total Xylenes	14.2	0.0250	15.0	ND	94.4	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.96*		*8.00*		*87.1*	*70-130*			
Matrix Spike Dup (2535007-MSD1)				**Source: E508259-06**					Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	5.48	0.0250	5.00	ND	110	70-130	13.0	27	
Ethylbenzene	5.34	0.0250	5.00	ND	107	70-130	13.4	26	
Toluene	5.43	0.0250	5.00	ND	109	70-130	13.0	20	
o-Xylene	5.28	0.0250	5.00	ND	106	70-130	12.1	25	
p,m-Xylene	10.8	0.0500	10.0	ND	108	70-130	12.9	23	
Total Xylenes	16.1	0.0250	15.0	ND	107	70-130	12.7	26	
Surrogate: 4-Bromochlorobenzene-PID	*6.97*		*8.00*		*87.2*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535012-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.04*		*8.00*		*88.0*	*70-130*			
LCS (2535012-BS1)									Prepared: 08/25/25 Analyzed: 08/25/25
Benzene	4.11	0.0250	5.00		82.1	70-130			
Ethylbenzene	3.98	0.0250	5.00		79.6	70-130			
Toluene	4.08	0.0250	5.00		81.7	70-130			
o-Xylene	4.10	0.0250	5.00		81.9	70-130			
p,m-Xylene	8.13	0.0500	10.0		81.3	70-130			
Total Xylenes	12.2	0.0250	15.0		81.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.09*		*8.00*		*88.7*	*70-130*			
Matrix Spike (2535012-MS1)				**Source: E508261-01**					Prepared: 08/25/25 Analyzed: 08/26/25
Benzene	5.25	0.0250	5.00	ND	105	70-130			
Ethylbenzene	5.13	0.0250	5.00	ND	103	70-130			
Toluene	5.23	0.0250	5.00	ND	105	70-130			
o-Xylene	5.09	0.0250	5.00	ND	102	70-130			
p,m-Xylene	10.4	0.0500	10.0	ND	104	70-130			
Total Xylenes	15.4	0.0250	15.0	ND	103	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*6.91*		*8.00*		*86.3*	*70-130*			
Matrix Spike Dup (2535012-MSD1)				**Source: E508261-01**					Prepared: 08/25/25 Analyzed: 08/26/25
Benzene	5.39	0.0250	5.00	ND	108	70-130	2.64	27	
Ethylbenzene	5.26	0.0250	5.00	ND	105	70-130	2.54	26	
Toluene	5.36	0.0250	5.00	ND	107	70-130	2.45	20	
o-Xylene	5.23	0.0250	5.00	ND	105	70-130	2.66	25	
p,m-Xylene	10.6	0.0500	10.0	ND	106	70-130	2.62	23	
Total Xylenes	15.9	0.0250	15.0	ND	106	70-130	2.63	26	
Surrogate: 4-Bromochlorobenzene-PID	*6.90*		*8.00*		*86.2*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535007-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.40*		*8.00*		*92.5*	*70-130*			
LCS (2535007-BS2)									Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	46.2	20.0	50.0		92.4	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.49*		*8.00*		*93.7*	*70-130*			
Matrix Spike (2535007-MS2)				**Source: E508259-06**					Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	52.5	20.0	50.0	ND	105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.40*		*8.00*		*92.6*	*70-130*			
Matrix Spike Dup (2535007-MSD2)				**Source: E508259-06**					Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	48.6	20.0	50.0	ND	97.3	70-130	7.71	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.49*		*8.00*		*93.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535012-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.40*		*8.00*		*92.6*	*70-130*			
LCS (2535012-BS2)									Prepared: 08/25/25 Analyzed: 08/25/25
Gasoline Range Organics (C6-C10)	37.9	20.0	50.0		75.8	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.52*		*8.00*		*94.1*	*70-130*			
Matrix Spike (2535012-MS2)				**Source: E508261-01**					Prepared: 08/25/25 Analyzed: 08/26/25
Gasoline Range Organics (C6-C10)	48.3	20.0	50.0	ND	96.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.53*		*8.00*		*94.1*	*70-130*			
Matrix Spike Dup (2535012-MSD2)				**Source: E508261-01**					Prepared: 08/25/25 Analyzed: 08/26/25
Gasoline Range Organics (C6-C10)	50.8	20.0	50.0	ND	102	70-130	5.16	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.48*		*8.00*		*93.5*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535010-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*46.7*		*50.0*		*93.4*	*61-141*			
LCS (2535010-BS1)									Prepared: 08/25/25 Analyzed: 08/25/25
Diesel Range Organics (C10-C28)	252	25.0	250		101	66-144			
Surrogate: n-Nonane	*47.5*		*50.0*		*94.9*	*61-141*			
Matrix Spike (2535010-MS1)				**Source: E508260-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Diesel Range Organics (C10-C28)	260	25.0	250	ND	104	56-156			
Surrogate: n-Nonane	*47.6*		*50.0*		*95.2*	*61-141*			
Matrix Spike Dup (2535010-MSD1)				**Source: E508260-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Diesel Range Organics (C10-C28)	267	25.0	250	ND	107	56-156	2.41	20	
Surrogate: n-Nonane	*48.4*		*50.0*		*96.7*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: HM

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535014-BLK1)									Prepared: 08/25/25 Analyzed: 08/26/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*51.8*		*50.0*		*104*	*61-141*			
LCS (2535014-BS1)									Prepared: 08/25/25 Analyzed: 08/26/25
Diesel Range Organics (C10-C28)	241	25.0	250		96.3	66-144			
Surrogate: n-Nonane	*43.6*		*50.0*		*87.2*	*61-141*			
Matrix Spike (2535014-MS1)				**Source: E508261-05**					Prepared: 08/25/25 Analyzed: 08/29/25
Diesel Range Organics (C10-C28)	886	50.0	250	524	145	56-156			
Surrogate: n-Nonane	*48.0*		*50.0*		*96.0*	*61-141*			
Matrix Spike Dup (2535014-MSD1)				**Source: E508261-05**					Prepared: 08/25/25 Analyzed: 08/29/25
Diesel Range Organics (C10-C28)	840	50.0	250	524	126	56-156	5.34	20	
Surrogate: n-Nonane	*48.1*		*50.0*		*96.3*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535015-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	ND	20.0							
LCS (2535015-BS1)									Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	255	20.0	250		102	90-110			
Matrix Spike (2535015-MS1)				**Source: E508260-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	288	20.0	250	28.8	104	80-120			
Matrix Spike Dup (2535015-MSD1)				**Source: E508260-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	288	20.0	250	28.8	104	80-120	0.0240	20	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
6488 7 Rivers Hwy	Project Number:	01058-0007	
Artesia NM, 88210	Project Manager:	Ashley Giovengo	8/29/2025 11:58:28AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2535016-BLK1)									Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	ND	20.0							
LCS (2535016-BS1)									Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	250	20.0	250		99.8	90-110			
Matrix Spike (2535016-MS1)				**Source: E508261-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	1080	20.0	250	818	103	80-120			
Matrix Spike Dup (2535016-MSD1)				**Source: E508261-04**					Prepared: 08/25/25 Analyzed: 08/25/25
Chloride	1050	20.0	250	818	93.9	80-120	2.10	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
6488 7 Rivers Hwy	Project Number:	01058-0007	**Reported:**
Artesia NM, 88210	Project Manager:	Ashley Giovengo	08/29/25 11:58

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508261	Job Number 01058-0007	1D 2D 3D Std: x	NM x CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Samle Temp	Remarks
9:35	8/21/2025	Soil	1	BH05 - 1'		1									x			3.6	
9:40	8/21/2025	Soil	1	BH05 - 3'		2									x			3.4	
9:59	8/21/2025	Soil	1	BH06 - 2'		3									x			3.4	
10:01	8/21/2025	Soil	1	BH06 - 3.5'		4									x			4.0	
10:03	8/21/2025	Soil	1	BH07 - 0'		5									x			3.0	
10:04	8/21/2025	Soil	1	BH07 - 1'		6									x			2.8	
10:08	8/21/2025	Soil	1	BH07 - 2.5'		7									x			2.6	
10:11	8/21/2025	Soil	1	BH08 - 0'		8									x			3.4	
10:13	8/21/2025	Soil	1	BH08 - 1'		9									x			3.6	
10:18	8/21/2025	Soil	1	BH08 - 2.5'		10									x			4.0	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance | Y | or | N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Israel Estrella

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/22/25	7:11	Michelle Gonzales	8.22.25	0711
Michelle Gonzales	8-22-25	1215	Marissa Gonzales	8-22-25	1215
Marissa Gonzales	8-22-25	1550	[signature]	8-22-25	1550
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only

Received on ice: (Y) N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508261	Job Number 01058-0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Samle Temp	Remarks
10:21	8/21/2025	Soil	1	BH09 - 0'		11									x			4.2	
10:25	8/21/2025	Soil	1	BH09 - 2'		12									x			4.0	
10:28	8/21/2025	Soil	1	BH09 - 4'		13									x			4.0	
12:52	8/21/2025	Soil	1	BH18 - 0'		14									x			3.6	
12:54	8/21/2025	Soil	1	BH18 - 1'		15									x			3.0	
13:00	8/21/2025	Soil	1	BH19 - 0'		16									x			3.4	
13:03	8/21/2025	Soil	1	BH19 - 2'		17									x			3.0	
13:07	8/21/2025	Soil	1	BH19 - 4'		18									x			3.6	
13:10	8/21/2025	Soil	1	BH20 - 0'		19									x			3.2	
13:14	8/21/2025	Soil	1	BH20 - 2'		20									x			3.0	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Israel Estrella

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	8/22/25	7:11	Michelle Gonzales	0711	8-22-25
Michelle Gonzales	8-22-25	1215	Marissa Gonzales	8-22-25	1215
Marissa Gonzales	8-22-25	1550	[signature]	8-22-25	1550
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E508261	Job Number 01058-0001	1D 2D 3D Std: x	NM: x CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
13:18	8/21/2025	Soil	1	BH20 - 4'		21									x			3.8	
13:23	8/21/2025	Soil	1	BH21 - 0'		22									x			4.0	
13:29	8/21/2025	Soil	1	BH21 - 2'		23									x			3.6	
13:36	8/21/2025	Soil	1	BH21 - 4'		24									x			3.2	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Israel Estrella

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	8/22/25	7:11	Michelle Gonzales	82225	0711
Michelle Gonzales	8-22-25	1215	Marissa Gonzales	8-22-25	1215
Marissa Gonzales	8-22-25	1556		8-22-25	1550

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 8/25/2025 9:31:30AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	08/22/25 15:50	Work Order ID:	E508261
Phone:	(505) 382-1211	Date Logged In:	08/22/25 15:37	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	08/29/25 07:00 (5 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E510362
Job Number:	01058-0007
Received:	10/30/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
11/4/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 11/4/25

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E510362
Date Received: 10/30/2025 6:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 10/30/2025 6:15:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- BH06-4’ 5
- BH06-7’ 6
- BH06-9’ 7
- BH06-12’ 8
- BH06-16’ 9

QC Summary Data 10

- QC - Volatile Organics by EPA 8021B 10
- QC - Nonhalogenated Organics by EPA 8015D - GRO 11
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 12
- QC - Anions by EPA 300.0/9056A 13

Definitions and Notes 14

Chain of Custody etc. 15

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/04/25 16:41

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH06-4'	E510362-01A	Soil	10/28/25	10/30/25	Glass Jar, 2 oz.
BH06-7'	E510362-02A	Soil	10/28/25	10/30/25	Glass Jar, 2 oz.
BH06-9'	E510362-03A	Soil	10/28/25	10/30/25	Glass Jar, 2 oz.
BH06-12'	E510362-04A	Soil	10/28/25	10/30/25	Glass Jar, 2 oz.
BH06-16'	E510362-05A	Soil	10/28/25	10/30/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

BH06-4'

E510362-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Benzene	ND	0.0250	1	10/30/25	10/31/25	
Ethylbenzene	ND	0.0250	1	10/30/25	10/31/25	
Toluene	ND	0.0250	1	10/30/25	10/31/25	
o-Xylene	ND	0.0250	1	10/30/25	10/31/25	
p,m-Xylene	ND	0.0500	1	10/30/25	10/31/25	
Total Xylenes	ND	0.0250	1	10/30/25	10/31/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.0 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Gasoline Range Organics (C6-C10)	ND	20.0	1	10/30/25	10/31/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.0 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2544128
Diesel Range Organics (C10-C28)	**2790**	25.0	1	10/30/25	10/31/25	
Oil Range Organics (C28-C36)	**2040**	50.0	1	10/30/25	10/31/25	
Surrogate: n-Nonane		*94.6 %*	*61-141*	*10/30/25*	*10/31/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2544155
Chloride	**551**	20.0	1	10/31/25	10/31/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

BH06-7'

E510362-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Benzene	ND	0.0250	1	10/30/25	10/31/25	
Ethylbenzene	ND	0.0250	1	10/30/25	10/31/25	
Toluene	ND	0.0250	1	10/30/25	10/31/25	
o-Xylene	ND	0.0250	1	10/30/25	10/31/25	
p,m-Xylene	ND	0.0500	1	10/30/25	10/31/25	
Total Xylenes	ND	0.0250	1	10/30/25	10/31/25	
Surrogate: 4-Bromochlorobenzene-PID		*92.6 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Gasoline Range Organics (C6-C10)	ND	20.0	1	10/30/25	10/31/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.0 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2544128
Diesel Range Organics (C10-C28)	**271**	25.0	1	10/30/25	10/31/25	
Oil Range Organics (C28-C36)	**280**	50.0	1	10/30/25	10/31/25	
Surrogate: n-Nonane		*95.3 %*	*61-141*	*10/30/25*	*10/31/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2544155
Chloride	**692**	20.0	1	10/31/25	10/31/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

BH06-9'

E510362-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Benzene	ND	0.0250	1	10/30/25	10/31/25	
Ethylbenzene	ND	0.0250	1	10/30/25	10/31/25	
Toluene	ND	0.0250	1	10/30/25	10/31/25	
o-Xylene	ND	0.0250	1	10/30/25	10/31/25	
p,m-Xylene	ND	0.0500	1	10/30/25	10/31/25	
Total Xylenes	ND	0.0250	1	10/30/25	10/31/25	
Surrogate: 4-Bromochlorobenzene-PID		*92.0 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Gasoline Range Organics (C6-C10)	ND	20.0	1	10/30/25	10/31/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.0 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2544128
Diesel Range Organics (C10-C28)	ND	25.0	1	10/30/25	10/31/25	
Oil Range Organics (C28-C36)	ND	50.0	1	10/30/25	10/31/25	
Surrogate: n-Nonane		*91.8 %*	*61-141*	*10/30/25*	*10/31/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2544155
Chloride	**483**	20.0	1	10/31/25	10/31/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

BH06-12'

E510362-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Benzene	ND	0.0250	1	10/30/25	10/31/25	
Ethylbenzene	ND	0.0250	1	10/30/25	10/31/25	
Toluene	ND	0.0250	1	10/30/25	10/31/25	
o-Xylene	ND	0.0250	1	10/30/25	10/31/25	
p,m-Xylene	ND	0.0500	1	10/30/25	10/31/25	
Total Xylenes	ND	0.0250	1	10/30/25	10/31/25	
Surrogate: 4-Bromochlorobenzene-PID		*94.9 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Gasoline Range Organics (C6-C10)	ND	20.0	1	10/30/25	10/31/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.5 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2544128
Diesel Range Organics (C10-C28)	ND	25.0	1	10/30/25	10/31/25	
Oil Range Organics (C28-C36)	ND	50.0	1	10/30/25	10/31/25	
Surrogate: n-Nonane		*91.3 %*	*61-141*	*10/30/25*	*10/31/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2544155
Chloride	**874**	20.0	1	10/31/25	10/31/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

BH06-16'

E510362-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Benzene	ND	0.0250	1	10/30/25	10/31/25	
Ethylbenzene	ND	0.0250	1	10/30/25	10/31/25	
Toluene	ND	0.0250	1	10/30/25	10/31/25	
o-Xylene	ND	0.0250	1	10/30/25	10/31/25	
p,m-Xylene	ND	0.0500	1	10/30/25	10/31/25	
Total Xylenes	ND	0.0250	1	10/30/25	10/31/25	
Surrogate: 4-Bromochlorobenzene-PID		*92.7 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2544109
Gasoline Range Organics (C6-C10)	ND	20.0	1	10/30/25	10/31/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*86.9 %*	*70-130*	*10/30/25*	*10/31/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2544128
Diesel Range Organics (C10-C28)	ND	25.0	1	10/30/25	10/31/25	
Oil Range Organics (C28-C36)	ND	50.0	1	10/30/25	10/31/25	
Surrogate: n-Nonane		*89.9 %*	*61-141*	*10/30/25*	*10/31/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2544155
Chloride	**474**	20.0	1	10/31/25	10/31/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2544109-BLK1)									Prepared: 10/30/25 Analyzed: 10/30/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.45*		*8.00*		*93.1*	*70-130*			
LCS (2544109-BS1)									Prepared: 10/30/25 Analyzed: 10/30/25
Benzene	5.15	0.0250	5.00		103	70-130			
Ethylbenzene	4.82	0.0250	5.00		96.3	70-130			
Toluene	5.01	0.0250	5.00		100	70-130			
o-Xylene	4.90	0.0250	5.00		98.0	70-130			
p,m-Xylene	9.80	0.0500	10.0		98.0	70-130			
Total Xylenes	14.7	0.0250	15.0		98.0	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.53*		*8.00*		*94.2*	*70-130*			
Matrix Spike (2544109-MS1)				**Source: E510359-04**					Prepared: 10/30/25 Analyzed: 10/30/25
Benzene	4.94	0.0250	5.00	ND	98.8	70-130			
Ethylbenzene	4.60	0.0250	5.00	ND	91.9	70-130			
Toluene	4.80	0.0250	5.00	ND	95.9	70-130			
o-Xylene	4.69	0.0250	5.00	ND	93.8	70-130			
p,m-Xylene	9.37	0.0500	10.0	ND	93.7	70-130			
Total Xylenes	14.1	0.0250	15.0	ND	93.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.36*		*8.00*		*92.1*	*70-130*			
Matrix Spike Dup (2544109-MSD1)				**Source: E510359-04**					Prepared: 10/30/25 Analyzed: 10/30/25
Benzene	5.22	0.0250	5.00	ND	104	70-130	5.63	27	
Ethylbenzene	4.89	0.0250	5.00	ND	97.8	70-130	6.16	26	
Toluene	5.08	0.0250	5.00	ND	102	70-130	5.70	20	
o-Xylene	4.98	0.0250	5.00	ND	99.5	70-130	5.94	25	
p,m-Xylene	9.95	0.0500	10.0	ND	99.5	70-130	5.99	23	
Total Xylenes	14.9	0.0250	15.0	ND	99.5	70-130	5.98	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.31*		*8.00*		*91.4*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2544109-BLK1)									Prepared: 10/30/25 Analyzed: 10/30/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.21*		*8.00*		*90.1*	*70-130*			
LCS (2544109-BS2)									Prepared: 10/30/25 Analyzed: 10/30/25
Gasoline Range Organics (C6-C10)	49.8	20.0	50.0		99.5	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.00*		*8.00*		*87.5*	*70-130*			
Matrix Spike (2544109-MS2)				**Source: E510359-04**					Prepared: 10/30/25 Analyzed: 10/30/25
Gasoline Range Organics (C6-C10)	49.4	20.0	50.0	ND	98.8	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.94*		*8.00*		*86.7*	*70-130*			
Matrix Spike Dup (2544109-MSD2)				**Source: E510359-04**					Prepared: 10/30/25 Analyzed: 10/30/25
Gasoline Range Organics (C6-C10)	49.2	20.0	50.0	ND	98.3	70-130	0.493	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.17*		*8.00*		*89.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2544128-BLK1)									Prepared: 10/30/25 Analyzed: 10/31/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*47.0*		*50.0*		*93.9*	*61-141*			
LCS (2544128-BS1)									Prepared: 10/30/25 Analyzed: 10/31/25
Diesel Range Organics (C10-C28)	248	25.0	250		99.2	66-144			
Surrogate: n-Nonane	*46.0*		*50.0*		*92.1*	*61-141*			
Matrix Spike (2544128-MS1)				**Source: E510347-22**					Prepared: 10/30/25 Analyzed: 10/31/25
Diesel Range Organics (C10-C28)	264	25.0	250	ND	106	56-156			
Surrogate: n-Nonane	*46.9*		*50.0*		*93.7*	*61-141*			
Matrix Spike Dup (2544128-MSD1)				**Source: E510347-22**					Prepared: 10/30/25 Analyzed: 10/31/25
Diesel Range Organics (C10-C28)	247	25.0	250	ND	99.0	56-156	6.62	20	
Surrogate: n-Nonane	*45.2*		*50.0*		*90.5*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/4/2025 4:41:43PM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2544155-BLK1)									Prepared: 10/31/25 Analyzed: 10/31/25
Chloride	ND	20.0							
LCS (2544155-BS1)									Prepared: 10/31/25 Analyzed: 10/31/25
Chloride	252	20.0	250		101	90-110			
Matrix Spike (2544155-MS1)				**Source: E510362-04**					Prepared: 10/31/25 Analyzed: 10/31/25
Chloride	1160	20.0	250	874	113	80-120			
Matrix Spike Dup (2544155-MSD1)				**Source: E510362-04**					Prepared: 10/31/25 Analyzed: 11/04/25
Chloride	1190	20.0	250	874	126	80-120	2.77	20	M2

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/04/25 16:41

M2	Matrix spike recovery was outside quality control limits. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E5108102 / Job Number 01058-0007	1D 2D 3D Std: x	NM: x; CO UT TX
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
1213	10/28/25	S	1	BH06 - 4'		1									x			3.7	
1215	"	"	"	BH06 - 7'		2									"			3.1	
1216	"	"	"	BH06 - 9'		3									"			3.0	
1252	"	"	"	BH06 - 12'		4									"			2.6	
1303	"	"	"	BH06 - 16'		5									"			2.9	

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	10/29/25	900	Michelle Gonzales	10-29-25	0900
Michelle Gonzales	10-29-25	1430	Marissa Gonzales	10-29-25	1430
Marissa Gonzales	10-29-25	2015	Andrew Musso	10-29-25	2015
Andrew Musso	10-30-25	0100	[signature]	10-30-25	0615
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____ Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 10/30/2025 9:31:55AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	10/30/25 06:15	Work Order ID:	E510362
Phone:	(505) 382-1211	Date Logged In:	10/29/25 15:48	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	11/05/25 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E510380
Job Number:	01058-0007
Received:	11/3/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
11/5/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 11/5/25

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E510380
Date Received: 11/3/2025 7:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 11/3/2025 7:00:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

- BH16-8’ 6
- BH16-10’ 7
- BH16-14’ 8
- BH16-20’ 9
- BH16-24’ 10
- BH16-30’ 11
- BH16-35’ 12
- BH16-40’ 13
- BH16-45’ 14
- BH16-50’ 15
- BH03-8’ 16
- BH03-10’ 17
- BH03-14’ 18
- BH03-16’ 19

QC Summary Data 20

- QC - Volatile Organics by EPA 8021B 20
- QC - Nonhalogenated Organics by EPA 8015D - GRO 21
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 22
- QC - Anions by EPA 300.0/9056A 23

Definitions and Notes 24

Table of Contents (continued)

Chain of Custody etc. 25

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/05/25 16:54

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BH16-8'	E510380-01A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-10'	E510380-02A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-14'	E510380-03A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-20'	E510380-04A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-24'	E510380-05A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-30'	E510380-06A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-35'	E510380-07A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-40'	E510380-08A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-45'	E510380-09A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH16-50'	E510380-10A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH03-8'	E510380-11A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH03-10'	E510380-12A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH03-14'	E510380-13A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.
BH03-16'	E510380-14A	Soil	10/29/25	11/03/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-8'

E510380-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*106 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/03/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/03/25	
Surrogate: n-Nonane		*98.5 %*	*61-141*	*11/03/25*	*11/03/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**4520**	40.0	2	11/03/25	11/03/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-10'

E510380-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*105 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/03/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/03/25	
Surrogate: n-Nonane		*97.9 %*	*61-141*	*11/03/25*	*11/03/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**1140**	20.0	1	11/03/25	11/03/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-14'

E510380-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*97.8 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**4400**	40.0	2	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-20'

E510380-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*106 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*95.7 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**1380**	20.0	1	11/03/25	11/03/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-24'

E510380-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*106 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*95.5 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**756**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-30'

E510380-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*98.9 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**2470**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-35'

E510380-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*106 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*102 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**1560**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-40'

E510380-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/04/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/04/25	
Toluene	ND	0.0250	1	11/03/25	11/04/25	
o-Xylene	ND	0.0250	1	11/03/25	11/04/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/04/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/04/25	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/04/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*11/03/25*	*11/04/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*100 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**1260**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-45'

E510380-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	ND	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/05/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*98.3 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**693**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH16-50'

E510380-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	ND	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/05/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*112 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*97.9 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**447**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH03-8'

E510380-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	ND	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/05/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*109 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	**229**	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	**164**	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*99.6 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**22.0**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH03-10'

E510380-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	**0.0892**	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	**0.0524**	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	**0.228**	0.0500	1	11/03/25	11/05/25	
Total Xylenes	**0.280**	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*112 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*107 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	**7500**	25.0	1	11/03/25	11/04/25	
Oil Range Organics (C28-C36)	**3330**	50.0	1	11/03/25	11/04/25	
Surrogate: n-Nonane		*99.7 %*	*61-141*	*11/03/25*	*11/04/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	ND	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH03-14'

E510380-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	ND	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/05/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*114 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	**206**	25.0	1	11/03/25	11/05/25	
Oil Range Organics (C28-C36)	**169**	50.0	1	11/03/25	11/05/25	
Surrogate: n-Nonane		*95.0 %*	*61-141*	*11/03/25*	*11/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**58.0**	20.0	1	11/03/25	11/04/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

BH03-16'

E510380-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Benzene	ND	0.0250	1	11/03/25	11/05/25	
Ethylbenzene	ND	0.0250	1	11/03/25	11/05/25	
Toluene	ND	0.0250	1	11/03/25	11/05/25	
o-Xylene	ND	0.0250	1	11/03/25	11/05/25	
p,m-Xylene	ND	0.0500	1	11/03/25	11/05/25	
Total Xylenes	ND	0.0250	1	11/03/25	11/05/25	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2545004
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/03/25	11/05/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*108 %*	*70-130*	*11/03/25*	*11/05/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2545010
Diesel Range Organics (C10-C28)	ND	25.0	1	11/03/25	11/05/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/03/25	11/05/25	
Surrogate: n-Nonane		*95.0 %*	*61-141*	*11/03/25*	*11/05/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2545030
Chloride	**96.0**	20.0	1	11/03/25	11/04/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2545004-BLK1)									Prepared: 11/03/25 Analyzed: 11/04/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.49*		*8.00*		*106*	*70-130*			
LCS (2545004-BS1)									Prepared: 11/03/25 Analyzed: 11/04/25
Benzene	4.24	0.0250	5.00		84.8	70-130			
Ethylbenzene	4.30	0.0250	5.00		85.9	70-130			
Toluene	4.34	0.0250	5.00		86.8	70-130			
o-Xylene	4.35	0.0250	5.00		87.1	70-130			
p,m-Xylene	8.81	0.0500	10.0		88.1	70-130			
Total Xylenes	13.2	0.0250	15.0		87.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.50*		*8.00*		*106*	*70-130*			
Matrix Spike (2545004-MS1)				**Source: E510380-03**					Prepared: 11/03/25 Analyzed: 11/04/25
Benzene	4.76	0.0250	5.00	ND	95.3	70-130			
Ethylbenzene	4.79	0.0250	5.00	ND	95.9	70-130			
Toluene	4.86	0.0250	5.00	ND	97.3	70-130			
o-Xylene	4.87	0.0250	5.00	ND	97.4	70-130			
p,m-Xylene	9.80	0.0500	10.0	ND	98.0	70-130			
Total Xylenes	14.7	0.0250	15.0	ND	97.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.24*		*8.00*		*103*	*70-130*			
Matrix Spike Dup (2545004-MSD1)				**Source: E510380-03**					Prepared: 11/03/25 Analyzed: 11/04/25
Benzene	4.31	0.0250	5.00	ND	86.2	70-130	10.0	27	
Ethylbenzene	4.38	0.0250	5.00	ND	87.7	70-130	8.94	26	
Toluene	4.43	0.0250	5.00	ND	88.5	70-130	9.44	20	
o-Xylene	4.42	0.0250	5.00	ND	88.4	70-130	9.75	25	
p,m-Xylene	8.98	0.0500	10.0	ND	89.8	70-130	8.76	23	
Total Xylenes	13.4	0.0250	15.0	ND	89.3	70-130	9.09	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.24*		*8.00*		*103*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2545004-BLK1)									Prepared: 11/03/25 Analyzed: 11/04/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.73*		*8.00*		*109*	*70-130*			
LCS (2545004-BS2)									Prepared: 11/03/25 Analyzed: 11/04/25
Gasoline Range Organics (C6-C10)	55.4	20.0	50.0		111	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.85*		*8.00*		*111*	*70-130*			
Matrix Spike (2545004-MS2)				**Source: E510380-03**					Prepared: 11/03/25 Analyzed: 11/04/25
Gasoline Range Organics (C6-C10)	52.0	20.0	50.0	ND	104	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.89*		*8.00*		*111*	*70-130*			
Matrix Spike Dup (2545004-MSD2)				**Source: E510380-03**					Prepared: 11/03/25 Analyzed: 11/04/25
Gasoline Range Organics (C6-C10)	55.5	20.0	50.0	ND	111	70-130	6.67	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.87*		*8.00*		*111*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2545010-BLK1)									Prepared: 11/03/25 Analyzed: 11/03/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*51.7*		*50.0*		*103*	*61-141*			
LCS (2545010-BS1)									Prepared: 11/03/25 Analyzed: 11/03/25
Diesel Range Organics (C10-C28)	256	25.0	250		103	66-144			
Surrogate: n-Nonane	*48.7*		*50.0*		*97.3*	*61-141*			
Matrix Spike (2545010-MS1)				**Source: E510379-04**					Prepared: 11/03/25 Analyzed: 11/03/25
Diesel Range Organics (C10-C28)	258	25.0	250	ND	103	56-156			
Surrogate: n-Nonane	*48.3*		*50.0*		*96.6*	*61-141*			
Matrix Spike Dup (2545010-MSD1)				**Source: E510379-04**					Prepared: 11/03/25 Analyzed: 11/03/25
Diesel Range Organics (C10-C28)	247	25.0	250	ND	98.8	56-156	4.36	20	
Surrogate: n-Nonane	*47.9*		*50.0*		*95.8*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/5/2025 4:54:58PM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2545030-BLK1)									Prepared: 11/03/25 Analyzed: 11/03/25
Chloride	ND	20.0							
LCS (2545030-BS1)									Prepared: 11/03/25 Analyzed: 11/03/25
Chloride	258	20.0	250		103	90-110			
Matrix Spike (2545030-MS1)				**Source: E510380-04**					Prepared: 11/03/25 Analyzed: 11/03/25
Chloride	1460	20.0	250	1380	32.8	80-120			M4
Matrix Spike Dup (2545030-MSD1)				**Source: E510380-04**					Prepared: 11/03/25 Analyzed: 11/03/25
Chloride	1490	20.0	250	1380	43.5	80-120	1.83	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/05/25 16:54

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO# 21658526

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E510380	Job Number 21058-0007	1D 2D 3D Std: x	NM CO UT TX: x
Project: Jones Federal B 3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
1206	10/29/25	S	1	BH16 -8'		1									x			2.9	
1207				BH16 - 10'		2												2.6	
1213				BH16 - 14'		3												2.1	
1250				BH16 - 20'		4												3.5	
1305				BH16 - 24'		5												2.9	
1319				BH16 - 30'		6												3.3	
1332				BH16 - 35'		7												3.6	
1341				BH16 - 40'		8												3.3	
1353				BH16 - 45'		9												3.1	
1357				BH16 - 50'		10												3.8	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	10/30/25	900	Michelle Gonzales	10-30-25	0900
Michelle Gonzales	10-30-25	1445	Nathan Gonzales	10-30-25	1445
Nathan Gonzales	10-30-25	1907	Rana Bryan	10/30/25	1907
Rana Bryan	10/31/25	2332	[signature]	11-3-25	0700
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only

Received on ice: (Y) N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

WO # 21658526

Client Information	Invoice Information	Lab Use Only		TAT				State					
Client: Devon	Company: Devon Energy	Lab WO#	Job Number	1D	2D	3D	Std	NM	CO	UT	TX		
Project: Jones Federal B 3 Battery	Address: 5310880	01058-0007					x	x					
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220												
Address: 3122 National Parks Hwy	Phone: (575)689-7597												
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com												
Phone: 575-988-0055	Miscellaneous: Jim Raley												
Email: agiovengo@ensolum.com													

Sample Information							Analysis and Method										EPA Program				
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		SDWA	CWA	RCRA	
																		Compliance	Y	or	N
																		PWSID #			
925	10/29/25	S	1	BH03-8'		11									x			Sample Temp	Remarks		
926	↓	↓	↓	BH03-10'		12									↓			1.3			
933				BH03-14'		13												1.9			
1046				BH03-16'		14												2.1			

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, usantillana@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Uriel Santillana

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	10/30/25	900	Michelle Gonzales	10-30-25	0900
Michelle Gonzales	10-30-25	1445	Nathan Gonzales	10-30-25	1445
Nathan Gonzales	10-30-25	1907		10/30/25	1907
	10/31/25	2338	Noe Sosa	11-3-25	0700
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) N

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 11/3/2025 11:04:23AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	11/03/25 07:00	Work Order ID:	E510380
Phone:	(505) 382-1211	Date Logged In:	10/30/25 16:04	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	11/06/25 17:00 (3 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Comments/Resolution

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E511203
Job Number:	01058-0007
Received:	11/14/2025

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
11/18/25

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 11/18/25

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E511203
Date Received: 11/14/2025 8:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 11/14/2025 8:00:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- SS14-0’ 5
- SS14-1’ 6
- SS15-0’ 7
- SS15-1’ 8
- SS16-0’ 9
- SS16-1’ 10
- SS17-0’ 11
- SS17-1’ 12
- SS18-0’ 13
- SS18-1’ 14

QC Summary Data 15

- QC - Volatile Organics by EPA 8021B 15
- QC - Nonhalogenated Organics by EPA 8015D - GRO 16
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 17
- QC - Anions by EPA 300.0/9056A 18

Definitions and Notes 19

Chain of Custody etc. 20

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/25 16:46

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
SS14-0'	E511203-01A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS14-1'	E511203-02A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS15-0'	E511203-03A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS15-1'	E511203-04A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS16-0'	E511203-05A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS16-1'	E511203-06A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS17-0'	E511203-07A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS17-1'	E511203-08A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS18-0'	E511203-09A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.
SS18-1'	E511203-10A	Soil	11/12/25	11/14/25	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS14-0'

E511203-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*102 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*118 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	**66.1**	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS14-1'

E511203-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.1 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS15-0'

E511203-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*99.8 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.9 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*108 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS15-1'

E511203-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.3 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*103 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	**42.0**	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS16-0'

E511203-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.8 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS16-1'

E511203-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*102 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*106 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS17-0'

E511203-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*96.8 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*105 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*105 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	**27.2**	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS17-1'

E511203-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*98.2 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*104 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*107 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	**39.5**	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS18-0'

E511203-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*101 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*110 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

SS18-1'

E511203-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Benzene	ND	0.0250	1	11/14/25	11/15/25	
Ethylbenzene	ND	0.0250	1	11/14/25	11/15/25	
Toluene	ND	0.0250	1	11/14/25	11/15/25	
o-Xylene	ND	0.0250	1	11/14/25	11/15/25	
p,m-Xylene	ND	0.0500	1	11/14/25	11/15/25	
Total Xylenes	ND	0.0250	1	11/14/25	11/15/25	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2546169
Gasoline Range Organics (C6-C10)	ND	20.0	1	11/14/25	11/15/25	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*102 %*	*70-130*	*11/14/25*	*11/15/25*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: HM			Batch: 2546162
Diesel Range Organics (C10-C28)	ND	25.0	1	11/14/25	11/17/25	
Oil Range Organics (C28-C36)	ND	50.0	1	11/14/25	11/17/25	
Surrogate: n-Nonane		*108 %*	*61-141*	*11/14/25*	*11/17/25*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2546163
Chloride	ND	20.0	1	11/17/25	11/17/25	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2546169-BLK1)									Prepared: 11/14/25 Analyzed: 11/15/25
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.87*		*8.00*		*98.4*	*70-130*			
LCS (2546169-BS1)									Prepared: 11/14/25 Analyzed: 11/15/25
Benzene	4.66	0.0250	5.00		93.1	70-130			
Ethylbenzene	4.42	0.0250	5.00		88.4	70-130			
Toluene	4.59	0.0250	5.00		91.7	70-130			
o-Xylene	4.54	0.0250	5.00		90.8	70-130			
p,m-Xylene	9.08	0.0500	10.0		90.8	70-130			
Total Xylenes	13.6	0.0250	15.0		90.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.21*		*8.00*		*103*	*70-130*			
Matrix Spike (2546169-MS1)				**Source: E511203-06**					Prepared: 11/14/25 Analyzed: 11/15/25
Benzene	5.21	0.0250	5.00	ND	104	70-130			
Ethylbenzene	4.94	0.0250	5.00	ND	98.9	70-130			
Toluene	5.13	0.0250	5.00	ND	103	70-130			
o-Xylene	5.02	0.0250	5.00	ND	100	70-130			
p,m-Xylene	10.1	0.0500	10.0	ND	101	70-130			
Total Xylenes	15.2	0.0250	15.0	ND	101	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.14*		*8.00*		*102*	*70-130*			
Matrix Spike Dup (2546169-MSD1)				**Source: E511203-06**					Prepared: 11/14/25 Analyzed: 11/15/25
Benzene	5.51	0.0250	5.00	ND	110	70-130	5.58	27	
Ethylbenzene	5.26	0.0250	5.00	ND	105	70-130	6.18	26	
Toluene	5.44	0.0250	5.00	ND	109	70-130	5.77	20	
o-Xylene	5.30	0.0250	5.00	ND	106	70-130	5.32	25	
p,m-Xylene	10.8	0.0500	10.0	ND	108	70-130	6.02	23	
Total Xylenes	16.1	0.0250	15.0	ND	107	70-130	5.79	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.16*		*8.00*		*102*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2546169-BLK1)									Prepared: 11/14/25 Analyzed: 11/15/25
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.28*		*8.00*		*104*	*70-130*			
LCS (2546169-BS2)									Prepared: 11/14/25 Analyzed: 11/15/25
Gasoline Range Organics (C6-C10)	46.7	20.0	50.0		93.4	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.35*		*8.00*		*104*	*70-130*			
Matrix Spike (2546169-MS2)				**Source: E511203-06**					Prepared: 11/14/25 Analyzed: 11/15/25
Gasoline Range Organics (C6-C10)	47.1	20.0	50.0	ND	94.2	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.10*		*8.00*		*101*	*70-130*			
Matrix Spike Dup (2546169-MSD2)				**Source: E511203-06**					Prepared: 11/14/25 Analyzed: 11/15/25
Gasoline Range Organics (C6-C10)	50.0	20.0	50.0	ND	100	70-130	5.93	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.04*		*8.00*		*100*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: HM

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2546162-BLK1)									Prepared: 11/14/25 Analyzed: 11/17/25
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*51.4*		*50.0*		*103*	*61-141*			
LCS (2546162-BS1)									Prepared: 11/14/25 Analyzed: 11/17/25
Diesel Range Organics (C10-C28)	254	25.0	250		102	66-144			
Surrogate: n-Nonane	*52.6*		*50.0*		*105*	*61-141*			
Matrix Spike (2546162-MS1)				**Source: E511203-09**					Prepared: 11/14/25 Analyzed: 11/17/25
Diesel Range Organics (C10-C28)	265	25.0	250	ND	106	56-156			
Surrogate: n-Nonane	*53.2*		*50.0*		*106*	*61-141*			
Matrix Spike Dup (2546162-MSD1)				**Source: E511203-09**					Prepared: 11/14/25 Analyzed: 11/17/25
Diesel Range Organics (C10-C28)	267	25.0	250	ND	107	56-156	0.697	20	
Surrogate: n-Nonane	*53.8*		*50.0*		*108*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/2025 4:46:32PM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2546163-BLK1)									Prepared: 11/17/25 Analyzed: 11/17/25
Chloride	ND	20.0							
LCS (2546163-BS1)									Prepared: 11/17/25 Analyzed: 11/17/25
Chloride	254	20.0	250		102	90-110			
Matrix Spike (2546163-MS1)				**Source: E511203-03**					Prepared: 11/17/25 Analyzed: 11/17/25
Chloride	261	20.0	250	ND	105	80-120			
Matrix Spike Dup (2546163-MSD1)				**Source: E511203-03**					Prepared: 11/17/25 Analyzed: 11/17/25
Chloride	262	20.0	250	ND	105	80-120	0.220	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	11/18/25 16:46

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

01058-0007 CM
WO# 216585 26

Client Information	Invoice Information	Lab Use Only		TAT				State				
Client: Devon Energy Production Company	Company: Ensolum LLC	Lab WO#	Job Number	1D	2D	3D	Std	NM	CO	UT	TX	
Project Name: Jones Federal B 3 Battery	Address: 3122 National Parks Hwy	E511203	~~23003-0002~~				X	X				
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220											
Address: 3122 National Parks Hwy	Phone: 575-988-0055											
City, State, Zip: Carlsbad NM, 88220	Email: agiovengo@ensolum.com											
Phone: 575-988-0055	Miscellaneous:											
Email: agiovengo@ensolum.com												

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals		BGDOC - NM	BGDOC - TX		Sample Temp	Remarks
849	11/12/2025	S	1	~~SS01-0'~~ 14-0'		1									X			4.6	
1019	11/12/2025	S	1	~~SS01-1'~~ 14-1'		2									X			4.2	
952	11/12/2025	S	1	~~SS02-0'~~ 15-0'		3									X			4.0	
1021	11/12/2025	S	1	~~SS02-1'~~ 15-1'		4									X			4.0	
848	11/12/2025	S	1	~~SS03-0'~~ 16-0'		5									X			4.8	
1014	11/12/2025	S	1	~~SS03-1'~~ 16-1'		6									X			4.4	
957	11/12/2025	S	1	~~SS04-0'~~ 17-0'		7									X			4.4	
1011	11/12/2025	S	1	~~SS04-1'~~ 17-1'		8									X			4.6	
852	11/12/2025	S	1	~~SS05-0'~~ 18-0'		9									X			5.0	
1024	11/12/2025	S	1	~~SS05-1'~~ 18-1'		10									X			5.0	

EPA Program: SDWA | CWA | RCRA

Compliance: Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, jmccauley@ensolum.com, akone@ensolum.com, jgonzalezz@ensolum.com, jhinkle@ensolum.com, eplugge@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Jarad McCauley

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	11.13.25	800	Marissa Gonzales	11-13-25	0800
Marissa Gonzales	11-13-25	1515	Nathan Gonzales	11-13-25	1515
Nathan Gonzales	11-13-25	1930		11/13/25	1930
	11-13-25	2345	Caitlin Mason	11.14.25	800
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

envirotech
Analytical Laboratory

Chain of Custody

01058.0007 CM
WO# 216585 26

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon Energy Production Company	Company: Ensolum LLC	Lab WO# E511203	1D 2D 3D Std	NM CO UT TX
Project Name: Jones Federal B 3 Battery	Address: 3122 National Parks Hwy	Job Number ~~23003-0002~~	X	X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: 575-988-0055			
City, State, Zip: Carlsbad NM, 88220	Email: agiovengo@ensolum.com			
Phone: 575-988-0055	Miscellaneous:			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	TCEQ 1005 - TX	RCRA 8 Metals	BGDOC - NM	BGDOC - TX	Sample Temp	Remarks
849	11/12/2025	S	1	SS01 - 0'		1								X		4.6	
1019	11/12/2025	S	1	SS01 - 1'		2								X		4.2	
952	11/12/2025	S	1	SS02 - 0'		3								X		4.0	
1021	11/12/2025	S	1	SS02 - 1'		4								X		4.0	
848	11/12/2025	S	1	SS03 - 0'		5								X		4.8	
1014	11/12/2025	S	1	SS03 - 1'		6								X		4.4	
957	11/12/2025	S	1	SS04 - 0'		7								X		4.4	
1011	11/12/2025	S	1	SS04 - 1'		8								X		4.6	
852	11/12/2025	S	1	SS05 - 0'		9								X		5.0	
1024	11/12/2025	S	1	SS05 - 1'		10								X		5.0	

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, iestrella@ensolum.com, chamilton@ensolum.com, bmoir@ensolum.com, jmccauley@ensolum.com, akone@ensolum.com, jgonzalezz@ensolum.com, jhinkle@ensolum.com, eplugge@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Jarad McCauley

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	11.13.25	800	Marissa Gonzales	11-13-25	0800
Marissa Gonzales	11-13-25	1515	Nathan Gonzales	11-13-25	1515
Nathan Gonzales	11-13-25	1930		11-13-25	1930
	11-13-25	2345	Caitlin Mars	11.14.25	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed on ice at a temp above 0 but less than 6°C on subsequent days.

Lab Use Only
Received on ice: (Y) / N

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

Envirotech Analytical Laboratory

Printed: 11/14/2025 2:31:25PM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	11/14/25 08:00	Work Order ID:	E511203
Phone:	(505) 382-1211	Date Logged In:	11/14/25 09:05	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	11/20/25 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	No	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes

Sample Cooler

7. Was a sample cooler received?	Yes
8. If yes, was cooler received in good condition?	Yes
9. Was the sample(s) received intact, i.e., not broken?	Yes
10. Were custody/security seals present?	No
11. If yes, were custody/security seals intact?	NA
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.	

Sample Container

14. Are aqueous VOC samples present?	No
15. Are VOC samples collected in VOA Vials?	NA
16. Is the head space less than 6-8 mm (pea sized or less)?	NA
17. Was a trip blank (TB) included for VOC analyses?	NA
18. Are non-VOC samples collected in the correct containers?	Yes
19. Is the appropriate volume/weight or number of sample containers collected?	Yes

Field Label

20. Were field sample labels filled out with the minimum information:	
Sample ID?	Yes
Date/Time Collected?	Yes
Collectors name?	Yes

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No
22. Are sample(s) correctly preserved?	NA
24. Is lab filtration required and/or requested for dissolved metals?	No

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Sample names on containers did not match names on COC. Changed COC to match names on containers per client.

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E601182
Job Number:	01058-0007
Received:	1/21/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
1/26/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 1/26/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E601182
Date Received: 1/21/2026 7:45:19AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 1/21/2026 7:45:19AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

BF01 5

QC Summary Data 6

QC - Volatile Organics by EPA 8021B 6

QC - Nonhalogenated Organics by EPA 8015D - GRO 7

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 8

QC - Anions by EPA 300.0/9056A 9

Definitions and Notes 10

Chain of Custody etc. 11

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	01/26/26 15:51

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BF01	E601182-01A	Soil	01/19/26	01/21/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	1/26/2026 3:51:51PM

BF01

E601182-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2604075
Benzene	ND	0.0250	1	01/21/26	01/23/26	
Ethylbenzene	ND	0.0250	1	01/21/26	01/23/26	
Toluene	ND	0.0250	1	01/21/26	01/23/26	
o-Xylene	ND	0.0250	1	01/21/26	01/23/26	
p,m-Xylene	ND	0.0500	1	01/21/26	01/23/26	
Total Xylenes	ND	0.0250	1	01/21/26	01/23/26	
Surrogate: 4-Bromochlorobenzene-PID		*114 %*	*70-130*	*01/21/26*	*01/23/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2604075
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/21/26	01/23/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.6 %*	*70-130*	*01/21/26*	*01/23/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2604080
Diesel Range Organics (C10-C28)	ND	25.0	1	01/21/26	01/22/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/21/26	01/22/26	
Surrogate: n-Nonane		*94.9 %*	*61-141*	*01/21/26*	*01/22/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2604106
Chloride	ND	20.0	1	01/22/26	01/22/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	1/26/2026 3:51:51PM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2604075-BLK1)									Prepared: 01/21/26 Analyzed: 01/23/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.77*		*8.00*		*110*	*70-130*			
LCS (2604075-BS1)									Prepared: 01/21/26 Analyzed: 01/23/26
Benzene	4.55	0.0250	5.00		91.0	70-130			
Ethylbenzene	4.37	0.0250	5.00		87.5	70-130			
Toluene	4.47	0.0250	5.00		89.4	70-130			
o-Xylene	4.48	0.0250	5.00		89.7	70-130			
p,m-Xylene	8.95	0.0500	10.0		89.5	70-130			
Total Xylenes	13.4	0.0250	15.0		89.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.70*		*8.00*		*109*	*70-130*			
Matrix Spike (2604075-MS1)				**Source: E601184-03**					Prepared: 01/21/26 Analyzed: 01/23/26
Benzene	5.17	0.0250	5.00	ND	103	70-130			
Ethylbenzene	4.97	0.0250	5.00	ND	99.4	70-130			
Toluene	5.07	0.0250	5.00	ND	101	70-130			
o-Xylene	5.08	0.0250	5.00	ND	102	70-130			
p,m-Xylene	10.2	0.0500	10.0	ND	102	70-130			
Total Xylenes	15.2	0.0250	15.0	ND	102	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.80*		*8.00*		*110*	*70-130*			
Matrix Spike Dup (2604075-MSD1)				**Source: E601184-03**					Prepared: 01/21/26 Analyzed: 01/23/26
Benzene	5.26	0.0250	5.00	ND	105	70-130	1.77	27	
Ethylbenzene	5.07	0.0250	5.00	ND	101	70-130	1.96	26	
Toluene	5.17	0.0250	5.00	ND	103	70-130	1.83	20	
o-Xylene	5.19	0.0250	5.00	ND	104	70-130	2.20	25	
p,m-Xylene	10.4	0.0500	10.0	ND	104	70-130	2.02	23	
Total Xylenes	15.5	0.0250	15.0	ND	104	70-130	2.08	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.79*		*8.00*		*110*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	1/26/2026 3:51:51PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2604075-BLK1)									Prepared: 01/21/26 Analyzed: 01/23/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.74*		*8.00*		*84.2*	*70-130*			
LCS (2604075-BS2)									Prepared: 01/21/26 Analyzed: 01/23/26
Gasoline Range Organics (C6-C10)	44.0	20.0	50.0		88.0	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.76*		*8.00*		*84.5*	*70-130*			
Matrix Spike (2604075-MS2)				**Source: E601184-03**					Prepared: 01/21/26 Analyzed: 01/23/26
Gasoline Range Organics (C6-C10)	52.8	20.0	50.0	ND	106	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.80*		*8.00*		*85.0*	*70-130*			
Matrix Spike Dup (2604075-MSD2)				**Source: E601184-03**					Prepared: 01/21/26 Analyzed: 01/23/26
Gasoline Range Organics (C6-C10)	50.6	20.0	50.0	ND	101	70-130	4.23	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*6.75*		*8.00*		*84.4*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	1/26/2026 3:51:51PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2604080-BLK1)									Prepared: 01/21/26 Analyzed: 01/21/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*46.7*		*50.0*		*93.4*	*61-141*			
LCS (2604080-BS1)									Prepared: 01/21/26 Analyzed: 01/21/26
Diesel Range Organics (C10-C28)	255	25.0	250		102	66-144			
Surrogate: n-Nonane	*45.7*		*50.0*		*91.4*	*61-141*			
Matrix Spike (2604080-MS1)				**Source: E601187-02**					Prepared: 01/21/26 Analyzed: 01/21/26
Diesel Range Organics (C10-C28)	269	25.0	250	ND	108	56-156			
Surrogate: n-Nonane	*48.3*		*50.0*		*96.5*	*61-141*			
Matrix Spike Dup (2604080-MSD1)				**Source: E601187-02**					Prepared: 01/21/26 Analyzed: 01/21/26
Diesel Range Organics (C10-C28)	273	25.0	250	ND	109	56-156	1.23	20	
Surrogate: n-Nonane	*49.2*		*50.0*		*98.5*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	1/26/2026 3:51:51PM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2604106-BLK1)									Prepared: 01/22/26 Analyzed: 01/22/26
Chloride	ND	20.0							
LCS (2604106-BS1)									Prepared: 01/22/26 Analyzed: 01/22/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2604106-MS1)				**Source: E601185-06**					Prepared: 01/22/26 Analyzed: 01/22/26
Chloride	354	20.0	250	88.7	106	80-120			
Matrix Spike Dup (2604106-MSD1)				**Source: E601185-06**					Prepared: 01/22/26 Analyzed: 01/22/26
Chloride	355	20.0	250	88.7	106	80-120	0.310	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	01/26/26 15:51

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

WO# 216585 26

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E601182	1D 2D 3D Std	NM CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	Job Number 01058-0007	X	X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
14:15	1/19/2026	S	1	BF01		1						X						3.9

Analysis and Method

EPA Program

SDWA	CWA	RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	1/20/26	7:11	Michelle Gonzales	1-20-26	0711
Michelle Gonzales	1-20-26	1215	Marissa Gonzales	1-20-26	1215
Marissa Gonzales	1-20-26	1600		1-20-26	1600
	1-20-26	1745		1-21-26	745

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 1/21/2026 9:19:52AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	01/21/26 07:45	Work Order ID:	E601182
Phone:	(505) 382-1211	Date Logged In:	01/20/26 15:33	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	01/27/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-CM
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E601264
Job Number:	01058-0007
Received:	1/29/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/2/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/2/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E601264
Date Received: 1/29/2026 6:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 1/29/2026 6:15:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS61-4’ 5
- FS62-4’ 6
- FS63-4’ 7
- FS66-4’ 8
- FS69-4’ 9
- FS72-4’ 10
- FS73-4’ 11
- FS74-4’ 12
- FS88-4’ 13

QC Summary Data 14

- QC - Volatile Organics by EPA 8021B 14
- QC - Nonhalogenated Organics by EPA 8015D - GRO 15
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 16
- QC - Anions by EPA 300.0/9056A 17

Definitions and Notes 18

Chain of Custody etc. 19

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/02/26 13:58

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS61-4'	E601264-01A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS62-4'	E601264-02A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS63-4'	E601264-03A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS66-4'	E601264-04A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS69-4'	E601264-05A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS72-4'	E601264-06A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS73-4'	E601264-07A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS74-4'	E601264-08A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.
FS88-4'	E601264-09A	Soil	01/23/26	01/29/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS61-4'

E601264-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*90.8 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.0 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	**452**	25.0	1	01/29/26	01/29/26	
Oil Range Organics (C28-C36)	**490**	50.0	1	01/29/26	01/29/26	
Surrogate: n-Nonane		*98.5 %*	*61-141*	*01/29/26*	*01/29/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**453**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS62-4'

E601264-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.7 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.3 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	ND	25.0	1	01/29/26	01/29/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/29/26	01/29/26	
Surrogate: n-Nonane		*98.9 %*	*61-141*	*01/29/26*	*01/29/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**221**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS63-4'

E601264-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.9 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.8 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	ND	25.0	1	01/29/26	01/29/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/29/26	01/29/26	
Surrogate: n-Nonane		*98.2 %*	*61-141*	*01/29/26*	*01/29/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**30.2**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS66-4'

E601264-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.9 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.0 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	**494**	25.0	1	01/29/26	01/29/26	
Oil Range Organics (C28-C36)	**441**	50.0	1	01/29/26	01/29/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*01/29/26*	*01/29/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**1010**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS69-4'

E601264-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.1 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.4 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	**651**	25.0	1	01/29/26	01/29/26	
Oil Range Organics (C28-C36)	**709**	50.0	1	01/29/26	01/29/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*01/29/26*	*01/29/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**1890**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS72-4'

E601264-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.6 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.1 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	ND	25.0	1	01/29/26	01/30/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/29/26	01/30/26	
Surrogate: n-Nonane		*96.5 %*	*61-141*	*01/29/26*	*01/30/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**39.6**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS73-4'

E601264-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*91.6 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.4 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	ND	25.0	1	01/29/26	01/30/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/29/26	01/30/26	
Surrogate: n-Nonane		*98.8 %*	*61-141*	*01/29/26*	*01/30/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	ND	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS74-4'

E601264-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*91.2 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.3 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	**32.0**	25.0	1	01/29/26	01/30/26	
Oil Range Organics (C28-C36)	**55.8**	50.0	1	01/29/26	01/30/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*01/29/26*	*01/30/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**1140**	20.0	1	01/29/26	01/29/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

FS88-4'

E601264-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Benzene	ND	0.0250	1	01/29/26	01/31/26	
Ethylbenzene	ND	0.0250	1	01/29/26	01/31/26	
Toluene	ND	0.0250	1	01/29/26	01/31/26	
o-Xylene	ND	0.0250	1	01/29/26	01/31/26	
p,m-Xylene	ND	0.0500	1	01/29/26	01/31/26	
Total Xylenes	ND	0.0250	1	01/29/26	01/31/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.8 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605097
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/29/26	01/31/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.2 %*	*70-130*	*01/29/26*	*01/31/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605094
Diesel Range Organics (C10-C28)	**38.1**	25.0	1	01/29/26	01/30/26	
Oil Range Organics (C28-C36)	**69.0**	50.0	1	01/29/26	01/30/26	
Surrogate: n-Nonane		*97.8 %*	*61-141*	*01/29/26*	*01/30/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2605096
Chloride	**1850**	40.0	2	01/29/26	01/29/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605097-BLK1)									Prepared: 01/29/26 Analyzed: 01/31/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.43*		*8.00*		*92.9*	*70-130*			
LCS (2605097-BS1)									Prepared: 01/29/26 Analyzed: 01/31/26
Benzene	4.21	0.0250	5.00		84.3	70-130			
Ethylbenzene	4.08	0.0250	5.00		81.7	70-130			
Toluene	4.21	0.0250	5.00		84.2	70-130			
o-Xylene	4.18	0.0250	5.00		83.7	70-130			
p,m-Xylene	8.34	0.0500	10.0		83.4	70-130			
Total Xylenes	12.5	0.0250	15.0		83.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.29*		*8.00*		*91.1*	*70-130*			
Matrix Spike (2605097-MS1)				**Source: E601265-05**					Prepared: 01/29/26 Analyzed: 01/31/26
Benzene	4.44	0.0250	5.00	ND	88.8	70-130			
Ethylbenzene	4.32	0.0250	5.00	ND	86.3	70-130			
Toluene	4.44	0.0250	5.00	ND	88.9	70-130			
o-Xylene	4.41	0.0250	5.00	ND	88.1	70-130			
p,m-Xylene	8.81	0.0500	10.0	ND	88.1	70-130			
Total Xylenes	13.2	0.0250	15.0	ND	88.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.36*		*8.00*		*92.0*	*70-130*			
Matrix Spike Dup (2605097-MSD1)				**Source: E601265-05**					Prepared: 01/29/26 Analyzed: 01/31/26
Benzene	4.24	0.0250	5.00	ND	84.9	70-130	4.56	27	
Ethylbenzene	4.14	0.0250	5.00	ND	82.9	70-130	4.07	26	
Toluene	4.26	0.0250	5.00	ND	85.3	70-130	4.17	20	
o-Xylene	4.23	0.0250	5.00	ND	84.6	70-130	4.10	25	
p,m-Xylene	8.48	0.0500	10.0	ND	84.8	70-130	3.80	23	
Total Xylenes	12.7	0.0250	15.0	ND	84.7	70-130	3.90	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.28*		*8.00*		*91.0*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605097-BLK1)									Prepared: 01/29/26 Analyzed: 01/31/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.79*		*8.00*		*97.3*	*70-130*			
LCS (2605097-BS2)									Prepared: 01/29/26 Analyzed: 01/31/26
Gasoline Range Organics (C6-C10)	45.8	20.0	50.0		91.5	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.70*		*8.00*		*96.2*	*70-130*			
Matrix Spike (2605097-MS2)				**Source: E601265-05**					Prepared: 01/29/26 Analyzed: 01/31/26
Gasoline Range Organics (C6-C10)	52.0	20.0	50.0	ND	104	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.93*		*8.00*		*99.2*	*70-130*			
Matrix Spike Dup (2605097-MSD2)				**Source: E601265-05**					Prepared: 01/29/26 Analyzed: 01/31/26
Gasoline Range Organics (C6-C10)	52.4	20.0	50.0	ND	105	70-130	0.729	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.80*		*8.00*		*97.5*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605094-BLK1)									Prepared: 01/29/26 Analyzed: 01/29/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*47.1*		*50.0*		*94.1*	*61-141*			
LCS (2605094-BS1)									Prepared: 01/29/26 Analyzed: 01/29/26
Diesel Range Organics (C10-C28)	247	25.0	250		98.9	66-144			
Surrogate: n-Nonane	*47.4*		*50.0*		*94.8*	*61-141*			
Matrix Spike (2605094-MS1)				**Source: E601264-03**					Prepared: 01/29/26 Analyzed: 01/29/26
Diesel Range Organics (C10-C28)	257	25.0	250	ND	103	56-156			
Surrogate: n-Nonane	*48.8*		*50.0*		*97.6*	*61-141*			
Matrix Spike Dup (2605094-MSD1)				**Source: E601264-03**					Prepared: 01/29/26 Analyzed: 01/29/26
Diesel Range Organics (C10-C28)	254	25.0	250	ND	102	56-156	1.03	20	
Surrogate: n-Nonane	*48.8*		*50.0*		*97.5*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/2/2026 1:58:34PM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605096-BLK1)									Prepared: 01/29/26 Analyzed: 01/29/26
Chloride	ND	20.0							
LCS (2605096-BS1)									Prepared: 01/29/26 Analyzed: 01/29/26
Chloride	251	20.0	250		100	90-110			
Matrix Spike (2605096-MS1)				**Source: E601261-06**					Prepared: 01/29/26 Analyzed: 01/29/26
Chloride	251	20.0	250	ND	100	80-120			
Matrix Spike Dup (2605096-MSD1)				**Source: E601261-06**					Prepared: 01/29/26 Analyzed: 01/29/26
Chloride	251	20.0	250	ND	101	80-120	0.141	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/02/26 13:58

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

WO# 216585 26

Chain of Custody

Client Information	Invoice Information	Lab Use Only		TAT				State				
Client: Devon	Company: Devon Energy	Lab WO#	Job Number	1D	2D	3D	Std	NM	CO	UT	TX	
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	E601264	01058-0007				X	X				
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220											
Address: 3122 National Parks Hwy	Phone: (575)689-7597											
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com											
Phone: 575-988-0055	Miscellaneous: Jim Raley											
Email: agiovengo@ensolum.com												

Sample Information							Analysis and Method										EPA Program			
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				SDWA	CWA	RCRA
8:53	1/23/2026	S	1	FS61-4'		1						X					5.4°	Compliance	Y	or N
8:57	1/23/2026	S	1	FS62-4'		2						X					5.5°	PWSID #		
8:58	1/23/2026	S	1	FS63-4'		3						X					5.1°		Remarks	
8:51	1/23/2026	S	1	FS66-4'		4						X					5.4°			
8:49	1/23/2026	S	1	FS69-4'		5						X					5.1°			
8:46	1/23/2026	S	1	FS72-4'		6						X					5.3°			
9:01	1/23/2026	S	1	FS73-4'		7						X					5.4°			
9:04	1/23/2026	S	1	FS74-4'		8						X					5.6°			
9:06	1/23/2026	S	1	FS88-4'		9						X					5.3°			

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	1/26/26	7:11	Michelle Gonzales	1-26-26	0711
Michelle Gonzales	1-28-26	1400	Marissa Gonzales	1-28-26	1400
Marissa Gonzales	1-28-26	1755	Johnny Urchuleta	1-28-26	1755
Johnny Urchuleta	1-28-26	2140	Noe Sato	1-29-26	0615

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 1/29/2026 7:58:27AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	01/29/26 06:15	Work Order ID:	E601264
Phone:	(505) 382-1211	Date Logged In:	01/28/26 14:27	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/02/26 17:00 (2 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E601278
Job Number:	01058-0007
Received:	1/30/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/4/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/4/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E601278
Date Received: 1/30/2026 8:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 1/30/2026 8:15:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS70-4’ 5
- FS71-4’ 6
- FS86-4’ 7
- FS87-4’ 8
- FS89-4’ 9
- FS90-4’ 10

QC Summary Data 11

- QC - Volatile Organics by EPA 8021B 11
- QC - Nonhalogenated Organics by EPA 8015D - GRO 12
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 13
- QC - Anions by EPA 300.0/9056A 14

Definitions and Notes 15

Chain of Custody etc. 16

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/04/26 16:40

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS70-4'	E601278-01A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.
FS71-4'	E601278-02A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.
FS86-4'	E601278-03A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.
FS87-4'	E601278-04A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.
FS89-4'	E601278-05A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.
FS90-4'	E601278-06A	Soil	01/28/26	01/30/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS70-4'

E601278-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*91.8 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.2 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	**131**	25.0	1	01/30/26	01/30/26	
Oil Range Organics (C28-C36)	**206**	50.0	1	01/30/26	01/30/26	
Surrogate: n-Nonane		*99.6 %*	*61-141*	*01/30/26*	*01/30/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**61.6**	20.0	1	01/30/26	01/30/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS71-4'

E601278-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.1 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.6 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	ND	25.0	1	01/30/26	01/31/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/30/26	01/31/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*01/30/26*	*01/31/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**111**	20.0	1	01/30/26	01/30/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS86-4'

E601278-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.1 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.9 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	ND	25.0	1	01/30/26	01/31/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/30/26	01/31/26	
Surrogate: n-Nonane		*99.2 %*	*61-141*	*01/30/26*	*01/31/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**998**	20.0	1	01/30/26	01/30/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS87-4'

E601278-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.5 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*94.9 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	**44.9**	25.0	1	01/30/26	01/31/26	
Oil Range Organics (C28-C36)	**67.0**	50.0	1	01/30/26	01/31/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*01/30/26*	*01/31/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**86.9**	20.0	1	01/30/26	01/30/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS89-4'

E601278-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.7 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.4 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	**30.9**	25.0	1	01/30/26	01/31/26	
Oil Range Organics (C28-C36)	ND	50.0	1	01/30/26	01/31/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*01/30/26*	*01/31/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**1580**	20.0	1	01/30/26	01/30/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

FS90-4'

E601278-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Benzene	ND	0.0250	1	01/30/26	02/01/26	
Ethylbenzene	ND	0.0250	1	01/30/26	02/01/26	
Toluene	ND	0.0250	1	01/30/26	02/01/26	
o-Xylene	ND	0.0250	1	01/30/26	02/01/26	
p,m-Xylene	ND	0.0500	1	01/30/26	02/01/26	
Total Xylenes	ND	0.0250	1	01/30/26	02/01/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.6 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2605112
Gasoline Range Organics (C6-C10)	ND	20.0	1	01/30/26	02/01/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.9 %*	*70-130*	*01/30/26*	*02/01/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2605124
Diesel Range Organics (C10-C28)	**102**	25.0	1	01/30/26	01/31/26	
Oil Range Organics (C28-C36)	**99.4**	50.0	1	01/30/26	01/31/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*01/30/26*	*01/31/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2605120
Chloride	**2460**	40.0	2	01/30/26	01/30/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605112-BLK1)									Prepared: 01/30/26 Analyzed: 02/01/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.39*		*8.00*		*92.4*	*70-130*			
LCS (2605112-BS1)									Prepared: 01/30/26 Analyzed: 02/01/26
Benzene	4.93	0.0250	5.00		98.7	70-130			
Ethylbenzene	4.60	0.0250	5.00		91.9	70-130			
Toluene	4.81	0.0250	5.00		96.2	70-130			
o-Xylene	4.69	0.0250	5.00		93.7	70-130			
p,m-Xylene	9.39	0.0500	10.0		93.9	70-130			
Total Xylenes	14.1	0.0250	15.0		93.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.25*		*8.00*		*90.6*	*70-130*			
Matrix Spike (2605112-MS1)				**Source: E601279-03**					Prepared: 01/30/26 Analyzed: 02/01/26
Benzene	5.02	0.0250	5.00	ND	100	70-130			
Ethylbenzene	4.64	0.0250	5.00	ND	92.7	70-130			
Toluene	4.86	0.0250	5.00	ND	97.3	70-130			
o-Xylene	4.73	0.0250	5.00	ND	94.6	70-130			
p,m-Xylene	9.44	0.0500	10.0	ND	94.4	70-130			
Total Xylenes	14.2	0.0250	15.0	ND	94.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.37*		*8.00*		*92.1*	*70-130*			
Matrix Spike Dup (2605112-MSD1)				**Source: E601279-03**					Prepared: 01/30/26 Analyzed: 02/01/26
Benzene	4.92	0.0250	5.00	ND	98.3	70-130	2.00	27	
Ethylbenzene	4.57	0.0250	5.00	ND	91.4	70-130	1.48	26	
Toluene	4.78	0.0250	5.00	ND	95.6	70-130	1.73	20	
o-Xylene	4.66	0.0250	5.00	ND	93.3	70-130	1.41	25	
p,m-Xylene	9.32	0.0500	10.0	ND	93.2	70-130	1.35	23	
Total Xylenes	14.0	0.0250	15.0	ND	93.2	70-130	1.37	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.27*		*8.00*		*90.8*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605112-BLK1)									Prepared: 01/30/26 Analyzed: 02/01/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.88*		*8.00*		*98.4*	*70-130*			
LCS (2605112-BS2)									Prepared: 01/30/26 Analyzed: 02/01/26
Gasoline Range Organics (C6-C10)	52.3	20.0	50.0		105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.77*		*8.00*		*97.2*	*70-130*			
Matrix Spike (2605112-MS2)				**Source: E601279-03**					Prepared: 01/30/26 Analyzed: 02/01/26
Gasoline Range Organics (C6-C10)	51.1	20.0	50.0	ND	102	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.71*		*8.00*		*96.4*	*70-130*			
Matrix Spike Dup (2605112-MSD2)				**Source: E601279-03**					Prepared: 01/30/26 Analyzed: 02/01/26
Gasoline Range Organics (C6-C10)	51.8	20.0	50.0	ND	104	70-130	1.21	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.84*		*8.00*		*98.0*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605124-BLK1)									Prepared: 01/30/26 Analyzed: 01/30/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*46.3*		*50.0*		*92.5*	*61-141*			
LCS (2605124-BS1)									Prepared: 01/30/26 Analyzed: 01/30/26
Diesel Range Organics (C10-C28)	248	25.0	250		99.1	66-144			
Surrogate: n-Nonane	*47.5*		*50.0*		*95.0*	*61-141*			
Matrix Spike (2605124-MS1)				**Source: E601275-04**					Prepared: 01/30/26 Analyzed: 01/30/26
Diesel Range Organics (C10-C28)	12000	250	250	12700	NR	56-156			M5
Surrogate: n-Nonane	*180*		*50.0*		*361*	*61-141*			*S5*
Matrix Spike Dup (2605124-MSD1)				**Source: E601275-04**					Prepared: 01/30/26 Analyzed: 01/30/26
Diesel Range Organics (C10-C28)	11500	250	250	12700	NR	56-156	4.45	20	M5
Surrogate: n-Nonane	*175*		*50.0*		*349*	*61-141*			*S5*

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/4/2026 4:40:35PM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2605120-BLK1)									Prepared: 01/30/26 Analyzed: 01/30/26
Chloride	ND	20.0							
LCS (2605120-BS1)									Prepared: 01/30/26 Analyzed: 01/30/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2605120-MS1)				**Source: E601278-03**					Prepared: 01/30/26 Analyzed: 01/30/26
Chloride	1220	20.0	250	998	87.9	80-120			
Matrix Spike Dup (2605120-MSD1)				**Source: E601278-03**					Prepared: 01/30/26 Analyzed: 01/30/26
Chloride	1240	20.0	250	998	95.3	80-120	1.50	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/04/26 16:40

M5	The analysis of the MS sample required a dilution such that the spike recovery calculation does not provide useful information. The accociated LCS spike recovery was acceptable.
S5	Surrogate spike recovery exceeded acceptance limits due to interfering target and/or non-target analytes.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# EL001278	1D 2D 3D Std	NM CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	Job Number 01058-0007	X	X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
12:40	1/28/2026	S	1	FS70-4'		1						X			2.5
13:02	1/28/1900	S	1	FS71-4'		2						X			3.7
13:12	1/28/2026	S	1	FS86-4'		3						X			4.9
13:11	1/28/1900	S	1	FS87-4'		4						X			1.9
13:06	1/28/2026	S	1	FS89-4'		5						X			5.3
13:08	1/28/1900	S	1	FS90-4'		6						X			4.9

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
[signature]	1/29/26	7:11	Michelle Gonzales	1-29-26	0711
Michelle Gonzales	1-29-26	1315	Nathan Gonzales	1-29-26	1315
Nathan Gonzales	1-29-26	1650	Johnny Archuleta	1-29-26	1650
Johnny Archuleta	1-29-26	2100	[signature]	1-30-26	815

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 1/30/2026 9:23:41AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	01/30/26 08:15	Work Order ID:	E601278
Phone:	(505) 382-1211	Date Logged In:	01/29/26 15:51	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/05/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-CM
R-NS

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E601289
Job Number:	01058-0007
Received:	2/2/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/6/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/6/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E601289
Date Received: 2/2/2026 6:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/2/2026 6:15:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS06-10’ 5
- FS36-4’ 6
- FS38-4’ 7
- FS67-4’ 8
- FS68-4’ 9
- FS94-4’ 10
- FS95-4’ 11
- FS96-4’ 12

QC Summary Data 13

- QC - Volatile Organics by EPA 8021B 13
- QC - Nonhalogenated Organics by EPA 8015D - GRO 14
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 15
- QC - Anions by EPA 300.0/9056A 16

Definitions and Notes 17

Chain of Custody etc. 18

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/06/26 10:03

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS06-10'	E601289-01A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS36-4'	E601289-02A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS38-4'	E601289-03A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS67-4'	E601289-04A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS68-4'	E601289-05A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS94-4'	E601289-06A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS95-4'	E601289-07A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.
FS96-4'	E601289-08A	Soil	01/29/26	02/02/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS06-10'

E601289-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.0 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**1240**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS36-4'

E601289-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.4 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**920**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS38-4'

E601289-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.6 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**62.3**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS67-4'

E601289-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.0 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	**56.2**	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	**56.3**	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**513**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS68-4'

E601289-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*112 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.4 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**219**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS94-4'

E601289-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.2 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**3850**	40.0	2	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS95-4'

E601289-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.5 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	**56.4**	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	**66.7**	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**850**	20.0	1	02/02/26	02/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

FS96-4'

E601289-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Benzene	ND	0.0250	1	02/02/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/02/26	02/03/26	
Toluene	ND	0.0250	1	02/02/26	02/03/26	
o-Xylene	ND	0.0250	1	02/02/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/02/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/02/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*113 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606014
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/02/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.5 %*	*70-130*	*02/02/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606013
Diesel Range Organics (C10-C28)	ND	25.0	1	02/02/26	02/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/02/26	02/03/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*02/02/26*	*02/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606016
Chloride	**4020**	40.0	2	02/02/26	02/02/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606014-BLK1)									Prepared: 02/02/26 Analyzed: 02/03/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*9.06*		*8.00*		*113*	*70-130*			
LCS (2606014-BS1)									Prepared: 02/02/26 Analyzed: 02/03/26
Benzene	4.83	0.0250	5.00		96.6	70-130			
Ethylbenzene	4.62	0.0250	5.00		92.4	70-130			
Toluene	4.75	0.0250	5.00		95.0	70-130			
o-Xylene	4.72	0.0250	5.00		94.4	70-130			
p,m-Xylene	9.42	0.0500	10.0		94.2	70-130			
Total Xylenes	14.1	0.0250	15.0		94.3	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.91*		*8.00*		*111*	*70-130*			
Matrix Spike (2606014-MS1)				**Source: E601286-02**					Prepared: 02/02/26 Analyzed: 02/03/26
Benzene	4.88	0.0250	5.00	ND	97.6	70-130			
Ethylbenzene	4.64	0.0250	5.00	ND	92.8	70-130			
Toluene	4.78	0.0250	5.00	ND	95.5	70-130			
o-Xylene	4.74	0.0250	5.00	ND	94.8	70-130			
p,m-Xylene	9.47	0.0500	10.0	ND	94.7	70-130			
Total Xylenes	14.2	0.0250	15.0	ND	94.7	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.78*		*8.00*		*110*	*70-130*			
Matrix Spike Dup (2606014-MSD1)				**Source: E601286-02**					Prepared: 02/02/26 Analyzed: 02/03/26
Benzene	4.88	0.0250	5.00	ND	97.6	70-130	0.00513	27	
Ethylbenzene	4.65	0.0250	5.00	ND	93.1	70-130	0.266	26	
Toluene	4.78	0.0250	5.00	ND	95.5	70-130	0.0115	20	
o-Xylene	4.76	0.0250	5.00	ND	95.2	70-130	0.460	25	
p,m-Xylene	9.50	0.0500	10.0	ND	95.0	70-130	0.269	23	
Total Xylenes	14.3	0.0250	15.0	ND	95.0	70-130	0.333	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.87*		*8.00*		*111*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606014-BLK1)									Prepared: 02/02/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.90*		*8.00*		*98.7*	*70-130*			
LCS (2606014-BS2)									Prepared: 02/02/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	52.9	20.0	50.0		106	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.94*		*8.00*		*99.3*	*70-130*			
Matrix Spike (2606014-MS2)				**Source: E601286-02**					Prepared: 02/02/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	51.9	20.0	50.0	ND	104	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.84*		*8.00*		*98.0*	*70-130*			
Matrix Spike Dup (2606014-MSD2)				**Source: E601286-02**					Prepared: 02/02/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	52.5	20.0	50.0	ND	105	70-130	1.33	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.97*		*8.00*		*99.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606013-BLK1)									Prepared: 02/02/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*52.7*		*50.0*		*105*	*61-141*			
LCS (2606013-BS1)									Prepared: 02/02/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	267	25.0	250		107	66-144			
Surrogate: n-Nonane	*51.9*		*50.0*		*104*	*61-141*			
Matrix Spike (2606013-MS1)				**Source: E601291-21**					Prepared: 02/02/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	272	25.0	250	ND	109	56-156			
Surrogate: n-Nonane	*52.1*		*50.0*		*104*	*61-141*			
Matrix Spike Dup (2606013-MSD1)				**Source: E601291-21**					Prepared: 02/02/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	266	25.0	250	ND	106	56-156	2.35	20	
Surrogate: n-Nonane	*51.3*		*50.0*		*103*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/6/2026 10:03:13AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606016-BLK1)									Prepared: 02/02/26 Analyzed: 02/02/26
Chloride	ND	20.0							
LCS (2606016-BS1)									Prepared: 02/02/26 Analyzed: 02/02/26
Chloride	261	20.0	250		105	90-110			
Matrix Spike (2606016-MS1)				**Source: E601289-01**					Prepared: 02/02/26 Analyzed: 02/02/26
Chloride	1520	20.0	250	1240	115	80-120			
Matrix Spike Dup (2606016-MSD1)				**Source: E601289-01**					Prepared: 02/02/26 Analyzed: 02/02/26
Chloride	1540	20.0	250	1240	121	80-120	0.898	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/06/26 10:03

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479.01.ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E601248 E601289	Job Number 01058-0007	1D 2D 3D Std: X	NM: X CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRD/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
11:48	1/29/2026	S	1	FS06-10'		1						X			Temp. 5.3°
11:20	~~1/26/2026~~ 1/29/26	S	1	FS36-4'		2						X			5.4°
11:18	~~1/23/2026~~ 1/29/26	S	1	FS38-4'		3						X			5.6°
11:46	~~1/20/2026~~ 1/29/26	S	1	FS67-4'		4						X			5.9°
11:45	~~1/17/2026~~ 1/29/26	S	1	FS68-4'		5						X			5.6°
11:22	~~1/14/2026~~ 1/29/26	S	1	FS94-4'		6						X			5.3°
11:53	~~1/11/2026~~ 1/29/26	S	1	FS95-4'		7						X			5.7°
11:21	~~1/8/2026~~ 1/29/26	S	1	FS96-4'		8						X			5.4°

EPA Program: SDWA | CWA | RCRA

Compliance | Y | or | N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Aboubakar Kone

Corrected sample dates per Client. 2/2/26 CM

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	1/30/26	7:11	Michelle Gonzales	1-30-26	0711
Michelle Gonzales	1-30-26	1045	Nathan Gonzales	1-30-26	1045
Nathan Gonzales	1-30-26	1424	Johnny Archuleta	1-30-26	1424
Johnny Archuleta	1-30-26	1800	Noe Soto	2-2-26	0615

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479. 01. ABJ

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# NS E601298 E601289	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
11:48	1/29/2026	S	1	FS06-10'		1						X			Temp. 5.3°
11:20	1/26/2026	S	1	FS36-4'		2						X			5.4°
11:18	1/23/2026	S	1	FS38-4'		3						X			5.6°
11:46	1/20/2026	S	1	FS67-4'		4						X			5.9°
11:45	1/17/2026	S	1	FS68-4'		5						X			5.6°
11:22	1/14/2026	S	1	FS94-4'		6						X			5.3°
11:53	1/11/2026	S	1	FS95-4'		7						X			5.7°
11:21	1/8/2026	S	1	FS96-4'		8						X			5.4°

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	1/30/26	7:11	Michelle Gonzales	1-30-26	0711
Michelle Gonzales	1-30-26	1045	Nathan Gonzales	1-30-26	1045
Nathan Gonzales	1-30-26	1424	Johnny Archuleta	1-30-26	1424
Johnny Archuleta	1/30/26	1800	Noe Soto	2-2-26	0615

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/2/2026 9:40:07AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/02/26 06:15	Work Order ID:	E601289
Phone:	(505) 382-1211	Date Logged In:	01/30/26 14:43	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/06/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Date sampled on COC does not match dates on containers.
L-NS
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B 3 Battery
Work Order:	E602012
Job Number:	01058-0007
Received:	2/3/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/9/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/9/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B 3 Battery
Workorder: E602012
Date Received: 2/3/2026 8:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/3/2026 8:30:00AM, under the Project Name: Jones Federal B 3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B 3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS05-10’ 5
- FS08-10’ 6
- FS37-4’ 7
- FS40-4’ 8
- FS41-4’ 9
- FS50-4’ 10
- FS52-4’ 11
- FS82-4’ 12
- FS92-4’ 13
- FS93-4’ 14
- FS95-4’ 15
- SW01-0’-4’ 16
- SW04-0’-4’ 17

QC Summary Data 18

- QC - Volatile Organics by EPA 8021B 18
- QC - Nonhalogenated Organics by EPA 8015D - GRO 19
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 20
- QC - Anions by EPA 300.0/9056A 21

Definitions and Notes 22

Chain of Custody etc. 23

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/09/26 07:42

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS05-10'	E602012-01A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS08-10'	E602012-02A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS37-4'	E602012-03A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS40-4'	E602012-04A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS41-4'	E602012-05A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS50-4'	E602012-06A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS52-4'	E602012-07A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS82-4'	E602012-08A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS92-4'	E602012-09A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS93-4'	E602012-10A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
FS95-4'	E602012-11A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
SW01-0'-4'	E602012-12A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.
SW04-0'-4'	E602012-13A	Soil	01/30/26	02/03/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS05-10'

E602012-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.2 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*126 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**1160**	20.0	1	02/03/26	02/03/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS08-10'

E602012-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.8 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	**1150**	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	**627**	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*115 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**33.6**	20.0	1	02/03/26	02/03/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS37-4'

E602012-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.4 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	ND	20.0	1	02/03/26	02/03/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS40-4'

E602012-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*98.5 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**198**	20.0	1	02/03/26	02/03/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS41-4'

E602012-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.9 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*113 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**1310**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS50-4'

E602012-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.1 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*113 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**2070**	40.0	2	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS52-4'

E602012-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.4 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	**28.5**	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**189**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS82-4'

E602012-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/03/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/03/26	
Toluene	ND	0.0250	1	02/03/26	02/03/26	
o-Xylene	ND	0.0250	1	02/03/26	02/03/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/03/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.2 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/03/26*	*02/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	**95.9**	50.0	2	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	**117**	100	2	02/03/26	02/04/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**530**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS92-4'

E602012-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/04/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/04/26	
Toluene	ND	0.0250	1	02/03/26	02/04/26	
o-Xylene	ND	0.0250	1	02/03/26	02/04/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/04/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/04/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.5 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/04/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	**187**	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	**222**	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*109 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**807**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS93-4'

E602012-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/04/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/04/26	
Toluene	ND	0.0250	1	02/03/26	02/04/26	
o-Xylene	ND	0.0250	1	02/03/26	02/04/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/04/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/04/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.8 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/04/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	**139**	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	**158**	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*112 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**1330**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

FS95-4'

E602012-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/04/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/04/26	
Toluene	ND	0.0250	1	02/03/26	02/04/26	
o-Xylene	ND	0.0250	1	02/03/26	02/04/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/04/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/04/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.9 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/04/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*109 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**2300**	40.0	2	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

SW01-0'-4'

E602012-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/04/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/04/26	
Toluene	ND	0.0250	1	02/03/26	02/04/26	
o-Xylene	ND	0.0250	1	02/03/26	02/04/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/04/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/04/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.0 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/04/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*121 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**105**	20.0	1	02/03/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

SW04-0'-4'

E602012-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Benzene	ND	0.0250	1	02/03/26	02/04/26	
Ethylbenzene	ND	0.0250	1	02/03/26	02/04/26	
Toluene	ND	0.0250	1	02/03/26	02/04/26	
o-Xylene	ND	0.0250	1	02/03/26	02/04/26	
p,m-Xylene	ND	0.0500	1	02/03/26	02/04/26	
Total Xylenes	ND	0.0250	1	02/03/26	02/04/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.5 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606044
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/03/26	02/04/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/03/26*	*02/04/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606050
Diesel Range Organics (C10-C28)	ND	25.0	1	02/03/26	02/04/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/03/26	02/04/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/03/26*	*02/04/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606053
Chloride	**31.8**	20.0	1	02/03/26	02/04/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606044-BLK1)									Prepared: 02/03/26 Analyzed: 02/03/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.70*		*8.00*		*96.2*	*70-130*			
LCS (2606044-BS1)									Prepared: 02/03/26 Analyzed: 02/03/26
Benzene	4.22	0.0250	5.00		84.4	70-130			
Ethylbenzene	4.01	0.0250	5.00		80.3	70-130			
Toluene	4.18	0.0250	5.00		83.7	70-130			
o-Xylene	4.08	0.0250	5.00		81.7	70-130			
p,m-Xylene	8.24	0.0500	10.0		82.4	70-130			
Total Xylenes	12.3	0.0250	15.0		82.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.56*		*8.00*		*94.6*	*70-130*			
Matrix Spike (2606044-MS1)				**Source: E602012-08**					Prepared: 02/03/26 Analyzed: 02/03/26
Benzene	4.68	0.0250	5.00	ND	93.5	70-130			
Ethylbenzene	4.43	0.0250	5.00	ND	88.6	70-130			
Toluene	4.62	0.0250	5.00	ND	92.4	70-130			
o-Xylene	4.49	0.0250	5.00	ND	89.7	70-130			
p,m-Xylene	9.08	0.0500	10.0	ND	90.8	70-130			
Total Xylenes	13.6	0.0250	15.0	ND	90.4	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.96*		*8.00*		*99.5*	*70-130*			
Matrix Spike Dup (2606044-MSD1)				**Source: E602012-08**					Prepared: 02/03/26 Analyzed: 02/03/26
Benzene	4.81	0.0250	5.00	ND	96.3	70-130	2.87	27	
Ethylbenzene	4.59	0.0250	5.00	ND	91.8	70-130	3.52	26	
Toluene	4.77	0.0250	5.00	ND	95.3	70-130	3.08	20	
o-Xylene	4.64	0.0250	5.00	ND	92.7	70-130	3.32	25	
p,m-Xylene	9.40	0.0500	10.0	ND	94.0	70-130	3.45	23	
Total Xylenes	14.0	0.0250	15.0	ND	93.5	70-130	3.40	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.65*		*8.00*		*95.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606044-BLK1)									Prepared: 02/03/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.64*		*8.00*		*121*	*70-130*			
LCS (2606044-BS2)									Prepared: 02/03/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	45.1	20.0	50.0		90.2	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.40*		*8.00*		*118*	*70-130*			
Matrix Spike (2606044-MS2)				**Source: E602012-08**					Prepared: 02/03/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	45.7	20.0	50.0	ND	91.4	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.44*		*8.00*		*118*	*70-130*			
Matrix Spike Dup (2606044-MSD2)				**Source: E602012-08**					Prepared: 02/03/26 Analyzed: 02/03/26
Gasoline Range Organics (C6-C10)	39.7	20.0	50.0	ND	79.3	70-130	14.2	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.60*		*8.00*		*120*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606050-BLK1)									Prepared: 02/03/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*51.5*		*50.0*		*103*	*61-141*			
LCS (2606050-BS1)									Prepared: 02/03/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	236	25.0	250		94.5	66-144			
Surrogate: n-Nonane	*53.9*		*50.0*		*108*	*61-141*			
Matrix Spike (2606050-MS1)				**Source: E602008-04**					Prepared: 02/03/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	248	25.0	250	ND	99.1	56-156			
Surrogate: n-Nonane	*55.9*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2606050-MSD1)				**Source: E602008-04**					Prepared: 02/03/26 Analyzed: 02/03/26
Diesel Range Organics (C10-C28)	252	25.0	250	ND	101	56-156	1.74	20	
Surrogate: n-Nonane	*56.9*		*50.0*		*114*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/9/2026 7:42:22AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606053-BLK1)									Prepared: 02/03/26 Analyzed: 02/03/26
Chloride	ND	20.0							
LCS (2606053-BS1)									Prepared: 02/03/26 Analyzed: 02/03/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2606053-MS1)				**Source: E602008-05**					Prepared: 02/03/26 Analyzed: 02/03/26
Chloride	275	200	250	ND	110	80-120			
Matrix Spike Dup (2606053-MSD1)				**Source: E602008-05**					Prepared: 02/03/26 Analyzed: 02/03/26
Chloride	274	200	250	ND	109	80-120	0.496	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B 3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/09/26 07:42

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479.01-ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602012	Job Number 01053-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information / **Analysis and Method** / **EPA Program**

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
10:14	1/30/2026	S	1	FS05-10'		1						X						4.9°
10:13	1/30/2026	S	1	FS08-10'		2						X						4.7°
10:16	1/30/2026	S	1	FS37-4'		3						X						4.9°
12:41	1/30/2026	S	1	FS40-4'		4						X						4.6°
12:39	1/30/2026	S	1	FS41-4'		5						X						5.2°
12:44	1/30/2026	S	1	FS50-4'		6						X						5.4°
12:45	1/30/2026	S	1	FS52-4		7						X						5.1°
10:08	1/30/2026	S	1	FS82-4'		8						X						4.8°
10:59	1/30/2026	S	1	FS92-4'		9						X						4.6°
10:10	1/30/2026	S	1	FS93-4'		10						X						4.9°

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/2/26	7:11	Michelle Gonzales	2-2-26	0711
Michelle Gonzales	2-2-26	1515	Marissa Gonzales	2-2-26	1515
Marissa Gonzales	2-2-26	1910	Johnny Archuleta	2-2-26	1910
Johnny Archuleta	2-2-26	2240	Noe Soto	2-3-26	0830

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Page 478 of 574

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602012	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
10:12	1/30/2026	S	1	FS95-4'		11						X						5.0°
11:48	1/30/2026	S	1	SW01-0'-4'		12						X						4.8°
11:56	1/30/2026	S	1	SW04-0'-4'		13						X						5.3°

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/2/26	7:11	Michelle Gonzales	2-2-26	0711
Michelle Gonzales	2-2-26	1515	Marissa Gonzales	2-2-26	1515
Marissa Gonzales	2-2-26	1910	Johnny Archuleta	2-2-26	1910
Johnny Archuleta	2-2-26	2240	Noe Soto	2-3-26	0830

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/3/2026 12:13:15PM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/03/26 08:30	Work Order ID:	E602012
Phone:	(505) 382-1211	Date Logged In:	02/02/26 16:43	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	02/09/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-KH

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602022
Job Number:	01058-0007
Received:	2/4/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/10/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/10/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602022
Date Received: 2/4/2026 8:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/4/2026 8:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS15-4’ 5
- FS16-4’ 6
- FS31-4’ 7
- FS32-4’ 8
- FS47-4’ 9
- FS48-4’ 10
- FS49-4’ 11
- FS51-4’ 12

QC Summary Data 13

- QC - Volatile Organics by EPA 8021B 13
- QC - Nonhalogenated Organics by EPA 8015D - GRO 14
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 15
- QC - Anions by EPA 300.0/9056A 16

Definitions and Notes 17

Chain of Custody etc. 18

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/10/26 12:44

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS15-4'	E602022-01A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS16-4'	E602022-02A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS31-4'	E602022-03A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS32-4'	E602022-04A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS47-4'	E602022-05A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS48-4'	E602022-06A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS49-4'	E602022-07A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS51-4'	E602022-08A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS15-4'

E602022-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*89.8 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.4 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	ND	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**449**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS16-4'

E602022-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*90.4 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.5 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**404**	50.0	2	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**494**	100	2	02/05/26	02/05/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**66.9**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS31-4'

E602022-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.1 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.0 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**52.7**	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**93.3**	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**543**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS32-4'

E602022-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*91.7 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.5 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	ND	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**270**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS47-4'

E602022-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.7 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.4 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**182**	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**195**	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**1670**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS48-4'

E602022-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.6 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.9 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**353**	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**373**	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**2040**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS49-4'

E602022-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.9 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.0 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**611**	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**486**	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**1350**	20.0	1	02/04/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

FS51-4'

E602022-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.4 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606066
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.2 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**298**	25.0	1	02/05/26	02/05/26	
Oil Range Organics (C28-C36)	**261**	50.0	1	02/05/26	02/05/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/05/26*	*02/05/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2606086
Chloride	**2250**	20.0	1	02/04/26	02/05/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606066-BLK1)									Prepared: 02/04/26 Analyzed: 02/04/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.45*		*8.00*		*93.2*	*70-130*			
LCS (2606066-BS1)									Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	4.67	0.0250	5.00		93.4	70-130			
Ethylbenzene	4.34	0.0250	5.00		86.9	70-130			
Toluene	4.54	0.0250	5.00		90.8	70-130			
o-Xylene	4.44	0.0250	5.00		88.7	70-130			
p,m-Xylene	8.87	0.0500	10.0		88.7	70-130			
Total Xylenes	13.3	0.0250	15.0		88.7	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.44*		*8.00*		*93.0*	*70-130*			
Matrix Spike (2606066-MS1)				**Source: E602018-05**					Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	4.93	0.0250	5.00	ND	98.6	70-130			
Ethylbenzene	4.61	0.0250	5.00	ND	92.1	70-130			
Toluene	4.78	0.0250	5.00	ND	95.7	70-130			
o-Xylene	4.68	0.0250	5.00	ND	93.5	70-130			
p,m-Xylene	9.39	0.0500	10.0	ND	93.9	70-130			
Total Xylenes	14.1	0.0250	15.0	ND	93.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.37*		*8.00*		*92.1*	*70-130*			
Matrix Spike Dup (2606066-MSD1)				**Source: E602018-05**					Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	4.79	0.0250	5.00	ND	95.8	70-130	2.85	27	
Ethylbenzene	4.48	0.0250	5.00	ND	89.5	70-130	2.85	26	
Toluene	4.65	0.0250	5.00	ND	93.0	70-130	2.81	20	
o-Xylene	4.55	0.0250	5.00	ND	91.0	70-130	2.72	25	
p,m-Xylene	9.14	0.0500	10.0	ND	91.4	70-130	2.74	23	
Total Xylenes	13.7	0.0250	15.0	ND	91.3	70-130	2.73	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.41*		*8.00*		*92.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606066-BLK1)									Prepared: 02/04/26 Analyzed: 02/04/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.96*		*8.00*		*99.5*	*70-130*			
LCS (2606066-BS2)									Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	49.5	20.0	50.0		99.1	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.97*		*8.00*		*99.6*	*70-130*			
Matrix Spike (2606066-MS2)				**Source: E602018-05**					Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	53.9	20.0	50.0	ND	108	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.94*		*8.00*		*99.3*	*70-130*			
Matrix Spike Dup (2606066-MSD2)				**Source: E602018-05**					Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	53.9	20.0	50.0	ND	108	70-130	0.00231	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.85*		*8.00*		*98.1*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606089-BLK1)									Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*49.0*		*50.0*		*98.0*	*61-141*			
LCS (2606089-BS1)									Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	249	25.0	250		99.8	66-144			
Surrogate: n-Nonane	*49.0*		*50.0*		*98.1*	*61-141*			
Matrix Spike (2606089-MS1)				**Source: E602022-02**					Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	595	50.0	250	404	76.4	56-156			
Surrogate: n-Nonane	*51.1*		*50.0*		*102*	*61-141*			
Matrix Spike Dup (2606089-MSD1)				**Source: E602022-02**					Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	679	50.0	250	404	110	56-156	13.1	20	
Surrogate: n-Nonane	*51.1*		*50.0*		*102*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 12:44:06PM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606086-BLK1)									Prepared: 02/04/26 Analyzed: 02/05/26
Chloride	ND	20.0							
LCS (2606086-BS1)									Prepared: 02/04/26 Analyzed: 02/05/26
Chloride	258	20.0	250		103	90-110			
Matrix Spike (2606086-MS1)				**Source: E602025-03**					Prepared: 02/04/26 Analyzed: 02/05/26
Chloride	793	20.0	250	534	103	80-120			
Matrix Spike Dup (2606086-MSD1)				**Source: E602025-03**					Prepared: 02/04/26 Analyzed: 02/05/26
Chloride	782	20.0	250	534	99.1	80-120	1.35	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/10/26 12:44

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479.01.ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only		TAT				State				
Client: Devon	Company: Devon Energy	Lab WO#	Job Number	1D	2D	3D	Std	NM	CO	UT	TX	
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	E602022	01058-0007				X	X				
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220											
Address: 3122 National Parks Hwy	Phone: (575)689-7597											
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com											
Phone: 575-988-0055	Miscellaneous: Jim Raley											
Email: agiovengo@ensolum.com												

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
11:46	2/2/2026	S	1	FS15-4'		1						X						4.3°
11:48	2/2/2026	S	1	FS16-4'		2						X						4.6°
11:45	2/2/2026	S	1	FS31-4'		3						X						4.2°
11:43	2/2/2026	S	1	FS32-4'		4						X						3.9°
12:02	2/2/2026	S	1	FS47-4'		5						X						4.3°
12:04	2/2/2026	S	1	FS48-4'		6						X						4.6°
11:06	2/2/2026	S	1	FS49-4'		7						X						4.7°
11:41	2/2/2026	S	1	FS51-4'		8						X						4.4°
												X						
												X						

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/3/26	7:11	Michelle Gonzales	2-3-26	0711
Michelle Gonzales	2-3-26	1400	Marissa Gonzales	2-3-26	1400
Marissa Gonzales	2-3-26	1800	Johnny Archuleta	2-3-26	1800
Johnny Archuleta	2-3-26	2140		2-4-26	0830

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/4/2026 11:22:12AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/04/26 08:30	Work Order ID:	E602022
Phone:	(505) 382-1211	Date Logged In:	02/03/26 15:42	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	02/10/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-DL

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602023
Job Number:	01058-0007
Received:	2/4/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/10/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/10/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602023
Date Received: 2/4/2026 8:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/4/2026 8:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

FS33-4’ 5

FS34-4’ 6

QC Summary Data 7

QC - Volatile Organics by EPA 8021B 7

QC - Nonhalogenated Organics by EPA 8015D - GRO 8

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 9

QC - Anions by EPA 300.0/9056A 10

Definitions and Notes 11

Chain of Custody etc. 12

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/10/26 09:15

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS33-4'	E602023-01A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.
FS34-4'	E602023-02A	Soil	02/02/26	02/04/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

FS33-4'

E602023-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2606073
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	ND	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	ND	0.0500	1	02/04/26	02/05/26	
Total Xylenes	ND	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2606073
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.0 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**640**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**487**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606081
Chloride	**404**	20.0	1	02/04/26	02/04/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

FS34-4'

E602023-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2606073
Benzene	ND	0.0250	1	02/04/26	02/05/26	
Ethylbenzene	ND	0.0250	1	02/04/26	02/05/26	
Toluene	ND	0.0250	1	02/04/26	02/05/26	
o-Xylene	**0.0273**	0.0250	1	02/04/26	02/05/26	
p,m-Xylene	**0.139**	0.0500	1	02/04/26	02/05/26	
Total Xylenes	**0.166**	0.0250	1	02/04/26	02/05/26	
Surrogate: 4-Bromochlorobenzene-PID		*105 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2606073
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/04/26	02/05/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.8 %*	*70-130*	*02/04/26*	*02/05/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606089
Diesel Range Organics (C10-C28)	**810**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**371**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606081
Chloride	**285**	20.0	1	02/04/26	02/04/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606073-BLK1)									Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.84*		*8.00*		*98.0*	*70-130*			
LCS (2606073-BS1)									Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	5.64	0.0250	5.00		113	70-130			
Ethylbenzene	5.41	0.0250	5.00		108	70-130			
Toluene	5.55	0.0250	5.00		111	70-130			
o-Xylene	5.44	0.0250	5.00		109	70-130			
p,m-Xylene	11.0	0.0500	10.0		110	70-130			
Total Xylenes	16.5	0.0250	15.0		110	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.03*		*8.00*		*100*	*70-130*			
Matrix Spike (2606073-MS1)				**Source: E602024-06**					Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	5.63	0.0250	5.00	ND	113	70-130			
Ethylbenzene	5.40	0.0250	5.00	ND	108	70-130			
Toluene	5.54	0.0250	5.00	ND	111	70-130			
o-Xylene	5.45	0.0250	5.00	ND	109	70-130			
p,m-Xylene	11.0	0.0500	10.0	ND	110	70-130			
Total Xylenes	16.5	0.0250	15.0	ND	110	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.33*		*8.00*		*104*	*70-130*			
Matrix Spike Dup (2606073-MSD1)				**Source: E602024-06**					Prepared: 02/04/26 Analyzed: 02/05/26
Benzene	5.03	0.0250	5.00	ND	101	70-130	11.1	27	
Ethylbenzene	4.83	0.0250	5.00	ND	96.6	70-130	11.2	26	
Toluene	4.95	0.0250	5.00	ND	98.9	70-130	11.3	20	
o-Xylene	4.87	0.0250	5.00	ND	97.3	70-130	11.2	25	
p,m-Xylene	9.86	0.0500	10.0	ND	98.6	70-130	11.1	23	
Total Xylenes	14.7	0.0250	15.0	ND	98.2	70-130	11.1	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.29*		*8.00*		*104*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606073-BLK1)									Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.33*		*8.00*		*91.7*	*70-130*			
LCS (2606073-BS2)									Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	60.1	20.0	50.0		120	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.47*		*8.00*		*93.4*	*70-130*			
Matrix Spike (2606073-MS2)				**Source: E602024-06**					Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	58.2	20.0	50.0	ND	116	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.36*		*8.00*		*92.0*	*70-130*			
Matrix Spike Dup (2606073-MSD2)				**Source: E602024-06**					Prepared: 02/04/26 Analyzed: 02/05/26
Gasoline Range Organics (C6-C10)	57.5	20.0	50.0	ND	115	70-130	1.15	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.33*		*8.00*		*91.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606089-BLK1)									Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*49.0*		*50.0*		*98.0*	*61-141*			
LCS (2606089-BS1)									Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	249	25.0	250		99.8	66-144			
Surrogate: n-Nonane	*49.0*		*50.0*		*98.1*	*61-141*			
Matrix Spike (2606089-MS1)				**Source: E602022-02**					Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	595	50.0	250	404	76.4	56-156			
Surrogate: n-Nonane	*51.1*		*50.0*		*102*	*61-141*			
Matrix Spike Dup (2606089-MSD1)				**Source: E602022-02**					Prepared: 02/05/26 Analyzed: 02/05/26
Diesel Range Organics (C10-C28)	679	50.0	250	404	110	56-156	13.1	20	
Surrogate: n-Nonane	*51.1*		*50.0*		*102*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/10/2026 9:15:01AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606081-BLK1)									Prepared: 02/04/26 Analyzed: 02/04/26
Chloride	ND	20.0							
LCS (2606081-BS1)									Prepared: 02/04/26 Analyzed: 02/04/26
Chloride	256	20.0	250		102	90-110			
Matrix Spike (2606081-MS1)				**Source: E602024-02**					Prepared: 02/04/26 Analyzed: 02/04/26
Chloride	1370	20.0	250	1150	85.4	80-120			
Matrix Spike Dup (2606081-MSD1)				**Source: E602024-02**					Prepared: 02/04/26 Analyzed: 02/04/26
Chloride	1330	20.0	250	1150	72.1	80-120	2.46	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/10/26 09:15

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602023	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
11:53	2/2/2026	S	1	FS33-4'		1						X						4.9°
11:58	2/2/2026	S	1	FS34-4'		2						X						5.1°

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/3/26	7:11	Michelle Gonzales	2-3-26	0711
Michelle Gonzales	2-3-26	1400	Marissa Gonzales	2-3-26	1400
Marissa Gonzales	2-3-26	1890	Johnny Archuleta	2-3-26	1800
Johnny Archuleta	2-3-26	2140	Noe Sotelo	2-4-26	0830

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/4/2026 11:25:23AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/04/26 08:30	Work Order ID:	E602023
Phone:	(505) 382-1211	Date Logged In:	02/03/26 15:47	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	02/10/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-DL

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602045
Job Number:	01058-0007
Received:	2/4/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/11/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/11/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602045
Date Received: 2/4/2026 11:15:23PM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/4/2026 11:15:23PM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS01-5’ 5
- FS02-5’ 6
- FS03-5’ 7
- FS04-5’ 8
- FS09-11’ 9
- FS17-5’ 10
- FS42-4’ 11
- FS43-4’ 12
- FS91-5’ 13
- FS108-2’ 14
- FS109-2’ 15
- FS110-2’ 16

QC Summary Data 17

- QC - Volatile Organics by EPA 8021B 17
- QC - Nonhalogenated Organics by EPA 8015D - GRO 18
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 19
- QC - Anions by EPA 300.0/9056A 20

Definitions and Notes 21

Chain of Custody etc. 22

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/11/26 10:00

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS01-5'	E602045-01A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS02-5'	E602045-02A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS03-5'	E602045-03A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS04-5'	E602045-04A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS09-11'	E602045-05A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS17-5'	E602045-06A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS42-4'	E602045-07A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS43-4'	E602045-08A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS91-5'	E602045-09A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS108-2'	E602045-10A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS109-2'	E602045-11A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.
FS110-2'	E602045-12A	Soil	02/03/26	02/04/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS01-5'

E602045-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*104 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.0 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**1030**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**698**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**784**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS02-5'

E602045-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*104 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.7 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**1160**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**825**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**924**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS03-5'

E602045-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*87.6 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**68.6**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**113**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**669**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS04-5'

E602045-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*104 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.9 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**47.9**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**65.0**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**631**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS09-11'

E602045-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.3 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**565**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**394**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	ND	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS17-5'

E602045-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.4 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**124**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**141**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**88.7**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS42-4'

E602045-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**328**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**307**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**987**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS43-4'

E602045-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/06/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/06/26	
Toluene	ND	0.0250	1	02/05/26	02/06/26	
o-Xylene	ND	0.0250	1	02/05/26	02/06/26	
p,m-Xylene	**0.0536**	0.0500	1	02/05/26	02/06/26	
Total Xylenes	**0.0536**	0.0250	1	02/05/26	02/06/26	
Surrogate: 4-Bromochlorobenzene-PID		*104 %*	*70-130*	*02/05/26*	*02/06/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/06/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.2 %*	*70-130*	*02/05/26*	*02/06/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**1130**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**971**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*136 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**2370**	40.0	2	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS91-5'

E602045-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	**101**	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	**123**	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**1130**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS108-2'

E602045-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.1 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	ND	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**308**	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS109-2'

E602045-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.4 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	ND	25.0	1	02/05/26	02/06/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/05/26	02/06/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/05/26*	*02/06/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	ND	20.0	1	02/05/26	02/05/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

FS110-2'

E602045-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Benzene	ND	0.0250	1	02/05/26	02/07/26	
Ethylbenzene	ND	0.0250	1	02/05/26	02/07/26	
Toluene	ND	0.0250	1	02/05/26	02/07/26	
o-Xylene	ND	0.0250	1	02/05/26	02/07/26	
p,m-Xylene	ND	0.0500	1	02/05/26	02/07/26	
Total Xylenes	ND	0.0250	1	02/05/26	02/07/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.7 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606104
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/05/26	02/07/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.1 %*	*70-130*	*02/05/26*	*02/07/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2606117
Diesel Range Organics (C10-C28)	ND	25.0	1	02/05/26	02/07/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/05/26	02/07/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/05/26*	*02/07/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2606113
Chloride	**49.3**	20.0	1	02/05/26	02/05/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606104-BLK1)									Prepared: 02/05/26 Analyzed: 02/06/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.30*		*8.00*		*104*	*70-130*			
LCS (2606104-BS1)									Prepared: 02/05/26 Analyzed: 02/06/26
Benzene	5.30	0.0250	5.00		106	70-130			
Ethylbenzene	5.07	0.0250	5.00		101	70-130			
Toluene	5.22	0.0250	5.00		104	70-130			
o-Xylene	5.17	0.0250	5.00		103	70-130			
p,m-Xylene	10.3	0.0500	10.0		103	70-130			
Total Xylenes	15.5	0.0250	15.0		103	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.21*		*8.00*		*103*	*70-130*			
Matrix Spike (2606104-MS1)				**Source: E602045-08**					Prepared: 02/05/26 Analyzed: 02/06/26
Benzene	5.62	0.0250	5.00	ND	112	70-130			
Ethylbenzene	5.39	0.0250	5.00	ND	108	70-130			
Toluene	5.54	0.0250	5.00	ND	111	70-130			
o-Xylene	5.45	0.0250	5.00	ND	109	70-130			
p,m-Xylene	11.0	0.0500	10.0	0.0536	109	70-130			
Total Xylenes	16.4	0.0250	15.0	0.0536	109	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.31*		*8.00*		*104*	*70-130*			
Matrix Spike Dup (2606104-MSD1)				**Source: E602045-08**					Prepared: 02/05/26 Analyzed: 02/06/26
Benzene	5.55	0.0250	5.00	ND	111	70-130	1.36	27	
Ethylbenzene	5.33	0.0250	5.00	ND	107	70-130	1.08	26	
Toluene	5.46	0.0250	5.00	ND	109	70-130	1.42	20	
o-Xylene	5.39	0.0250	5.00	ND	108	70-130	1.22	25	
p,m-Xylene	10.9	0.0500	10.0	0.0536	108	70-130	1.28	23	
Total Xylenes	16.2	0.0250	15.0	0.0536	108	70-130	1.26	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.28*		*8.00*		*103*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606104-BLK1)									Prepared: 02/05/26 Analyzed: 02/06/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.13*		*8.00*		*89.2*	*70-130*			
LCS (2606104-BS2)									Prepared: 02/05/26 Analyzed: 02/06/26
Gasoline Range Organics (C6-C10)	52.4	20.0	50.0		105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.15*		*8.00*		*89.3*	*70-130*			
Matrix Spike (2606104-MS2)				**Source: E602045-08**					Prepared: 02/05/26 Analyzed: 02/06/26
Gasoline Range Organics (C6-C10)	60.8	20.0	50.0	ND	122	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.16*		*8.00*		*89.5*	*70-130*			
Matrix Spike Dup (2606104-MSD2)				**Source: E602045-08**					Prepared: 02/05/26 Analyzed: 02/06/26
Gasoline Range Organics (C6-C10)	60.3	20.0	50.0	ND	121	70-130	0.804	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.25*		*8.00*		*90.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606117-BLK1)									Prepared: 02/05/26 Analyzed: 02/06/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*49.0*		*50.0*		*98.1*	*61-141*			
LCS (2606117-BS1)									Prepared: 02/05/26 Analyzed: 02/06/26
Diesel Range Organics (C10-C28)	260	25.0	250		104	66-144			
Surrogate: n-Nonane	*51.2*		*50.0*		*102*	*61-141*			
Matrix Spike (2606117-MS1)				**Source: E602045-09**					Prepared: 02/05/26 Analyzed: 02/06/26
Diesel Range Organics (C10-C28)	375	25.0	250	101	109	56-156			
Surrogate: n-Nonane	*53.3*		*50.0*		*107*	*61-141*			
Matrix Spike Dup (2606117-MSD1)				**Source: E602045-09**					Prepared: 02/05/26 Analyzed: 02/06/26
Diesel Range Organics (C10-C28)	395	25.0	250	101	117	56-156	5.13	20	
Surrogate: n-Nonane	*53.7*		*50.0*		*107*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/11/2026 10:00:15AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606113-BLK1)									Prepared: 02/05/26 Analyzed: 02/05/26
Chloride	ND	20.0							
LCS (2606113-BS1)									Prepared: 02/05/26 Analyzed: 02/05/26
Chloride	261	20.0	250		104	90-110			
Matrix Spike (2606113-MS1)				**Source: E602045-06**					Prepared: 02/05/26 Analyzed: 02/05/26
Chloride	339	20.0	250	88.7	100	80-120			
Matrix Spike Dup (2606113-MSD1)				**Source: E602045-06**					Prepared: 02/05/26 Analyzed: 02/05/26
Chloride	346	20.0	250	88.7	103	80-120	1.87	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/11/26 10:00

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E002045	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
10:48	2/3/2026	S	1	FS01-5'		1						X						3.9
10:47	2/3/2026	S	1	FS02-5'		2						X						3.7
10:43	2/3/2026	S	1	FS03-5'		3						X						3.8
10:45	2/3/2026	S	1	FS04-5'		4						X						4.0
11:16	2/3/2026	S	1	FS09-11'		5						X						4.2
11:10	2/3/2026	S	1	FS17-5'		6						X						3.8
11:00	2/3/2026	S	1	FS42-4'		7						X						4.4
10:58	2/3/2026	S	1	FS43-4'		8						X						3.9
11:14	2/3/2026	S	1	FS91-5'		9						X						4.1
13:00	2/3/2026	S	1	~~FS08-2'~~ 108-2'		10						X						4.4

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Aboubakar Kone

Corrected sample name per Client AK 2/5/26 CM

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/4/26	7:11	Michelle Gonzales	2-4-26	0711
Michelle Gonzales	2-4-26	1545	Marissa Gonzales	2-4-26	1545
Marissa Gonzales	2-4-26	1950	Johnny Archuleta	2-4-26	1950
Johnny Archuleta	2-4-26	2315		2-4-26	2315

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602045	Job Number 01058-0007	1D 2D 3D Std: X	NM X CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
13:09	2/3/2026	S	1	FS109-2'		11						X			3.5
13:11	2/3/2026	S	1	FS110-2'		12						X			3.9

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: Aboubakar Kone

Corrected Sample name per Client AH 2/5/26 CM

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/4/26	7:11	Michelle Gonzales	2-4-26	0711
Michelle Gonzales	2-4-26	1545	Marissa Gonzales	2-4-26	1545
Marissa Gonzales	2-4-26	1950	Johnny Archuleta	2-4-26	1950
Johnny Archuleta	2-4-26	2315	Noe	2-4-26	2315

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 T2 T3

AVG Temp °C

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602045	Job Number 01058-0007	1D 2D 3D Std:	NM CO UT TX:
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr				X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220				
Address: 3122 National Parks Hwy	Phone: (575)689-7597				
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com				
Phone: 575-988-0055	Miscellaneous: Jim Raley				
Email: agiovengo@ensolum.com					

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
10:48	2/3/2026	S	1	FS01-5'		1						X			3.9
10:47	2/3/2026	S	1	FS02-5'		2						X			3.7
10:43	2/3/2026	S	1	FS03-5'		3						X			3.8
10:45	2/3/2026	S	1	FS04-5'		4						X			4.0
11:16	2/3/2026	S	1	FS09-11'		5						X			4.2
11:10	2/3/2026	S	1	FS17-5'		6						X			3.8
11:00	2/3/2026	S	1	FS42-4'		7						X			4.4
10:58	2/3/2026	S	1	FS43-4'		8						X			3.9
11:14	2/3/2026	S	1	FS91-5'		9						X			4.1
13:00	2/3/2026	S	1	FS08-2'		10						X			4.4

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/4/26	7:11	Michelle Gonzales	2-4-26	0711
Michelle Gonzales	2-4-26	1545	Marissa Gonzales	2-4-26	1545
Marissa Gonzales	2-4-26	1950	Johnny Archuleta	2-4-26	1950
Johnny Archuleta	2-4-26	2315		2-4-26	2315

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 T2 T3

AVG Temp °C

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602045	Job Number 01059-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
13:09	2/3/2026	S	1	FS109-2'		11						X						3.5
13:11	2/3/2026	S	1	FS110-2'		12						X						3.9

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/4/26	7:11	Michelle Gonzales	2-4-26	0711
Michelle Gonzales	2-4-26	1545	Marissa Gonzales	2-4-26	1545
Marissa Gonzales	2-4-26	1950	Johnny Archuleta	2-4-26	1950
Johnny Archuleta	2-4-26	2315	Noe	2-4-26	2315

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 T2 T3

AVG Temp °C

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/5/2026 10:37:38AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/04/26 23:15	Work Order ID:	E602045
Phone:	(505) 382-1211	Date Logged In:	02/04/26 16:39	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	02/11/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	No	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Sample #10 name on container did not match name on COC.
L-NS
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602071
Job Number:	01058-0007
Received:	2/6/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/12/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/12/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602071
Date Received: 2/6/2026 8:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/6/2026 8:00:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

FS18-5’ 6

FS19-5’ 7

FS26-4’ 8

FS27-4’ 9

FS29-4’ 10

FS39-5’ 11

FS104-2’ 12

FS105-3’ 13

FS107-3’ 14

FS111-2’ 15

FS112-2’ 16

SW03-0’-4’ 17

SW05-0’-4’ 18

SW33-4’-10’ 19

SW34-4’-10’ 20

SW35-4’-10’ 21

SW37-4’-10’ 22

SW38-4’-10’ 23

QC Summary Data 24

QC - Volatile Organics by EPA 8021B 24

Table of Contents (continued)

QC - Nonhalogenated Organics by EPA 8015D - GRO 25

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 26

QC - Anions by EPA 300.0/9056A 27

Definitions and Notes 28

Chain of Custody etc. 29

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/12/26 12:31

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS18-5'	E602071-01A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS19-5'	E602071-02A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS26-4'	E602071-03A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS27-4'	E602071-04A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS29-4'	E602071-05A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS39-5'	E602071-06A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS104-2'	E602071-07A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS105-3'	E602071-08A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS107-3'	E602071-09A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS111-2'	E602071-10A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
FS112-2'	E602071-11A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW03-0'-4'	E602071-12A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW05-0'-4'	E602071-13A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW33-4'-10'	E602071-14A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW34-4'-10'	E602071-15A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW35-4'-10'	E602071-16A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW37-4'-10'	E602071-17A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.
SW38-4'-10'	E602071-18A	Soil	02/04/26	02/06/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS18-5'

E602071-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.2 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**27.5**	25.0	1	02/09/26	02/09/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/09/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/09/26*	*02/09/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**526**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS19-5'

E602071-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	**0.0374**	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	**0.0651**	0.0500	1	02/06/26	02/10/26	
Total Xylenes	**0.102**	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.3 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**863**	25.0	1	02/09/26	02/09/26	
Oil Range Organics (C28-C36)	**313**	50.0	1	02/09/26	02/09/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/09/26*	*02/09/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**2370**	40.0	2	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS26-4'

E602071-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.1 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**670**	25.0	1	02/09/26	02/09/26	
Oil Range Organics (C28-C36)	**335**	50.0	1	02/09/26	02/09/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/09/26*	*02/09/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**1930**	40.0	2	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS27-4'

E602071-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.9 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**1660**	25.0	1	02/09/26	02/09/26	
Oil Range Organics (C28-C36)	**904**	50.0	1	02/09/26	02/09/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/09/26*	*02/09/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**824**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS29-4'

E602071-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.3 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**970**	25.0	1	02/09/26	02/09/26	
Oil Range Organics (C28-C36)	**807**	50.0	1	02/09/26	02/09/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/09/26*	*02/09/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**444**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS39-5'

E602071-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*108 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.1 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	**170**	25.0	1	02/09/26	02/11/26	
Oil Range Organics (C28-C36)	**172**	50.0	1	02/09/26	02/11/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/09/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**574**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS104-2'

E602071-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/11/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/09/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**73.3**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS105-3'

E602071-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.8 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/11/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/09/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**304**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS107-3'

E602071-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*109 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*94.3 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**236**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS111-2'

E602071-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*98.3 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**50.3**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

FS112-2'

E602071-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*98.4 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	ND	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW03-0'-4'

E602071-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.5 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	ND	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW05-0'-4'

E602071-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.0 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**49.8**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW33-4'-10'

E602071-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*110 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.1 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**1290**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW34-4'-10'

E602071-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.1 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*109 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**44.5**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW35-4'-10'

E602071-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.3 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**1880**	20.0	1	02/06/26	02/06/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW37-4'-10'

E602071-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.4 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**3220**	40.0	2	02/06/26	02/07/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

SW38-4'-10'

E602071-18

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Benzene	ND	0.0250	1	02/06/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/06/26	02/10/26	
Toluene	ND	0.0250	1	02/06/26	02/10/26	
o-Xylene	ND	0.0250	1	02/06/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/06/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/06/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*111 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2606153
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/06/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.8 %*	*70-130*	*02/06/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607020
Diesel Range Organics (C10-C28)	ND	25.0	1	02/09/26	02/10/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/09/26	02/10/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/09/26*	*02/10/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2606151
Chloride	**423**	20.0	1	02/06/26	02/07/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606153-BLK1)									Prepared: 02/06/26 Analyzed: 02/10/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.78*		*8.00*		*110*	*70-130*			
LCS (2606153-BS1)									Prepared: 02/06/26 Analyzed: 02/10/26
Benzene	4.95	0.0250	5.00		99.0	70-130			
Ethylbenzene	4.72	0.0250	5.00		94.5	70-130			
Toluene	4.85	0.0250	5.00		97.0	70-130			
o-Xylene	4.83	0.0250	5.00		96.7	70-130			
p,m-Xylene	9.63	0.0500	10.0		96.3	70-130			
Total Xylenes	14.5	0.0250	15.0		96.4	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.83*		*8.00*		*110*	*70-130*			
Matrix Spike (2606153-MS1)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/10/26
Benzene	4.92	0.0250	5.00	ND	98.4	70-130			
Ethylbenzene	4.69	0.0250	5.00	ND	93.8	70-130			
Toluene	4.82	0.0250	5.00	ND	96.4	70-130			
o-Xylene	4.82	0.0250	5.00	ND	96.3	70-130			
p,m-Xylene	9.55	0.0500	10.0	ND	95.5	70-130			
Total Xylenes	14.4	0.0250	15.0	ND	95.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.89*		*8.00*		*111*	*70-130*			
Matrix Spike Dup (2606153-MSD1)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/10/26
Benzene	5.05	0.0250	5.00	ND	101	70-130	2.52	27	
Ethylbenzene	4.82	0.0250	5.00	ND	96.5	70-130	2.86	26	
Toluene	4.95	0.0250	5.00	ND	98.9	70-130	2.58	20	
o-Xylene	4.96	0.0250	5.00	ND	99.2	70-130	2.92	25	
p,m-Xylene	9.84	0.0500	10.0	ND	98.4	70-130	3.01	23	
Total Xylenes	14.8	0.0250	15.0	ND	98.7	70-130	2.98	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.84*		*8.00*		*110*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606153-BLK1)									Prepared: 02/06/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.56*		*8.00*		*94.5*	*70-130*			
LCS (2606153-BS2)									Prepared: 02/06/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	51.2	20.0	50.0		102	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.56*		*8.00*		*94.4*	*70-130*			
Matrix Spike (2606153-MS2)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	52.5	20.0	50.0	ND	105	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.41*		*8.00*		*92.6*	*70-130*			
Matrix Spike Dup (2606153-MSD2)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	52.7	20.0	50.0	ND	105	70-130	0.399	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.51*		*8.00*		*93.8*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607020-BLK1)									Prepared: 02/09/26 Analyzed: 02/09/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*49.2*		*50.0*		*98.3*	*61-141*			
LCS (2607020-BS1)									Prepared: 02/09/26 Analyzed: 02/09/26
Diesel Range Organics (C10-C28)	250	25.0	250		99.9	66-144			
Surrogate: n-Nonane	*49.6*		*50.0*		*99.2*	*61-141*			
Matrix Spike (2607020-MS1)				**Source: E602071-08**					Prepared: 02/09/26 Analyzed: 02/09/26
Diesel Range Organics (C10-C28)	272	25.0	250	ND	109	56-156			
Surrogate: n-Nonane	*51.9*		*50.0*		*104*	*61-141*			
Matrix Spike Dup (2607020-MSD1)				**Source: E602071-08**					Prepared: 02/09/26 Analyzed: 02/09/26
Diesel Range Organics (C10-C28)	266	25.0	250	ND	107	56-156	2.10	20	
Surrogate: n-Nonane	*50.3*		*50.0*		*101*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/12/2026 12:31:11PM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606151-BLK1)									Prepared: 02/06/26 Analyzed: 02/06/26
Chloride	ND	20.0							
LCS (2606151-BS1)									Prepared: 02/06/26 Analyzed: 02/06/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2606151-MS1)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/06/26
Chloride	1090	20.0	250	824	106	80-120			
Matrix Spike Dup (2606151-MSD1)				**Source: E602071-04**					Prepared: 02/06/26 Analyzed: 02/06/26
Chloride	1190	20.0	250	824	148	80-120	9.30	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/12/26 12:31

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602071	Job Number 01058.0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
9:48	2/4/2026	S	1	FS18-5'		1						X			3.7
12:18	2/4/2026	S	1	FS19-5'		2						X			4.2
9:56	2/4/2026	S	1	FS26-4'		3						X			3.9
9:57	2/4/2026	S	1	FS27-4'		4						X			3.1
9:58	2/4/2026	S	1	FS29-4'		5						X			3.4
9:51	2/4/2026	S	1	FS39-5'		6						X			4.2
9:36	2/4/2026	S	1	FS104-2'		7						X			3.6
12:08	2/4/2026	S	1	FS105-3'		8						X			4.4
12:04	2/4/2026	S	1	FS107-3'		9						X			3.9
9:15	2/4/2026	S	1	FS111-2'		10						X			3.6

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/5/26	7:11	Michelle Gonzales	2-5-26	0711
Michelle Gonzales	2-5-26	1515	Nathan Gonzales	2-5-26	1515
Nathan Gonzales	2-5-26	1854	Johnny Archuleta	2-5-26	1854
Johnny Archuleta	2-5-26	2245		2.6.26	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: Y / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E002071	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
9:16	2/4/2026	S	1	FS112-2'		11						X			3.6
10:06	2/4/2026	S	1	SW03-0'-4'		12						X			3.4
12:22	2/4/2026	S	1	Sw05-0'-4'		13						X			3.2
12:29	2/4/2026	S	1	SW33-4'-10'		14						X			3.0
10:09	2/4/2026	S	1	SW34-4'-10'		15						X			2.8
12:30	2/4/2026	S	1	SW35-4'-10'		16						X			3.1
12:35	2/4/2026	S	1	SW37-4'-10'		17						X			3.8
12:37	2/4/2026	S	1	SW38-4'-10'		18						X			3.5

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, LL

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/5/26	7:11	Michelle Gonzales	2-5-26	0711
Michelle Gonzales	2-5-26	1515	Nathan Gonzales	2-5-26	1515
Nathan Gonzales	2-5-26	1954	Johnny Archuleta	2-5-26	1854
Johnny Archuleta	2-5-26	2245		2.6.26	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: Y / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/6/2026 3:42:11PM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/06/26 08:00	Work Order ID:	E602071
Phone:	(505) 382-1211	Date Logged In:	02/05/26 15:14	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/12/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	No	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Sample name on sample #5 container did not match name listed on COC.
L-NS
R-CM

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602091
Job Number:	01058-0007
Received:	2/7/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/13/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/13/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602091
Date Received: 2/7/2026 10:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/7/2026 10:15:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

BF02 5

QC Summary Data 6

QC - Volatile Organics by EPA 8021B 6

QC - Nonhalogenated Organics by EPA 8015D - GRO 7

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 8

QC - Anions by EPA 300.0/9056A 9

Definitions and Notes 10

Chain of Custody etc. 11

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/13/26 07:53

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
BF02	E602091-01A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:53:17AM

BF02

E602091-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2606166
Benzene	ND	0.0250	1	02/07/26	02/08/26	
Ethylbenzene	ND	0.0250	1	02/07/26	02/08/26	
Toluene	ND	0.0250	1	02/07/26	02/08/26	
o-Xylene	ND	0.0250	1	02/07/26	02/08/26	
p,m-Xylene	ND	0.0500	1	02/07/26	02/08/26	
Total Xylenes	ND	0.0250	1	02/07/26	02/08/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.1 %*	*70-130*	*02/07/26*	*02/08/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2606166
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/07/26	02/08/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*02/07/26*	*02/08/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607032
Diesel Range Organics (C10-C28)	ND	25.0	1	02/10/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/10/26	02/11/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/10/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2607009
Chloride	**71.1**	20.0	1	02/09/26	02/09/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:53:17AM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606166-BLK1)									Prepared: 02/07/26 Analyzed: 02/08/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.20*		*8.00*		*90.0*	*70-130*			
LCS (2606166-BS1)									Prepared: 02/07/26 Analyzed: 02/08/26
Benzene	4.88	0.0250	5.00		97.5	70-130			
Ethylbenzene	4.59	0.0250	5.00		91.7	70-130			
Toluene	4.77	0.0250	5.00		95.3	70-130			
o-Xylene	4.68	0.0250	5.00		93.6	70-130			
p,m-Xylene	9.35	0.0500	10.0		93.5	70-130			
Total Xylenes	14.0	0.0250	15.0		93.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.37*		*8.00*		*92.1*	*70-130*			
Matrix Spike (2606166-MS1)				**Source: E602087-03**					Prepared: 02/07/26 Analyzed: 02/08/26
Benzene	5.06	0.0250	5.00	ND	101	70-130			
Ethylbenzene	4.79	0.0250	5.00	ND	95.8	70-130			
Toluene	4.96	0.0250	5.00	ND	99.3	70-130			
o-Xylene	4.88	0.0250	5.00	ND	97.6	70-130			
p,m-Xylene	9.75	0.0500	10.0	ND	97.5	70-130			
Total Xylenes	14.6	0.0250	15.0	ND	97.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.41*		*8.00*		*92.6*	*70-130*			
Matrix Spike Dup (2606166-MSD1)				**Source: E602087-03**					Prepared: 02/07/26 Analyzed: 02/08/26
Benzene	4.92	0.0250	5.00	ND	98.4	70-130	2.84	27	
Ethylbenzene	4.66	0.0250	5.00	ND	93.1	70-130	2.78	26	
Toluene	4.82	0.0250	5.00	ND	96.4	70-130	2.95	20	
o-Xylene	4.74	0.0250	5.00	ND	94.7	70-130	2.98	25	
p,m-Xylene	9.50	0.0500	10.0	ND	95.0	70-130	2.56	23	
Total Xylenes	14.2	0.0250	15.0	ND	94.9	70-130	2.70	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.45*		*8.00*		*93.1*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:53:17AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2606166-BLK1)									Prepared: 02/07/26 Analyzed: 02/08/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.36*		*8.00*		*92.0*	*70-130*			
LCS (2606166-BS2)									Prepared: 02/07/26 Analyzed: 02/08/26
Gasoline Range Organics (C6-C10)	50.4	20.0	50.0		101	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.54*		*8.00*		*94.3*	*70-130*			
Matrix Spike (2606166-MS2)				**Source: E602087-03**					Prepared: 02/07/26 Analyzed: 02/08/26
Gasoline Range Organics (C6-C10)	49.4	20.0	50.0	ND	98.7	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.59*		*8.00*		*94.8*	*70-130*			
Matrix Spike Dup (2606166-MSD2)				**Source: E602087-03**					Prepared: 02/07/26 Analyzed: 02/08/26
Gasoline Range Organics (C6-C10)	47.5	20.0	50.0	ND	94.9	70-130	3.97	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.41*		*8.00*		*92.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:53:17AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607032-BLK1)									Prepared: 02/10/26 Analyzed: 02/10/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*53.7*		*50.0*		*107*	*61-141*			
LCS (2607032-BS1)									Prepared: 02/10/26 Analyzed: 02/10/26
Diesel Range Organics (C10-C28)	239	25.0	250		95.5	66-144			
Surrogate: n-Nonane	*54.5*		*50.0*		*109*	*61-141*			
Matrix Spike (2607032-MS1)				**Source: E602064-07**					Prepared: 02/10/26 Analyzed: 02/10/26
Diesel Range Organics (C10-C28)	243	25.0	250	ND	97.1	56-156			
Surrogate: n-Nonane	*55.6*		*50.0*		*111*	*61-141*			
Matrix Spike Dup (2607032-MSD1)				**Source: E602064-07**					Prepared: 02/10/26 Analyzed: 02/10/26
Diesel Range Organics (C10-C28)	236	25.0	250	ND	94.5	56-156	2.66	20	
Surrogate: n-Nonane	*54.5*		*50.0*		*109*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:53:17AM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607009-BLK1)									Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	ND	20.0							
LCS (2607009-BS1)									Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	255	20.0	250		102	90-110			
Matrix Spike (2607009-MS1)				**Source: E602074-06**					Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	402	20.0	250	151	101	80-120			
Matrix Spike Dup (2607009-MSD1)				**Source: E602074-06**					Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	406	20.0	250	151	102	80-120	0.941	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/13/26 07:53

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479.01.ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602091	1D 2D 3D Std	NM CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	Job Number 21058.0007	X	X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
9:26	2/5/2026	S	1	BF02		1						X			2.9

Analysis and Method

EPA Program

SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, LL

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/6/26	7:11	Michelle Gonzales	2-6-26	0711
Michelle Gonzales	2-6-26	1515	Nathan Gonzales	2-6-26	1515
Nathan Gonzales	2-6-26	1940	Johnny Archuleta	2-6-26	1940
Johnny Archuleta	2-6-26	2330	Caitlin Mason	2.7.26	1015

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: Y / N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/9/2026 10:16:07AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/07/26 10:15	Work Order ID:	E602091
Phone:	(505) 382-1211	Date Logged In:	02/06/26 16:42	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/13/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-RAS
R-CM

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602092
Job Number:	01058-0007
Received:	2/7/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/13/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/13/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602092
Date Received: 2/7/2026 10:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/7/2026 10:15:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

FS12-4’ 6

FS20-4’ 7

FS35-6’ 8

FS53-4’ 9

FS54-4’ 10

FS55-4’ 11

FS56-4’ 12

SW11-0’-4’ 13

SW12-0’-4’ 14

SW13-0’-4’ 15

SW14-0’-4’ 16

SW15-0’-4’ 17

SW16-0’-4’ 18

SW26-0’-4’ 19

QC Summary Data 20

QC - Volatile Organics by EPA 8021B 20

QC - Nonhalogenated Organics by EPA 8015D - GRO 21

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 22

QC - Anions by EPA 300.0/9056A 23

Definitions and Notes 24

Table of Contents (continued)

Chain of Custody etc. 25

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/13/26 07:55

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS12-4'	E602092-01A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS20-4'	E602092-02A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS35-6'	E602092-03A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS53-4'	E602092-04A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS54-4'	E602092-05A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS55-4'	E602092-06A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
FS56-4'	E602092-07A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW11-0'-4'	E602092-08A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW12-0'-4'	E602092-09A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW13-0'-4'	E602092-10A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW14-0'-4'	E602092-11A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW15-0'-4'	E602092-12A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW16-0'-4'	E602092-13A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.
SW26-0'-4'	E602092-14A	Soil	02/05/26	02/07/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS12-4'

E602092-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/10/26	
Toluene	ND	0.0250	1	02/09/26	02/10/26	
o-Xylene	ND	0.0250	1	02/09/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.0 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**83.6**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS20-4'

E602092-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/10/26	
Toluene	ND	0.0250	1	02/09/26	02/10/26	
o-Xylene	ND	0.0250	1	02/09/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.7 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*97.9 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**391**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS35-6'

E602092-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/10/26	
Toluene	ND	0.0250	1	02/09/26	02/10/26	
o-Xylene	ND	0.0250	1	02/09/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.8 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	**481**	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	**319**	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*98.3 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**552**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS53-4'

E602092-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/10/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/10/26	
Toluene	ND	0.0250	1	02/09/26	02/10/26	
o-Xylene	ND	0.0250	1	02/09/26	02/10/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/10/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/10/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.4 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/10/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*114 %*	*70-130*	*02/09/26*	*02/10/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	**34.4**	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*97.8 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**645**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS54-4'

E602092-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	**0.0472**	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.3 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	**40.3**	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*99.4 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**485**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS55-4'

E602092-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	**0.0270**	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*98.3 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*121 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	**241**	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	**172**	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**153**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

FS56-4'

E602092-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.7 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	**45.2**	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*100 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**77.2**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW11-0'-4'

E602092-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.1 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*116 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*95.5 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW12-0'-4'

E602092-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.8 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/11/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/11/26	
Surrogate: n-Nonane		*99.6 %*	*61-141*	*02/11/26*	*02/11/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW13-0'-4'

E602092-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.0 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/12/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/12/26	
Surrogate: n-Nonane		*99.2 %*	*61-141*	*02/11/26*	*02/12/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW14-0'-4'

E602092-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.7 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/12/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/12/26	
Surrogate: n-Nonane		*96.8 %*	*61-141*	*02/11/26*	*02/12/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW15-0'-4'

E602092-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.6 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/12/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/12/26	
Surrogate: n-Nonane		*99.0 %*	*61-141*	*02/11/26*	*02/12/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW16-0'-4'

E602092-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*98.0 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/12/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/12/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/11/26*	*02/12/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	**29.2**	20.0	1	02/09/26	02/09/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

SW26-0'-4'

E602092-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Benzene	ND	0.0250	1	02/09/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/09/26	02/11/26	
Toluene	ND	0.0250	1	02/09/26	02/11/26	
o-Xylene	ND	0.0250	1	02/09/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/09/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/09/26	02/11/26	
Surrogate: 4-Bromochlorobenzene-PID		*98.4 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607001
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/09/26	02/11/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/09/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2607055
Diesel Range Organics (C10-C28)	ND	25.0	1	02/11/26	02/12/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/11/26	02/12/26	
Surrogate: n-Nonane		*97.2 %*	*61-141*	*02/11/26*	*02/12/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607010
Chloride	ND	20.0	1	02/09/26	02/09/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607001-BLK1)									Prepared: 02/09/26 Analyzed: 02/10/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.75*		*8.00*		*96.9*	*70-130*			
LCS (2607001-BS1)									Prepared: 02/09/26 Analyzed: 02/10/26
Benzene	4.43	0.0250	5.00		88.5	70-130			
Ethylbenzene	4.23	0.0250	5.00		84.5	70-130			
Toluene	4.38	0.0250	5.00		87.7	70-130			
o-Xylene	4.29	0.0250	5.00		85.9	70-130			
p,m-Xylene	8.68	0.0500	10.0		86.8	70-130			
Total Xylenes	13.0	0.0250	15.0		86.5	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.80*		*8.00*		*97.5*	*70-130*			
Matrix Spike (2607001-MS1)				**Source: E602092-04**					Prepared: 02/09/26 Analyzed: 02/10/26
Benzene	4.74	0.0250	5.00	ND	94.9	70-130			
Ethylbenzene	4.51	0.0250	5.00	ND	90.2	70-130			
Toluene	4.69	0.0250	5.00	ND	93.8	70-130			
o-Xylene	4.58	0.0250	5.00	ND	91.5	70-130			
p,m-Xylene	9.25	0.0500	10.0	ND	92.5	70-130			
Total Xylenes	13.8	0.0250	15.0	ND	92.2	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.66*		*8.00*		*95.7*	*70-130*			
Matrix Spike Dup (2607001-MSD1)				**Source: E602092-04**					Prepared: 02/09/26 Analyzed: 02/10/26
Benzene	4.08	0.0250	5.00	ND	81.6	70-130	15.1	27	
Ethylbenzene	3.85	0.0250	5.00	ND	77.0	70-130	15.8	26	
Toluene	4.02	0.0250	5.00	ND	80.3	70-130	15.5	20	
o-Xylene	3.90	0.0250	5.00	ND	77.9	70-130	16.1	25	
p,m-Xylene	7.92	0.0500	10.0	ND	79.1	70-130	15.6	23	
Total Xylenes	11.8	0.0250	15.0	ND	78.7	70-130	15.7	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.77*		*8.00*		*97.1*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607001-BLK1)									Prepared: 02/09/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.15*		*8.00*		*114*	*70-130*			
LCS (2607001-BS2)									Prepared: 02/09/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	50.1	20.0	50.0		100	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.27*		*8.00*		*116*	*70-130*			
Matrix Spike (2607001-MS2)				**Source: E602092-04**					Prepared: 02/09/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	49.0	20.0	50.0	ND	98.1	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.11*		*8.00*		*114*	*70-130*			
Matrix Spike Dup (2607001-MSD2)				**Source: E602092-04**					Prepared: 02/09/26 Analyzed: 02/10/26
Gasoline Range Organics (C6-C10)	49.1	20.0	50.0	ND	98.2	70-130	0.118	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.26*		*8.00*		*116*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607055-BLK1)									Prepared: 02/11/26 Analyzed: 02/11/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*48.6*		*50.0*		*97.2*	*61-141*			
LCS (2607055-BS1)									Prepared: 02/11/26 Analyzed: 02/11/26
Diesel Range Organics (C10-C28)	260	25.0	250		104	66-144			
Surrogate: n-Nonane	*48.2*		*50.0*		*96.4*	*61-141*			
Matrix Spike (2607055-MS1)				**Source: E602092-01**					Prepared: 02/11/26 Analyzed: 02/11/26
Diesel Range Organics (C10-C28)	253	25.0	250	ND	101	56-156			
Surrogate: n-Nonane	*47.9*		*50.0*		*95.9*	*61-141*			
Matrix Spike Dup (2607055-MSD1)				**Source: E602092-01**					Prepared: 02/11/26 Analyzed: 02/11/26
Diesel Range Organics (C10-C28)	257	25.0	250	ND	103	56-156	1.56	20	
Surrogate: n-Nonane	*49.1*		*50.0*		*98.2*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/13/2026 7:55:41AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607010-BLK1)									Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	ND	20.0							
LCS (2607010-BS1)									Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	263	20.0	250		105	90-110			
Matrix Spike (2607010-MS1)				**Source: E602090-01**					Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	594	20.0	250	326	107	80-120			
Matrix Spike Dup (2607010-MSD1)				**Source: E602090-01**					Prepared: 02/09/26 Analyzed: 02/09/26
Chloride	591	20.0	250	326	106	80-120	0.377	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/13/26 07:55

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

E602092

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602092	Job Number 01058.0007	1D 2D 3D Std: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			NM CO UT TX: X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220	CM 2/7/26		
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method

EPA Program

SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
13:17	2/5/2026	S	1	FS12-4'		1						X			2.4
13:21	2/5/2026	S	1	FS20-4'		2						X			2.9
11:46	2/5/2026	S	1	FS35-6'		3						X			2.2
9:21	2/5/2026	S	1	FS53-4'		4						X			2.2
9:22	2/5/2026	S	1	FS54-4'		5						X			2.3
10:01	2/5/2026	S	1	FS55-4'		6						X			1.9
10:09	2/5/2026	S	1	FS56-4'		7						X			2.7
10:08	2/5/2026	S	1	SW11-0'-4'		8						X			2.1
9:24	2/5/2026	S	1	SW12-0'-4'		9						X			2.2
13:18	2/5/2026	S	1	SW13-0'-4'		10						X			1.6

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, LL

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/6/26	7:11	Michelle Gonzales	2-6-26	0711
Michelle Gonzales	2-6-26	1515	Nathan Gonzales	2-6-26	1515
Nathan Gonzales	2-6-26	1940	Johnny Archuleta	2-6-26	1940
Johnny Archuleta	2-6-26	2330		2.7.26	1015

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: Y / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602092	Job Number 01058:0007	1D 2D 3D Std: — — — X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
11:13	2/5/2026	S	1	SW14-0'-4'		11						X						1.0
10:07	2/5/2026	S	1	SW15-0'-4'		12						X						0.9
10:12	2/5/2026	S	1	SW16-0'-4'		13						X						1.3
13:25	2/5/2026	S	1	SW26-0'-4'		14						X						1.4

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: AK, LL

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/6/26	7:11	Michelle Gonzales	2-6-26	0711
Michelle Gonzales	2-6-26	1515	Nathan Gonzales	2-6-26	1515
Nathan Gonzales	2-6-26	1940	Johnny Archuleta	2-6-26	1940
Johnny Archuleta	2-6-26	2330	Caitlin Mars	2-7-26	1015

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 T2 T3

AVG Temp °C

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Page 607 of 624

Envirotech Analytical Laboratory

Printed: 2/9/2026 10:21:27AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/07/26 10:15	Work Order ID:	E602092
Phone:	(505) 382-1211	Date Logged In:	02/06/26 16:43	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/13/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-RAS
R-CM

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602110
Job Number:	01058-0007
Received:	2/10/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/16/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/16/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602110
Date Received: 2/10/2026 6:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/10/2026 6:15:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS44-7’ 5
- FS46-6’ 6
- FS57-4’ 7
- FS58-4’ 8
- FS100-3’ 9
- FS101-2’ 10
- FS102-2’ 11
- SW09-0’-4’ 12
- SW10-0’-4’ 13
- SW17-0’-4’ 14

QC Summary Data 15

- QC - Volatile Organic Compounds by EPA8260B 15
- QC - Nonhalogenated Organics by EPA 8015D - GRO 16
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 17
- QC - Anions by EPA 300.0/9056A 18

Definitions and Notes 19

Chain of Custody etc. 20

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/16/26 11:35

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS44-7'	E602110-01A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS46-6'	E602110-02A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS57-4'	E602110-03A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS58-4'	E602110-04A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS100-3'	E602110-05A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS101-2'	E602110-06A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
FS102-2'	E602110-07A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
SW09-0'-4'	E602110-08A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
SW10-0'-4'	E602110-09A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.
SW17-0'-4'	E602110-10A	Soil	02/06/26	02/10/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS44-7'

E602110-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*107 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*98.8 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*107 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*107 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*98.8 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*107 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	**1750**	25.0	1	02/12/26	02/14/26	
Oil Range Organics (C28-C36)	**791**	50.0	1	02/12/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/12/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**2030**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS46-6'

E602110-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*99.1 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*99.1 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	**391**	25.0	1	02/12/26	02/15/26	
Oil Range Organics (C28-C36)	**299**	50.0	1	02/12/26	02/15/26	
Surrogate: n-Nonane		*98.1 %*	*61-141*	*02/12/26*	*02/15/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**1620**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS57-4'

E602110-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*97.9 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*103 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*97.9 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/15/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/15/26	
Surrogate: n-Nonane		*96.5 %*	*61-141*	*02/12/26*	*02/15/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**966**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS58-4'

E602110-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*104 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*96.5 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*104 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*96.5 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/14/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/12/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**1480**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS100-3'

E602110-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*101 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*101 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*104 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	**49.6**	25.0	1	02/12/26	02/14/26	
Oil Range Organics (C28-C36)	**68.2**	50.0	1	02/12/26	02/14/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/12/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**230**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS101-2'

E602110-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*101 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*101 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/14/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/12/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**223**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

FS102-2'

E602110-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*96.0 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*96.0 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/14/26	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*02/12/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**290**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

SW09-0'-4'

E602110-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*97.1 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*97.1 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/15/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/15/26	
Surrogate: n-Nonane		*99.7 %*	*61-141*	*02/12/26*	*02/15/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**66.6**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

SW10-0'-4'

E602110-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*100 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/15/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/15/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/12/26*	*02/15/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	**21.8**	20.0	1	02/11/26	02/11/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

SW17-0'-4'

E602110-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organic Compounds by EPA 8260B	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Benzene	ND	0.0250	1	02/10/26	02/11/26	
Ethylbenzene	ND	0.0250	1	02/10/26	02/11/26	
Toluene	ND	0.0250	1	02/10/26	02/11/26	
o-Xylene	ND	0.0250	1	02/10/26	02/11/26	
p,m-Xylene	ND	0.0500	1	02/10/26	02/11/26	
Total Xylenes	ND	0.0250	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*94.9 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2607053
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/10/26	02/11/26	
Surrogate: Bromofluorobenzene		*102 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: 1,2-Dichloroethane-d4		*94.9 %*	*70-130*	*02/10/26*	*02/11/26*	
Surrogate: Toluene-d8		*105 %*	*70-130*	*02/10/26*	*02/11/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607096
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/15/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/15/26	
Surrogate: n-Nonane		*98.9 %*	*61-141*	*02/12/26*	*02/15/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2607071
Chloride	ND	20.0	1	02/11/26	02/11/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

Volatile Organic Compounds by EPA 8260B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607053-BLK1)									Prepared: 02/10/26 Analyzed: 02/11/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: Bromofluorobenzene	*0.507*		*0.500*		*101*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.482*		*0.500*		*96.3*	*70-130*			
Surrogate: Toluene-d8	*0.530*		*0.500*		*106*	*70-130*			
LCS (2607053-BS1)									Prepared: 02/10/26 Analyzed: 02/11/26
Benzene	2.13	0.0250	2.50		85.3	70-130			
Ethylbenzene	2.15	0.0250	2.50		86.2	70-130			
Toluene	2.10	0.0250	2.50		83.9	70-130			
o-Xylene	2.12	0.0250	2.50		84.8	70-130			
p,m-Xylene	4.26	0.0500	5.00		85.1	70-130			
Total Xylenes	6.38	0.0250	7.50		85.0	70-130			
Surrogate: Bromofluorobenzene	*0.494*		*0.500*		*98.8*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.500*		*0.500*		*99.9*	*70-130*			
Surrogate: Toluene-d8	*0.521*		*0.500*		*104*	*70-130*			
Matrix Spike (2607053-MS1)				**Source: E602122-02**					Prepared: 02/10/26 Analyzed: 02/11/26
Benzene	1.85	0.0250	2.50	ND	74.0	48-131			
Ethylbenzene	1.84	0.0250	2.50	ND	73.4	45-135			
Toluene	1.80	0.0250	2.50	ND	71.9	48-130			
o-Xylene	1.83	0.0250	2.50	ND	73.3	43-135			
p,m-Xylene	3.71	0.0500	5.00	ND	74.1	43-135			
Total Xylenes	5.54	0.0250	7.50	ND	73.9	43-135			
Surrogate: Bromofluorobenzene	*0.497*		*0.500*		*99.4*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.495*		*0.500*		*99.0*	*70-130*			
Surrogate: Toluene-d8	*0.516*		*0.500*		*103*	*70-130*			
Matrix Spike Dup (2607053-MSD1)				**Source: E602122-02**					Prepared: 02/10/26 Analyzed: 02/11/26
Benzene	2.18	0.0250	2.50	ND	87.2	48-131	16.4	23	
Ethylbenzene	2.18	0.0250	2.50	ND	87.3	45-135	17.3	27	
Toluene	2.13	0.0250	2.50	ND	85.4	48-130	17.1	24	
o-Xylene	2.21	0.0250	2.50	ND	88.4	43-135	18.6	27	
p,m-Xylene	4.44	0.0500	5.00	ND	88.8	43-135	17.9	27	
Total Xylenes	6.65	0.0250	7.50	ND	88.6	43-135	18.2	27	
Surrogate: Bromofluorobenzene	*0.507*		*0.500*		*101*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.482*		*0.500*		*96.4*	*70-130*			
Surrogate: Toluene-d8	*0.515*		*0.500*		*103*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607053-BLK1)									Prepared: 02/10/26 Analyzed: 02/11/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: Bromofluorobenzene	*0.507*		*0.500*		*101*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.482*		*0.500*		*96.3*	*70-130*			
Surrogate: Toluene-d8	*0.530*		*0.500*		*106*	*70-130*			
LCS (2607053-BS2)									Prepared: 02/10/26 Analyzed: 02/11/26
Gasoline Range Organics (C6-C10)	42.3	20.0	50.0		84.7	70-130			
Surrogate: Bromofluorobenzene	*0.508*		*0.500*		*102*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.497*		*0.500*		*99.4*	*70-130*			
Surrogate: Toluene-d8	*0.529*		*0.500*		*106*	*70-130*			
Matrix Spike (2607053-MS2)				**Source: E602122-02**					Prepared: 02/10/26 Analyzed: 02/11/26
Gasoline Range Organics (C6-C10)	49.3	20.0	50.0	ND	98.5	70-130			
Surrogate: Bromofluorobenzene	*0.504*		*0.500*		*101*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.503*		*0.500*		*101*	*70-130*			
Surrogate: Toluene-d8	*0.530*		*0.500*		*106*	*70-130*			
Matrix Spike Dup (2607053-MSD2)				**Source: E602122-02**					Prepared: 02/10/26 Analyzed: 02/11/26
Gasoline Range Organics (C6-C10)	44.0	20.0	50.0	ND	88.1	70-130	11.2	20	
Surrogate: Bromofluorobenzene	*0.511*		*0.500*		*102*	*70-130*			
Surrogate: 1,2-Dichloroethane-d4	*0.494*		*0.500*		*98.7*	*70-130*			
Surrogate: Toluene-d8	*0.525*		*0.500*		*105*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607096-BLK1)									Prepared: 02/12/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*49.2*		*50.0*		*98.4*	*61-141*			
LCS (2607096-BS1)									Prepared: 02/12/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	260	25.0	250		104	66-144			
Surrogate: n-Nonane	*50.4*		*50.0*		*101*	*61-141*			
Matrix Spike (2607096-MS1)				**Source: E602110-08**					Prepared: 02/12/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	286	25.0	250	ND	114	56-156			
Surrogate: n-Nonane	*53.3*		*50.0*		*107*	*61-141*			
Matrix Spike Dup (2607096-MSD1)				**Source: E602110-08**					Prepared: 02/12/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	281	25.0	250	ND	112	56-156	1.83	20	
Surrogate: n-Nonane	*52.4*		*50.0*		*105*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/16/2026 11:35:41AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607071-BLK1)									Prepared: 02/11/26 Analyzed: 02/11/26
Chloride	ND	20.0							
LCS (2607071-BS1)									Prepared: 02/11/26 Analyzed: 02/11/26
Chloride	251	20.0	250		100	90-110			
Matrix Spike (2607071-MS1)				**Source: E602110-08**					Prepared: 02/11/26 Analyzed: 02/11/26
Chloride	322	20.0	250	66.6	102	80-120			
Matrix Spike Dup (2607071-MSD1)				**Source: E602110-08**					Prepared: 02/11/26 Analyzed: 02/11/26
Chloride	325	20.0	250	66.6	103	80-120	1.02	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/16/26 11:35

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

1E-176479.01.ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602110	Job Number 01058-0007	1D 2D 3D Std: — — — X	NM CO UT TX: X — — —
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
8:53	2/6/2026	S	1	FS44-7'		1						X						4.9
8:44	2/6/2026	S	1	FS46-6'		2						X						4.0
8:37	2/6/2026	S	1	FS57-4'		3						X						3.7
9:49	2/6/2026	S	1	FS58-4'		4						X						4.2
8:28	2/6/2026	S	1	FS100-3'		5						X						4.6
9:27	2/6/2026	S	1	FS101-2'		6						X						4.4
9:28	2/6/2026	S	1	FS102-2'		7						X						3.9
10:19	2/6/2026	S	1	SW09-0'-4'		8						X						3.6
8:43	2/6/2026	S	1	SW10-0'-4'		9						X						4.0
10:20	2/6/2026	S	1	SW17-0'-4'		10						X						3.9

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, LL

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/9/26	7:11	Michelle Gonzales	2-9-26	0711
Michelle Gonzales	2-9-26	1545	Marissa Gonzales	2-9-26	1545
Marissa Gonzales	2-9-26	1940	Johnny Archuleta	2-9-26	1940
Johnny Archuleta	2-9-26	2330	Nel Sets	2-10-26	0615

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: Y / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/10/2026 9:24:32AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/10/26 06:15	Work Order ID:	E602110
Phone:	(505) 382-1211	Date Logged In:	02/09/26 14:29	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/16/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	No	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Sample name on on sample #9 does not match name on COC.
L-NS
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602127
Job Number:	01058-0007
Received:	2/11/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/17/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/17/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602127
Date Received: 2/11/2026 6:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/11/2026 6:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS08-11’ 5
- FS07-10’ 6
- SW36-4’-10’ 7
- FS59-5’ 8
- FS65-4’ 9
- FS77-5’ 10
- FS79-4’ 11
- FS99-4’ 12

QC Summary Data 13

- QC - Volatile Organics by EPA 8021B 13
- QC - Nonhalogenated Organics by EPA 8015D - GRO 14
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 15
- QC - Anions by EPA 300.0/9056A 16

Definitions and Notes 17

Chain of Custody etc. 18

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/17/26 13:22

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS08-11'	E602127-01A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS07-10'	E602127-02A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
SW36-4'-10'	E602127-03A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS59-5'	E602127-04A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS65-4'	E602127-05A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS77-5'	E602127-06A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS79-4'	E602127-07A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.
FS99-4'	E602127-08A	Soil	02/09/26	02/11/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS08-11'

E602127-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.4 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**562**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	**313**	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*118 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**22.2**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS07-10'

E602127-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.8 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**924**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	**400**	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*115 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	ND	40.0	2	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

SW36-4'-10'

E602127-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.5 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*117 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**1070**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS59-5'

E602127-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.6 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	ND	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*112 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**2080**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS65-4'

E602127-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.8 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**84.8**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**1660**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS77-5'

E602127-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.4 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**455**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	**262**	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**1310**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS79-4'

E602127-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.2 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*120 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**80.2**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	**58.1**	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**865**	20.0	1	02/12/26	02/12/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

FS99-4'

E602127-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Benzene	ND	0.0250	1	02/11/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/11/26	02/13/26	
Toluene	ND	0.0250	1	02/11/26	02/13/26	
o-Xylene	ND	0.0250	1	02/11/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/11/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/11/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.6 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607063
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/11/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/11/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607132
Diesel Range Organics (C10-C28)	**457**	25.0	1	02/12/26	02/13/26	
Oil Range Organics (C28-C36)	**445**	50.0	1	02/12/26	02/13/26	
Surrogate: n-Nonane		*115 %*	*61-141*	*02/12/26*	*02/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607100
Chloride	**534**	20.0	1	02/12/26	02/12/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607063-BLK1)									Prepared: 02/11/26 Analyzed: 02/13/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.77*		*8.00*		*97.2*	*70-130*			
LCS (2607063-BS1)									Prepared: 02/11/26 Analyzed: 02/13/26
Benzene	3.73	0.0250	5.00		74.6	70-130			
Ethylbenzene	3.80	0.0250	5.00		76.1	70-130			
Toluene	3.87	0.0250	5.00		77.3	70-130			
o-Xylene	3.89	0.0250	5.00		77.9	70-130			
p,m-Xylene	7.82	0.0500	10.0		78.2	70-130			
Total Xylenes	11.7	0.0250	15.0		78.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.97*		*8.00*		*99.7*	*70-130*			
Matrix Spike (2607063-MS1)				**Source: E602126-08**					Prepared: 02/11/26 Analyzed: 02/13/26
Benzene	4.12	0.0250	5.00	ND	82.3	70-130			
Ethylbenzene	4.22	0.0250	5.00	ND	84.5	70-130			
Toluene	4.29	0.0250	5.00	ND	85.8	70-130			
o-Xylene	4.30	0.0250	5.00	ND	85.9	70-130			
p,m-Xylene	8.67	0.0500	10.0	ND	86.6	70-130			
Total Xylenes	13.0	0.0250	15.0	ND	86.4	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.79*		*8.00*		*97.4*	*70-130*			
Matrix Spike Dup (2607063-MSD1)				**Source: E602126-08**					Prepared: 02/11/26 Analyzed: 02/13/26
Benzene	4.21	0.0250	5.00	ND	84.3	70-130	2.35	27	
Ethylbenzene	4.37	0.0250	5.00	ND	87.5	70-130	3.46	26	
Toluene	4.42	0.0250	5.00	ND	88.4	70-130	3.02	20	
o-Xylene	4.45	0.0250	5.00	ND	88.9	70-130	3.39	25	
p,m-Xylene	8.97	0.0500	10.0	ND	89.7	70-130	3.44	23	
Total Xylenes	13.4	0.0250	15.0	ND	89.4	70-130	3.42	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.95*		*8.00*		*99.4*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607063-BLK1)									Prepared: 02/11/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.43*		*8.00*		*118*	*70-130*			
LCS (2607063-BS2)									Prepared: 02/11/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	41.8	20.0	50.0		83.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.28*		*8.00*		*116*	*70-130*			
Matrix Spike (2607063-MS2)				**Source: E602126-08**					Prepared: 02/11/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	49.8	20.0	50.0	ND	99.7	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.41*		*8.00*		*118*	*70-130*			
Matrix Spike Dup (2607063-MSD2)				**Source: E602126-08**					Prepared: 02/11/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	49.7	20.0	50.0	ND	99.4	70-130	0.287	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.45*		*8.00*		*118*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607132-BLK1)									Prepared: 02/12/26 Analyzed: 02/13/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*58.2*		*50.0*		*116*	*61-141*			
LCS (2607132-BS1)									Prepared: 02/12/26 Analyzed: 02/13/26
Diesel Range Organics (C10-C28)	231	25.0	250		92.3	66-144			
Surrogate: n-Nonane	*56.7*		*50.0*		*113*	*61-141*			
Matrix Spike (2607132-MS1)				**Source: E602127-02**					Prepared: 02/12/26 Analyzed: 02/13/26
Diesel Range Organics (C10-C28)	1550	25.0	250	924	249	56-156			M4
Surrogate: n-Nonane	*56.2*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2607132-MSD1)				**Source: E602127-02**					Prepared: 02/12/26 Analyzed: 02/13/26
Diesel Range Organics (C10-C28)	1320	25.0	250	924	158	56-156	16.0	20	M4
Surrogate: n-Nonane	*55.4*		*50.0*		*111*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/17/2026 1:22:25PM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607100-BLK1)									Prepared: 02/12/26 Analyzed: 02/12/26
Chloride	ND	20.0							
LCS (2607100-BS1)									Prepared: 02/12/26 Analyzed: 02/12/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2607100-MS1)				**Source: E602149-02**					Prepared: 02/12/26 Analyzed: 02/12/26
Chloride	337	20.0	250	78.9	103	80-120			
Matrix Spike Dup (2607100-MSD1)				**Source: E602149-02**					Prepared: 02/12/26 Analyzed: 02/12/26
Chloride	333	20.0	250	78.9	101	80-120	1.41	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/17/26 13:22

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602127	Job Number 01058.0007	1D 2D 3D Std: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			NM: X; CO UT TX
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Analysis and Method: DRO/ORO by 8015; GRO/DRO by 8015; BTEX by 8021; VOC by 8260; Chloride 300.0; BGDOC - NM; TCEQ 1005 TX; RCRA 8 Metals

EPA Program: SDWA | CWA | RCRA; Compliance Y or N; PWSID #

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	BGDOC - NM	Remarks
14:04	2/9/2026	S	1	FS08-11'		1	X	2.8
12:50	2/9/2026	S	1	FS07-10'		2	X	3.5
12:49	2/9/2026	S	1	SW36-4' – 10'		3	X	3.0
11:07	2/9/2026	S	1	FS59-5'		4	X	3.5
12:44	2/9/2026	S	1	FS65-4'		5	X	3.9
14:35	2/9/2026	S	1	FS77-5'		6	X	3.1
12:47	2/9/2026	S	1	FS79-4'		7	X	3.3
9:48	2/9/2026	S	1	FS99-4'		8	X	3.1

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: AK, JH

Corrected sample depth per A.H. 2/11/26 CM

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/10/26	7:11	Michelle Gonzales	2.10.26	0711
Michelle Gonzales	2.10.26	1415	Maghan Gonzales	2.10.26	1415
Maghan Gonzales	2.10.26	1800	Johnny Archuleta	2.10.26	1800
Johnny Archuleta	2.10.26	2345	Noe Soto	2-11-26	0630

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only: Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602127	Job Number 01058.0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
14:04	2/9/2026	S	1	FS08-11'		1						X			2.8
12:50	2/9/2026	S	1	FS07-10'		2						X			3.5
12:49	2/9/2026	S	1	SW36-4'		3						X			3.0
11:07	2/9/2026	S	1	FS59-5'		4						X			3.5
12:44	2/9/2026	S	1	FS65-4'		5						X			3.9
14:35	2/9/2026	S	1	FS77-5'		6						X			3.1
12:47	2/9/2026	S	1	FS79-4'		7						X			3.3
9:48	2/9/2026	S	1	FS99-4'		8						X			3.1

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, JH

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/10/26	7:11	Michelle Gonzales	2.10.26	0711
Michelle Gonzales	2-10 26	1415	Nathan Gonzales	210.26	1415
Nathan Gonzales	2-10-26	1800	Johnny Archuleta	2-10-26	1800
Johnny Archuleta	2-10-26	2245	Noe Soto	2-11-26	0630

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/11/2026 8:38:03AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/11/26 06:30	Work Order ID:	E602127
Phone:	(505) 382-1211	Date Logged In:	02/10/26 15:47	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	02/17/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	No	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

Sample #3 name on container does not match name on COC.
L-NS
R-DT

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602144
Job Number:	01058-0007
Received:	2/12/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/18/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/18/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602144
Date Received: 2/12/2026 6:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/12/2026 6:00:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

- FS10-4’ 6
- FS11-4’ 7
- FS14-4’ 8
- FS25-4’ 9
- FS30-8’ 10
- FS81-4’ 11
- FS84-4’ 12
- FS85-4’ 13
- FS103-9’ 14
- SW02-0’-4’ 15
- SW06-0’-4’ 16
- SW07-0’-4’ 17
- SW24-0’-4’ 18
- SW29-0’-2’ 19
- SW30-0’-5’ 20
- SW31-0’-4’ 21
- SW32-0’-4’ 22

QC Summary Data 23

- QC - Volatile Organics by EPA 8021B 23
- QC - Nonhalogenated Organics by EPA 8015D - GRO 24

Table of Contents (continued)

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 25

QC - Anions by EPA 300.0/9056A 26

Definitions and Notes 27

Chain of Custody etc. 28

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/18/26 11:03

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS10-4'	E602144-01A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS11-4'	E602144-02A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS14-4'	E602144-03A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS25-4'	E602144-04A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS30-8'	E602144-05A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS81-4'	E602144-06A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS84-4'	E602144-07A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS85-4'	E602144-08A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
FS103-9'	E602144-09A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW02-0'-4'	E602144-10A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW06-0'-4'	E602144-11A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW07-0'-4'	E602144-12A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW24-0'-4'	E602144-13A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW29-0'-2'	E602144-14A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW30-0'-5'	E602144-15A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW31-0'-4'	E602144-16A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.
SW32-0'-4'	E602144-17A	Soil	02/10/26	02/12/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS10-4'

E602144-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/13/26	
Toluene	ND	0.0250	1	02/12/26	02/13/26	
o-Xylene	ND	0.0250	1	02/12/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.5 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.8 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*116 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**686**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS11-4'

E602144-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/13/26	
Toluene	ND	0.0250	1	02/12/26	02/13/26	
o-Xylene	ND	0.0250	1	02/12/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.3 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.6 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*114 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**355**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS14-4'

E602144-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/13/26	
Toluene	ND	0.0250	1	02/12/26	02/13/26	
o-Xylene	ND	0.0250	1	02/12/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.4 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*86.4 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**103**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS25-4'

E602144-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/13/26	
Toluene	ND	0.0250	1	02/12/26	02/13/26	
o-Xylene	ND	0.0250	1	02/12/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.9 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.5 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	**54.5**	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**135**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS30-8'

E602144-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.9 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.2 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**674**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS81-4'

E602144-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.7 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.6 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**5560**	100	5	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS84-4'

E602144-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.4 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.8 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*111 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**5130**	40.0	2	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS85-4'

E602144-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/13/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/13/26	
Toluene	ND	0.0250	1	02/12/26	02/13/26	
o-Xylene	ND	0.0250	1	02/12/26	02/13/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/13/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.4 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.4 %*	*70-130*	*02/12/26*	*02/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	**39.9**	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*109 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**815**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

FS103-9'

E602144-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.3 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.8 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*111 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**264**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW02-0'-4'

E602144-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.0 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.2 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**116**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW06-0'-4'

E602144-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.5 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.7 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	ND	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW07-0'-4'

E602144-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*92.0 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.9 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	ND	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW24-0'-4'

E602144-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.2 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.7 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*111 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**246**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW29-0'-2'

E602144-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.4 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.6 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	ND	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW30-0'-5'

E602144-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.8 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.1 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**82.6**	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW31-0'-4'

E602144-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.1 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.2 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	ND	20.0	1	02/12/26	02/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

SW32-0'-4'

E602144-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Benzene	ND	0.0250	1	02/12/26	02/14/26	
Ethylbenzene	ND	0.0250	1	02/12/26	02/14/26	
Toluene	ND	0.0250	1	02/12/26	02/14/26	
o-Xylene	ND	0.0250	1	02/12/26	02/14/26	
p,m-Xylene	ND	0.0500	1	02/12/26	02/14/26	
Total Xylenes	ND	0.0250	1	02/12/26	02/14/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.9 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2607117
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/12/26	02/14/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*85.6 %*	*70-130*	*02/12/26*	*02/14/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: NV			Batch: 2607137
Diesel Range Organics (C10-C28)	ND	25.0	1	02/13/26	02/14/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/13/26	02/14/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*02/13/26*	*02/14/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2607123
Chloride	**81.8**	20.0	1	02/12/26	02/13/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607117-BLK1)									Prepared: 02/12/26 Analyzed: 02/13/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.55*		*8.00*		*94.3*	*70-130*			
LCS (2607117-BS1)									Prepared: 02/12/26 Analyzed: 02/13/26
Benzene	4.88	0.0250	5.00		97.5	70-130			
Ethylbenzene	4.54	0.0250	5.00		90.7	70-130			
Toluene	4.72	0.0250	5.00		94.3	70-130			
o-Xylene	4.63	0.0250	5.00		92.7	70-130			
p,m-Xylene	9.28	0.0500	10.0		92.8	70-130			
Total Xylenes	13.9	0.0250	15.0		92.8	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.63*		*8.00*		*95.4*	*70-130*			
Matrix Spike (2607117-MS1)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Benzene	4.87	0.0250	5.00	ND	97.4	70-130			
Ethylbenzene	4.56	0.0250	5.00	ND	91.3	70-130			
Toluene	4.73	0.0250	5.00	ND	94.5	70-130			
o-Xylene	4.63	0.0250	5.00	ND	92.7	70-130			
p,m-Xylene	9.33	0.0500	10.0	ND	93.3	70-130			
Total Xylenes	14.0	0.0250	15.0	ND	93.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.65*		*8.00*		*95.6*	*70-130*			
Matrix Spike Dup (2607117-MSD1)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Benzene	4.97	0.0250	5.00	ND	99.5	70-130	2.10	27	
Ethylbenzene	4.64	0.0250	5.00	ND	92.8	70-130	1.65	26	
Toluene	4.82	0.0250	5.00	ND	96.3	70-130	1.87	20	
o-Xylene	4.71	0.0250	5.00	ND	94.3	70-130	1.70	25	
p,m-Xylene	9.48	0.0500	10.0	ND	94.8	70-130	1.57	23	
Total Xylenes	14.2	0.0250	15.0	ND	94.6	70-130	1.62	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.68*		*8.00*		*96.0*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607117-BLK1)									Prepared: 02/12/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.27*		*8.00*		*90.9*	*70-130*			
LCS (2607117-BS2)									Prepared: 02/12/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	43.0	20.0	50.0		86.0	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.39*		*8.00*		*92.4*	*70-130*			
Matrix Spike (2607117-MS2)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	47.8	20.0	50.0	ND	95.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.54*		*8.00*		*94.3*	*70-130*			
Matrix Spike Dup (2607117-MSD2)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Gasoline Range Organics (C6-C10)	50.9	20.0	50.0	ND	102	70-130	6.39	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.41*		*8.00*		*92.6*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: NV

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607137-BLK1)									Prepared: 02/13/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*53.9*		*50.0*		*108*	*61-141*			
LCS (2607137-BS1)									Prepared: 02/13/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	236	25.0	250		94.4	66-144			
Surrogate: n-Nonane	*52.8*		*50.0*		*106*	*61-141*			
Matrix Spike (2607137-MS1)				**Source: E602144-03**					Prepared: 02/13/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	259	25.0	250	ND	104	56-156			
Surrogate: n-Nonane	*56.2*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2607137-MSD1)				**Source: E602144-03**					Prepared: 02/13/26 Analyzed: 02/14/26
Diesel Range Organics (C10-C28)	288	25.0	250	ND	115	56-156	10.5	20	
Surrogate: n-Nonane	*62.8*		*50.0*		*126*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/18/2026 11:03:37AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2607123-BLK1)									Prepared: 02/12/26 Analyzed: 02/13/26
Chloride	ND	20.0							
LCS (2607123-BS1)									Prepared: 02/12/26 Analyzed: 02/13/26
Chloride	260	20.0	250		104	90-110			
Matrix Spike (2607123-MS1)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Chloride	1040	20.0	250	815	91.2	80-120			
Matrix Spike Dup (2607123-MSD1)				**Source: E602144-08**					Prepared: 02/12/26 Analyzed: 02/13/26
Chloride	1050	20.0	250	815	94.1	80-120	0.683	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/18/26 11:03

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

EE-176479.01.ABD

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602144	1D 2D 3D Std	NM CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	Job Number 01058.0007	X	X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
12:21	2/10/2026	S	1	FS10-4'		1						X						4.1
12:24	2/10/2026	S	1	FS11-4'		2						X						4.0
14:17	2/10/2026	S	1	FS14-4'		3						X						4.3
14:19	2/10/2026	S	1	FS25-4'		4						X						4.5
9:30	2/10/2026	S	1	FS30-8'		5						X						4.2
9:36	2/10/2026	S	1	FS81-4'		6						X						4.6
9:24	2/10/2026	S	1	F84-4'		7						X						4.4
9:22	2/10/2026	S	1	FS85-4'		8						X						4.2
12:45	2/10/2026	S	1	FS103-9'		9						X						4.0
14:24	2/10/2026	S	1	SW02-0'-4'		10						X						3.7

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, MC

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/11/26	7:11	Michelle Gonzales	2-11-26	0711
Michelle Gonzales	2-11-26	1515	Marissa Gonzales	2-11-26	1515
Marissa Gonzales	2-11-26	1920	Johnny Archuleta	2-11-26	1920
Johnny Archuleta	2-11-26	2308	Nx Soto	2-12-26	0600

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only		TAT				State				
Client: Devon	Company: Devon Energy	Lab WO#	Job Number	1D	2D	3D	Std	NM	CO	UT	TX	
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	E602144	01058-0007				X	X				
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220											
Address: 3122 National Parks Hwy	Phone: (575)689-7597											
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com											
Phone: 575-988-0055	Miscellaneous: Jim Raley											
Email: agiovengo@ensolum.com												

Sample Information							Analysis and Method											EPA Program		
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				SDWA / CWA / RCRA		
12:26	2/10/2026	S	1	SW06-0'-4'		11						X						Compliance	Y	or N
12:30	2/10/2026	S	1	SW07-0'-4'		12						X						PWSID #		
12:22	2/10/2026	S	1	SW24-0'-4'		13						X						Remarks		
11:14	2/10/2026	S	1	SW29-0'-2'		14						X								
12:35	2/10/2026	S	1	SW30-0'-5'		15						X								
11:20	2/10/2026	S	1	SW31-0'-4'		16						X								
11:25	2/10/2026	S	1	SW32-0'-4'		17						X								

3.9
4.4
4.0
4.2
3.6
3.7
3.6

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, JL

Relinquished by: (Signature)	Date 2/11/26	Time 7:11	Received by: (Signature) Michelle Gonzales	Date 2-11-26	Time 0711	
Relinquished by: (Signature) Michelle Gonzales	Date 2-11-26	Time 1515	Received by: (Signature) Marissa Gonzales	Date 2.11.26	Time 1515	
Relinquished by: (Signature) Marissa Gonzales	Date 2-11-26	Time 1920	Received by: (Signature) Johnny Archuleta	Date 2-11-26	Time 1920	
Relinquished by: (Signature) Johnny Archuleta	Date 2-11-26	Time 2300	Received by: (Signature)	Date 2-12-26	Time 0600	

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/12/2026 10:40:29AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/12/26 06:00	Work Order ID:	E602144
Phone:	(505) 382-1211	Date Logged In:	02/11/26 14:57	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/18/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Comments/Resolution

L-NS
R-DT

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602159
Job Number:	01058-0007
Received:	2/13/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/19/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/19/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602159
Date Received: 2/13/2026 6:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/13/2026 6:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS24-4’ 5
- FS28-4’ 6
- FS60-4’ 7
- FS64-4’ 8
- FS97-8’ 9
- FS98-8’ 10
- SW08-0’-4’ 11
- SW18-0’-4’ 12
- SW19-0’-4’ 13
- SW28-0’-2’ 14

QC Summary Data 15

- QC - Volatile Organics by EPA 8021B 15
- QC - Nonhalogenated Organics by EPA 8015D - GRO 16
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 17
- QC - Anions by EPA 300.0/9056A 18

Definitions and Notes 19

Chain of Custody etc. 20

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/19/26 12:49

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS24-4'	E602159-01A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
FS28-4'	E602159-02A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
FS60-4'	E602159-03A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
FS64-4'	E602159-04A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
FS97-8'	E602159-05A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
FS98-8'	E602159-06A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
SW08-0'-4'	E602159-07A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
SW18-0'-4'	E602159-08A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
SW19-0'-4'	E602159-09A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.
SW28-0'-2'	E602159-10A	Soil	02/11/26	02/13/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS24-4'

E602159-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*98.8 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**1330**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	**673**	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*112 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**1530**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS28-4'

E602159-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.1 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**483**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	**373**	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*116 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**993**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS60-4'

E602159-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.0 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**136**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	**90.8**	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*115 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**1180**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS64-4'

E602159-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.6 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**30.6**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*118 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**587**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS97-8'

E602159-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.4 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*116 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**59.5**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*112 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**623**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

FS98-8'

E602159-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.5 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	**54.3**	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*113 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**815**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

SW08-0'-4'

E602159-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.8 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	ND	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*111 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	ND	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

SW18-0'-4'

E602159-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.9 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*118 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	ND	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*113 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**56.5**	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

SW19-0'-4'

E602159-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/16/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/16/26	
Toluene	ND	0.0250	1	02/16/26	02/16/26	
o-Xylene	ND	0.0250	1	02/16/26	02/16/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/16/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/16/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.8 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/16/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*119 %*	*70-130*	*02/16/26*	*02/16/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	ND	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*112 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	ND	20.0	1	02/16/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

SW28-0'-2'

E602159-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Benzene	ND	0.0250	1	02/16/26	02/17/26	
Ethylbenzene	ND	0.0250	1	02/16/26	02/17/26	
Toluene	ND	0.0250	1	02/16/26	02/17/26	
o-Xylene	ND	0.0250	1	02/16/26	02/17/26	
p,m-Xylene	ND	0.0500	1	02/16/26	02/17/26	
Total Xylenes	ND	0.0250	1	02/16/26	02/17/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.5 %*	*70-130*	*02/16/26*	*02/17/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608011
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/16/26	02/17/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*117 %*	*70-130*	*02/16/26*	*02/17/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608012
Diesel Range Organics (C10-C28)	ND	25.0	1	02/16/26	02/17/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/16/26	02/17/26	
Surrogate: n-Nonane		*111 %*	*61-141*	*02/16/26*	*02/17/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608028
Chloride	**55.9**	20.0	1	02/16/26	02/17/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608011-BLK1)									Prepared: 02/16/26 Analyzed: 02/16/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.39*		*8.00*		*92.4*	*70-130*			
LCS (2608011-BS1)									Prepared: 02/16/26 Analyzed: 02/18/26
Benzene	4.30	0.0250	5.00		86.0	70-130			
Ethylbenzene	4.04	0.0250	5.00		80.9	70-130			
Toluene	4.23	0.0250	5.00		84.6	70-130			
o-Xylene	4.09	0.0250	5.00		81.7	70-130			
p,m-Xylene	8.30	0.0500	10.0		83.0	70-130			
Total Xylenes	12.4	0.0250	15.0		82.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.61*		*8.00*		*95.1*	*70-130*			
Matrix Spike (2608011-MS1)				**Source: E602160-05**					Prepared: 02/16/26 Analyzed: 02/16/26
Benzene	4.31	0.0250	5.00	ND	86.1	70-130			
Ethylbenzene	4.10	0.0250	5.00	ND	82.0	70-130			
Toluene	4.27	0.0250	5.00	ND	85.4	70-130			
o-Xylene	4.13	0.0250	5.00	ND	82.6	70-130			
p,m-Xylene	8.41	0.0500	10.0	ND	84.1	70-130			
Total Xylenes	12.5	0.0250	15.0	ND	83.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.57*		*8.00*		*94.6*	*70-130*			
Matrix Spike Dup (2608011-MSD1)				**Source: E602160-05**					Prepared: 02/16/26 Analyzed: 02/16/26
Benzene	4.47	0.0250	5.00	ND	89.3	70-130	3.61	27	
Ethylbenzene	4.28	0.0250	5.00	ND	85.5	70-130	4.24	26	
Toluene	4.44	0.0250	5.00	ND	88.7	70-130	3.82	20	
o-Xylene	4.31	0.0250	5.00	ND	86.3	70-130	4.30	25	
p,m-Xylene	8.76	0.0500	10.0	ND	87.6	70-130	4.15	23	
Total Xylenes	13.1	0.0250	15.0	ND	87.2	70-130	4.20	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.44*		*8.00*		*93.0*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608011-BLK1)									Prepared: 02/16/26 Analyzed: 02/16/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.75*		*8.00*		*122*	*70-130*			
LCS (2608011-BS2)									Prepared: 02/16/26 Analyzed: 02/16/26
Gasoline Range Organics (C6-C10)	41.3	20.0	50.0		82.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.80*		*8.00*		*122*	*70-130*			
Matrix Spike (2608011-MS2)				**Source: E602160-05**					Prepared: 02/16/26 Analyzed: 02/16/26
Gasoline Range Organics (C6-C10)	45.0	20.0	50.0	ND	89.9	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.66*		*8.00*		*121*	*70-130*			
Matrix Spike Dup (2608011-MSD2)				**Source: E602160-05**					Prepared: 02/16/26 Analyzed: 02/16/26
Gasoline Range Organics (C6-C10)	47.8	20.0	50.0	ND	95.5	70-130	5.99	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*9.64*		*8.00*		*121*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608012-BLK1)									Prepared: 02/16/26 Analyzed: 02/16/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*57.2*		*50.0*		*114*	*61-141*			
LCS (2608012-BS1)									Prepared: 02/16/26 Analyzed: 02/16/26
Diesel Range Organics (C10-C28)	268	25.0	250		107	66-144			
Surrogate: n-Nonane	*54.8*		*50.0*		*110*	*61-141*			
Matrix Spike (2608012-MS1)				**Source: E602158-08**					Prepared: 02/16/26 Analyzed: 02/16/26
Diesel Range Organics (C10-C28)	333	25.0	250	50.2	113	56-156			
Surrogate: n-Nonane	*56.0*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2608012-MSD1)				**Source: E602158-08**					Prepared: 02/16/26 Analyzed: 02/16/26
Diesel Range Organics (C10-C28)	351	25.0	250	50.2	120	56-156	5.23	20	
Surrogate: n-Nonane	*56.1*		*50.0*		*112*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/19/2026 12:49:12PM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608028-BLK1)									Prepared: 02/16/26 Analyzed: 02/17/26
Chloride	ND	20.0							
LCS (2608028-BS1)									Prepared: 02/16/26 Analyzed: 02/17/26
Chloride	239	20.0	250		95.6	90-110			
Matrix Spike (2608028-MS1)				**Source: E602159-05**					Prepared: 02/16/26 Analyzed: 02/17/26
Chloride	883	20.0	250	623	104	80-120			
Matrix Spike Dup (2608028-MSD1)				**Source: E602159-05**					Prepared: 02/16/26 Analyzed: 02/17/26
Chloride	887	20.0	250	623	105	80-120	0.467	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/19/26 12:49

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E002159	Job Number 01958.0007	1D 2D 3D Std: — — — X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
9:30	2/11/2026	S	1	FS24-4'		1						X			2.4
9:31	2/11/2026	S	1	FS28-4'		2						X			1.8
13:01	2/11/2026	S	1	FS60-4'		3						X			1.0
14:02	2/11/2026	S	1	FS64-4'		4						X			1.3
17:01	2/11/2026	S	1	FS97-8'		5						X			1.9
17:02	2/11/2026	S	1	FS98-8'		6						X			1.5
14:12	2/11/2026	S	1	SW08-0'-4'		7						X			1.0
12:21	2/11/2026	S	1	SW18-0'-4'		8						X			2.2
14:16	2/11/2026	S	1	SW19-0'-4'		9						X			3.5
11:30	2/11/2026	S	1	SW28-0'-2'		10						X			1.1

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, IE

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/12/26	7:11	Michelle Gonzales	2.12.26	0711
Michelle Gonzales	2-12-26	1245	Marissa Gonzales	2-12-26	1245
Marissa Gonzales	2-12-26	1800	Johnny Archuleta	2-12-26	1800
Johnny Archuleta	2-12-26	2330	Noe Soto	2-13-26	0630

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/13/2026 7:54:22AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/13/26 06:30	Work Order ID:	E602159
Phone:	(505) 382-1211	Date Logged In:	02/12/26 15:34	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/19/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-DT

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602173
Job Number:	01058-0007
Received:	2/16/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/20/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/20/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602173
Date Received: 2/16/2026 8:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/16/2026 8:00:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 5

Sample Data 6

FS01-6’ 6

FS02-6’ 7

FS13-4’ 8

FS21-4’ 9

FS22-4’ 10

FS23-4’ 11

FS45-7’ 12

FS43-5’ 13

FS75-4’ 14

FS76-4’ 15

FS78-4’ 16

FS80-4’ 17

FS83-4’ 18

SW20-0’-4’ 19

SW21-0’-4’ 20

SW22-0’-4’ 21

SW23-0’-4’ 22

SW25-0’-4’ 23

SW27-0’-4’ 24

QC Summary Data 25

Table of Contents (continued)

QC - Volatile Organics by EPA 8021B 25

QC - Nonhalogenated Organics by EPA 8015D - GRO 26

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 27

QC - Anions by EPA 300.0/9056A 28

Definitions and Notes 29

Chain of Custody etc. 30

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/20/26 14:41

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS01-6'	E602173-01A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS02-6'	E602173-02A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS13-4'	E602173-03A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS21-4'	E602173-04A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS22-4'	E602173-05A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS23-4'	E602173-06A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS45-7'	E602173-07A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS43-5'	E602173-08A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS75-4'	E602173-09A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS76-4'	E602173-10A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS78-4'	E602173-11A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS80-4'	E602173-12A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
FS83-4'	E602173-13A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW20-0'-4'	E602173-14A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW21-0'-4'	E602173-15A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW22-0'-4'	E602173-16A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW23-0'-4'	E602173-17A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW25-0'-4'	E602173-18A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.
SW27-0'-4'	E602173-19A	Soil	02/12/26	02/16/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS01-6'

E602173-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**1870**	25.0	1	02/17/26	02/20/26	
Oil Range Organics (C28-C36)	**752**	50.0	1	02/17/26	02/20/26	
Surrogate: n-Nonane		*99.3 %*	*61-141*	*02/17/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**1170**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS02-6'

E602173-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.8 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**1680**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS13-4'

E602173-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**124**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**80.8**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**436**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS21-4'

E602173-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*102 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.1 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**737**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS22-4'

E602173-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.6 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*97.8 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**259**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS23-4'

E602173-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.0 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**218**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**141**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*104 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**420**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS45-7'

E602173-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**1670**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS43-5'

E602173-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*103 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**2080**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS75-4'

E602173-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/17/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/17/26	
Toluene	ND	0.0250	1	02/17/26	02/17/26	
o-Xylene	ND	0.0250	1	02/17/26	02/17/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/17/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/17/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/17/26*	*02/17/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/17/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.4 %*	*70-130*	*02/17/26*	*02/17/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**307**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**271**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**935**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS76-4'

E602173-10

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.1 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**420**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**278**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**764**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS78-4'

E602173-11

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*101 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**313**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**295**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**921**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS80-4'

E602173-12

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*88.8 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**214**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**213**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**1500**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

FS83-4'

E602173-13

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.7 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	**295**	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	**214**	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**2430**	40.0	2	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW20-0'-4'

E602173-14

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**43.9**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW21-0'-4'

E602173-15

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.7 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.3 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	**41.7**	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW22-0'-4'

E602173-16

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*100 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	ND	20.0	1	02/17/26	02/17/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW23-0'-4'

E602173-17

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.8 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	ND	20.0	1	02/17/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW25-0'-4'

E602173-18

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.6 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	ND	20.0	1	02/17/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

SW27-0'-4'

E602173-19

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*99.6 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2608039
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*89.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608033
Diesel Range Organics (C10-C28)	ND	25.0	1	02/17/26	02/18/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/17/26	02/18/26	
Surrogate: n-Nonane		*99.5 %*	*61-141*	*02/17/26*	*02/18/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2608036
Chloride	ND	20.0	1	02/17/26	02/18/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

Volatile Organics by EPA 8021B

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608039-BLK1)									Prepared: 02/17/26 Analyzed: 02/17/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.01*		*8.00*		*100*	*70-130*			
LCS (2608039-BS1)									Prepared: 02/17/26 Analyzed: 02/17/26
Benzene	5.22	0.0250	5.00		104	70-130			
Ethylbenzene	4.96	0.0250	5.00		99.1	70-130			
Toluene	5.10	0.0250	5.00		102	70-130			
o-Xylene	4.98	0.0250	5.00		99.5	70-130			
p,m-Xylene	10.1	0.0500	10.0		101	70-130			
Total Xylenes	15.1	0.0250	15.0		101	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.06*		*8.00*		*101*	*70-130*			
Matrix Spike (2608039-MS1)				**Source: E602173-09**					Prepared: 02/17/26 Analyzed: 02/17/26
Benzene	5.50	0.0250	5.00	ND	110	70-130			
Ethylbenzene	5.22	0.0250	5.00	ND	104	70-130			
Toluene	5.38	0.0250	5.00	ND	108	70-130			
o-Xylene	5.25	0.0250	5.00	ND	105	70-130			
p,m-Xylene	10.6	0.0500	10.0	ND	106	70-130			
Total Xylenes	15.9	0.0250	15.0	ND	106	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.14*		*8.00*		*102*	*70-130*			
Matrix Spike Dup (2608039-MSD1)				**Source: E602173-09**					Prepared: 02/17/26 Analyzed: 02/17/26
Benzene	4.95	0.0250	5.00	ND	99.0	70-130	10.5	27	
Ethylbenzene	4.69	0.0250	5.00	ND	93.9	70-130	10.6	26	
Toluene	4.83	0.0250	5.00	ND	96.6	70-130	10.7	20	
o-Xylene	4.72	0.0250	5.00	ND	94.4	70-130	10.6	25	
p,m-Xylene	9.58	0.0500	10.0	ND	95.8	70-130	10.5	23	
Total Xylenes	14.3	0.0250	15.0	ND	95.3	70-130	10.5	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.03*		*8.00*		*100*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: SL

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608039-BLK1)									Prepared: 02/17/26 Analyzed: 02/17/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.23*		*8.00*		*90.4*	*70-130*			
LCS (2608039-BS2)									Prepared: 02/17/26 Analyzed: 02/17/26
Gasoline Range Organics (C6-C10)	56.5	20.0	50.0		113	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.29*		*8.00*		*91.1*	*70-130*			
Matrix Spike (2608039-MS2)				**Source: E602173-09**					Prepared: 02/17/26 Analyzed: 02/18/26
Gasoline Range Organics (C6-C10)	57.6	20.0	50.0	ND	115	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.20*		*8.00*		*90.1*	*70-130*			
Matrix Spike Dup (2608039-MSD2)				**Source: E602173-09**					Prepared: 02/17/26 Analyzed: 02/17/26
Gasoline Range Organics (C6-C10)	55.5	20.0	50.0	ND	111	70-130	3.77	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.18*		*8.00*		*89.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608033-BLK1)									Prepared: 02/17/26 Analyzed: 02/18/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*60.4*		*50.0*		*121*	*61-141*			
LCS (2608033-BS1)									Prepared: 02/17/26 Analyzed: 02/18/26
Diesel Range Organics (C10-C28)	253	25.0	250		101	66-144			
Surrogate: n-Nonane	*48.8*		*50.0*		*97.6*	*61-141*			
Matrix Spike (2608033-MS1)				**Source: E602173-11**					Prepared: 02/17/26 Analyzed: 02/18/26
Diesel Range Organics (C10-C28)	555	25.0	250	313	96.7	56-156			
Surrogate: n-Nonane	*51.5*		*50.0*		*103*	*61-141*			
Matrix Spike Dup (2608033-MSD1)				**Source: E602173-11**					Prepared: 02/17/26 Analyzed: 02/18/26
Diesel Range Organics (C10-C28)	583	25.0	250	313	108	56-156	4.95	20	
Surrogate: n-Nonane	*49.7*		*50.0*		*99.5*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/20/2026 2:41:38PM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608036-BLK1)									Prepared: 02/17/26 Analyzed: 02/17/26
Chloride	ND	20.0							
LCS (2608036-BS1)									Prepared: 02/17/26 Analyzed: 02/17/26
Chloride	246	20.0	250		98.5	90-110			
Matrix Spike (2608036-MS1)				**Source: E602173-04**					Prepared: 02/17/26 Analyzed: 02/17/26
Chloride	1020	20.0	250	737	113	80-120			
Matrix Spike Dup (2608036-MSD1)				**Source: E602173-04**					Prepared: 02/17/26 Analyzed: 02/17/26
Chloride	996	20.0	250	737	104	80-120	2.30	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/20/26 14:41

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602173	Job Number 01058.0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information							Analysis and Method											EPA Program		
Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				SDWA / CWA / RCRA		
15:01	2/12/2026	S	1	FS01-6'		1						X						Compliance Y or N		
15:07	2/12/2026	S	1	FS02-6'		2						X						PWSID #		
12:57	2/12/2026	S	1	FS13-4'		3						X						Remarks		
14:07	2/12/2026	S	1	FS21-4'		4						X								
11:38	2/12/2026	S	1	FS22-4'		5						X								
14:09	2/12/2026	S	1	FS23-4'		6						X								
15:10	2/12/2026	S	1	FS45-7'		7						X								
15:13	2/12/2026	S	1	FS43-5'		8						X								
8:47	2/12/2026	S	1	FS75-4'		9						X								
8:50	2/12/2026	S	1	FS76-4'		10						X								

Remarks
1.4
1.2
0.7
1.0
2.3
1.3
0.8
0.8
1.0
2.1

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: AK, AP

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/13/26	7:11	Michelle Gonzales	2.13.26	0711
Michelle Gonzales	2.13.26	1445	Nathan Gonzales	2.13.26	1445
Nathan Gonzales	2.13.26	1835	Johnny Archuleta	2.13.26	1835
Johnny Archuleta	2-13-26	2315	Cath Mar	2.14.26	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602173	1D 2D 3D Std	NM CO UT TX
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr	Job Number 01058.0007		X
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220		X	
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
9:56	2/12/2026	S	1	FS78-4'		11						X						1.8
10:05	2/12/2026	S	1	FS80-4'		12						X						0.8
10:08	2/12/2026	S	1	FS83-4'		13						X						1.6
8:45	2/12/2026	S	1	SW20-0'-4'		14						X						2.2
8:52	2/12/2026	S	1	SW21-0'-4'		15						X						1.1
10:58	2/12/2026	S	1	SW22-0'-4'		16						X						2.1
11:01	2/12/2026	S	1	SW23-0'-4'		17						X						2.2
11:41	2/12/2026	S	1	SW25-0'-4'		18						X						2.1
14:10	2/12/2026	S	1	SW27-0'-4'		19						X						2.4

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, JF

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/13/26	7:11	Michelle Gonzales	2-13-26	0711
Michelle Gonzales	2-13-26	1445	Nathan Gonzales	2-13-26	1445
Nathan Gonzales	2-13-26	1835	Johnny Archuleta	2-13-26	1835
Johnny Archuleta	2-13-26	2215	Cath Mcn	2-16-26	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/16/2026 8:48:08AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/16/26 08:00	Work Order ID:	E602173
Phone:	(505) 382-1211	Date Logged In:	02/13/26 15:49	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/20/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-CM

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602186
Job Number:	01058-0007
Received:	2/17/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
2/23/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 2/23/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602186
Date Received: 2/17/2026 8:00:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/17/2026 8:00:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- SW39-4’-9’ 5
- SW40-4’-9’ 6
- SW41-4’-8’ 7
- SW42-4’-8’ 8
- SW43-4’-8’ 9
- SW44-4’-8’ 10
- SW45-4’-7’ 11
- SW46-4’-7’ 12
- SW47-3’-6’ 13

QC Summary Data 14

- QC - Volatile Organics by EPA 8021B 14
- QC - Nonhalogenated Organics by EPA 8015D - GRO 15
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 16
- QC - Anions by EPA 300.0/9056A 17

Definitions and Notes 18

Chain of Custody etc. 19

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/23/26 08:22

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
SW39-4'-9'	E602186-01A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW40-4'-9'	E602186-02A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW41-4'-8'	E602186-03A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW42-4'-8'	E602186-04A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW43-4'-8'	E602186-05A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW44-4'-8'	E602186-06A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW45-4'-7'	E602186-07A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW46-4'-7'	E602186-08A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.
SW47-3'-6'	E602186-09A	Soil	02/13/26	02/17/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW39-4'-9'

E602186-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**2190**	40.0	2	02/18/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW40-4'-9'

E602186-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.8 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*90.7 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*108 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**1200**	20.0	1	02/18/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW41-4'-8'

E602186-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.3 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.1 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**172**	20.0	1	02/18/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW42-4'-8'

E602186-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.3 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*92.9 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*109 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**329**	20.0	1	02/18/26	02/18/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW43-4'-8'

E602186-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*96.3 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**162**	20.0	1	02/18/26	02/19/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW44-4'-8'

E602186-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.7 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*91.5 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*106 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**179**	20.0	1	02/18/26	02/19/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW45-4'-7'

E602186-07

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*91.0 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.2 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**224**	20.0	1	02/18/26	02/19/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW46-4'-7'

E602186-08

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.1 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.7 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**588**	20.0	1	02/18/26	02/19/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

SW47-3'-6'

E602186-09

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Benzene	ND	0.0250	1	02/17/26	02/18/26	
Ethylbenzene	ND	0.0250	1	02/17/26	02/18/26	
Toluene	ND	0.0250	1	02/17/26	02/18/26	
o-Xylene	ND	0.0250	1	02/17/26	02/18/26	
p,m-Xylene	ND	0.0500	1	02/17/26	02/18/26	
Total Xylenes	ND	0.0250	1	02/17/26	02/18/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.0 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2608048
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/17/26	02/18/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*95.1 %*	*70-130*	*02/17/26*	*02/18/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2608068
Diesel Range Organics (C10-C28)	ND	25.0	1	02/18/26	02/20/26	
Oil Range Organics (C28-C36)	ND	50.0	1	02/18/26	02/20/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*02/18/26*	*02/20/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2608075
Chloride	**183**	20.0	1	02/18/26	02/19/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608048-BLK1)									Prepared: 02/17/26 Analyzed: 02/18/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*7.44*		*8.00*		*93.0*	*70-130*			
LCS (2608048-BS1)									Prepared: 02/17/26 Analyzed: 02/18/26
Benzene	4.14	0.0250	5.00		82.8	70-130			
Ethylbenzene	3.85	0.0250	5.00		76.9	70-130			
Toluene	4.01	0.0250	5.00		80.2	70-130			
o-Xylene	3.91	0.0250	5.00		78.3	70-130			
p,m-Xylene	7.88	0.0500	10.0		78.8	70-130			
Total Xylenes	11.8	0.0250	15.0		78.6	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.52*		*8.00*		*94.0*	*70-130*			
Matrix Spike (2608048-MS1)				**Source: E602186-08**					Prepared: 02/17/26 Analyzed: 02/18/26
Benzene	4.76	0.0250	5.00	ND	95.2	70-130			
Ethylbenzene	4.43	0.0250	5.00	ND	88.6	70-130			
Toluene	4.61	0.0250	5.00	ND	92.3	70-130			
o-Xylene	4.50	0.0250	5.00	ND	89.9	70-130			
p,m-Xylene	9.04	0.0500	10.0	ND	90.4	70-130			
Total Xylenes	13.5	0.0250	15.0	ND	90.2	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.55*		*8.00*		*94.4*	*70-130*			
Matrix Spike Dup (2608048-MSD1)				**Source: E602186-08**					Prepared: 02/17/26 Analyzed: 02/18/26
Benzene	4.81	0.0250	5.00	ND	96.3	70-130	1.13	27	
Ethylbenzene	4.49	0.0250	5.00	ND	89.8	70-130	1.35	26	
Toluene	4.67	0.0250	5.00	ND	93.4	70-130	1.17	20	
o-Xylene	4.56	0.0250	5.00	ND	91.2	70-130	1.43	25	
p,m-Xylene	9.17	0.0500	10.0	ND	91.7	70-130	1.47	23	
Total Xylenes	13.7	0.0250	15.0	ND	91.5	70-130	1.45	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.55*		*8.00*		*94.4*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608048-BLK1)									Prepared: 02/17/26 Analyzed: 02/18/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.76*		*8.00*		*97.0*	*70-130*			
LCS (2608048-BS2)									Prepared: 02/17/26 Analyzed: 02/18/26
Gasoline Range Organics (C6-C10)	42.5	20.0	50.0		84.9	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.68*		*8.00*		*96.0*	*70-130*			
Matrix Spike (2608048-MS2)				**Source: E602186-08**					Prepared: 02/17/26 Analyzed: 02/18/26
Gasoline Range Organics (C6-C10)	47.4	20.0	50.0	ND	94.7	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.76*		*8.00*		*97.0*	*70-130*			
Matrix Spike Dup (2608048-MSD2)				**Source: E602186-08**					Prepared: 02/17/26 Analyzed: 02/18/26
Gasoline Range Organics (C6-C10)	46.1	20.0	50.0	ND	92.2	70-130	2.73	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.72*		*8.00*		*96.5*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608068-BLK1)									Prepared: 02/18/26 Analyzed: 02/20/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*55.9*		*50.0*		*112*	*61-141*			
LCS (2608068-BS1)									Prepared: 02/18/26 Analyzed: 02/20/26
Diesel Range Organics (C10-C28)	261	25.0	250		104	66-144			
Surrogate: n-Nonane	*50.4*		*50.0*		*101*	*61-141*			
Matrix Spike (2608068-MS1)				**Source: E602185-01**					Prepared: 02/18/26 Analyzed: 02/20/26
Diesel Range Organics (C10-C28)	693	25.0	250	410	113	56-156			
Surrogate: n-Nonane	*56.0*		*50.0*		*112*	*61-141*			
Matrix Spike Dup (2608068-MSD1)				**Source: E602185-01**					Prepared: 02/18/26 Analyzed: 02/20/26
Diesel Range Organics (C10-C28)	720	25.0	250	410	124	56-156	3.91	20	
Surrogate: n-Nonane	*62.4*		*50.0*		*125*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	2/23/2026 8:22:16AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2608075-BLK1)									Prepared: 02/18/26 Analyzed: 02/18/26
Chloride	ND	20.0							
LCS (2608075-BS1)									Prepared: 02/18/26 Analyzed: 02/18/26
Chloride	260	20.0	250		104	90-110			
Matrix Spike (2608075-MS1)				**Source: E602176-05**					Prepared: 02/18/26 Analyzed: 02/18/26
Chloride	372	20.0	250	115	103	80-120			
Matrix Spike Dup (2608075-MSD1)				**Source: E602176-05**					Prepared: 02/18/26 Analyzed: 02/18/26
Chloride	373	20.0	250	115	103	80-120	0.177	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	02/23/26 08:22

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602186	Job Number 01058.0007	1D 2D 3D Std: — — — X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals	Remarks
9:38	2/13/2026	S	1	SW39-4'-9'		1						X			3.0
9:40	2/13/2026	S	1	SW40-4'-9'		2						X			1.7
9:52	2/13/2026	S	1	SW41-4'-8'		3						X			2.4
9:56	2/13/2026	S	1	SW42-4'-8'		4						X			1.8
10:00	2/13/2026	S	1	SW43-4'-8'		5						X			1.0
10:15	2/13/2026	S	1	SW44-4'-8'		6						X			1.1
11:35	2/13/2026	S	1	SW45-4'-7'		7						X			1.8
12:02	2/13/2026	S	1	SW46-4'-7'		8						X			1.8
13:14	2/13/2026	S	1	SW47-3'-6'		9						X			1.1

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ AK, JE

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/16/26	7:11	Michelle Gonzales	2.16.26	0711
Michelle Gonzales	2-16-26	1615	Marissa Gonzales	2-16-26	1615
Marissa Gonzales	2-16-26	2100	Johnny Archuleta	2-16-26	2100
Johnny Archuleta	2-16-26	0030		2.17.26	800

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/17/2026 9:41:25AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/17/26 08:00	Work Order ID:	E602186
Phone:	(505) 382-1211	Date Logged In:	02/16/26 15:55	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	02/23/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-CM
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602318
Job Number:	01058-0007
Received:	2/27/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
3/4/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 3/4/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602318
Date Received: 2/27/2026 7:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 2/27/2026 7:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

- FS01-7’ 5
- FS24-5’ 6
- FS27-7’ 7
- FS44-8’ 8
- FS106-4’ 9

QC Summary Data 10

- QC - Volatile Organics by EPA 8021B 10
- QC - Nonhalogenated Organics by EPA 8015D - GRO 11
- QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 12
- QC - Anions by EPA 300.0/9056A 13

Definitions and Notes 14

Chain of Custody etc. 15

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/04/26 17:09

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS01-7'	E602318-01A	Soil	02/25/26	02/27/26	Glass Jar, 2 oz.
FS24-5'	E602318-02A	Soil	02/25/26	02/27/26	Glass Jar, 2 oz.
FS27-7'	E602318-03A	Soil	02/25/26	02/27/26	Glass Jar, 2 oz.
FS44-8'	E602318-04A	Soil	02/25/26	02/27/26	Glass Jar, 2 oz.
FS106-4'	E602318-05A	Soil	02/25/26	02/27/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

FS01-7'

E602318-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Benzene	ND	0.0250	1	02/27/26	02/28/26	
Ethylbenzene	ND	0.0250	1	02/27/26	02/28/26	
Toluene	ND	0.0250	1	02/27/26	02/28/26	
o-Xylene	ND	0.0250	1	02/27/26	02/28/26	
p,m-Xylene	ND	0.0500	1	02/27/26	02/28/26	
Total Xylenes	ND	0.0250	1	02/27/26	02/28/26	
Surrogate: 4-Bromochlorobenzene-PID		*97.3 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/27/26	02/28/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610020
Diesel Range Organics (C10-C28)	**286**	25.0	1	03/02/26	03/03/26	
Oil Range Organics (C28-C36)	**163**	50.0	1	03/02/26	03/03/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*03/02/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2609145
Chloride	**1330**	20.0	1	02/27/26	02/28/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

FS24-5'

E602318-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Benzene	ND	0.0250	1	02/27/26	02/28/26	
Ethylbenzene	ND	0.0250	1	02/27/26	02/28/26	
Toluene	ND	0.0250	1	02/27/26	02/28/26	
o-Xylene	ND	0.0250	1	02/27/26	02/28/26	
p,m-Xylene	ND	0.0500	1	02/27/26	02/28/26	
Total Xylenes	ND	0.0250	1	02/27/26	02/28/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.3 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/27/26	02/28/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610020
Diesel Range Organics (C10-C28)	**41.9**	25.0	1	03/02/26	03/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/02/26	03/03/26	
Surrogate: n-Nonane		*98.7 %*	*61-141*	*03/02/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2609145
Chloride	**154**	20.0	1	02/27/26	02/28/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

FS27-7'

E602318-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Benzene	ND	0.0250	1	02/27/26	02/28/26	
Ethylbenzene	ND	0.0250	1	02/27/26	02/28/26	
Toluene	ND	0.0250	1	02/27/26	02/28/26	
o-Xylene	ND	0.0250	1	02/27/26	02/28/26	
p,m-Xylene	ND	0.0500	1	02/27/26	02/28/26	
Total Xylenes	ND	0.0250	1	02/27/26	02/28/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.6 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/27/26	02/28/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*111 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610020
Diesel Range Organics (C10-C28)	**194**	25.0	1	03/02/26	03/03/26	
Oil Range Organics (C28-C36)	**112**	50.0	1	03/02/26	03/03/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*03/02/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2609145
Chloride	**953**	20.0	1	02/27/26	02/28/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

FS44-8'

E602318-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Benzene	ND	0.0250	1	02/27/26	02/28/26	
Ethylbenzene	**0.0558**	0.0250	1	02/27/26	02/28/26	
Toluene	ND	0.0250	1	02/27/26	02/28/26	
o-Xylene	**0.0619**	0.0250	1	02/27/26	02/28/26	
p,m-Xylene	**0.301**	0.0500	1	02/27/26	02/28/26	
Total Xylenes	**0.363**	0.0250	1	02/27/26	02/28/26	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/27/26	02/28/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*113 %*	*70-130*	*02/27/26*	*02/28/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610020
Diesel Range Organics (C10-C28)	**1590**	25.0	1	03/02/26	03/03/26	
Oil Range Organics (C28-C36)	**727**	50.0	1	03/02/26	03/03/26	
Surrogate: n-Nonane		*98.8 %*	*61-141*	*03/02/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2609145
Chloride	**1510**	20.0	1	02/27/26	02/28/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

FS106-4'

E602318-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Benzene	ND	0.0250	1	02/27/26	02/27/26	
Ethylbenzene	ND	0.0250	1	02/27/26	02/27/26	
Toluene	ND	0.0250	1	02/27/26	02/27/26	
o-Xylene	ND	0.0250	1	02/27/26	02/27/26	
p,m-Xylene	ND	0.0500	1	02/27/26	02/27/26	
Total Xylenes	ND	0.0250	1	02/27/26	02/27/26	
Surrogate: 4-Bromochlorobenzene-PID		*96.1 %*	*70-130*	*02/27/26*	*02/27/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: MB			Batch: 2609134
Gasoline Range Organics (C6-C10)	ND	20.0	1	02/27/26	02/27/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*110 %*	*70-130*	*02/27/26*	*02/27/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610020
Diesel Range Organics (C10-C28)	**671**	25.0	1	03/02/26	03/03/26	
Oil Range Organics (C28-C36)	**378**	50.0	1	03/02/26	03/03/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*03/02/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2609145
Chloride	**602**	20.0	1	02/27/26	02/28/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

Volatile Organics by EPA 8021B

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2609134-BLK1)									Prepared: 02/27/26 Analyzed: 02/27/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.00*		*8.00*		*100*	*70-130*			
LCS (2609134-BS1)									Prepared: 02/27/26 Analyzed: 02/27/26
Benzene	3.84	0.0250	5.00		76.7	70-130			
Ethylbenzene	3.62	0.0250	5.00		72.4	70-130			
Toluene	3.79	0.0250	5.00		75.9	70-130			
o-Xylene	3.69	0.0250	5.00		73.8	70-130			
p,m-Xylene	7.46	0.0500	10.0		74.6	70-130			
Total Xylenes	11.1	0.0250	15.0		74.3	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.72*		*8.00*		*96.5*	*70-130*			
Matrix Spike (2609134-MS1)				**Source: E602318-05**					Prepared: 02/27/26 Analyzed: 02/27/26
Benzene	4.18	0.0250	5.00	ND	83.5	70-130			
Ethylbenzene	3.96	0.0250	5.00	ND	79.2	70-130			
Toluene	4.14	0.0250	5.00	ND	82.8	70-130			
o-Xylene	4.02	0.0250	5.00	ND	80.5	70-130			
p,m-Xylene	8.14	0.0500	10.0	ND	81.4	70-130			
Total Xylenes	12.2	0.0250	15.0	ND	81.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*7.72*		*8.00*		*96.6*	*70-130*			
Matrix Spike Dup (2609134-MSD1)				**Source: E602318-05**					Prepared: 02/27/26 Analyzed: 02/27/26
Benzene	4.35	0.0250	5.00	ND	87.0	70-130	4.13	27	
Ethylbenzene	4.12	0.0250	5.00	ND	82.3	70-130	3.86	26	
Toluene	4.31	0.0250	5.00	ND	86.2	70-130	3.97	20	
o-Xylene	4.17	0.0250	5.00	ND	83.4	70-130	3.52	25	
p,m-Xylene	8.46	0.0500	10.0	ND	84.6	70-130	3.79	23	
Total Xylenes	12.6	0.0250	15.0	ND	84.2	70-130	3.70	26	
Surrogate: 4-Bromochlorobenzene-PID	*7.85*		*8.00*		*98.1*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: MB

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2609134-BLK1)									Prepared: 02/27/26 Analyzed: 02/27/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.75*		*8.00*		*109*	*70-130*			
LCS (2609134-BS2)									Prepared: 02/27/26 Analyzed: 02/27/26
Gasoline Range Organics (C6-C10)	40.1	20.0	50.0		80.2	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.78*		*8.00*		*110*	*70-130*			
Matrix Spike (2609134-MS2)				**Source: E602318-05**					Prepared: 02/27/26 Analyzed: 02/27/26
Gasoline Range Organics (C6-C10)	44.8	20.0	50.0	ND	89.6	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.88*		*8.00*		*111*	*70-130*			
Matrix Spike Dup (2609134-MSD2)				**Source: E602318-05**					Prepared: 02/27/26 Analyzed: 02/27/26
Gasoline Range Organics (C6-C10)	46.6	20.0	50.0	ND	93.3	70-130	4.06	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*8.96*		*8.00*		*112*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610020-BLK1)									Prepared: 03/02/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*47.5*		*50.0*		*95.1*	*61-141*			
LCS (2610020-BS1)									Prepared: 03/02/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	248	25.0	250		99.1	66-144			
Surrogate: n-Nonane	*46.7*		*50.0*		*93.4*	*61-141*			
Matrix Spike (2610020-MS1)				**Source: E602318-04**					Prepared: 03/02/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	1730	25.0	250	1590	58.7	56-156			
Surrogate: n-Nonane	*49.9*		*50.0*		*99.8*	*61-141*			
Matrix Spike Dup (2610020-MSD1)				**Source: E602318-04**					Prepared: 03/02/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	1590	25.0	250	1590	1.13	56-156	8.67	20	M4
Surrogate: n-Nonane	*49.5*		*50.0*		*99.0*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/4/2026 5:09:35PM

Anions by EPA 300.0/9056A

Analyst: IY

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2609145-BLK1)									Prepared: 02/27/26 Analyzed: 02/28/26
Chloride	ND	20.0							
LCS (2609145-BS1)									Prepared: 02/27/26 Analyzed: 02/28/26
Chloride	257	20.0	250		103	90-110			
Matrix Spike (2609145-MS1)				**Source: E602318-03**					Prepared: 02/27/26 Analyzed: 02/28/26
Chloride	1180	20.0	250	953	91.3	80-120			
Matrix Spike Dup (2609145-MSD1)				**Source: E602318-03**					Prepared: 02/27/26 Analyzed: 02/28/26
Chloride	1150	20.0	250	953	78.3	80-120	2.78	20	M4

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/04/26 17:09

M4	Matrix spike recovery value is suspect since the analyte concentration in the sample is disproportionate to the spike level. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E002318	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
13:44	2/25/2026	S	1	FS01-7'		1						X						2.5
8:42	2/25/2026	S	1	FS24-5'		2						X						3.1
13:25	2/25/2026	S	1	FS27-7'		3						X						2.6
13:45	2/25/2026	S	1	FS44-8'		4						X						2.6
9:00	2/25/2026	S	1	FS106-4'		5						X						3.5

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _ Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/26/26	7:11	Michelle Gonzales	2.26.26	0711
Michelle Gonzales	2.26.26	1430	Nathan Gonzales	2.26.26	1430
Nathan Gonzales	2.26.26	1900	Johnny Archuleta	2-26-26	1900
Johnny Archuleta	2-26-26	2315	Cath Mar	2.27.26	730

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 T2 T3

AVG Temp °C

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 2/27/2026 9:19:25AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	02/27/26 07:30	Work Order ID:	E602318
Phone:	(505) 382-1211	Date Logged In:	02/26/26 15:32	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	03/05/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-CM
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo

5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E602331
Job Number:	01058-0007
Received:	3/2/2026

Revision: 2

Report Reviewed By:

Walter Hinchman
Laboratory Director
3/10/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 3/10/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E602331
Date Received: 3/2/2026 6:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 3/2/2026 6:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

FS100-9’ 5

FS113-4’ 6

SW50-4’-7’ 7

QC Summary Data 8

QC - Volatile Organics by EPA 8021B 8

QC - Nonhalogenated Organics by EPA 8015D - GRO 9

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 10

QC - Anions by EPA 300.0/9056A 11

Definitions and Notes 12

Chain of Custody etc. 13

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/10/26 10:38

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS100-9'	E602331-01A	Soil	02/26/26	03/02/26	Glass Jar, 2 oz.
FS113-4'	E602331-02A	Soil	02/26/26	03/02/26	Glass Jar, 2 oz.
SW50-4'-7'	E602331-03A	Soil	02/26/26	03/02/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

FS100-9'

E602331-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Benzene	ND	0.0250	1	03/02/26	03/02/26	
Ethylbenzene	ND	0.0250	1	03/02/26	03/02/26	
Toluene	ND	0.0250	1	03/02/26	03/02/26	
o-Xylene	ND	0.0250	1	03/02/26	03/02/26	
p,m-Xylene	ND	0.0500	1	03/02/26	03/02/26	
Total Xylenes	ND	0.0250	1	03/02/26	03/02/26	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/02/26	03/02/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.9 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2610021
Diesel Range Organics (C10-C28)	**93.8**	25.0	1	03/02/26	03/02/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/02/26	03/02/26	
Surrogate: n-Nonane		*97.1 %*	*61-141*	*03/02/26*	*03/02/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2610005
Chloride	**537**	20.0	1	03/02/26	03/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

FS113-4'

E602331-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Benzene	ND	0.0250	1	03/02/26	03/02/26	
Ethylbenzene	ND	0.0250	1	03/02/26	03/02/26	
Toluene	ND	0.0250	1	03/02/26	03/02/26	
o-Xylene	ND	0.0250	1	03/02/26	03/02/26	
p,m-Xylene	ND	0.0500	1	03/02/26	03/02/26	
Total Xylenes	ND	0.0250	1	03/02/26	03/02/26	
Surrogate: 4-Bromochlorobenzene-PID		*108 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/02/26	03/02/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*94.9 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2610021
Diesel Range Organics (C10-C28)	ND	25.0	1	03/02/26	03/02/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/02/26	03/02/26	
Surrogate: n-Nonane		*89.5 %*	*61-141*	*03/02/26*	*03/02/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2610005
Chloride	**1230**	20.0	1	03/02/26	03/02/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

SW50-4'-7'

E602331-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Benzene	ND	0.0250	1	03/02/26	03/02/26	
Ethylbenzene	ND	0.0250	1	03/02/26	03/02/26	
Toluene	ND	0.0250	1	03/02/26	03/02/26	
o-Xylene	ND	0.0250	1	03/02/26	03/02/26	
p,m-Xylene	ND	0.0500	1	03/02/26	03/02/26	
Total Xylenes	ND	0.0250	1	03/02/26	03/02/26	
Surrogate: 4-Bromochlorobenzene-PID		*107 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2610001
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/02/26	03/02/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.9 %*	*70-130*	*03/02/26*	*03/02/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: RAS			Batch: 2610021
Diesel Range Organics (C10-C28)	**116**	25.0	1	03/02/26	03/02/26	
Oil Range Organics (C28-C36)	**92.3**	50.0	1	03/02/26	03/02/26	
Surrogate: n-Nonane		*91.8 %*	*61-141*	*03/02/26*	*03/02/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: DT			Batch: 2610005
Chloride	**1370**	20.0	1	03/02/26	03/02/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610001-BLK1)									Prepared: 03/02/26 Analyzed: 03/02/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.53*		*8.00*		*107*	*70-130*			
LCS (2610001-BS1)									Prepared: 03/02/26 Analyzed: 03/02/26
Benzene	4.84	0.0250	5.00		96.7	70-130			
Ethylbenzene	4.60	0.0250	5.00		92.0	70-130			
Toluene	4.75	0.0250	5.00		95.0	70-130			
o-Xylene	4.71	0.0250	5.00		94.3	70-130			
p,m-Xylene	9.37	0.0500	10.0		93.7	70-130			
Total Xylenes	14.1	0.0250	15.0		93.9	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.46*		*8.00*		*106*	*70-130*			
Matrix Spike (2610001-MS1)				**Source: E602330-04**					Prepared: 03/02/26 Analyzed: 03/02/26
Benzene	4.42	0.0250	5.00	ND	88.5	70-130			
Ethylbenzene	4.17	0.0250	5.00	ND	83.3	70-130			
Toluene	4.31	0.0250	5.00	ND	86.2	70-130			
o-Xylene	4.26	0.0250	5.00	ND	85.2	70-130			
p,m-Xylene	8.49	0.0500	10.0	ND	84.9	70-130			
Total Xylenes	12.8	0.0250	15.0	ND	85.0	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.44*		*8.00*		*105*	*70-130*			
Matrix Spike Dup (2610001-MSD1)				**Source: E602330-04**					Prepared: 03/02/26 Analyzed: 03/02/26
Benzene	4.48	0.0250	5.00	ND	89.7	70-130	1.39	27	
Ethylbenzene	4.22	0.0250	5.00	ND	84.5	70-130	1.35	26	
Toluene	4.37	0.0250	5.00	ND	87.4	70-130	1.32	20	
o-Xylene	4.33	0.0250	5.00	ND	86.6	70-130	1.62	25	
p,m-Xylene	8.60	0.0500	10.0	ND	86.0	70-130	1.29	23	
Total Xylenes	12.9	0.0250	15.0	ND	86.2	70-130	1.40	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.53*		*8.00*		*107*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610001-BLK1)									Prepared: 03/02/26 Analyzed: 03/02/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.68*		*8.00*		*96.1*	*70-130*			
LCS (2610001-BS2)									Prepared: 03/02/26 Analyzed: 03/02/26
Gasoline Range Organics (C6-C10)	50.3	20.0	50.0		101	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.78*		*8.00*		*97.2*	*70-130*			
Matrix Spike (2610001-MS2)				**Source: E602330-04**					Prepared: 03/02/26 Analyzed: 03/02/26
Gasoline Range Organics (C6-C10)	49.1	20.0	50.0	ND	98.2	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.73*		*8.00*		*96.7*	*70-130*			
Matrix Spike Dup (2610001-MSD2)				**Source: E602330-04**					Prepared: 03/02/26 Analyzed: 03/02/26
Gasoline Range Organics (C6-C10)	48.8	20.0	50.0	ND	97.5	70-130	0.672	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.63*		*8.00*		*95.4*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: RAS

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610021-BLK1)									Prepared: 03/02/26 Analyzed: 03/02/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*45.6*		*50.0*		*91.2*	*61-141*			
LCS (2610021-BS1)									Prepared: 03/02/26 Analyzed: 03/02/26
Diesel Range Organics (C10-C28)	241	25.0	250		96.3	66-144			
Surrogate: n-Nonane	*43.7*		*50.0*		*87.3*	*61-141*			
Matrix Spike (2610021-MS1)				**Source: E602337-21**					Prepared: 03/02/26 Analyzed: 03/02/26
Diesel Range Organics (C10-C28)	252	25.0	250	ND	101	56-156			
Surrogate: n-Nonane	*44.5*		*50.0*		*88.9*	*61-141*			
Matrix Spike Dup (2610021-MSD1)				**Source: E602337-21**					Prepared: 03/02/26 Analyzed: 03/02/26
Diesel Range Organics (C10-C28)	247	25.0	250	ND	98.8	56-156	1.91	20	
Surrogate: n-Nonane	*44.2*		*50.0*		*88.4*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/10/2026 10:38:09AM

Anions by EPA 300.0/9056A

Analyst: DT

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610005-BLK1)									Prepared: 03/02/26 Analyzed: 03/02/26
Chloride	ND	20.0							
LCS (2610005-BS1)									Prepared: 03/02/26 Analyzed: 03/02/26
Chloride	259	20.0	250		103	90-110			
Matrix Spike (2610005-MS1)				**Source: E602332-02**					Prepared: 03/02/26 Analyzed: 03/02/26
Chloride	713	20.0	250	388	130	80-120			M2
Matrix Spike Dup (2610005-MSD1)				**Source: E602332-02**					Prepared: 03/02/26 Analyzed: 03/02/26
Chloride	675	20.0	250	388	115	80-120	5.50	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/10/26 10:38

M2	Matrix spike recovery was outside quality control limits. The associated LCS spike recovery was acceptable.
ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E 602331	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
14:15	2/26/2026	S	1	FS100-9'		1						X						2.2
10:11	2/26/2026	S	1	FS113-4'		2						X						1.1
9:23	2/26/2026	S	1	SW47-4'-7'		3						X						2.5

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/27/26	7:11	Michelle Gonzales	2-27-26	0711
Michelle Gonzales	2-27-26	1430	Marissa Gonzales	2-27-26	1430
Marissa Gonzales	2-27-26	1900	Johnny Archuleta	2-27-26	1900
Johnny Archuleta	2-27-26	2245		3-2-26	0630

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 3/2/2026 10:05:55AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	03/02/26 06:30	Work Order ID:	E602331
Phone:	(505) 382-1211	Date Logged In:	02/27/26 15:40	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	03/06/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-NS
R-NV

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E602331	Job Number 01058-0007	1D 2D 3D Std: X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
14:15	2/26/2026	S	1	FS100-9'		1						X						2.2
10:11	2/26/2026	S	1	FS113-4'		2						X						1.1
9:23	2/26/2026	S	1	~~SW47-4'-7'~~ SW50-4'-7'		3						X						2.5

Analysis and Method

EPA Program

SDWA	CWA	RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone Corrected Sample Name per AM 3/10/26 cm

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	2/27/26	7:11	Michelle Gonzales	2-27-26	0711
Michelle Gonzales	2-27-26	1430	Marissa Gonzales	2-27-26	1430
Marissa Gonzales	2-27-26	1900	Johnny Archuleta	2-27-26	1900
Johnny Archuleta	2-27-26	2245		3-2-26	0630

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C _____

Sample Matrix: S - Soil, Sd - Solid, Sg - Sludge, A - Aqueous, O - Other _____

Container Type: g - glass, p - poly/plastic, ag - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E603006
Job Number:	01058-0007
Received:	3/3/2026

Revision: 1

Report Reviewed By:

Walter Hinchman
Laboratory Director
3/9/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 3/9/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E603006
Date Received: 3/3/2026 8:15:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 3/3/2026 8:15:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

SW48-4’-9’ 5

SW49-4’-9’ 6

QC Summary Data 7

QC - Volatile Organics by EPA 8021B 7

QC - Nonhalogenated Organics by EPA 8015D - GRO 8

QC - Nonhalogenated Organics by EPA 8015D - DRO/ORO 9

QC - Anions by EPA 300.0/9056A 10

Definitions and Notes 11

Chain of Custody etc. 12

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/09/26 09:50

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
SW48-4'-9'	E603006-01A	Soil	02/27/26	03/03/26	Glass Jar, 2 oz.
SW49-4'-9'	E603006-02A	Soil	02/27/26	03/03/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

SW48-4'-9'

E603006-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2610033
Benzene	ND	0.0250	1	03/03/26	03/03/26	
Ethylbenzene	ND	0.0250	1	03/03/26	03/03/26	
Toluene	ND	0.0250	1	03/03/26	03/03/26	
o-Xylene	ND	0.0250	1	03/03/26	03/03/26	
p,m-Xylene	ND	0.0500	1	03/03/26	03/03/26	
Total Xylenes	ND	0.0250	1	03/03/26	03/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*105 %*	*70-130*	*03/03/26*	*03/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2610033
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/03/26	03/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*94.6 %*	*70-130*	*03/03/26*	*03/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610037
Diesel Range Organics (C10-C28)	ND	25.0	1	03/03/26	03/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/03/26	03/03/26	
Surrogate: n-Nonane		*102 %*	*61-141*	*03/03/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2610035
Chloride	**677**	20.0	1	03/03/26	03/03/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

SW49-4'-9'

E603006-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2610033
Benzene	ND	0.0250	1	03/03/26	03/03/26	
Ethylbenzene	ND	0.0250	1	03/03/26	03/03/26	
Toluene	ND	0.0250	1	03/03/26	03/03/26	
o-Xylene	ND	0.0250	1	03/03/26	03/03/26	
p,m-Xylene	ND	0.0500	1	03/03/26	03/03/26	
Total Xylenes	ND	0.0250	1	03/03/26	03/03/26	
Surrogate: 4-Bromochlorobenzene-PID		*105 %*	*70-130*	*03/03/26*	*03/03/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2610033
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/03/26	03/03/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*93.8 %*	*70-130*	*03/03/26*	*03/03/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2610037
Diesel Range Organics (C10-C28)	**50.8**	25.0	1	03/03/26	03/03/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/03/26	03/03/26	
Surrogate: n-Nonane		*110 %*	*61-141*	*03/03/26*	*03/03/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2610035
Chloride	**765**	20.0	1	03/03/26	03/03/26	

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

Volatile Organics by EPA 8021B

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610033-BLK1)									Prepared: 03/03/26 Analyzed: 03/03/26
Benzene	ND	0.0250							
Ethylbenzene	ND	0.0250							
Toluene	ND	0.0250							
o-Xylene	ND	0.0250							
p,m-Xylene	ND	0.0500							
Total Xylenes	ND	0.0250							
Surrogate: 4-Bromochlorobenzene-PID	*8.50*		*8.00*		*106*	*70-130*			
LCS (2610033-BS1)									Prepared: 03/03/26 Analyzed: 03/03/26
Benzene	3.75	0.0250	5.00		75.0	70-130			
Ethylbenzene	3.53	0.0250	5.00		70.5	70-130			
Toluene	3.66	0.0250	5.00		73.2	70-130			
o-Xylene	3.60	0.0250	5.00		72.0	70-130			
p,m-Xylene	7.21	0.0500	10.0		72.1	70-130			
Total Xylenes	10.8	0.0250	15.0		72.1	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.32*		*8.00*		*104*	*70-130*			
Matrix Spike (2610033-MS1)				**Source: E603005-11**					Prepared: 03/03/26 Analyzed: 03/03/26
Benzene	4.70	0.0250	5.00	ND	94.1	70-130			
Ethylbenzene	4.51	0.0250	5.00	ND	90.1	70-130			
Toluene	4.64	0.0250	5.00	ND	92.7	70-130			
o-Xylene	4.60	0.0250	5.00	ND	92.0	70-130			
p,m-Xylene	9.19	0.0500	10.0	ND	91.9	70-130			
Total Xylenes	13.8	0.0250	15.0	ND	91.9	70-130			
Surrogate: 4-Bromochlorobenzene-PID	*8.43*		*8.00*		*105*	*70-130*			
Matrix Spike Dup (2610033-MSD1)				**Source: E603005-11**					Prepared: 03/03/26 Analyzed: 03/03/26
Benzene	4.85	0.0250	5.00	ND	97.0	70-130	3.13	27	
Ethylbenzene	4.66	0.0250	5.00	ND	93.2	70-130	3.38	26	
Toluene	4.77	0.0250	5.00	ND	95.5	70-130	2.93	20	
o-Xylene	4.78	0.0250	5.00	ND	95.5	70-130	3.70	25	
p,m-Xylene	9.50	0.0500	10.0	ND	95.0	70-130	3.32	23	
Total Xylenes	14.3	0.0250	15.0	ND	95.1	70-130	3.45	26	
Surrogate: 4-Bromochlorobenzene-PID	*8.40*		*8.00*		*105*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

Nonhalogenated Organics by EPA 8015D - GRO

Analyst: BA

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610033-BLK1)									Prepared: 03/03/26 Analyzed: 03/03/26
Gasoline Range Organics (C6-C10)	ND	20.0							
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.61*		*8.00*		*95.1*	*70-130*			
LCS (2610033-BS2)									Prepared: 03/03/26 Analyzed: 03/03/26
Gasoline Range Organics (C6-C10)	56.1	20.0	50.0		112	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.65*		*8.00*		*95.6*	*70-130*			
Matrix Spike (2610033-MS2)				**Source: E603005-11**					Prepared: 03/03/26 Analyzed: 03/03/26
Gasoline Range Organics (C6-C10)	55.4	20.0	50.0	ND	111	70-130			
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.56*		*8.00*		*94.5*	*70-130*			
Matrix Spike Dup (2610033-MSD2)				**Source: E603005-11**					Prepared: 03/03/26 Analyzed: 03/03/26
Gasoline Range Organics (C6-C10)	56.6	20.0	50.0	ND	113	70-130	2.19	20	
Surrogate: 1-Chloro-4-fluorobenzene-FID	*7.66*		*8.00*		*95.7*	*70-130*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

Nonhalogenated Organics by EPA 8015D - DRO/ORO

Analyst: KH

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610037-BLK1)									Prepared: 03/03/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	ND	25.0							
Oil Range Organics (C28-C36)	ND	50.0							
Surrogate: n-Nonane	*50.2*		*50.0*		*100*	*61-141*			
LCS (2610037-BS1)									Prepared: 03/03/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	250	25.0	250		100	66-144			
Surrogate: n-Nonane	*50.0*		*50.0*		*100*	*61-141*			
Matrix Spike (2610037-MS1)				**Source: E603005-05**					Prepared: 03/03/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	302	25.0	250	ND	121	56-156			
Surrogate: n-Nonane	*57.0*		*50.0*		*114*	*61-141*			
Matrix Spike Dup (2610037-MSD1)				**Source: E603005-05**					Prepared: 03/03/26 Analyzed: 03/03/26
Diesel Range Organics (C10-C28)	278	25.0	250	ND	111	56-156	8.54	20	
Surrogate: n-Nonane	*52.2*		*50.0*		*104*	*61-141*			

QC Summary Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/9/2026 9:50:02AM

Anions by EPA 300.0/9056A

Analyst: TP

Analyte	Result	Reporting Limit	Spike Level	Source Result	Rec	Rec Limits	RPD	RPD Limit	Notes
	mg/kg	mg/kg	mg/kg	mg/kg	%	%	%	%	
Blank (2610035-BLK1)									Prepared: 03/03/26 Analyzed: 03/03/26
Chloride	ND	20.0							
LCS (2610035-BS1)									Prepared: 03/03/26 Analyzed: 03/03/26
Chloride	259	20.0	250		104	90-110			
Matrix Spike (2610035-MS1)				**Source: E603005-07**					Prepared: 03/03/26 Analyzed: 03/03/26
Chloride	268	40.0	250	ND	107	80-120			
Matrix Spike Dup (2610035-MSD1)				**Source: E603005-07**					Prepared: 03/03/26 Analyzed: 03/03/26
Chloride	274	40.0	250	ND	110	80-120	2.23	20	

QC Summary Report Comment:
Calculations are based off of the raw (non-rounded) data. However, for reporting purposes all QC data is rounded to three significant figures. Therefore, hand calculated values may differ slightly.

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/09/26 09:50

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E603006	Job Number 01058 0007	1D 2D 3D Std: — — — X	NM CO UT TX: X
Project: Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
12:26	2/27/2026	S	1	SW48-4'-9'		1						X						4.3
12:29	2/27/2026	S	1	SW49-4'-9'		2						X						3.5

Analysis and Method

EPA Program

SDWA	CWA	RCRA

Compliance Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	3/2/26	7:11	Michelle Gonzales	3.2.26	0911
Michelle Gonzales	3-2-26	1330	Marissa Gonzales	3.2-26	1330
Marissa Gonzales	3-2-26	1730	Johnny Archuleta	3-2-26	1730
Johnny Archuleta	3-2-26	2115	Brittle Mar	3.3.26	815

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) / N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, **v** - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 3/3/2026 8:59:56AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	03/03/26 08:15	Work Order ID:	E603006
Phone:	(505) 382-1211	Date Logged In:	03/02/26 16:14	Logged In By:	Noe Soto
Email:	agiovengo@ensolum.com	Due Date:	03/09/26 17:00 (4 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Comments/Resolution

L-CM
R-NS

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

Report to:

Ashley Giovengo



5796 U.S. Hwy 64
Farmington, NM 87401

Phone: (505) 632-1881
Envirotech-inc.com

envirotech

Practical Solutions for a Better Tomorrow

Analytical Report

Devon Energy - Carlsbad

Project Name:	Jones Federal B3 Battery
Work Order:	E603130
Job Number:	01058-0007
Received:	3/13/2026

Revision: 0

Report Reviewed By:

Draft
Walter Hinchman
Laboratory Director
3/13/26

Envirotech Inc. certifies the test results meet all requirements of TNI unless noted otherwise.
Statement of Data Authenticity: Envirotech Inc, attests the data reported has not been altered in any way.
Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech Inc.
Envirotech Inc, holds the Utah TNI certification NM00979 for data reported.
Envirotech Inc, holds the Texas TNI certification T104704557 for data reported.

Date Reported: 3/13/26

Ashley Giovengo
333 W Sheridan Avenue
Oklahoma City, OK 73102-5010

Project Name: Jones Federal B3 Battery
Workorder: E603130
Date Received: 3/13/2026 7:30:00AM

Ashley Giovengo,

Thank you for choosing Envirotech, Inc. as your analytical testing laboratory for the sample(s) received on, 3/13/2026 7:30:00AM, under the Project Name: Jones Federal B3 Battery.

The analytical test results summarized in this report with the Project Name: Jones Federal B3 Battery apply to the individual samples collected, identified and submitted bearing the project name on the enclosed chain-of-custody. Subcontracted sample analyses not conducted by Envirotech, Inc., are attached in full as issued by the subcontract laboratory.

Please review the Chain-of-Custody (COC) and Sample Receipt Checklist (SRC) for any issues reguarding sample receipt temperature, containers, preservation etc. To best understand your test results, review the entire report summarizing your sample data and the associated quality control batch data.

All reported data in this analytical report were analyzed according to the referenced method(s) and are in compliance with the latest NELAC/TNI standards, unless otherwise noted. Samples or analytical quality control parameters not meeting specific QC criteria are qualified with a data flag. Data flag definitions are located in the Notes and Definitions section of this analytical report.

If you have any questions concerning this report, please feel free to contact Envirotech, Inc.

Respectfully,

Walter Hinchman
Laboratory Director
Office: 505-632-1881
Cell: 775-287-1762
whinchman@envirotech-inc.com

Raina Schwanz
Laboratory Administrator
Office: 505-632-1881
rainaschwanz@envirotech-inc.com

Field Offices:

Southern New Mexico Area

Lynn Jarboe
Laboratory Technical Representative
Office: 505-421-LABS(5227)
Cell: 505-320-4759
ljarboe@envirotech-inc.com

Michelle Gonzales
Client Representative
Office: 505-421-LABS(5227)
Cell: 505-947-8222
mgonzales@envirotech-inc.com

Envirotech Web Address: www.envirotech-inc.com

Table of Contents

Title Page 1

Cover Page 2

Table of Contents 3

Sample Summary 4

Sample Data 5

FS44-16’ 5

SW51-7’-16’ 6

SW52-7’-16’ 7

SW53-7’-16’ 8

SW54-7’-16’ 9

SW55-7’-16’ 10

Definitions and Notes 11

Chain of Custody etc. 12

Sample Summary

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	**Reported:**
333 W Sheridan Avenue	Project Number:	01058-0007	
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/13/26 14:33

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
FS44-16'	E603130-01A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.
SW51-7'-16'	E603130-02A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.
SW52-7'-16'	E603130-03A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.
SW53-7'-16'	E603130-04A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.
SW54-7'-16'	E603130-05A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.
SW55-7'-16'	E603130-06A	Soil	03/11/26	03/13/26	Glass Jar, 2 oz.

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

FS44-16'

E603130-01

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: SL			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	**0.0331**	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	**0.0612**	0.0500	1	03/13/26	03/13/26	
Total Xylenes	**0.0943**	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.5 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: SL			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*104 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	**80.7**	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*107 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2611155
Chloride	**293**	20.0	1	03/13/26	03/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

SW51-7'-16'

E603130-02

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	ND	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	ND	0.0500	1	03/13/26	03/13/26	
Total Xylenes	ND	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.5 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*97.4 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	ND	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*103 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2611155
Chloride	**130**	20.0	1	03/13/26	03/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

SW52-7'-16'

E603130-03

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	ND	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	ND	0.0500	1	03/13/26	03/13/26	
Total Xylenes	ND	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*94.6 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*101 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	ND	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*96.4 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2611155
Chloride	**457**	20.0	1	03/13/26	03/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

SW53-7'-16'

E603130-04

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	ND	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	ND	0.0500	1	03/13/26	03/13/26	
Total Xylenes	ND	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.1 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.0 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	ND	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*96.4 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2611155
Chloride	ND	20.0	1	03/13/26	03/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

SW54-7'-16'

E603130-05

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	ND	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	ND	0.0500	1	03/13/26	03/13/26	
Total Xylenes	ND	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*95.6 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*99.5 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	**67.1**	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*101 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: TP			Batch: 2611155
Chloride	**398**	20.0	1	03/13/26	03/13/26	

Sample Data

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	3/13/2026 2:33:52PM

SW55-7'-16'

E603130-06

Analyte	Result	Reporting Limit	Dilution	Prepared	Analyzed	Notes
Volatile Organics by EPA 8021B	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Benzene	ND	0.0250	1	03/13/26	03/13/26	
Ethylbenzene	ND	0.0250	1	03/13/26	03/13/26	
Toluene	ND	0.0250	1	03/13/26	03/13/26	
o-Xylene	ND	0.0250	1	03/13/26	03/13/26	
p,m-Xylene	ND	0.0500	1	03/13/26	03/13/26	
Total Xylenes	ND	0.0250	1	03/13/26	03/13/26	
Surrogate: 4-Bromochlorobenzene-PID		*93.5 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - GRO	mg/kg	mg/kg	Analyst: BA			Batch: 2611156
Gasoline Range Organics (C6-C10)	ND	20.0	1	03/13/26	03/13/26	
Surrogate: 1-Chloro-4-fluorobenzene-FID		*98.6 %*	*70-130*	*03/13/26*	*03/13/26*	
Nonhalogenated Organics by EPA 8015D - DRO/ORO	mg/kg	mg/kg	Analyst: KH			Batch: 2611161
Diesel Range Organics (C10-C28)	**74.2**	25.0	1	03/13/26	03/13/26	
Oil Range Organics (C28-C36)	ND	50.0	1	03/13/26	03/13/26	
Surrogate: n-Nonane		*105 %*	*61-141*	*03/13/26*	*03/13/26*	
Anions by EPA 300.0/9056A	mg/kg	mg/kg	Analyst: IY			Batch: 2611155
Chloride	**159**	20.0	1	03/13/26	03/13/26	

Definitions and Notes

Devon Energy - Carlsbad	Project Name:	Jones Federal B3 Battery	
333 W Sheridan Avenue	Project Number:	01058-0007	**Reported:**
Oklahoma City OK, 73102-5010	Project Manager:	Ashley Giovengo	03/13/26 14:33

ND	Analyte NOT DETECTED at or above the reporting limit
NR	Not Reported
RPD	Relative Percent Difference
DNI	Did Not Ignite
DNR	Did not react with the addition of acid or base.

Note (1): Methods marked with ** are non-accredited methods.

Note (2): Soil data is reported on an "as received" weight basis, unless reported otherwise.

Released to Imaging: 6/17/2026 3:16:23 PM
Received by OCD: 5/4/2026 10:36:24 AM

Chain of Custody EE - 176479.01.ABD

Client Information	Invoice Information	Lab Use Only	TAT	State
Client: Devon	Company: Devon Energy	Lab WO# E603130	Job Number 01058-0007	1D: X, 3D: *	NM: X
Project: ~~Cotton Draw Unit 114H Battery~~ Jones Federal B3 Battery	Address: 5315 Buena Vista Dr			
Project Manager: Ashley Giovengo	City, State, Zip: Carlsbad NM, 88220			
Address: 3122 National Parks Hwy	Phone: (575)689-7597			
City, State, Zip: Carlsbad NM, 88220	Email: jim.raley@dvn.com			
Phone: 575-988-0055	Miscellaneous: Jim Raley			
Email: agiovengo@ensolum.com				

Sample Information

Time Sampled	Date Sampled	Matrix	No. of Containers	Sample ID	Field Filter	Lab Number	DRO/ORO by 8015	GRO/DRO by 8015	BTEX by 8021	VOC by 8260	Chloride 300.0	BGDOC - NM	TCEQ 1005 - TX	RCRA 8 Metals				Remarks
10:45	3/11/2026	S	1	FS44-16'		1						X						3.6
11:45	3/11/2026	S	1	SW51-7'-16'		2						X						3.4
11:51	3/11/2026	S	1	SW52-7'-16'		3						X						4.0
11:56	3/11/2026	S	1	SW53-7'-16'		4						X						4.3
11:59	3/11/2026	S	1	SW54-7'-16'		5						X						4.3
12:06	3/11/2026	S	1	SW55-7'-16'		6						X						4.8

Analysis and Method

EPA Program: SDWA | CWA | RCRA

Compliance: Y or N

PWSID #

Additional Instructions: Please CC: cburton@ensolum.com, agiovengo@ensolum.com, jim.raley@dvn.com, iestrella@ensolum.com, chamilton@ensolum.com, bsimmons@ensolum.com

I, (field sampler), attest to the validity and authenticity of this sample. I am aware that tampering with or intentionally mislabeling the sample location, date or time of collection is considered fraud and may be grounds for legal action.

Sampled by: _Aboubakar Kone

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	3/12/26	7-11	Michelle Gonzales	3-12-26	0711
Michelle Gonzales	3-12-26	1600	Marissa Gonzales	3-12-26	1600
Marissa Gonzales	3-12-26	2015	Johnny Archuleta	3-12-26	2015
Johnny Archuleta	3-12-26	0015	Cath Mava	3.13.26	730

Samples requiring thermal preservation must be received on ice the day they are sampled or received packed in ice at an avg temp above 0 but less than 6 °C on subsequent days.

Lab Use Only

Received on ice: (Y) N

T1 _____ T2 _____ T3 _____

AVG Temp °C_____

Sample Matrix: **S** - Soil, **Sd** - Solid, **Sg** - Sludge, **A** - Aqueous, **O** - Other _____

Container Type: **g** - glass, **p** - poly/plastic, **ag** - amber glass, v - VOA

Note: Samples are discarded 14 days after results are reported unless other arrangements are made. Hazardous samples will be returned to client or disposed of at the client expense. The report for the analysis of the above samples is applicable only to those samples received by the laboratory with this COC. The liability of the laboratory is limited to the amount paid for on the report.

envirotech

Envirotech Analytical Laboratory

Printed: 3/13/2026 10:50:32AM

Sample Receipt Checklist (SRC)

Instructions: Please take note of any NO checkmarks.
If we receive no response concerning these items within 24 hours of the date of this notice, all the samples will be analyzed as requested.

Client:	Devon Energy - Carlsbad	Date Received:	03/13/26 07:30	Work Order ID:	E603130
Phone:	(505) 382-1211	Date Logged In:	03/13/26 07:29	Logged In By:	Caitlin Mars
Email:	agiovengo@ensolum.com	Due Date:	03/13/26 17:00 (0 day TAT)		

Chain of Custody (COC)

1. Does the sample ID match the COC?	Yes	
2. Does the number of samples per sampling site location match the COC	Yes	
3. Were samples dropped off by client or carrier?	Yes	Carrier: Courier
4. Was the COC complete, i.e., signatures, dates/times, requested analyses?	Yes	
5. Were all samples received within holding time? Note: Analysis, such as pH which should be conducted in the field, i.e, 15 minute hold time, are not included in this disucssion.	Yes	

Sample Turn Around Time (TAT)

6. Did the COC indicate standard TAT, or Expedited TAT?	Yes	

Sample Cooler

7. Was a sample cooler received?	Yes	
8. If yes, was cooler received in good condition?	Yes	
9. Was the sample(s) received intact, i.e., not broken?	Yes	
10. Were custody/security seals present?	No	
11. If yes, were custody/security seals intact?	NA	
12. Was the sample received on ice? Note: Thermal preservation is not required, if samples are received within 15 minutes of sampling	Yes	
13. See COC for individual sample temps. Samples outside of 0°C-6°C will be recorded in comments.		

Comments/Resolution

L-CM
R-NV

Sample Container

14. Are aqueous VOC samples present?	No	
15. Are VOC samples collected in VOA Vials?	NA	
16. Is the head space less than 6-8 mm (pea sized or less)?	NA	
17. Was a trip blank (TB) included for VOC analyses?	NA	
18. Are non-VOC samples collected in the correct containers?	Yes	
19. Is the appropriate volume/weight or number of sample containers collected?	Yes	

Field Label

20. Were field sample labels filled out with the minimum information:		
Sample ID?	Yes	
Date/Time Collected?	Yes	
Collectors name?	Yes	

Sample Preservation

21. Does the COC or field labels indicate the samples were preserved?	No	
22. Are sample(s) correctly preserved?	NA	
24. Is lab filtration required and/or requested for dissolved metals?	No	

Multiphase Sample Matrix

26. Does the sample have more than one phase, i.e., multiphase?	No	
27. If yes, does the COC specify which phase(s) is to be analyzed?	NA	

Subcontract Laboratory

28. Are samples required to get sent to a subcontract laboratory?	No	
29. Was a subcontract laboratory specified by the client and if so who?	NA	Subcontract Lab: NA

Client Instruction

Signature of client authorizing changes to the COC or sample disposition.

Date

envirotech Inc.

ENSOLUM

APPENDIX F

NMOCD Correspondence

From: Velez, Nelson, EMNRD
To: Cole Burton
Cc: Ashley Giovengo; Raley, Jim; Bratcher, Michael, EMNRD; Buchanan, Michael, EMNRD
Subject: Re: [EXTERNAL] Alternative Sampling Plan - Jones Federal B 3 Battery - nAPP2520569781
Date: Wednesday, January 21, 2026 8:02:41 AM
Attachments: image001.png
image002.png
image003.png
Outlook-4sodan05.png

[**EXTERNAL EMAIL**]
Good morning Cole,

Thank you for the request.

Your alternative sampling plan request not to exceed 400 square feet ($ft.^2$) from the excavation floor and 200 $ft.^2$ from the excavation sidewalls for each five (5) point composite per 19.15.29.12D (1b) NMAC is approved. All other provisions addressed in 19.15.29.12D NMAC remain in effect.

Please keep a copy of this communication for inclusion within the appropriate report submittal.

Have a safe and productive day!

Regards,

Nelson Velez • Senior Environmental Scientist
Environmental Bureau | EMNRD - Oil Conservation Division
1000 Rio Brazos Road | Aztec, NM 87410
(505) 469-6146 | nelson.velez@emnrd.nm.gov
http://www.emnrd.nm.gov/ocd

From: Buchanan, Michael, EMNRD <Michael.Buchanan@emnrd.nm.gov>
Sent: Tuesday, January 20, 2026 9:45 AM
To: Velez, Nelson, EMNRD <Nelson.Velez@emnrd.nm.gov>
Cc: Bratcher, Michael, EMNRD <mike.bratcher@emnrd.nm.gov>
Subject: FW: [EXTERNAL] Alternative Sampling Plan - Jones Federal B 3 Battery - nAPP2520569781

From: Cole Burton <cburton@ensolum.com>
Sent: Tuesday, January 20, 2026 8:57 AM
To: Enviro, OCD, EMNRD <OCD.Enviro@emnrd.nm.gov>
Cc: Ashley Giovengo <agiovengo@ensolum.com>; Raley, Jim <Jim.Raley@dvn.com>
Subject: [EXTERNAL] Alternative Sampling Plan - Jones Federal B 3 Battery - nAPP2520569781

CAUTION: This email originated outside of our organization. Exercise caution prior to clicking on links or opening attachments.

Hello,
Devon Energy Production Company, LP (Devon) is requesting an alternative sampling plan at the Jones Federal B 3 Battery (Site). On July 24, 2025, Lightning struck the tank battery, catching the remaining fluids in the production tank on fire. This resulted in the release of approximately 5 barrels (bbls) of crude oil and 2 bbls of produced water; 5 bbls of crude oil and 2 bbls of produced water were recovered from the release area. Devon reported the release to the New Mexico Oil Conservation Division (NMOCD) on July 24, 2025, and subsequently the release was assigned Incident Number nAPP2520569781. The release impacted an area approximately 12,395 square feet (sq. ft.) in size on Federal Land managed by the Bureau of Land Management (BLM). The closest permitted well with available depth to groundwater data is New Mexico Office of the State Engineer (NMOSE) soil boring CP 02091 POD1, located on Site; CP 02091 POD1 has a reported depth to water of greater than 105 feet below ground surface (bgs). A desktop review for potential site receptors has been completed, and the site is greater than 1,000 ft. to a freshwater well or spring and is not within a 100-year floodplain or overlying a subsurface mine (see Figure 1). The closest significant watercourse is an intermittent dry wash located approximately 0.9 miles southeast of the Site. The Site is not underlain by unstable geology (low potential karst designation area) and there are no indicators of surface or subsurface karst features observed at the Site. Based on the results of the desktop review, the following Site Closure Criteria will apply: 10 mg/kg benzene, 50 mg/kg BTEX, 1,000 mg/kg TPH – Gasoline Range Organics (GRO) and TPH – Diesel Range Organics (DRO), 2,500 mg/kg Total TPH and 20,000 mg/kg chloride.
Lateral and vertical delineation soil sampling has been completed at the Site (see Table 1 and Figure 2). Eighteen lateral delineation soil sample locations (SS01 through SS18) were collected from around the release extent at ground surface; lateral delineation soil samples SS02 and SS04 through SS18 were also collected at 1-foot bgs via hand auger. Lateral delineation soil samples SS01, SS03, SS05, SS06, SS08, SS10, SS11 and SS13 through SS18 were all in compliance with the strictest Closure Criteria per NMOCD Table I at ground surface. Vertical delineation soil sample locations (BH03, BH04, BH06, BH09 through BH13, BH16, BH18 and BH21) were all in compliance with the strictest Closure Criteria at depths ranging from 3 feet to 50 feet bgs (see Table 1). The Site will be reclaimed and will be excavated in accordance with the reclamation requirement for the top 4 feet of soils and in accordance with the Site Closure Criteria at depths greater than 4 feet bgs. Devon would like to request an alternative sampling plan for excavation floor samples collected every 400 sq. ft. from the floor of the excavation and every 200 sq. ft. from the sidewalls of the excavation where applicable. Excavation of the subject matter release will begin as soon as Devon selects a subcontractor. Devon will submit a closure report required in 19.15.29.12.B.(1) NMAC following excavation and confirmation soil sampling activities. Devon believes this alternative sampling plan will provide equal or better protection of public health, and the environment considering the Site is in a low potential karst designation area, and depth to groundwater at the Site is confirmed to be greater than 105 feet bgs. Devon respectfully requests approval for this *alternative sampling plan* associated with Incident Number (nAPP2520569781).
Thanks,

Cole Burton
Project Manager
575-706-5056
Ensolum, LLC

From:	Velez, Nelson, EMNRD
To:	Cole Burton
Cc:	Ashley Giovengo; Raley, Jim; Bratcher, Michael, EMNRD; Wells, Shelly, EMNRD
Subject:	Re: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781
Date:	Tuesday, January 20, 2026 11:44:39 AM
Attachments:	image001.png image002.png image003.png Outlook-brzjzpgn.png

[**EXTERNAL EMAIL**]

Cole,

Your 90-day time extension is denied. This is the second consecutive request and as you stated, the remediation activity initiated the day before the deadline (January 20, 2026). Please submit the appropriate or final remediation closure report as soon as possible.

Please keep a copy of this communication for inclusion within the appropriate report submittal.

Regards,

Nelson Velez ● Senior Environmental Scientist
Environmental Bureau | EMNRD - Oil Conservation Division
1000 Rio Brazos Road | Aztec, NM 87410
(505) 469-6146 | nelson.velez@emnrd.nm.gov
http://www.emnrd.nm.gov/ocd

From: Wells, Shelly, EMNRD <Shelly.Wells@emnrd.nm.gov>
Sent: Thursday, January 15, 2026 9:31 AM
To: Velez, Nelson, EMNRD <Nelson.Velez@emnrd.nm.gov>
Cc: Bratcher, Michael, EMNRD <mike.bratcher@emnrd.nm.gov>
Subject: FW: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781

From: Cole Burton <cburton@ensolum.com>
Sent: Thursday, January 15, 2026 9:15 AM

To: Enviro, OCD, EMNRD <OCD.Enviro@emnrd.nm.gov>
Cc: Ashley Giovengo <agiovengo@ensolum.com>; Raley, Jim <Jim.Raley@dvn.com>
Subject: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781

CAUTION: This email originated outside of our organization. Exercise caution prior to clicking on links or opening attachments.

Hello all,

Devon Energy Production Company, LP (Devon) is requesting an extension of the current deadline of January 20, 2026, for submitting a remediation work plan or closure report required in 19.15.29.12.B.(1) NMAC at the Jones Federal B 3 Battery (Site) (Incident Number nAPP2520569781). The release/fire occurred on July 24, 2025, and 2 barrels (bbls) of produced water and 5 bbls of crude oil were released; 0 bbls of produced water and 0 bbls of crude oil were recovered. The release impacted an area on-pad approximately 6,728 square feet in size and an off-pad area approximately 6,744 square feet in size on Federal Land managed by the Bureau of Land Management (BLM). Lateral delineation soil sampling in accordance with the strictest Closure Criteria per NMOCD Table I has been completed at the Site (see Table 1 and Figure 2). Devon has selected a subcontractor, and excavation of the subject matter release is scheduled to begin on January 19, 2026. Devon intends to submit a work plan or closure report upon receiving final laboratory analytical data from confirmation sampling activities. Devon respectfully requests a 90-day extension until April 20, 2026. Please let me know if you have any further questions regarding this site.

Thanks,

Cole Burton
Project Manager
575-706-5056
Ensolum, LLC

From:	Velez, Nelson, EMNRD
To:	Cole Burton
Cc:	Ashley Giovengo; Raley, Jim; Bratcher, Michael, EMNRD; Rodgers, Scott, EMNRD
Subject:	Re: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781
Date:	Tuesday, October 21, 2025 3:05:17 PM
Attachments:	image001.png image002.png image003.png Outlook-lr3nka03.png

[**EXTERNAL EMAIL**]
Good afternoon Cole,

Thank you for the correspondence.

Your 90-day time extension request is approved. Remediation Due date has been updated to January 20, 2025.

Please keep a copy of this communication for inclusion within the appropriate report submittal.

The OCD requires a copy of all correspondence related to remedial activities to be included in all proposals and/or final closure reports. Correspondence required to be included in reports may include, but not limited to, notifications for liner inspections, sample events, request for time extensions, an alternative sampling plan, and/or variances.

Regards,

Nelson Velez ● Environmental Specialist - Adv
Environmental Bureau | EMNRD - Oil Conservation Division
1000 Rio Brazos Road | Aztec, NM 87410
(505) 469-6146 | nelson.velez@emnrd.nm.gov
http://www.emnrd.nm.gov/ocd

From: Rodgers, Scott, EMNRD <Scott.Rodgers@emnrd.nm.gov>
Sent: Tuesday, October 21, 2025 7:51 AM
To: Velez, Nelson, EMNRD <Nelson.Velez@emnrd.nm.gov>
Cc: Bratcher, Michael, EMNRD <mike.bratcher@emnrd.nm.gov>
Subject: FW: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781

Scott Rodgers ● Environmental Specialist – Adv.

Environmental Bureau
EMNRD - Oil Conservation Division
5200 Oakland NE, Suite B | Albuquerque, NM 87113
505.469.1830 | scott.rodgers@emnrd.nm.gov
http://www.emnrd.nm.gov/ocd

From: Cole Burton <cburton@ensolum.com>
Sent: Tuesday, October 21, 2025 7:19 AM
To: Enviro, OCD, EMNRD <OCD.Enviro@emnrd.nm.gov>
Cc: Ashley Giovengo <agiovengo@ensolum.com>; Raley, Jim <Jim.Raley@dvn.com>
Subject: [EXTERNAL] Extension Request - Devon Energy Production Company, LP - Jones Federal B 3 Battery - nAPP2520569781

CAUTION: This email originated outside of our organization. Exercise caution prior to clicking on links or opening attachments.

Hello all,

Devon Energy Production Company, LP (Devon) is requesting an extension for the current deadline of October 23, 2025, for submitting a remediation work plan or closure report required in 19.15.29.12.B.(1) NMAC at the Jones Federal B 3 Battery (Site) (Incident Number nAPP2520569781). The release/fire occurred on July 13, 2025, and 2 barrels (bbls) of produced water and 5 bbls of crude oil were released; 0 bbls of produced water and 0 bbls of crude oil were recovered. The release impacted an area on-pad approximately 6,728 square feet in size and an off-pad area approximately 6,744 square feet in size on Federal Land managed by the Bureau of Land Management (BLM). Lateral delineation soil sampling in accordance with the strictest Closure Criteria per NMOCD Table I criteria has been completed at the Site (see Table 1 and Figure 2). Excavation of the subject matter release will begin as soon as Devon selects a subcontractor. All equipment has been removed and Devon intends to reclaim the Site. Devon intends to submit a work plan or closure report upon receiving final laboratory analytical data from confirmation sampling activities. Devon respectfully requests a 90-day extension until January 21, 2026. Please let me know if you have any further questions regarding this site.

Thanks,

Cole Burton
Project Manager
575-706-5056
Ensolum, LLC

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544232

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544232
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/21/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	6137
	Action Number: 544232
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544234

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544234
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/22/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	6137
	Action Number: 544234
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544235

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544235
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/23/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	6137
	Action Number: 544235
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544236

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544236
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/23/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544236
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544237

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544237
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/26/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	6137
	Action Number: 544237
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544238

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544238
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/27/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544238
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544239

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544239
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/28/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544239
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544240

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544240
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/29/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544240
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544241

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544241
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/29/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544241
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 544242

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544242
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	01/30/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 544242
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/19/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/19/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 547374

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547374
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/02/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547374
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/28/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/28/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 547376

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547376
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/03/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547376
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/28/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/28/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 547377

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547377
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/04/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547377
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/28/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/28/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 547379

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547379
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/06/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547379
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/28/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/28/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 547385

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547385
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/05/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 547385
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	1/28/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	1/28/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 549916

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549916
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/09/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549916
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/3/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/3/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 549927

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549927
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/12/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 549927

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549927
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/3/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/3/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 549933

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549933
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/13/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 549933
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/3/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/3/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 553591

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 553591
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/16/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 553591
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/12/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/12/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 553592

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 553592
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/17/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator:	OGRID:
DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	6137
	Action Number: 553592
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/12/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/12/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 553593

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 553593
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/18/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 553593
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/12/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/12/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 556831

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 556831
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/25/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 556831

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 556831
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/23/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/23/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 556834

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 556834
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/26/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubukar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 556834
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/23/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/23/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Action 557385

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 557385
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nAPP2520569781**
Incident Name	**NAPP2520569781 JONES FEDERAL B 3 BATTERY @ FAPP2130540873**
Incident Type	**Fire**
Incident Status	**Initial C-141 Approved**
Incident Facility	**[fAPP2130540873] JONES FEDERAL B 3 BATTERY**

Location of Release Source	
Site Name	**JONES FEDERAL B 3 BATTERY**
Date Release Discovered	**07/24/2025**
Surface Owner	**Federal**

Sampling Event General Information *Please answer all the questions in this group.*	
What is the sampling surface area in square feet	44,032
What is the estimated number of samples that will be gathered	145
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	02/27/2026
Time sampling will commence	09:00 AM
Please provide any information necessary for observers to contact samplers	Aboubakar Kone 202-569-0491
Please provide any information necessary for navigation to sampling site	32.64265223, -103.824532

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 557385
	Action Type: [NOTIFY] Notification Of Sampling (C-141N)

CONDITIONS

Created By	Condition	Condition Date
jraley	Failure to notify the OCD of sampling events including any changes in date/time per the requirements of 19.15.29.12.D.(1).(a) NMAC, may result in the remediation closure samples not being accepted.	2/24/2026
jraley	If confirmation sampling is going to take place over multiple days, individual C-141N applications must be submitted for each sampling date. Date ranges are not currently accepted on the C-141N application.	2/24/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Prerequisites	
Incident ID (n#)	**nMLB1129240104**
Incident Name	**NMLB1129240104 JONES FEDERAL B #3 @ 30-015-10394**
Incident Type	**Oil Release**
Incident Status	**Reclamation Report Received**
Incident Well	**[30-015-10394] JONES FEDERAL B #003**

Location of Release Source	
Please answer all the questions in this group.	
Site Name	JONES FEDERAL B #3
Date Release Discovered	10/01/2011
Surface Owner	Federal

Incident Details	
Please answer all the questions in this group.	
Incident Type	Oil Release
Did this release result in a fire or is the result of a fire	No
Did this release result in any injuries	No
Has this release reached or does it have a reasonable probability of reaching a watercourse	No
Has this release endangered or does it have a reasonable probability of endangering public health	No
Has this release substantially damaged or will it substantially damage property or the environment	No
Is this release of a volume that is or may with reasonable probability be detrimental to fresh water	No

Nature and Volume of Release	
Material(s) released, please answer all that apply below. Any calculations or specific justifications for the volumes provided should be attached to the follow-up C-141 submission.	
Crude Oil Released (bbls) Details	Cause: Equipment Failure | Separator | Crude Oil | Released: 32 BBL | Recovered: 24 BBL | Lost: 8 BBL.
Produced Water Released (bbls) Details	*Not answered.*
Is the concentration of chloride in the produced water >10,000 mg/l	No
Condensate Released (bbls) Details	*Not answered.*
Natural Gas Vented (Mcf) Details	*Not answered.*
Natural Gas Flared (Mcf) Details	*Not answered.*
Other Released Details	*Not answered.*
Are there additional details for the questions above (i.e. any answer containing Other, Specify, Unknown, and/or Fire, or any negative lost amounts)	*Not answered.*

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Nature and Volume of Release (continued)	
Is this a gas only submission (i.e. only significant Mcf values reported)	**No, according to supplied volumes this does not appear to be a "gas only" report.**
Was this a major release as defined by Subsection A of 19.15.29.7 NMAC	**Yes**
Reasons why this would be considered a submission for a notification of a major release	**From paragraph A. "Major release" determine using:** **(1) an unauthorized release of a volume, excluding gases, of 25 barrels or more.**

With the implementation of the 19.15.27 NMAC (05/25/2021), venting and/or flaring of natural gas (i.e. gas only) are to be submitted on the C-129 form.

Initial Response	
The responsible party must undertake the following actions immediately unless they could create a safety hazard that would result in injury.	
The source of the release has been stopped	True
The impacted area has been secured to protect human health and the environment	True
Released materials have been contained via the use of berms or dikes, absorbent pads, or other containment devices	True
All free liquids and recoverable materials have been removed and managed appropriately	True
If all the actions described above have not been undertaken, explain why	*Not answered.*

Per Paragraph (4) of Subsection B of 19.15.29.8 NMAC the responsible party may commence remediation immediately after discovery of a release. If remediation has begun, please prepare and attach a narrative of actions to date in the follow-up C-141 submission. If remedial efforts have been successfully completed or if the release occurred within a lined containment area (see Subparagraph (a) of Paragraph (5) of Subsection A of 19.15.29.11 NMAC), please prepare and attach all information needed for closure evaluation in the follow-up C-141 submission.

I hereby certify that the information given above is true and complete to the best of my knowledge and understand that pursuant to OCD rules and regulations all operators are required to report and/or file certain release notifications and perform corrective actions for releases which may endanger public health or the environment. The acceptance of a C-141 report by the OCD does not relieve the operator of liability should their operations have failed to adequately investigate and remediate contamination that pose a threat to groundwater, surface water, human health or the environment. In addition, OCD acceptance of a C-141 report does not relieve the operator of responsibility for compliance with any other federal, state, or local laws and/or regulations.

I hereby agree and sign off to the above statement	Name: James Raley Title: EHS Professional Email: jim.raley@dvn.com Date: 05/04/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Site Characterization	
Please answer all the questions in this group (only required when seeking remediation plan approval and beyond). This information must be provided to the appropriate district office no later than 90 days after the release discovery date.	
What is the shallowest depth to groundwater beneath the area affected by the release in feet below ground surface (ft bgs)	Between 26 and 50 (ft.)
What method was used to determine the depth to ground water	NM OSE iWaters Database Search
Did this release impact groundwater or surface water	No
What is the minimum distance, between the closest lateral extents of the release and the following surface areas:	
A continuously flowing watercourse or any other significant watercourse	Greater than 5 (mi.)
Any lakebed, sinkhole, or playa lake (measured from the ordinary high-water mark)	Between 1 and 5 (mi.)
An occupied permanent residence, school, hospital, institution, or church	Greater than 5 (mi.)
A spring or a private domestic fresh water well used by less than five households for domestic or stock watering purposes	Greater than 5 (mi.)
Any other fresh water well or spring	Between 1 and 5 (mi.)
Incorporated municipal boundaries or a defined municipal fresh water well field	Greater than 5 (mi.)
A wetland	Greater than 5 (mi.)
A subsurface mine	Greater than 5 (mi.)
An (non-karst) unstable area	Greater than 5 (mi.)
Categorize the risk of this well / site being in a karst geology	Low
A 100-year floodplain	Greater than 5 (mi.)
Did the release impact areas not on an exploration, development, production, or storage site	No

Remediation Plan	
Please answer all the questions that apply or are indicated. This information must be provided to the appropriate district office no later than 90 days after the release discovery date.	
Requesting a remediation plan approval with this submission	Yes
Attach a comprehensive report demonstrating the lateral and vertical extents of soil contamination associated with the release have been determined, pursuant to 19.15.29.11 NMAC and 19.15.29.13 NMAC.	
Have the lateral and vertical extents of contamination been fully delineated	Yes
Was this release entirely contained within a lined containment area	No
Soil Contamination Sampling: (Provide the highest observable value for each, in milligrams per kilograms.)	
Chloride (EPA 300.0 or SM4500 Cl B)	3000
TPH (GRO+DRO+MRO) (EPA SW-846 Method 8015M)	10266
GRO+DRO (EPA SW-846 Method 8015M)	15200
BTEX (EPA SW-846 Method 8021B or 8260B)	77.5
Benzene (EPA SW-846 Method 8021B or 8260B)	0.4
Per Subsection B of 19.15.29.11 NMAC unless the site characterization report includes completed efforts at remediation, the report must include a proposed remediation plan in accordance with 19.15.29.12 NMAC, which includes the anticipated timelines for beginning and completing the remediation.	
On what estimated date will the remediation commence	11/11/2024
On what date will (or did) the final sampling or liner inspection occur	11/15/2024
On what date will (or was) the remediation complete(d)	12/01/2024
What is the estimated surface area (in square feet) that will be reclaimed	200
What is the estimated volume (in cubic yards) that will be reclaimed	23
What is the estimated surface area (in square feet) that will be remediated	200
What is the estimated volume (in cubic yards) that will be remediated	23
These estimated dates and measurements are recognized to be the best guess or calculation at the time of submission and may (be) change(d) over time as more remediation efforts are completed.	
The OCD recognizes that proposed remediation measures may have to be minimally adjusted in accordance with the physical realities encountered during remediation. If the responsible party has any need to significantly deviate from the remediation plan proposed, then it should consult with the division to determine if another remediation plan submission is required.	

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Remediation Plan (continued)	
Please answer all the questions that apply or are indicated. This information must be provided to the appropriate district office no later than 90 days after the release discovery date.	
This remediation will (or is expected to) utilize the following processes to remediate / reduce contaminants:	
(Select all answers below that apply.)	
(Ex Situ) Excavation and **off-site** disposal (i.e. dig and haul, hydrovac, etc.)	Yes
Which OCD approved facility will be used for **off-site** disposal	fEEM0112340644 R360 ARTESIA LLC LANDFARM
OR which OCD approved well (API) will be used for **off-site** disposal	*Not answered.*
OR is the **off-site** disposal site, to be used, out-of-state	No
OR is the **off-site** disposal site, to be used, an NMED facility	No
(Ex Situ) Excavation and **on-site** remediation (i.e. On-Site Land Farms)	No
(In Situ) Soil Vapor Extraction	No
(In Situ) Chemical processing (i.e. Soil Shredding, Potassium Permanganate, etc.)	No
(In Situ) Biological processing (i.e. Microbes / Fertilizer, etc.)	No
(In Situ) Physical processing (i.e. Soil Washing, Gypsum, Disking, etc.)	No
Ground Water Abatement pursuant to 19.15.30 NMAC	No
OTHER (Non-listed remedial process)	No
Per Subsection B of 19.15.29.11 NMAC unless the site characterization report includes completed efforts at remediation, the report must include a proposed remediation plan in accordance with 19.15.29.12 NMAC, which includes the anticipated timelines for beginning and completing the remediation.	
I hereby certify that the information given above is true and complete to the best of my knowledge and understand that pursuant to OCD rules and regulations all operators are required to report and/or file certain release notifications and perform corrective actions for releases which may endanger public health or the environment. The acceptance of a C-141 report by the OCD does not relieve the operator of liability should their operations have failed to adequately investigate and remediate contamination that pose a threat to groundwater, surface water, human health or the environment. In addition, OCD acceptance of a C-141 report does not relieve the operator of responsibility for compliance with any other federal, state, or local laws and/or regulations.	
I hereby agree and sign off to the above statement	Name: James Raley Title: EHS Professional Email: jim.raley@dvn.com Date: 05/04/2026
The OCD recognizes that proposed remediation measures may have to be minimally adjusted in accordance with the physical realities encountered during remediation. If the responsible party has any need to significantly deviate from the remediation plan proposed, then it should consult with the division to determine if another remediation plan submission is required.	

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Deferral Requests Only *Only answer the questions in this group if seeking a deferral upon approval this submission. Each of the following items must be confirmed as part of any request for deferral of remediation.*	
Requesting a deferral of the remediation closure due date with the approval of this submission	No

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Sampling Event Information	
Last sampling notification (C-141N) recorded	**404332**
Sampling date pursuant to Subparagraph (a) of Paragraph (1) of Subsection D of 19.15.29.12 NMAC	**11/20/2024**
What was the (estimated) number of samples that were to be gathered	**2**
What was the sampling surface area in square feet	**200**

Remediation Closure Request	
Only answer the questions in this group if seeking remediation closure for this release because all remediation steps have been completed.	
Requesting a remediation closure approval with this submission	Yes
Have the lateral and vertical extents of contamination been fully delineated	**Yes**
Was this release entirely contained within a lined containment area	**No**
All areas reasonably needed for production or subsequent drilling operations have been stabilized, returned to the sites existing grade, and have a soil cover that prevents ponding of water, minimizing dust and erosion	Yes
What was the total surface area (in square feet) remediated	730
What was the total volume (cubic yards) remediated	93
All areas not reasonably needed for production or subsequent drilling operations have been reclaimed to contain a minimum of four feet of non-waste contain earthen material with concentrations less than 600 mg/kg chlorides, 100 mg/kg TPH, 50 mg/kg BTEX, and 10 mg/kg Benzene	Yes
What was the total surface area (in square feet) reclaimed	730
What was the total volume (in cubic yards) reclaimed	730
Summarize any additional remediation activities not included by answers (above)	Previous areas were excavated in 2021 totaling 530 sq ft and 71 cy. S1 is the area is newly remediated and totaled 200 sq ft and 22 cy.

The responsible party must attach information demonstrating they have complied with all applicable closure requirements and any conditions or directives of the OCD. This demonstration should be in the form of a comprehensive report (in .pdf format) including a scaled site map, sampling diagrams, relevant field notes, photographs of any excavation prior to backfilling, laboratory data including chain of custody documents of final sampling, and a narrative of the remedial activities. Refer to 19.15.29.12 NMAC.

I hereby certify that the information given above is true and complete to the best of my knowledge and understand that pursuant to OCD rules and regulations all operators are required to report and/or file certain release notifications and perform corrective actions for releases which may endanger public health or the environment. The acceptance of a C-141 report by the OCD does not relieve the operator of liability should their operations have failed to adequately investigate and remediate contamination that pose a threat to groundwater, surface water, human health or the environment. In addition, OCD acceptance of a C-141 report does not relieve the operator of responsibility for compliance with any other federal, state, or local laws and/or regulations. The responsible party acknowledges they must substantially restore, reclaim, and re-vegetate the impacted surface area to the conditions that existed prior to the release or their final land use in accordance with 19.15.29.13 NMAC including notification to the OCD when reclamation and re-vegetation are complete.

I hereby agree and sign off to the above statement	Name: James Raley Title: EHS Professional Email: jim.raley@dvn.com Date: 05/04/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Reclamation Report	
Only answer the questions in this group if all reclamation steps have been completed.	
Requesting a reclamation approval with this submission	Yes
What was the total reclamation surface area (in square feet) for this site	44032
What was the total volume of replacement material (in cubic yards) for this site	11176
Per Paragraph (1) of Subsection D of 19.15.29.13 NMAC the reclamation must contain a minimum of four feet of non-waste containing, uncontaminated, earthen material with chloride concentrations less than 600 mg/kg as analyzed by EPA Method 300.0, or other test methods approved by the division. The soil cover must include a top layer, which is either the background thickness of topsoil or one foot of suitable material to establish vegetation at the site, whichever is greater.	
Is the soil top layer complete and is it suitable material to establish vegetation	Yes
On what (estimated) date will (or was) the reseeding commence(d)	04/15/2026
Summarize any additional reclamation activities not included by answers (above)	Reclamation Complete
The responsible party must attach information demonstrating they have complied with all applicable reclamation requirements and any conditions or directives of the OCD. This demonstration should be in the form of attachments (in .pdf format) including a scaled site map, any proposed reseeding plans or relevant field notes, photographs of reclaimed area, and a narrative of the reclamation activities. Refer to 19.15.29.13 NMAC.	
I hereby certify that the information given above is true and complete to the best of my knowledge and understand that pursuant to OCD rules and regulations all operators are required to report and/or file certain release notifications and perform corrective actions for releases which may endanger public health or the environment. The acceptance of a C-141 report by the OCD does not relieve the operator of liability should their operations have failed to adequately investigate and remediate contamination that pose a threat to groundwater, surface water, human health or the environment. In addition, OCD acceptance of a C-141 report does not relieve the operator of responsibility for compliance with any other federal, state, or local laws and/or regulations. The responsible party acknowledges they must substantially restore, reclaim, and re-vegetate the impacted surface area to the conditions that existed prior to the release or their final land use in accordance with 19.15.29.13 NMAC including notification to the OCD when reclamation and re-vegetation are complete.	
I hereby agree and sign off to the above statement	Name: James Raley Title: EHS Professional Email: jim.raley@dvn.com Date: 05/04/2026

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS (continued)

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

QUESTIONS

Revegetation Report	
Only answer the questions in this group if all surface restoration, reclamation and re-vegetation obligations have been satisfied.	
Requesting a restoration complete approval with this submission	No
Per Paragraph (4) of Subsection (D) of 19.15.29.13 NMAC for any major or minor release containing liquids, the responsible party must notify the division when reclamation and re-vegetation are complete.	

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: DEVON ENERGY PRODUCTION COMPANY, LP 333 West Sheridan Ave. Oklahoma City, OK 73102	OGRID: 6137
	Action Number: 581375
	Action Type: [C-141] Reclamation Report C-141 (C-141-v-Reclamation)

CONDITIONS

Created By	Condition	Condition Date
nvelez	Reclamation report approved. Pending re-vegetation report.	6/17/2026
